New Modesto Courthouse - Master - Baseline Development

MILESTONES & SUMMARY

Activity ID	Activity Name	Original Duration	Start	Finish
A2075	AGENCY APPROVALS/PERMITS	85	17-Dec-18 A	26-Mar-21
A2395	BIDDING BUILDING TRADES	0	09-Jun-21	
A1770	NTP/START CONSTRUCTION	0		18-Oct-21
A1830	BUILDING CONSTRUCTION	1096	19-Oct-21	18-Oct-24
A1210	SHORING/U/G DEMO/MASS EXCAVATION & BACKFILL/ DE-WATERI	187	09-Nov-21	10-Aug-22
A1230	TOWER FOUNDATION SYSTEM	63	14-Jan-22	15-Apr-22
A1240	F/R/P BASEMENT RETAINING WALLS	74	18-Mar-22	01-Jul-22
A1750	SITE UTILITIES (5' OUTSIDE BUILDING)	8	04-Aug-22	15-Aug-22
A1270	TOWER ERECT / PLUMB / BOLT / WELD STRUCTURAL STEEL	79	22-Aug-22	14-Dec-22
A2135	MAN/MATERIAL HOIST DURATION	220	31-Aug-22	20-Jul-23
A1340	MECHANICAL / STAIR SHAFT BUILDOUT (IN FLOOR TEMPLATES)	286	08-Nov-22	03-Jan-24
A2145	SALLYPORT & SOUTHWEST STRUCTURES - MECH. BUILDING	125	01-Dec-22	02-Jun-23
MBSTR-1000	FOUNDATIONS AND SOG - MECH. BUILDING	34	01-Dec-22	20-Jan-23
A2155	LOW RISE ERECT / PLUMB / BOLT / WELD STRUCTURAL STEEL	41	12-Dec-22	09-Feb-23
A1290	TOWER ENCLOSURE TO DRY-IN	185	21-Dec-22	19-Sep-23
A1380	TOWER INTERIOR ROUGH-IN - L1	141	30-Dec-22	25-Jul-23
A1390	TOWER INTERIOR ROUGH-IN - L2	139	11-Jan-23	01-Aug-23
A1430	TOWER INTERIOR FINISHES - L1	140	23-Jan-23	11-Aug-23
A1835	TOWER INTERIOR ROUGH-IN - L3	146	31-Jan-23	29-Aug-23
A1985	PENTHOUSE BUILD-OUT	59	07-Feb-23	02-May-23
A1895	TOWER INTERIOR ROUGH-IN - L9	35	07-Feb-23	29-Mar-23
A2205	LOW RISE INTERIOR ROUGH-IN - L1	83	08-Feb-23	08-Jun-23
A2225	LOW RISE INTERIOR ROUGH-IN - L3	153	14-Feb-23	25-Sep-23
A2215	LOW RISE INTERIOR ROUGH-IN - L2	111	15-Feb-23	26-Jul-23
A1840	TOWER INTERIOR ROUGH-IN - L4	141	16-Feb-23	11-Sep-23
A1855	TOWER INTERIOR ROUGH-IN - L5	154	07-Mar-23	13-Oct-23
A2245	LOW RISE INTERIOR FINISHES - L2	184	10-Mar-23	01-Dec-23
A2185	LOW RISE ENCLOSURE TO DRY-IN	120	14-Mar-23	31-Aug-23
A1300	TOWER ROOFING SYSTEM	19	20-Mar-23	13-Apr-23
A1865	TOWER INTERIOR ROUGH-IN - L6	167	22-Mar-23	16-Nov-23
SPSTR-1000	FOUNDATIONS AND SOG - SALLYPORT	23	22-Mar-23	21-Apr-23
A1990	ROOF-TOP EQUIPMENT INSTALLATION	65	29-Mar-23	29-Jun-23
A2195	LOW RISE ROOFING SYSTEM	25	30-Mar-23	03-May-23
A1945	TOWER INTERIOR FINISHES - L9	15	04-Apr-23	24-Apr-23
A1860	TOWER INTERIOR ROUGH-IN - L7	183	06-Apr-23	28-Dec-23
A1420	TOWER INTERIOR FINISHES - BASEMENT	44	11-Apr-23	13-Jun-23
A1310	TOWER TEMPORARY BUILDING DRY-IN	0	14-Apr-23	
A1870	TOWER INTERIOR ROUGH-IN - L8	193	26-Apr-23	02-Feb-24
A2235	LOW RISE INTERIOR FINISHES - L1 TOWER AREA	20	10-May-23	08-Jun-23
A1440	TOWER INTERIOR FINISHES - L2	93	12-May-23	26-Sep-23
A1845	TOWER INTERIOR FINISHES - L3	99	31-May-23	19-Oct-23
A1330	REMAINING ENCLOSURE	40	07-Jul-23	31-Aug-23
A1850	TOWER INTERIOR FINISHES - L4	87	12-Jul-23	13-Nov-23
A1320	TOWER FINAL BUILDING DRY-IN	0		03-Aug-23

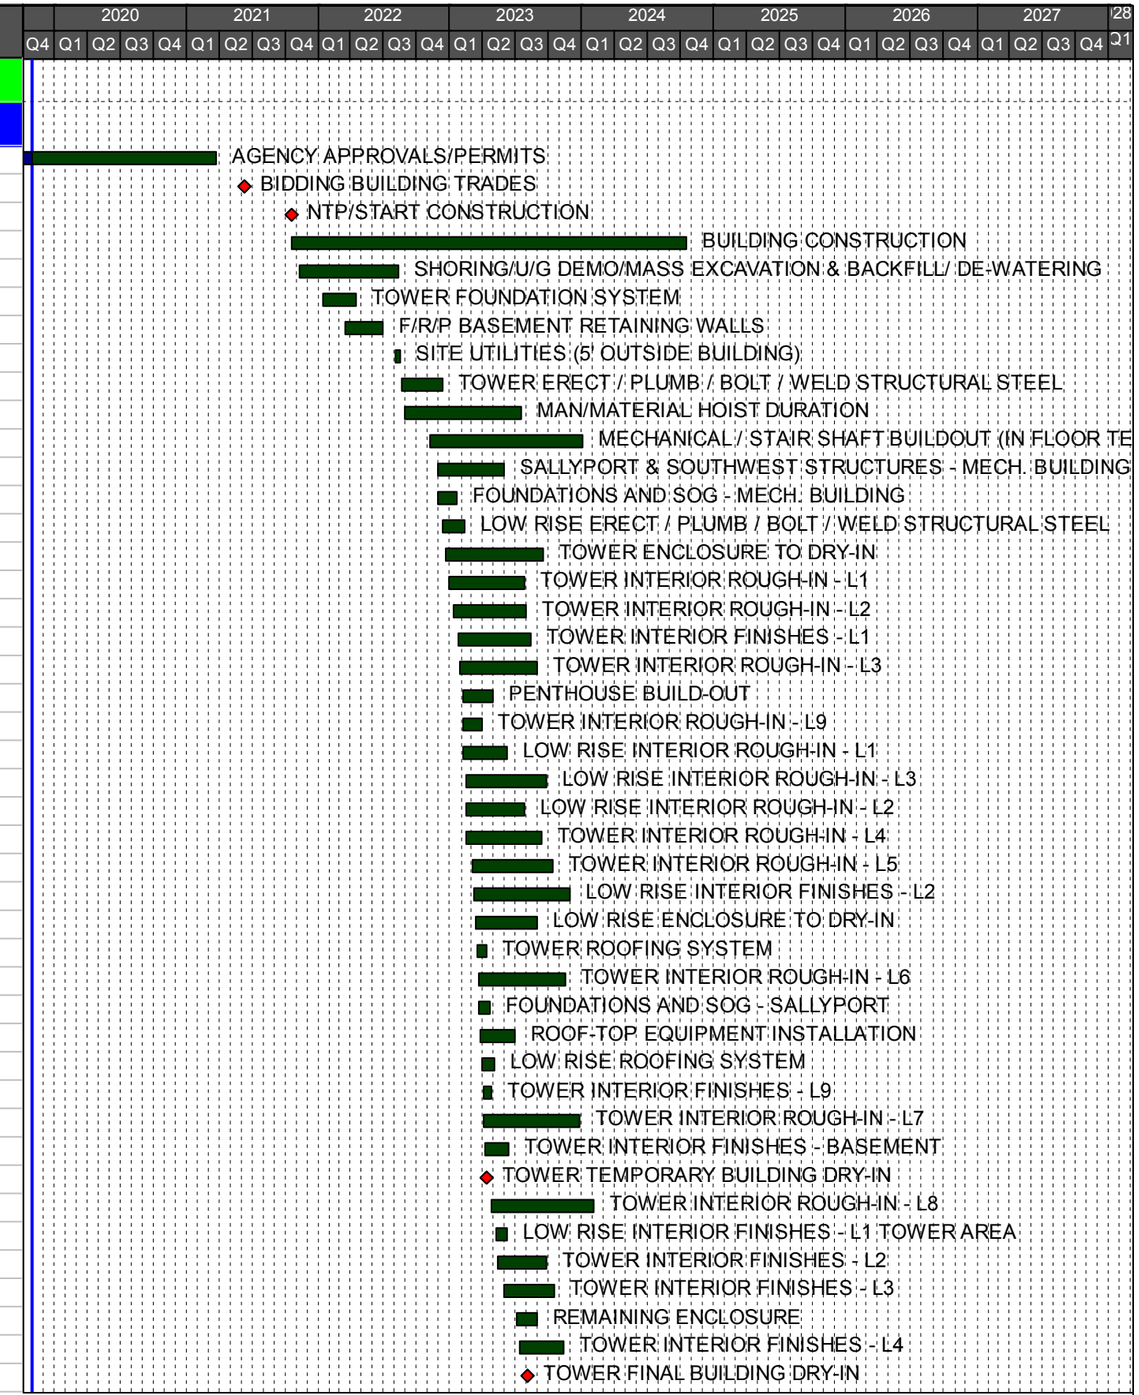

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
A1470	FINISH GRADING / SITE HARDSCAPE	151	04-Aug-23	14-Mar-24
A1490	LANDSCAPING / IRRIGATION	201	04-Aug-23	23-May-24
A1875	TOWER INTERIOR FINISHES - L5	87	10-Aug-23	14-Dec-23
A1885	TOWER INTERIOR FINISHES - L6	108	21-Aug-23	26-Jan-24
A1880	TOWER INTERIOR FINISHES - L7	127	28-Aug-23	04-Mar-24
LRD-110	LOW RISE ENCLOSURE COMPLETE	0		31-Aug-23
LRD-120	LOW RISE DRY-IN	0		31-Aug-23
A1480	FINAL PAVING	125	20-Sep-23	21-Mar-24
A1890	TOWER INTERIOR FINISHES - L8	89	27-Sep-23	05-Feb-24
A2255	LOW RISE INTERIOR FINISHES - L3	55	27-Sep-23	14-Dec-23
A1510	FINAL MCCARTHY COMPLETION LIST & CORRECTIONS	88	07-Dec-23	15-Apr-24
A1520	FINAL A/E PUNCHLIST & CORRECTIONS	78	16-Jan-24	06-May-24
A1500	MEP START-UP TESTING & INSPECTIONS	72	20-Mar-24	01-Jul-24
TAB-1000	ROUGH BALANCE AHU'S - BASEMENT TO LEVEL 4	32	20-Mar-24	02-May-24
TAB-1060	ROUGH BALANCE AHU'S - LEVEL 5 - LEVEL 8	20	03-May-24	03-Jun-24
A2415	BUILDING READY FOR USE	0		18-Oct-24
A1780	FINAL PROJECT COMPLETION (W/ CLOSEOUT)	0		15-Nov-24
PRECONSTRUCTION				
A2305	DESIGN PACKAGE DOF APPROVAL TO BID	45	29-Mar-21	01-Jun-21
A2375	JCC RELEASE MBC FOR PREQUAL	1	29-Mar-21	29-Mar-21
A2315	DESIGN PACKAGE PREQUAL	24	30-Mar-21	30-Apr-21
A2365	DESIGN PACKAGE ADVERTISEMENT	10	02-Jun-21	15-Jun-21
A2465	MBC PREPARE TO BID/GMP	5	02-Jun-21	08-Jun-21
A3420	DESIGN PACKAGE BID/GMP	48	09-Jun-21	16-Aug-21
A2325	DESIGN PACKAGE GMP NEGOTIATION	10	17-Aug-21	30-Aug-21
A2495	DOF/ JCC APPROVAL OF GMP	10	24-Aug-21	06-Sep-21
A2345	DESIGN PACKAGE ESTABLISH GMP & PROCESS CONTRACT AMEI	10	07-Sep-21	20-Sep-21
A3440	ISSUE & EXECUTE SUBCONTRACTS/ OCIP ENROLLMENT - BP 1	20	21-Sep-21	18-Oct-21
A3450	ISSUE & EXECUTE SUBCONTRACTS/ OCIP ENROLLMENT - BP 2	20	28-Sep-21	25-Oct-21
A3460	ISSUE & EXECUTE SUBCONTRACTS/ OCIP ENROLLMENT - BP 3	20	05-Oct-21	01-Nov-21
A2335	CONSTRUCTION PHASE NTP	0		18-Oct-21
AGENCY APPROVALS				
A2405	OSFM AGENCY REVIEW / APPROVAL	40	18-Oct-19 A	26-Mar-21
PROCUREMENT				
A1450	SHORING PART A/ PART B AGREEMENT	10	08-Mar-21	19-Mar-21
A1110	SHORING DESIGN	25	22-Mar-21	23-Apr-21
A1150	SHORING DESIGN SUBMIT/ REVIEW / APPROVAL (CALTRANS)	25	26-Apr-21	01-Jun-21
A1160	SHORING PROCUREMENT	30	31-Aug-21	11-Oct-21
A3430	REVIEW & AWARD SUBCONTRACTS	30	21-Sep-21	01-Nov-21
A1120	STRUCTURAL STEEL MILL ORDER / PROCUREMENT	65	19-Oct-21	24-Jan-22
A1130	STRUCTURAL STEEL SHOP DRAWINGS REVIEW / APPROVAL	65	19-Oct-21	24-Jan-22
A1140	EXTERIOR ENCLOSURE SHOP DRAWINGS / APPROVAL	70	19-Oct-21	31-Jan-22
A1400	ELEVATOR SUBMITTAL PREP AND APPROVAL	70	02-Nov-21	14-Feb-22
A2095	REBAR PROCUREMENT	30	23-Nov-21	07-Jan-22
A2485	PROCUREMENT	530	02-Dec-21	19-Jan-24

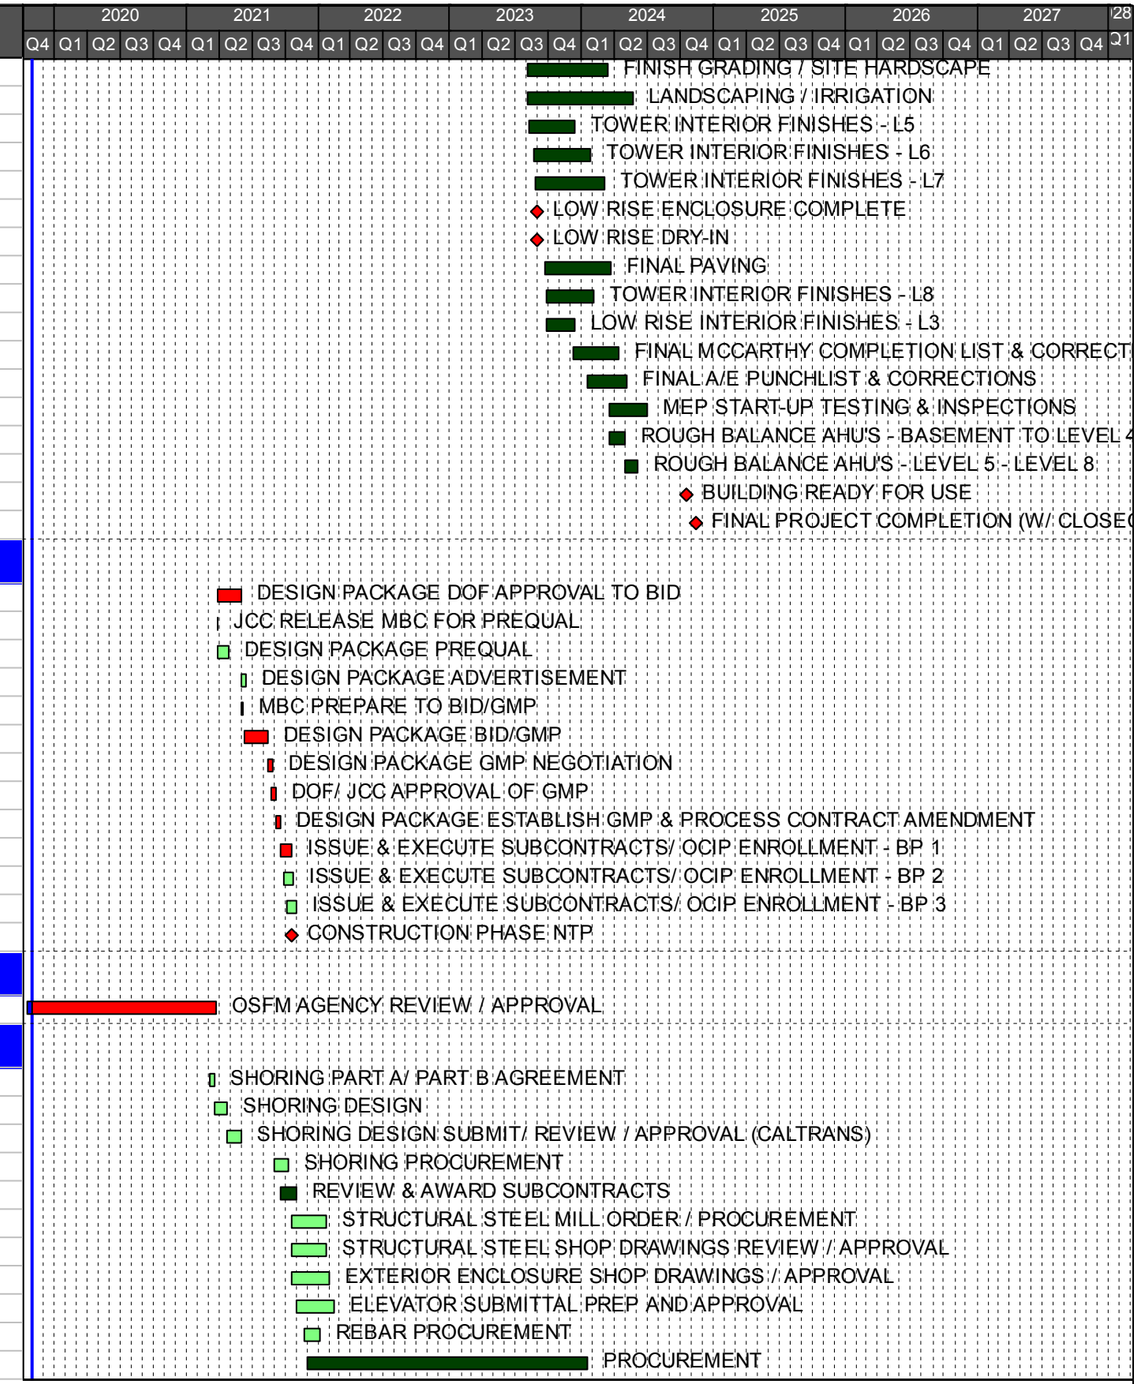

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
A1170	STRUCTURAL STEEL FABRICATION	80	25-Jan-22	18-May-22
A1180	EXTERIOR ENCLOSURE ENGINEERING	50	01-Feb-22	13-Apr-22
A1190	EXTERIOR ENCLOSURE PROCUREMENT / FABRICATION	120	01-Feb-22	25-Jul-22
A1410	ELEVATOR EQUIPMENT PROCUREMENT	80	15-Feb-22	10-Jun-22
SUBMITTALS				
COORDINATION				
COOR-1000	MEP COORDINATION - UNDERGROUND / MATT	10	19-Oct-21	01-Nov-21
COOR-1010	MEP COORDINATION - BASEMENT	20	02-Nov-21	01-Dec-21
COOR-1020	MEP COORDINATION - LEVEL 1	30	02-Dec-21	14-Jan-22
COOR-1030	MEP COORDINATION - LEVEL 2	30	18-Jan-22	02-Mar-22
COOR-1040	MEP COORDINATION - LEVEL 3	30	03-Mar-22	13-Apr-22
COOR-1050	MEP COORDINATION - LEVEL 4	20	14-Apr-22	11-May-22
COOR-1060	MEP COORDINATION - LEVEL 5	20	12-May-22	10-Jun-22
COOR-1070	MEP COORDINATION - LEVEL 6	20	26-May-22	24-Jun-22
COOR-1080	MEP COORDINATION - LEVEL 7	20	13-Jun-22	11-Jul-22
COOR-1090	MEP COORDINATION - LEVEL 8	20	27-Jun-22	25-Jul-22
COOR-1100	MEP COORDINATION - MECH LEVELS	20	12-Jul-22	08-Aug-22
CONSTRUCTION				
MOCK-UPS				
EXTERIOR SKIN SYSTEM				
STEEL AND DECKS				
EXTERIOR FRAMING				
MOCKS-100	FRAMING - EXTERIOR MOCKUP	1	29-Apr-22	29-Apr-22
MOCKS-110	PLUMB/BOLT/WELD - EXTERIOR MOCKUP	5	02-May-22	06-May-22
SLAB ON METAL DECK				
MOCKS-120	MEP ROUGH/DECK/PLACE - EXTERIOR MOCKUP	4	09-May-22	12-May-22
PRECAST AND GLAZING				
MOCKS-130	ERECT PRECAST - EXTERIOR MOCKUP	5	13-May-22	19-May-22
MOCKS-140	ALIGN/WELD PRECAST - EXTERIOR MOCKUP	3	18-May-22	20-May-22
MOCKS-160	INSTALL GLAZING - EXTERIOR MOCKUP	2	24-May-22	25-May-22
CURTAINWALL				
MOCKS-150	CURTAINWALL - EXTERIOR MOCKUP	3	23-May-22	25-May-22
ROOF				
MOCKS-170	INSTALL MISC METALS - EXTERIOR MOCKUP	1	26-May-22	26-May-22
MOCKS-180	APPLY ROOFING MEMBRANE - EXTERIOR MOCKUP	2	31-May-22	01-Jun-22
MOCKS-190	EXTERIOR MOCKUP TESTING	10	02-Jun-22	15-Jun-22
COURTROOMS				
ROUGH-IN'S AND FINISHES				
TCR1-1220	FRAME PERIMETER WALLS AT COURTROOMS MOCKUP	5	03-Mar-22	09-Mar-22
TCR1-1230	FLOOR LEVEL AT COURTROOMS MOCKUP	3	10-Mar-22	14-Mar-22
TOHC1-150	MECHANICAL ROUGH-IN DROPS AT COURTROOMS MOCKUP	7	15-Mar-22	23-Mar-22
TOHC1-160	PLUMBING ROUGH-IN DROPS AT COURTROOMS MOCKUP	5	17-Mar-22	23-Mar-22
TOHC1-170	ELECTRICAL ROUGH-IN DROPS AT COURTROOMS MOCKUP	6	21-Mar-22	28-Mar-22
TOHC1-180	LOW VOLTAGE ROUGH-IN DROPS AT COURTROOMS MOCKUP	6	21-Mar-22	28-Mar-22

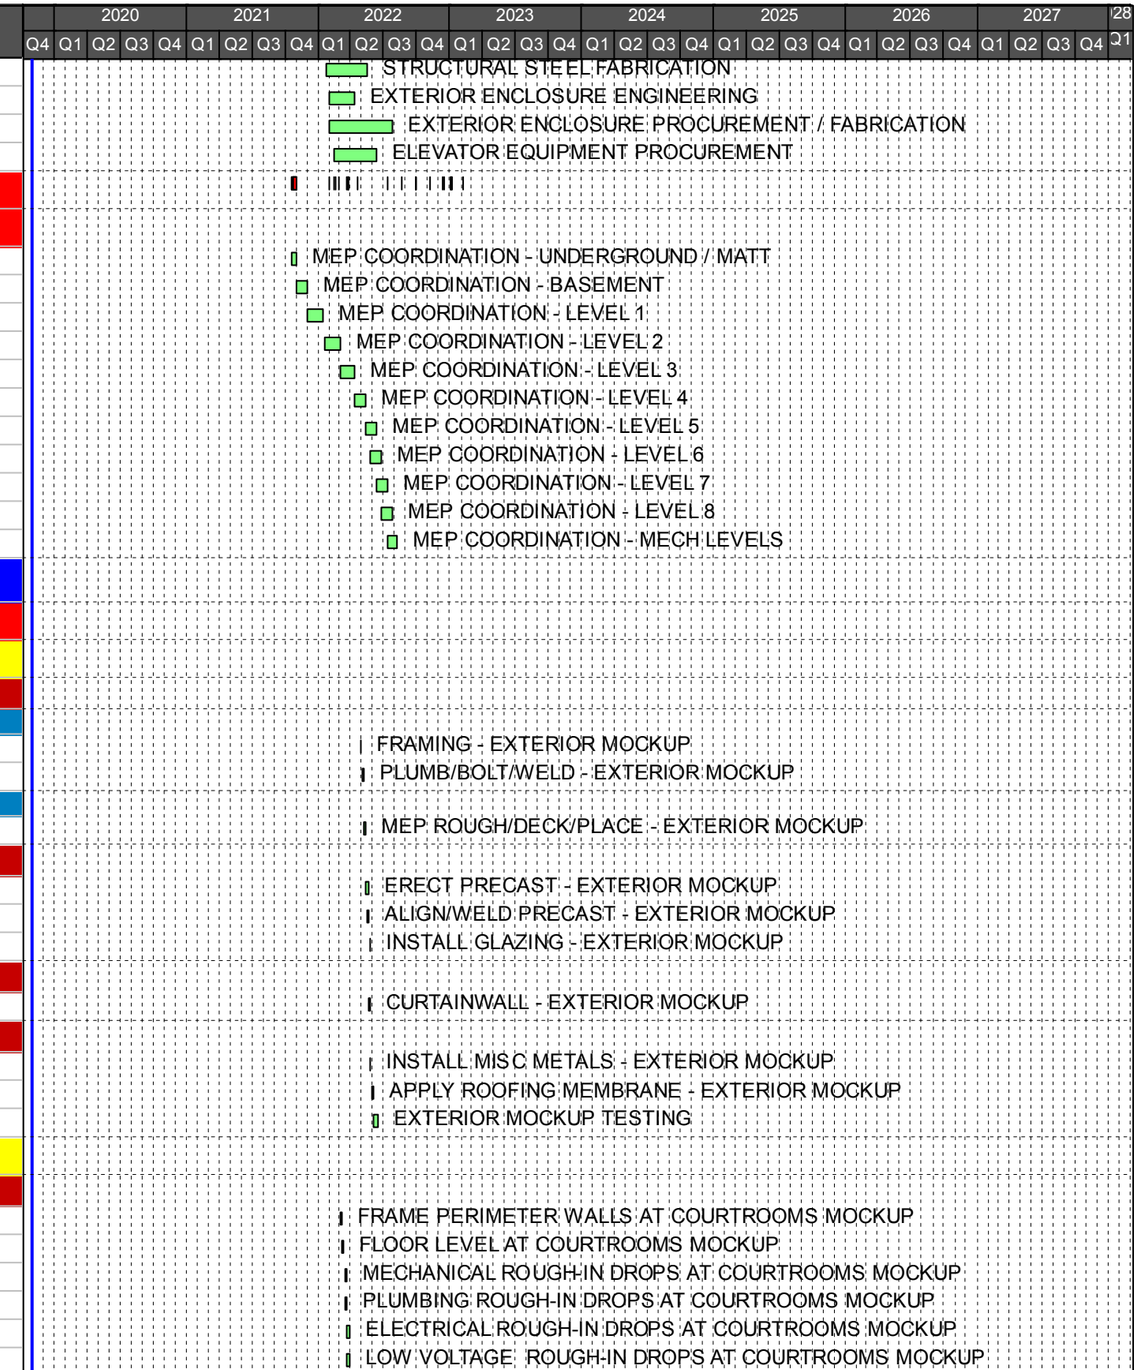

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

Activity ID	Activity Name	Original Duration	Start	Finish
TOHC1-220	INSTALL WALL BACKING AT COURTROOMS MOCKUP	2	29-Mar-22	30-Mar-22
TCR1-1260	FRAME CEILINGS AT COURTROOMS MOCKUP	4	31-Mar-22	05-Apr-22
TCR1-1270	LIGHT FIXTURES PRE-DRYWALL AT COURTROOMS MOCKUP	3	29-Apr-22	03-May-22
TCR1-1240	DRYWALL WALLS AT COURTROOMS MOCKUP	2	04-May-22	05-May-22
TCR1-1250	TAPE WALLS AT COURTROOMS MOCKUP	6	06-May-22	13-May-22
TCR1-1280	DRYWALL/TAPE GYP CEILINGS AT COURTROOMS MOCKUP	6	16-May-22	23-May-22
TCR1-1290	CEILING GRID & DEVICE TILES AT COURTROOMS MOCKUP	3	25-May-22	31-May-22
TCR1-1300	FRAME LOW WALLS AT COURTROOMS MOCKUP	3	01-Jun-22	03-Jun-22
TCR1-1340	DROP CEILING TILE AT COURTROOMS MOCKUP	2	01-Jun-22	02-Jun-22
TCR1-1320	ACCESS FLOORING LAYOUT AT COURTROOMS MOCKUP	1	06-Jun-22	06-Jun-22
TFINC1-260	INSTALL DOOR FRAMES AT COURTROOMS MOCKUP	3	06-Jun-22	08-Jun-22
TCR1-1310	DRYWALL/TAPE WALLS/CEILINGS AT COURTROOMS MOCKUP	7	09-Jun-22	17-Jun-22
TFINC1-220	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT COURTROOM	3	20-Jun-22	22-Jun-22
TFINC1-230	FLOOR PREP FOR TILE AT COURTROOMS MOCKUP	2	23-Jun-22	24-Jun-22
TFINC1-240	INSTALL FLOOR AND WALL TILE AT COURTROOMS MOCKUP	5	27-Jun-22	01-Jul-22
TCR1-1330	ACCESS FLOORING AT COURTROOMS MOCKUP	3	30-Jun-22	05-Jul-22
TFINC1-250	INSTALL PLUMBING FIXTURES AT COURTROOMS MOCKUP	4	05-Jul-22	08-Jul-22
TCR1-1350	CASEWORK AT COURTROOMS MOCKUP	10	08-Jul-22	21-Jul-22
TCR1-1360	INSTALL CARPET & BASE AT COURTROOMS MOCKUP	4	25-Jul-22	28-Jul-22
TCR1-1370	DOORS & HARDWARE AT COURTROOMS MOCKUP	10	29-Jul-22	11-Aug-22
TCR1-1380	FABRIC WALL PANELS AT COURTROOMS MOCKUP	3	10-Aug-22	12-Aug-22
TCR1-1400	MECHANICAL COMPLETE CEILING CONNECTIONS AT COURTROO	2	11-Aug-22	12-Aug-22
TFINC1-270	ELECTRICAL COMPLETE CEILING CONNECTIONS AT COURTROOM	2	11-Aug-22	12-Aug-22
TFINC1-280	PLUMBING COMPLETE CEILING CONNECTIONS AT COURTROOMS	2	11-Aug-22	12-Aug-22
TFINC1-290	LOW VOLTAGE TRIM AT COURTROOMS MOCKUP	2	11-Aug-22	12-Aug-22
TFINC1-300	FIRE SUPPRESSION COMPLETE CEILING CONNECTIONS AT COU	2	11-Aug-22	12-Aug-22
TCR1-1390	FF & E AT COURTROOMS MOCKUP	4	15-Aug-22	18-Aug-22
TCR1-1410	CLOSE-UP CASEWORK MEP ACCESSORIES MOCKUP	2	19-Aug-22	22-Aug-22
TCR1-1420	COURTROOM MOCKUP INCOMPLETE LIST	5	23-Aug-22	29-Aug-22
A5850	JCC COURTROOM MOCKUP APPROVAL	10	30-Aug-22	14-Sep-22
SUBSTRUCTURE				
EARLY SITE WORK				
TOWER AND LOW-RISE				
MOBILIZATION				
A2455	MOBILIZATION	10	19-Oct-21	01-Nov-21
MR-1000	SAFE OFF UTILITIES	3	28-Oct-21	01-Nov-21
A1200	SITE CLEARING / DEMO FOR SHORING	5	02-Nov-21	08-Nov-21
EARTHWORK				
MR-1010	SHORING	25	09-Nov-21	15-Dec-21
MR-1020	U/G DEMO	10	08-Dec-21	21-Dec-21
MR-1030	MASS EXCAVATION & PIT EXCAVATION	15	22-Dec-21	13-Jan-22
A1250	BACKFILL RETAINING WALLS	10	14-Jul-22	27-Jul-22
MR-1040	REMOVE SHORING	10	28-Jul-22	10-Aug-22
UTIL-1090	ROUGH GRADE SITE	7	11-Aug-22	19-Aug-22
UNDERGROUND UTILITIES				
UTIL-1000	INSTALL SANITARY SEWER	4	04-Aug-22	09-Aug-22

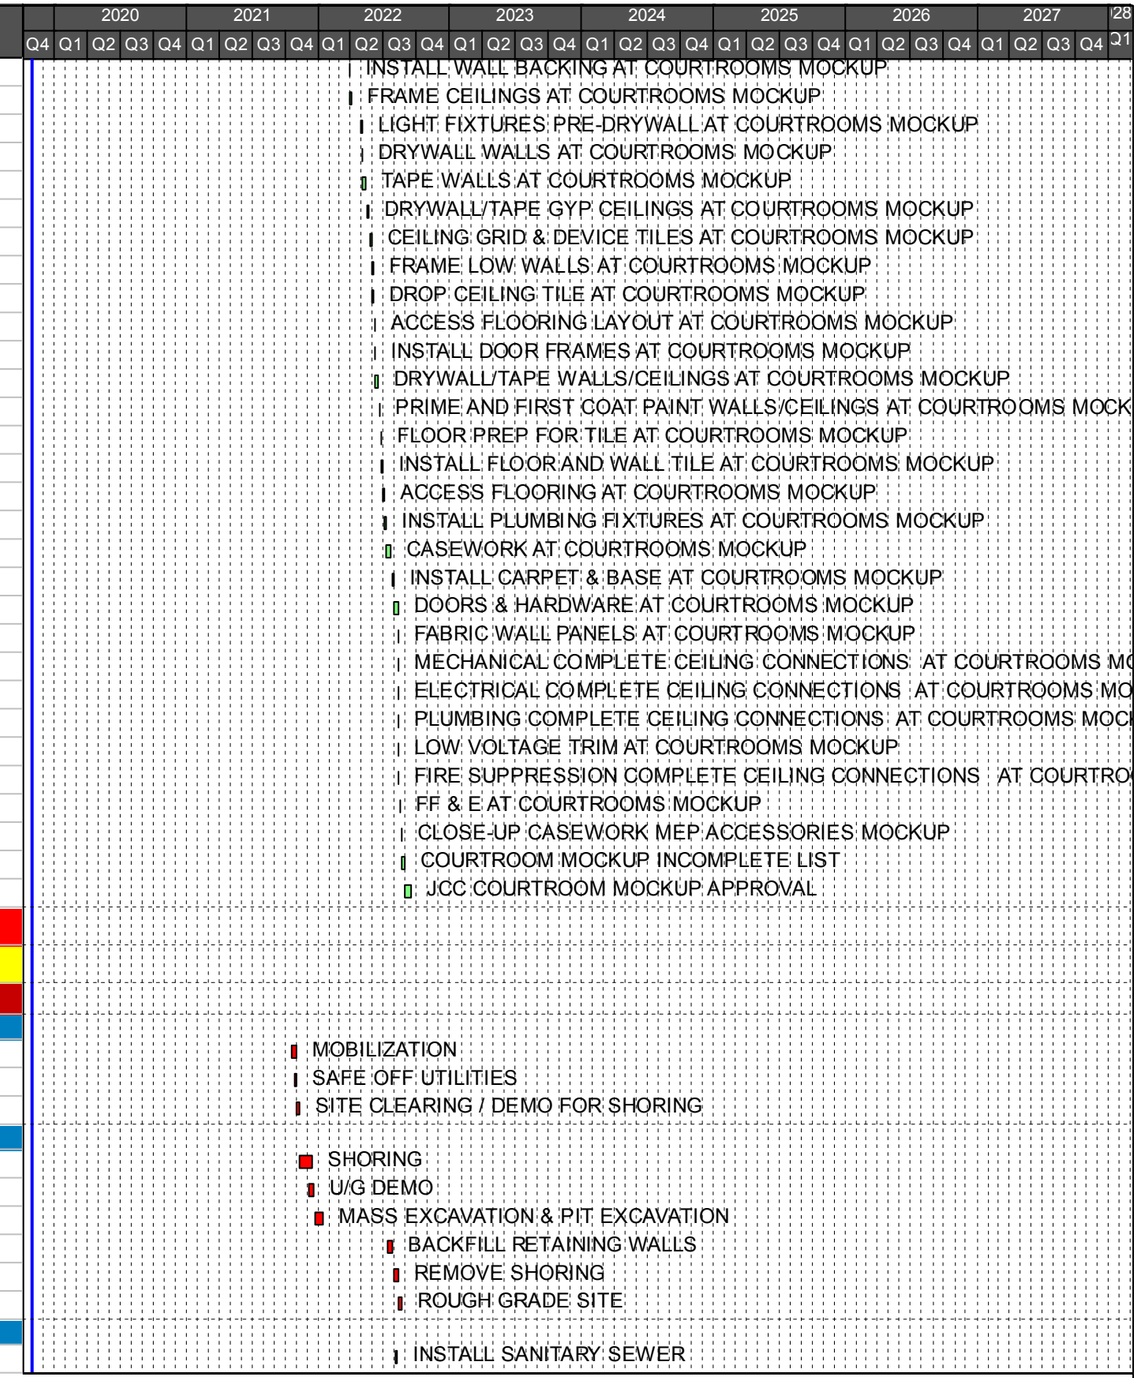

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
UTIL-1030	INSTALL DOMESTIC WATER SERVICE	4	04-Aug-22	09-Aug-22
UTIL-1040	INSTALL IRRIGATION SERVICE	4	04-Aug-22	09-Aug-22
UTIL-1050	INSTALL FIRE WATER SERVICE	4	10-Aug-22	15-Aug-22
UTIL-1100	INSTALL NATURAL GAS SERVICE	4	10-Aug-22	15-Aug-22
UTIL-1010	INSTALL STORM DRAIN SYSTEM WEST/ SOUTH	13	11-Aug-22	29-Aug-22
A5860	NATURAL GAS TERMINATES TO BUILDING	2	16-Aug-22	17-Aug-22
UTIL-1110	SITE FIRE WATER SERVICE INSPECTION	1	16-Aug-22	16-Aug-22
UTIL-1020	SITE UNDERGROUND ELECTRICAL UTILITIES.	7	25-Aug-22	06-Sep-22
UTIL-1070	STORM DRAINS TERMINATE TO BUILDING	2	30-Aug-22	31-Aug-22
UTIL-1080	DOMESTIC WATER TERMINATES TO BUILDING	2	01-Sep-22	06-Sep-22
A1730	FIRE WATER TERMINATE TO BUILDING	2	01-Sep-22	06-Sep-22
TOWER				
BASEMENT				
FOUNDATION AND MAT SLAB				
MUD SLAB & PROTECTION SLAB				
A1220	TOWER UNDER SLAB UTILITIES	10	14-Jan-22	28-Jan-22
A1460	PRE - POUR INSPECTION MUD SLAB	1	28-Jan-22	28-Jan-22
TFND-1000	POUR - MUD SLAB	2	31-Jan-22	01-Feb-22
TFND-1010	INSTALL BELOW GRADE WATERPROOFING	10	02-Feb-22	15-Feb-22
TFND-1020	PLACE PROTECTION SLAB	2	16-Feb-22	17-Feb-22
FOUNDATION POUR 1 & 2				
TFND-1030	POUR 1 - REBAR PITS & WALLS	3	22-Feb-22	24-Feb-22
TFND-1040	POUR 2 - REBAR MAT FOUNDATION ZONE1	7	22-Feb-22	02-Mar-22
TFND-1050	POUR 2 - REBAR MAT FOUNDATION ZONE 2	7	24-Feb-22	04-Mar-22
TFND-2320	POUR 1 - PRE - POUR INSPECTION PITS	1	24-Feb-22	24-Feb-22
TFND-1060	POUR 1 - POUR & CURE	3	25-Feb-22	01-Mar-22
TFND-1080	POUR 2 - REBAR MAT FOUNDATION ZONE 3	7	28-Feb-22	08-Mar-22
TFND-1090	POUR 2 - POUR & CURE	3	09-Mar-22	11-Mar-22
FOUNDATION POUR 3				
TFND-1070	POUR 3 - SINGLE SIDE WALL FORMS IN PITS (MAT SLAB POUR 1)	7	02-Mar-22	10-Mar-22
TFND-1100	POUR 3 - INSTALL AB TEMPLATES (MAT SLAB POUR 1)	4	07-Mar-22	10-Mar-22
TFND-1110	POUR 3 - FORM - CJS, WALLS, & COLUMN FORMS (MAT SLAB POU	4	08-Mar-22	11-Mar-22
TFND-2330	POUR 3 - PRE - POUR INSPECTION EJECTOR PIT/ MAT SLAB	1	11-Mar-22	11-Mar-22
TFND-1130	POUR 3 - EJECTOR PIT/ (MAT SLAB POUR 1)	1	14-Mar-22	14-Mar-22
TFND-1150	POUR 3 - EJECTOR PIT/ MAT SLAB POUR 1 CURE	3	15-Mar-22	17-Mar-22
FOUNDATION POUR 4				
A2425	POUR 4- FOUNDATION SYSTEM (MAT FOUNDATION POUR 2)	7	11-Mar-22	21-Mar-22
TFND-1120	POUR 4- INSTALL AB TEMPLATES (MAT FOUNDATION POUR 2)	4	11-Mar-22	16-Mar-22
TFND-1140	POUR 4- FORM CJS, WALLS, & COLUMN FORMS (MAT FOUNDATIOI	4	14-Mar-22	17-Mar-22
TFND-2340	POUR 4- PRE - POUR INSPECTION (MAT FOUNDATION POUR 2)	1	17-Mar-22	17-Mar-22
TFND-1170	POUR 4- MAT FOUNDATION POUR 2	1	18-Mar-22	18-Mar-22
TFND-1210	POUR 4- MAT FOUNDATION POUR 2 CURE	3	19-Mar-22	21-Mar-22
FOUNDATION POUR 5				
TFND-1160	POUR 5 - INSTALL AB TEMPLATES	4	17-Mar-22	22-Mar-22
TFND-1180	POUR 5 - FORM CJS, WALLS, & COLUMN FORMS	4	18-Mar-22	23-Mar-22
TFND-2350	POUR 5 - PRE - POUR INSPECTION POUR 3 - MAT SLAB	1	23-Mar-22	23-Mar-22
TFND-1250	POUR 5 - POUR MAT SLAB POUR 3	1	24-Mar-22	24-Mar-22

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TFND-1290	POUR 5 - MAT SLAB CURE	3	25-Mar-22	27-Mar-22
FOUNDATION POUR 6				
TFND-1220	POUR 6 - INSTALL AB TEMPLATE	4	23-Mar-22	28-Mar-22
TFND-1260	POUR 6 - FORM - CJS, WALLS, & COLUMN FORMS FOR POUR 4	4	24-Mar-22	29-Mar-22
TFND-2360	POUR 6 - PRE - POUR INSPECTION POUR 4 - MAT SLAB	1	29-Mar-22	29-Mar-22
TFND-1420	POUR 6 - POUR MAT SLAB POUR 4	1	30-Mar-22	30-Mar-22
TFND-1460	POUR 6 - MAT SLAB CURE	3	31-Mar-22	02-Apr-22
FOUNDATION POUR 7				
TFND-1410	POUR 7 - INSTALL AB TEMPLATES	4	29-Mar-22	01-Apr-22
TFND-1430	POUR 7 - FORM - CJS, WALLS, & COLUMN FORMS	4	30-Mar-22	04-Apr-22
TFND-2370	POUR 7 - PRE - POUR INSPECTION POUR 5 - MAT SLAB	1	04-Apr-22	04-Apr-22
TFND-1550	POUR 7 - POUR MAT SLAB 5	1	05-Apr-22	05-Apr-22
TFND-1470	POUR 7 - MAT SLAB CURE	3	06-Apr-22	08-Apr-22
FOUNDATION POUR 8				
TFND-1520	POUR 8 - INSTALL AB TEMPLATES FOR POUR 6	4	04-Apr-22	07-Apr-22
TFND-1560	POUR 8 - FORM - CJS,WALLS, & COLUMN FORMS FOR POUR 6	4	05-Apr-22	08-Apr-22
TFND-2380	POUR 8 - PRE - POUR INSPECTION POUR 6 - MAT SLAB	1	11-Apr-22	11-Apr-22
TFND-1590	POUR 8 - POUR MAT SLAB 6	1	12-Apr-22	12-Apr-22
TFND-1600	POUR 8 - MAT SLAB CURE	3	13-Apr-22	15-Apr-22
RAMPS AND WALLS				
WALL POUR 1				
TFND-1190	SINGLE SIDE WALL FORM - ZONE 1 WEST WALL	3	18-Mar-22	22-Mar-22
TFND-1230	REBAR - ZONE 1 WEST WALL	3	23-Mar-22	25-Mar-22
TFND-1270	INSTALL EMBEDS - ZONE 1 WEST WALL	3	25-Mar-22	29-Mar-22
TFND-1300	INSTALL MECHANICAL EMBEDS - ZONE 1 WEST WALL	3	25-Mar-22	29-Mar-22
TFND-1310	INSTALL ELECTRICAL EMBEDS - ZONE 1 WEST WALL	3	25-Mar-22	29-Mar-22
TFND-1320	INSTALL PLUMBING EMBEDS - ZONE 1 WEST WALL	3	25-Mar-22	29-Mar-22
TFND-1330	INSTALL FIRE PROTECTION EMBEDS - ZONE 1 WEST WALL	3	25-Mar-22	29-Mar-22
TFND-1350	MECHANICAL INSERTS - ZONE 1 WEST WALL	2	28-Mar-22	29-Mar-22
TFND-1360	ELECTRICAL INSERTS - ZONE 1 WEST WALL	2	28-Mar-22	29-Mar-22
TFND-1370	PLUMBING INSERTS - ZONE 1 WEST WALL	2	28-Mar-22	29-Mar-22
TFND-1380	FIRE PROTECTION INSERTS - ZONE 1 WEST WALL	2	28-Mar-22	29-Mar-22
TFND-1440	SECOND SIDE WALL FORM - ZONE 1 WEST WALL	3	30-Mar-22	01-Apr-22
TFND-1500	PRE - POUR INSPECTION ZONE 1 WEST WALL	0		01-Apr-22
TFND-1530	POUR - ZONE 1 WEST WALL	1	04-Apr-22	04-Apr-22
TFND-1570	CURE - ZONE 1 WEST WALL	7	05-Apr-22	11-Apr-22
TFND-1610	STRIP WALL FORM - ZONE 1 WEST WALL	2	12-Apr-22	13-Apr-22
WALL POUR 2				
TFND-1200	SINGLE SIDE WALL FORM - ZONE 1 NORTH WALL	3	18-Mar-22	22-Mar-22
TFND-1240	REBAR - ZONE 1 NORTH WALL	3	23-Mar-22	25-Mar-22
TFND-1280	INSTALL EMBEDS - ZONE 1 NORTH WALL	3	25-Mar-22	29-Mar-22
TFND-1340	MECHANICAL INSERTS - POUR 2 ZONE 1 NORTH WALL	2	28-Mar-22	29-Mar-22
TFND-1390	ELECTRICAL INSERTS - POUR 2 ZONE 1 NORTH WALL	2	28-Mar-22	29-Mar-22
TFND-1400	PLUMBING INSERTS - POUR 2 ZONE 1 NORTH WALL	2	28-Mar-22	29-Mar-22
TFND-1450	SECOND SIDE WALL FORM - ZONE 1 NORTH WALL	3	30-Mar-22	01-Apr-22
TFND-1510	PRE - POUR INSPECTION ZONE 1 NORTH WALL	0		01-Apr-22
TFND-1540	POUR - ZONE 1 NORTH WALL	1	04-Apr-22	04-Apr-22
TFND-1580	CURE - ZONE 1 NORTH WALL	7	05-Apr-22	11-Apr-22

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development

PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19

Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TFND-1620	STRIP WALL FORM - ZONE 1 NORTH WALL	2	12-Apr-22	13-Apr-22
WALL POUR 3				
TFND-1630	SINGLE SIDE WALL FORM - ZONE 1 EAST WALL	3	14-Apr-22	18-Apr-22
TFND-1650	REBAR - ZONE 1 EAST WALL	3	19-Apr-22	21-Apr-22
TFND-1670	INSTALL EMBEDS - ZONE 1 EAST WALL	3	21-Apr-22	25-Apr-22
TFND-1690	MECHANICAL INSERTS - POUR 3 EAST WALL	2	22-Apr-22	25-Apr-22
TFND-1710	ELECTRICAL INSERTS - POUR 3 EAST WALL	2	22-Apr-22	25-Apr-22
TFND-1720	PLUMBING INSERTS - POUR 3 EAST WALL	2	22-Apr-22	25-Apr-22
TFND-1750	SECOND SIDE WALL FORM - ZONE 1 EAST WALL	3	26-Apr-22	28-Apr-22
TFND-1770	PRE - POUR INSPECTION ZONE 1 EAST WALL	0		28-Apr-22
TFND-1790	POUR - ZONE 1 EAST WALL	1	29-Apr-22	29-Apr-22
TFND-1810	CURE - ZONE 1 EAST WALL	7	30-Apr-22	06-May-22
TFND-1830	STRIP WALL FORM - ZONE 1 EAST WALL	2	09-May-22	10-May-22
WALL POUR 4				
TFND-1640	SINGLE SIDE WALL FORM - ZONE 2 EAST WALL	3	14-Apr-22	18-Apr-22
TFND-1660	REBAR - ZONE 2 EAST WALL	3	19-Apr-22	21-Apr-22
TFND-1680	INSTALL EMBEDS - ZONE 2 EAST WALL	3	21-Apr-22	25-Apr-22
TFND-1700	MECHANICAL INSERTS - POUR 4 EAST WALL	2	22-Apr-22	25-Apr-22
TFND-1730	ELECTRICAL INSERTS - POUR 4 EAST WALL	2	22-Apr-22	25-Apr-22
TFND-1740	PLUMBING INSERTS - POUR 4 EAST WALL	2	22-Apr-22	25-Apr-22
TFND-1760	SECOND SIDE WALL FORM - ZONE 2 EAST WALL	3	26-Apr-22	28-Apr-22
TFND-1780	PRE - POUR INSPECTION ZONE 2 EAST WALL	0		28-Apr-22
TFND-1800	POUR - ZONE 2 EAST WALL	1	29-Apr-22	29-Apr-22
TFND-1820	CURE - ZONE 2 EAST WALL	7	30-Apr-22	06-May-22
TFND-1840	STRIP WALL FORM - ZONE 2 EAST WALL	2	09-May-22	10-May-22
WALL POUR 5				
TFND-1850	SINGLE SIDE WALL FORM - ZONE 3 EAST WALL	3	11-May-22	13-May-22
TFND-1870	REBAR - ZONE 3 EAST WALL	3	16-May-22	18-May-22
TFND-1890	INSTALL EMBEDS - ZONE 3 EAST WALL	3	18-May-22	20-May-22
TFND-1910	MECHANICAL INSERTS - POUR 5 ZONE 3 EAST WALL	2	19-May-22	20-May-22
TFND-1930	ELECTRICAL INSERTS - POUR 5 ZONE 3 EAST WALL	2	19-May-22	20-May-22
TFND-1940	PLUMBING INSERTS - POUR 5 ZONE 3 EAST WALL	2	19-May-22	20-May-22
TFND-1970	SECOND SIDE WALL FORM - ZONE 3 EAST WALL	3	23-May-22	25-May-22
TFND-1990	PRE - POUR INSPECTION ZONE 3 EAST WALL	0		25-May-22
TFND-2010	POUR - ZONE 3 EAST WALL	1	26-May-22	26-May-22
TFND-2030	CURE - ZONE 3 EAST WALL	7	27-May-22	02-Jun-22
TFND-2050	STRIP WALL FORM - ZONE 3 EAST WALL	2	03-Jun-22	06-Jun-22
WALL POUR 6				
TFND-1860	SINGLE SIDE WALL FORM - ZONE 3 SOUTH WALL	3	11-May-22	13-May-22
TFND-1880	REBAR - ZONE 3 SOUTH WALL	3	16-May-22	18-May-22
TFND-1900	INSTALL EMBEDS - ZONE 3 SOUTH WALL	3	18-May-22	20-May-22
TFND-1920	MECHANICAL INSERTS - POUR 6 ZONE 3 SOUTH WALL	2	19-May-22	20-May-22
TFND-1950	ELECTRICAL INSERTS - POUR 6 ZONE 3 SOUTH WALL	2	19-May-22	20-May-22
TFND-1960	PLUMBING INSERTS - POUR 6 ZONE 3 SOUTH WALL	2	19-May-22	20-May-22
TFND-1980	SECOND SIDE WALL FORM - ZONE 3 SOUTH WALL	3	23-May-22	25-May-22
TFND-2000	PRE - POUR INSPECTION ZONE 3 SOUTH WALL	0		25-May-22
TFND-2020	POUR - ZONE 3 SOUTH WALL	1	26-May-22	26-May-22

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

Activity ID	Activity Name	Original Duration	Start	Finish
TFND-2040	CURE - ZONE 3 SOUTH WALL	7	27-May-22	02-Jun-22
TFND-2060	STRIP WALL FORM - ZONE 3 SOUTH WALL	2	03-Jun-22	06-Jun-22
WALL POUR 7				
TFND-2070	SINGLE SIDE WALL FORM - ZONE 3 SOUTH WALL	3	07-Jun-22	09-Jun-22
TFND-2090	REBAR - ZONE 3 SOUTH WALL	3	10-Jun-22	14-Jun-22
TFND-2110	INSTALL EMBEDS - ZONE 3 SOUTH WALL	3	14-Jun-22	16-Jun-22
TFND-2130	MECHANICAL INSERTS - POUR 7 ZONE 3 SOUTH WALL	2	15-Jun-22	16-Jun-22
TFND-2150	ELECTRICAL INSERTS - POUR 7 ZONE 3 SOUTH WALL	2	15-Jun-22	16-Jun-22
TFND-2160	PLUMBING INSERTS - POUR 7 ZONE 3 SOUTH WALL	2	15-Jun-22	16-Jun-22
TFND-2190	SECOND SIDE WALL FORM - ZONE 3 SOUTH WALL	3	17-Jun-22	21-Jun-22
TFND-2210	PRE - POUR INSPECTION ZONE 3 SOUTH WALL	0		21-Jun-22
TFND-2230	POUR - ZONE 3 SOUTH WALL	1	22-Jun-22	22-Jun-22
TFND-2250	CURE - ZONE 3 SOUTH WALL	7	23-Jun-22	29-Jun-22
TFND-2280	STRIP WALL FORM - ZONE 3 SOUTH WALL	2	30-Jun-22	01-Jul-22
WALL POUR 8				
TFND-2080	SINGLE SIDE WALL FORM - ZONE 2/3 WEST WALL	3	07-Jun-22	09-Jun-22
TFND-2100	REBAR - ZONE 2/3 WEST WALL	3	10-Jun-22	14-Jun-22
TFND-2120	INSTALL EMBEDS - ZONE 2/3 WEST WALL	3	14-Jun-22	16-Jun-22
TFND-2140	MECHANICAL INSERTS - POUR 8 ZONE 2/3 WEST WALL	2	15-Jun-22	16-Jun-22
TFND-2170	ELECTRICAL INSERTS - POUR 8 ZONE 2/3 WEST WALL	2	15-Jun-22	16-Jun-22
TFND-2180	PLUMBING INSERTS - POUR 8 ZONE 2/3 WEST WALL	2	15-Jun-22	16-Jun-22
TFND-2200	SECOND SIDE WALL FORM - ZONE 2/3 WEST WALL	3	17-Jun-22	21-Jun-22
TFND-2220	PRE - POUR INSPECTION ZONE 2/3 WEST WALL	0		21-Jun-22
TFND-2240	POUR - ZONE 2/3 WEST WALL	1	22-Jun-22	22-Jun-22
TFND-2260	CURE - ZONE 2/3 WEST WALL	7	23-Jun-22	29-Jun-22
TFND-2290	STRIP WALL FORM - ZONE 2/3 WEST WALL	2	30-Jun-22	01-Jul-22
RETAINING WALLS AND SOG				
TFND-2310	INSTALL GRAVEL WRAPPED PERF PIPE	10	29-Jun-22	13-Jul-22
TFND-2270	INSTALL WATERPROOF MEMBRANE RETAINING WALL	10	30-Jun-22	14-Jul-22
TFND-2300	INSTALL FILTER FABRIC & DRAINAGE MAT	5	05-Jul-22	11-Jul-22
LOW-RISE				
LEVEL 1				
A2115	FOUNDATION SYSTEM (LOW RISE COL. A & B)	30	21-Jul-22	31-Aug-22
A2435	FOUNDATION SYSTEM (LOW RISE COL. C) (FOOTINGS & PILASTEI	30	21-Jul-22	31-Aug-22
A5870	EXCAVATE FOUNDATION SYSTEM - LOW RISE L1	5	21-Jul-22	27-Jul-22
A5880	DEEP MEPs FOUNDATION SYSTEM - LOW RISE L1	3	27-Jul-22	29-Jul-22
A5890	INSTALL REBAR FOUNDATION SYSTEM - LOW RISE L1	8	01-Aug-22	10-Aug-22
A5900	INSTALL AB's FOUNDATION SYSTEM - LOW RISE L1	8	05-Aug-22	16-Aug-22
A2445	GRADE BEAMS FOUNDATION SYSTEM - LOW RISE L1	10	11-Aug-22	24-Aug-22
A5910	FORM FOUNDATION SYSTEM - LOW RISE L1	3	17-Aug-22	19-Aug-22
A5940	PRE - POUR INSPECTION - POUR FOUNDATION SYSTEM LOW RISI	1	19-Aug-22	19-Aug-22
A5920	POUR FOUNDATION SYSTEM - LOW RISE L1	2	23-Aug-22	24-Aug-22
LFND-1000	PLUMBING UNDER SLAB UTILITIES - LOW RISE L1	15	25-Aug-22	16-Sep-22
A5930	CURE FOUNDATION SYSTEM - LOW RISE L1	7	25-Aug-22	31-Aug-22
A2755	LOW RISE - ELECTRICAL UNDER SLAB UTILITIES	15	07-Sep-22	27-Sep-22
A2175	LOW RISE FORM SLAB ON GRADE	4	29-Sep-22	04-Oct-22
LFND-1010	VAPOR BARRIER AND BASE ROCK SLAB ON GRADE - LOW RISE L1	2	05-Oct-22	06-Oct-22

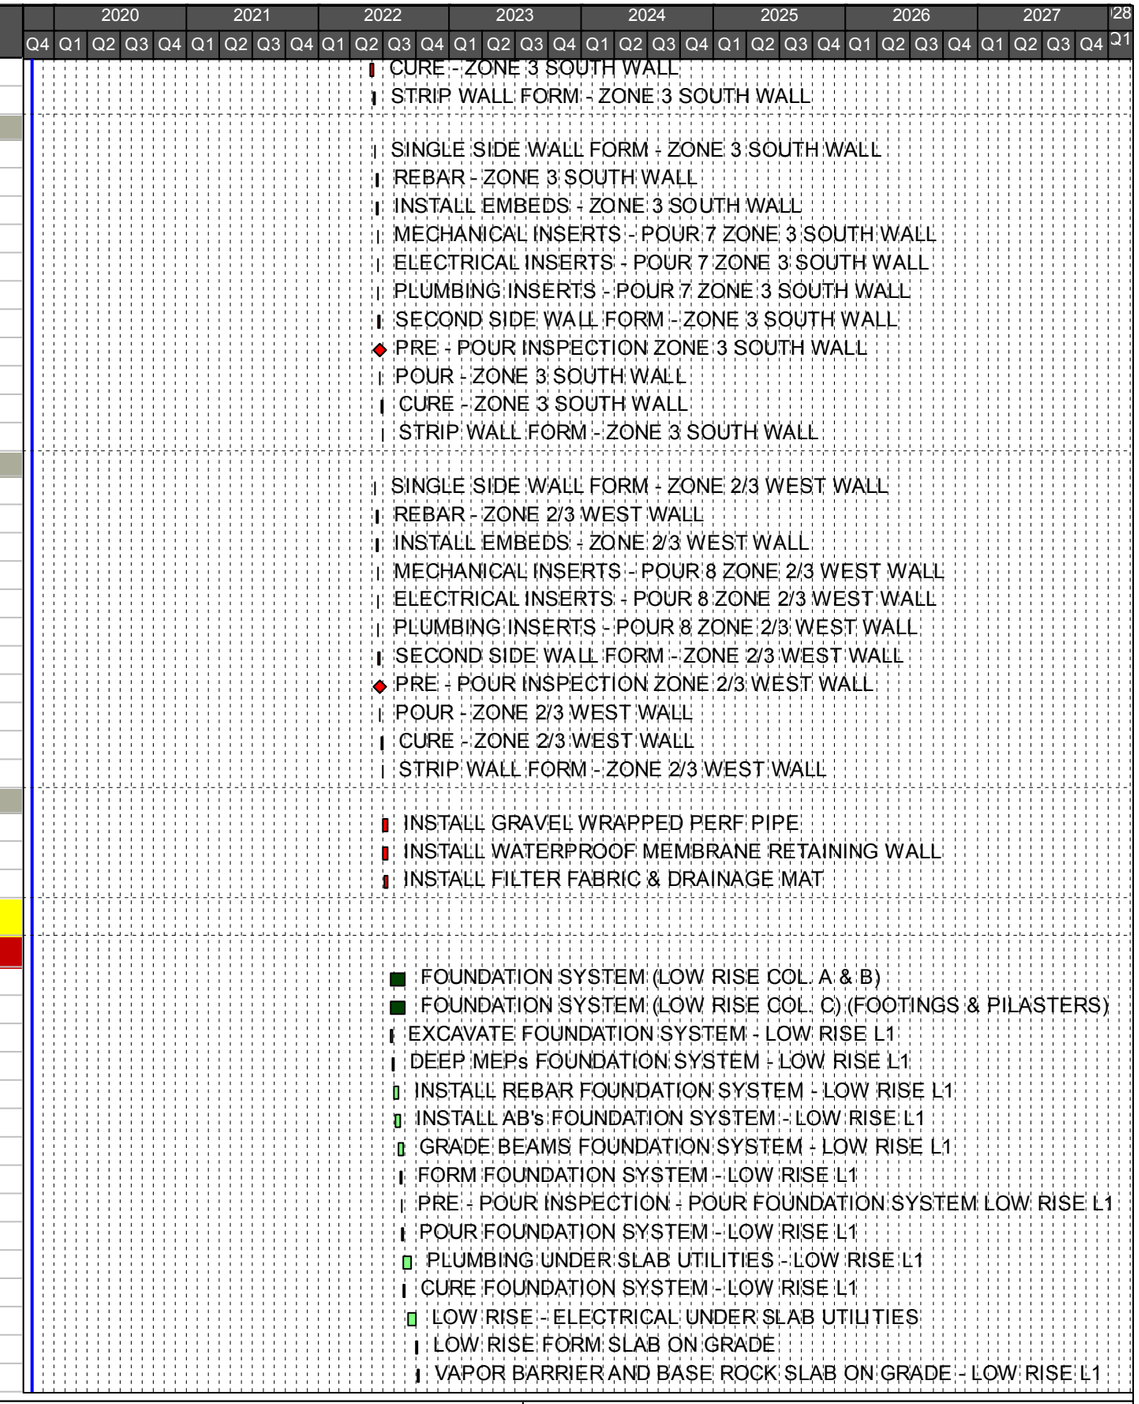

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
LFND-1020	REBAR SLAB ON GRADE - LOW RISE L1	3	07-Oct-22	11-Oct-22
LFND-1050	PRE - POUR INSPECTION SLAB ON GRADE LOW RISE L1	1	11-Oct-22	11-Oct-22
LFND-1030	POUR SLAB ON GRADE - LOW RISE L1	1	12-Oct-22	12-Oct-22
LFND-1040	CURE SLAB ON GRADE - LOW RISE L1	3	13-Oct-22	15-Oct-22
SALLYPORT				
LEVEL 1				
SFND-1000	EXCAVATE FOUNDATIONS - SALLYPORT	3	22-Mar-23	24-Mar-23
SFND-1010	FORM, AND REBAR TEMPLATE FOOTINGS - SOG/FOUNDATIONS - S	5	27-Mar-23	31-Mar-23
SFND-1020	REBAR FOOTINGS & SOG - SOG/FOUNDATIONS - SALLYPORT	6	03-Apr-23	10-Apr-23
SFND-1070	PRE - POUR INSPECTION SOG/FOUNDATIONS - SALLYPORT	1	10-Apr-23	10-Apr-23
SFND-1030	POUR - SOG/FOUNDATIONS - SALLYPORT	1	11-Apr-23	11-Apr-23
SFND-1040	CURE - SOG/FOUNDATIONS - SALLYPORT	3	12-Apr-23	14-Apr-23
SFND-1050	STRIP - SOG/FOUNDATIONS - SALLYPORT	1	17-Apr-23	17-Apr-23
SFND-1060	BACKFILL - SOG/FOUNDATIONS - SALLYPORT	4	18-Apr-23	21-Apr-23
MECHANICAL BUILDING				
LEVEL 1				
MFND-1000	DEEP U/G ELECTRICAL - MECH. BUILDING	7	01-Dec-22	09-Dec-22
MFND-1010	DEEP U/G PLUMBING - MECH. BUILDING	4	06-Dec-22	09-Dec-22
MFND-1020	EXCAVATE FOUNDATIONS - MECH. BUILDING	3	12-Dec-22	14-Dec-22
MFND-1030	PLACE MUD SLAB - MECH. BUILDING	2	15-Dec-22	16-Dec-22
MFND-1040	INSTALL WATERPROOFING - MECH. BUILDING	4	19-Dec-22	22-Dec-22
MFND-1050	UNDER SLAB ELECTRICAL CONDUIT - MECH. BUILDING	7	23-Dec-22	04-Jan-23
MFND-1060	ELECTRICAL SLEEVES - MECH. BUILDING	1	23-Dec-22	23-Dec-22
MFND-1070	UNDER SLAB PLUMBING - MECH. BUILDING	2	27-Dec-22	28-Dec-22
MFND-1080	PLUMBING SLEEVES- MECH. BUILDING	1	27-Dec-22	27-Dec-22
MFND-1090	FORM, AND REBAR TEMPLATE FOOTINGS - SOG/FOUNDATIONS - I	5	29-Dec-22	05-Jan-23
MFND-1100	REBAR FOOTINGS & SOG - SOG/FOUNDATIONS - MECH. BUILDING	6	06-Jan-23	13-Jan-23
MFND-1130	PRE - POUR INSPECTION SOG/FOUNDATIONS - MECH. BUILDING	1	13-Jan-23	13-Jan-23
MFND-1110	POUR - SOG/FOUNDATIONS - MECH. BUILDING	1	17-Jan-23	17-Jan-23
MFND-1120	CURE SOG - MECH. BUILDING	3	18-Jan-23	20-Jan-23
SUPERSTRUCTURE				
TOWER				
TOWER STAIRS				
STAIR1-1000	STAIR 1 (BASEMENT TO L2)	3	08-Nov-22	10-Nov-22
STAIR2-1000	STAIR 2 (BASEMENT TO L2)	3	11-Nov-22	15-Nov-22
STAIR3-1000	STAIR 3 (L1 TO L2)	3	16-Nov-22	18-Nov-22
STAIR4-1000	STAIR 4 (L1 TO L2)	3	21-Nov-22	23-Nov-22
STAIR1-1010	STAIR 1 (L2 TO L4)	3	28-Nov-22	30-Nov-22
STAIR2-1010	STAIR 2 (L2 TO L4)	3	01-Dec-22	05-Dec-22
STAIR3-1010	STAIR 3 (L2 TO L4)	3	06-Dec-22	08-Dec-22
STAIR4-1010	STAIR 4 (L2 TO L4)	3	09-Dec-22	13-Dec-22
STAIR1-1020	STAIR 1 (L4 TO L6)	3	19-Dec-22	21-Dec-22
STAIR2-1020	STAIR 2 (L4 TO L6)	3	22-Dec-22	27-Dec-22
STAIR3-1020	STAIR 3 (L4 TO L6)	3	28-Dec-22	30-Dec-22
STAIR4-1020	STAIR 4 (L4 TO L6)	3	03-Jan-23	05-Jan-23

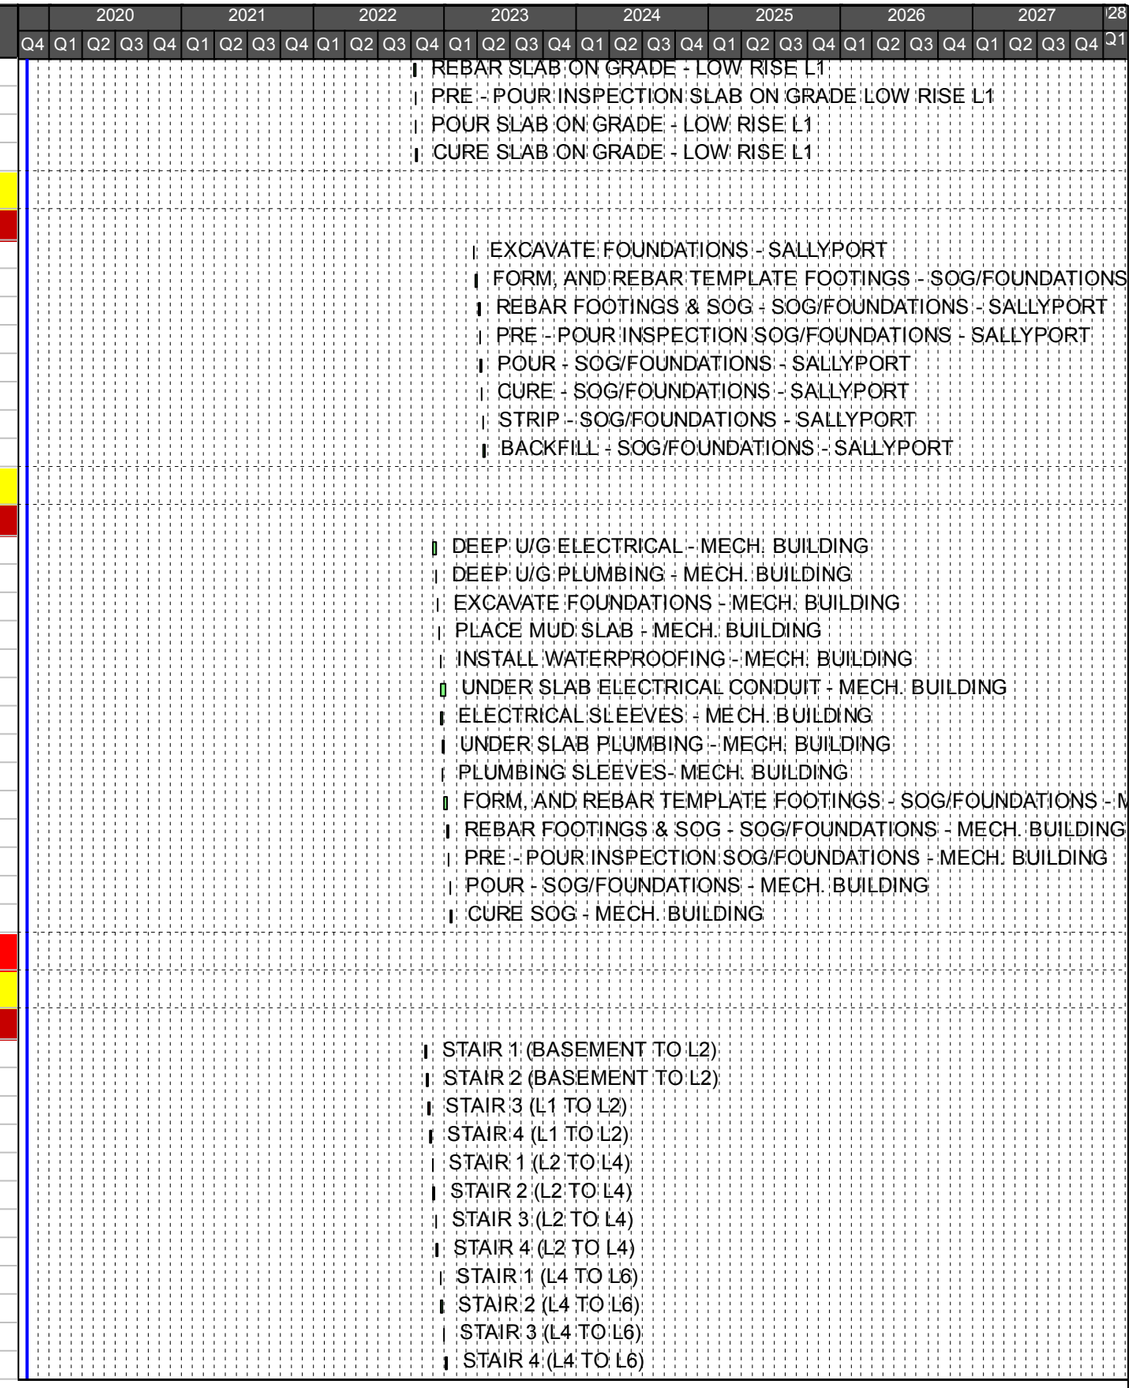

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

Activity ID	Activity Name	Original Duration	Start	Finish
STAIR1-1030	STAIR 1 (L6 TO L8)	3	06-Jan-23	10-Jan-23
STAIR2-1030	STAIR 2 (L6 TO L8)	3	11-Jan-23	13-Jan-23
STAIR3-1030	STAIR 3 (L6 TO L8)	3	17-Jan-23	19-Jan-23
STAIR4-1030	STAIR 4 (L6 TO L8)	3	20-Jan-23	24-Jan-23
STAIR3-1040	STAIR 3 (L8 TO MECH LEVEL)	5	25-Jan-23	31-Jan-23
STAIR4-1040	STAIR 4 (L8 TO MECH LEVEL)	5	01-Feb-23	07-Feb-23
STAIR5-1000	STAIR 12 (MECH. LEVEL) - PREVIOUSLY STR 5	3	16-Feb-23	22-Feb-23
STAIR6-1000	STAIR 13 (MECH. LEVEL) - PREVIOUSLY STR 6	3	16-Feb-23	22-Feb-23
STAIR7-1000	STAIR 7 - RAILS (LOADING DOCK - PLACES WITH CONCRETE)	5	03-Oct-23	09-Oct-23
STAIR8-1000	STAIR 8 - RAILS (SALLYPORT)	5	10-Oct-23	16-Oct-23
STAIR9-1000	STAIR 9 - RAILS (BY MECH BUILDING)	5	17-Oct-23	23-Oct-23
STAIR10-1000	STAIR 10 - RAILS (BY STORAGE ROOM)	5	24-Oct-23	30-Oct-23
STAIR11-1000	STAIR 11 - RAILS (EXTERIOR STAIR 2 EXIT)	5	31-Oct-23	06-Nov-23
STAIR1-1040	STAIR 1 WALL RAILS	10	05-Dec-23	18-Dec-23
STAIR2-1040	STAIR 2 WALL RAILS	10	05-Dec-23	18-Dec-23
STAIR3-1050	STAIR 3 WALL RAILS	10	19-Dec-23	03-Jan-24
STAIR4-1050	STAIR 4 WALL RAILS	10	19-Dec-23	03-Jan-24
BASEMENT				
COLUMNS AND TOPPING SLABS				
TTSCOLB-1000	BASEMENT - CONCRETE ENCASE COLUMNS	5	08-Nov-22	14-Nov-22
A3380	FIRE WATER STORAGE TANK WALLS AND COLUMNS	8	08-Nov-22	17-Nov-22
SLAB ON METAL DECK				
A3390	FIRE WATER STORAGE TANK CONCRETE LID	8	18-Nov-22	01-Dec-22
A3300	LEVEL 1 METAL DECK / PLACE OVER FIRE WATER STORAGE	5	02-Dec-22	08-Dec-22
TOWER CMU				
TRFB-1010	MASONRY WALLS - TOWER BASEMENT	15	31-Oct-22	18-Nov-22
TRFB-1250	MEP ROUGH-IN MASONRY WALLS - TOWER BASEMENT	10	31-Oct-22	11-Nov-22
TCMU1-1210	L0 - CMU - SET DOOR FRAMES	2	01-Nov-22	02-Nov-22
LEVEL 1				
EXTERIOR FRAMING				
TSTR1-1000	TOWER - ERECT LEVEL 1 FRAMING	7	22-Aug-22	30-Aug-22
TSTR1-1010	TOWER - PLUMB/BOLT/WELD LEVEL 1 FRAMING	7	31-Aug-22	12-Sep-22
COLUMNS AND TOPPING SLABS				
TTSCOL1-1010	L1 - CONCRETE ENCASE COLUMNS	7	08-Nov-22	16-Nov-22
TTSCOL1-1020	L1 - TOPPING SLABS	3	17-Nov-22	21-Nov-22
SLAB ON METAL DECK				
TSOMD1-1000	TOWER - MEP ROUGH/DECK/PLACE - LEVEL 1	22	29-Sep-22	28-Oct-22
TSOMD1-1010	SHAKE OUT AND WELD METAL DECK - TOWER L1	5	29-Sep-22	05-Oct-22
TSOMD1-1020	WELD OFF DECK EDGE - TOWER L1	4	30-Sep-22	05-Oct-22
TSOMD1-1030	MEP ROUGH - TOWER L1	4	13-Oct-22	18-Oct-22
TSOMD1-1060	SUPPLEMENTAL STEEL - TOWER L1	5	13-Oct-22	19-Oct-22
TSOMD1-1040	REBAR - TOWER L1	4	18-Oct-22	21-Oct-22
TSOMD1-1050	SET DEPRESSION FORMS & BLOCK-OUTS - TOWER L1	4	18-Oct-22	21-Oct-22
TSOMD1-1070	PLACE SOMD - TOWER L1	1	24-Oct-22	24-Oct-22
TSOMD1-1080	CURE SOMD - TOWER L1	7	24-Oct-22	30-Oct-22
TOWER CMU				
TCMU1-1000	L1 - CMU - SET DETENTION FRAMES	10	13-Dec-22	27-Dec-22

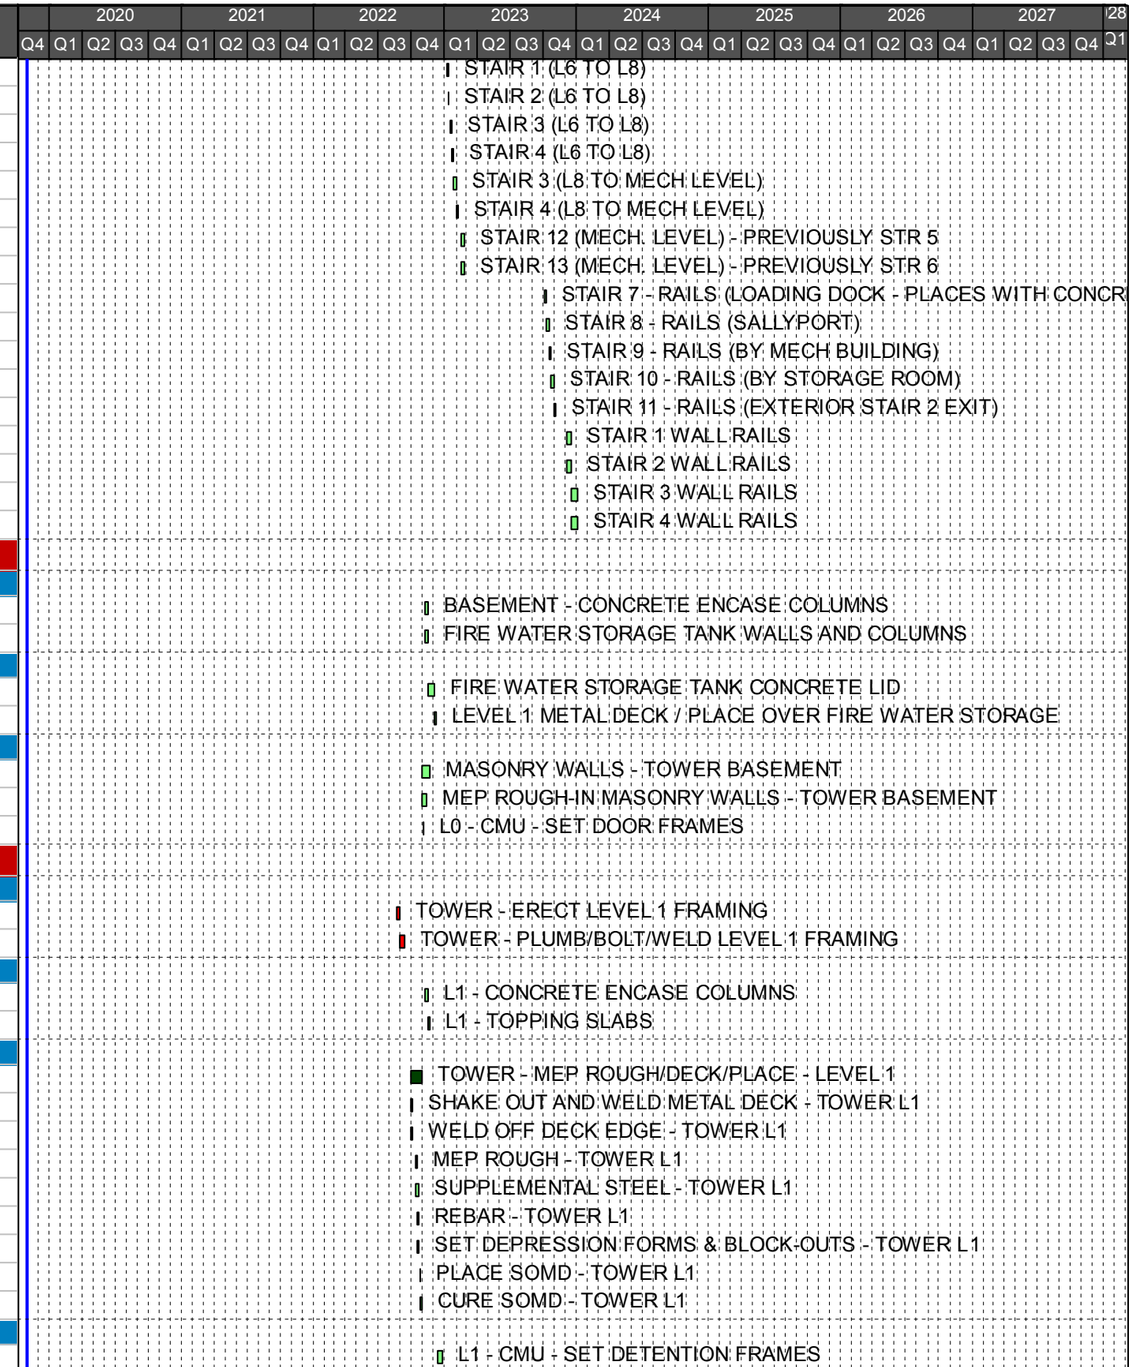

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TCMU1-1010	L1 - CMU - COURTROOM TO RAMP TO PASS. ELEVATORS & STAIR 4	10	15-Dec-22	29-Dec-22
TCMU1-1020	L1 - CMU - SHOWERS, J2, H2, AND CORRIDORS NEAR	10	15-Dec-22	29-Dec-22
TCMU1-1080	IN WALL ELECTRICAL AT CMU COURTROOM TO RAMP TO PASS. E	5	15-Dec-22	21-Dec-22
TCMU1-1110	IN WALL ELECTRICAL AT CMU SHOWERS, J2, H2, AND CORRIDORS	5	15-Dec-22	21-Dec-22
TCMU1-1030	L1 - CMU - ATTY INT, TOILET ROOMS, JC, AND STORAGE	7	30-Dec-22	10-Jan-23
TCMU1-1040	L1 - CMU - NORTH PODS OF CENTRAL HOLDING CELLS	10	30-Dec-22	13-Jan-23
TCMU1-1120	IN WALL ELECTRICAL AT CMU ATTY INT, TOILET ROOMS, JC, AND S	3	30-Dec-22	04-Jan-23
TCMU1-1130	IN WALL ELECTRICAL AT CMU NORTH PODS OF CENTRAL HOLDIN(	5	30-Dec-22	06-Jan-23
TCMU1-1150	DETENTION WINDOW FRAMES AT CMU ATTY INT, TOILET ROOMS,	2	04-Jan-23	05-Jan-23
TCMU1-1090	IN WALL PLUMBING AT CMU NORTH PODS OF CENTRAL HOLDING	2	12-Jan-23	13-Jan-23
TCMU1-1050	L1 - CMU - STORAGE ROOM AND RAMP AREAS	10	17-Jan-23	30-Jan-23
TCMU1-1140	IN WALL ELECTRICAL AT CMU STORAGE ROOM AND RAMP AREAS	5	17-Jan-23	23-Jan-23
TCMU1-1060	L1 - CMU - INTERIOR FACE OF EXTERIOR WALL IN CENTRAL HOLD	7	31-Jan-23	08-Feb-23
TCMU1-1070	L1 - CMU - SOUTH PODS & CONTROL ROOM OF CENTRAL HOLDIN(	10	31-Jan-23	13-Feb-23
TCMU1-1170	IN WALL ELECTRICAL AT CMU SOUTH PODS & CONTROL ROOM OF	5	31-Jan-23	06-Feb-23
TCMU1-1100	IN WALL PLUMBING SOUTH PODS & CONTROL ROOM OF CENTRAL	2	01-Feb-23	02-Feb-23
TCMU1-1160	DETENTION WINDOW FRAMES AT CMU ATTY INT, TOILET ROOMS,	2	02-Feb-23	03-Feb-23
LEVEL 2				
EXTERIOR FRAMING				
TSTR2-1020	TOWER - ERECT LEVEL 2 FRAMING	7	31-Aug-22	12-Sep-22
TSTR2-1030	TOWER - PLUMB/BOLT/WELD LEVEL 2 FRAMING	7	13-Sep-22	21-Sep-22
COLUMNS AND TOPPING SLABS				
TTSCOL2-1030	L2 - CONCRETE ENCASE COLUMNS	7	17-Nov-22	29-Nov-22
TTSCOL2-1050	L2 - TOPPING SLABS	3	30-Nov-22	02-Dec-22
SLAB ON METAL DECK				
TSOMD2-1010	TOWER - MEP ROUGH/DECK/PLACE - LEVEL 2	23	06-Oct-22	07-Nov-22
TSOMD2-1020	SHAKE OUT AND WELD METAL DECK - TOWER L2	5	06-Oct-22	12-Oct-22
TSOMD2-1030	WELD OFF DECK EDGE - TOWER L2	4	07-Oct-22	12-Oct-22
TSOMD2-1040	MEP ROUGH - TOWER L2	4	20-Oct-22	25-Oct-22
TSOMD2-1070	SUPPLEMENTAL STEEL - TOWER L2	5	20-Oct-22	26-Oct-22
TSOMD2-1050	REBAR - TOWER L2	4	26-Oct-22	31-Oct-22
TSOMD2-1060	SET DEPRESSION FORMS & BLOCK-OUTS - TOWER L2	4	26-Oct-22	31-Oct-22
TSOMD2-1080	PLACE SOMD - TOWER L2	1	01-Nov-22	01-Nov-22
TSOMD2-1090	CURE SOMD - TOWER L2	7	01-Nov-22	07-Nov-22
TOWER CMU				
TCMU2-1000	L2 - CMU - SET DETENTION FRAMES	2	05-Jan-23	06-Jan-23
TCMU2-1010	L2 - CMU AT DETENTION - EAST	10	09-Jan-23	23-Jan-23
TCMU2-1020	L2 - CMU AT DETENTION - WEST	10	09-Jan-23	23-Jan-23
TCMU2-1030	L2 - IN WALL PLUMBING & CASSETTES - DETENTION - EAST	2	10-Jan-23	11-Jan-23
TCMU2-1040	L2 - IN WALL PLUMBING & CASSETTES - DETENTION - WEST	2	10-Jan-23	11-Jan-23
TCMU2-1050	L2 - IN WALL ELECTRICAL - DETENTION - EAST	5	11-Jan-23	18-Jan-23
TCMU2-1060	L2 - IN WALL ELECTRICAL - DETENTION - WEST	5	11-Jan-23	18-Jan-23
LEVEL 3				
EXTERIOR FRAMING				
TSTR3-1040	TOWER - ERECT LEVEL 3 FRAMING	5	13-Sep-22	19-Sep-22
TSTR3-1060	TOWER - PLUMB/BOLT/WELD LEVEL 3 FRAMING	5	22-Sep-22	28-Sep-22
COLUMNS AND TOPPING SLABS				

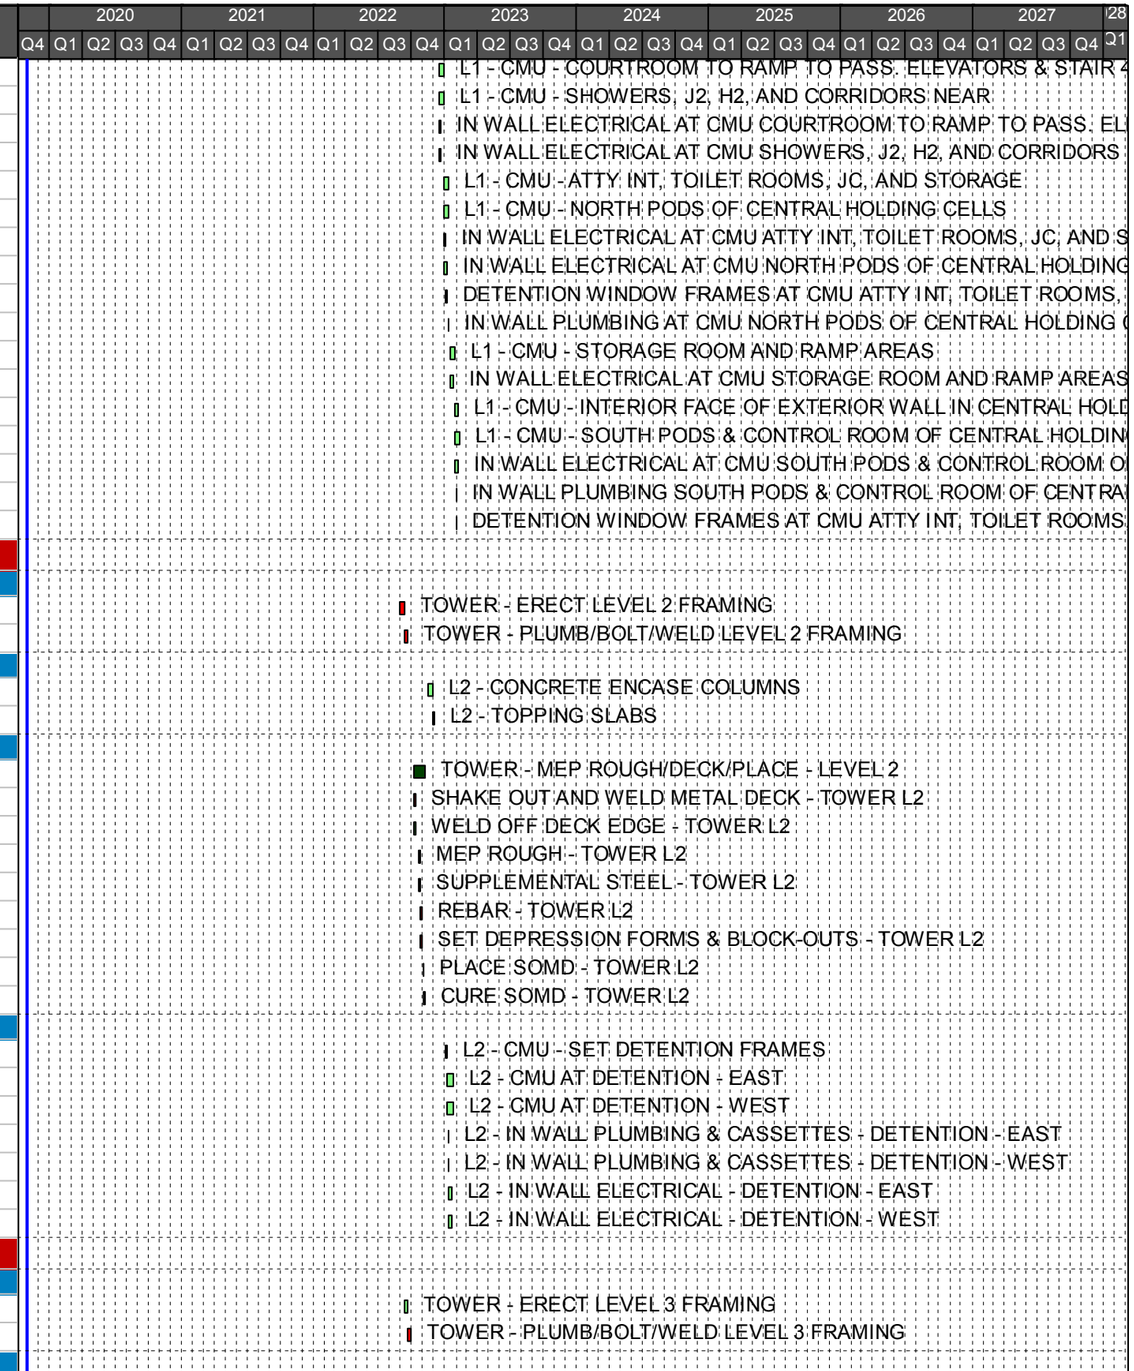

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TTSCOL3-1040	L3 - CONCRETE ENCASE COLUMNS	7	30-Nov-22	08-Dec-22
TTSCOL3-1070	L3 - TOPPING SLABS	3	09-Dec-22	13-Dec-22
SLAB ON METAL DECK				
TSOMD3-1020	TOWER - MEP ROUGH/DECK/PLACE - LEVEL 3	22	13-Oct-22	11-Nov-22
TSOMD2-1100	SHAKE OUT AND WELD METAL DECK - TOWER L3	5	13-Oct-22	19-Oct-22
TSOMD2-1110	WELD OFF DECK EDGE - TOWER L3	4	14-Oct-22	19-Oct-22
TSOMD2-1120	MEP ROUGH - TOWER L3	4	27-Oct-22	01-Nov-22
TSOMD2-1130	SUPPLEMENTAL STEEL - TOWER L3	5	27-Oct-22	02-Nov-22
TSOMD2-1140	REBAR - TOWER L3	4	01-Nov-22	04-Nov-22
TSOMD2-1150	SET DEPRESSION FORMS & BLOCK-OUTS - TOWER L3	4	01-Nov-22	04-Nov-22
TSOMD2-1160	PLACE SOMD - TOWER L3	1	07-Nov-22	07-Nov-22
TSOMD2-1170	CURE SOMD - TOWER L3	7	07-Nov-22	13-Nov-22
TOWER CMU				
TCMU3-1000	L3 - CMU - SET DETENTION FRAMES	2	12-Jan-23	13-Jan-23
TCMU3-1010	L3 - CMU AT DETENTION - EAST	10	24-Jan-23	06-Feb-23
TCMU3-1020	L3 - CMU AT DETENTION - WEST	10	24-Jan-23	06-Feb-23
TCMU2-1070	L3 - IN WALL PLUMBING & CASSETTES - DETENTION - EAST	2	25-Jan-23	26-Jan-23
TCMU2-1080	L3 - IN WALL PLUMBING & CASSETTES - DETENTION - WEST	2	25-Jan-23	26-Jan-23
TCMU2-1090	L3 - IN WALL ELECTRICAL - DETENTION - EAST	5	27-Jan-23	02-Feb-23
TCMU2-1100	L3 - IN WALL ELECTRICAL - DETENTION - WEST	5	27-Jan-23	02-Feb-23
LEVEL 4				
EXTERIOR FRAMING				
TSTR4-1050	TOWER - ERECT LEVEL 4 FRAMING	5	20-Sep-22	26-Sep-22
TSTR4-1080	TOWER - PLUMB/BOLT/WELD LEVEL 4 FRAMING	5	29-Sep-22	05-Oct-22
COLUMNS AND TOPPING SLABS				
TTSCOL4-1060	L4 - CONCRETE ENCASE COLUMNS	7	09-Dec-22	19-Dec-22
TTSCOL4-1090	L4 - TOPPING SLABS	3	20-Dec-22	22-Dec-22
SLAB ON METAL DECK				
TSOMD4-1030	TOWER - MEP ROUGH/DECK/PLACE - LEVEL 4	22	20-Oct-22	18-Nov-22
TSOMD2-1180	SHAKE OUT AND WELD METAL DECK - TOWER L4	5	20-Oct-22	26-Oct-22
TSOMD2-1190	WELD OFF DECK EDGE - TOWER L4	4	21-Oct-22	26-Oct-22
TSOMD2-1200	MEP ROUGH - TOWER L4	4	03-Nov-22	08-Nov-22
TSOMD2-1210	SUPPLEMENTAL STEEL - TOWER L4	5	03-Nov-22	09-Nov-22
TSOMD2-1220	REBAR - TOWER L4	4	08-Nov-22	11-Nov-22
TSOMD2-1230	SET DEPRESSION FORMS & BLOCK-OUTS - TOWER L4	4	08-Nov-22	11-Nov-22
TSOMD2-1240	PLACE SOMD - TOWER L4	1	14-Nov-22	14-Nov-22
TSOMD2-1250	CURE SOMD - TOWER L4	7	14-Nov-22	20-Nov-22
TOWER CMU				
TCMU4-1000	L4 - CMU - SET DETENTION FRAMES	2	03-Feb-23	06-Feb-23
TCMU4-1010	L4 - CMU AT DETENTION - EAST	10	07-Feb-23	22-Feb-23
TCMU4-1020	L4 - CMU AT DETENTION - WEST	10	07-Feb-23	22-Feb-23
TCMU2-1110	L4 - IN WALL PLUMBING & CASSETTES - DETENTION - EAST	2	08-Feb-23	09-Feb-23
TCMU2-1120	L4 - IN WALL PLUMBING & CASSETTES - DETENTION - WEST	2	08-Feb-23	09-Feb-23
TCMU2-1130	L4 - IN WALL ELECTRICAL - DETENTION - EAST	5	09-Feb-23	15-Feb-23
TCMU2-1140	L4 - IN WALL ELECTRICAL - DETENTION - WEST	5	09-Feb-23	15-Feb-23
LEVEL 5				
EXTERIOR FRAMING				

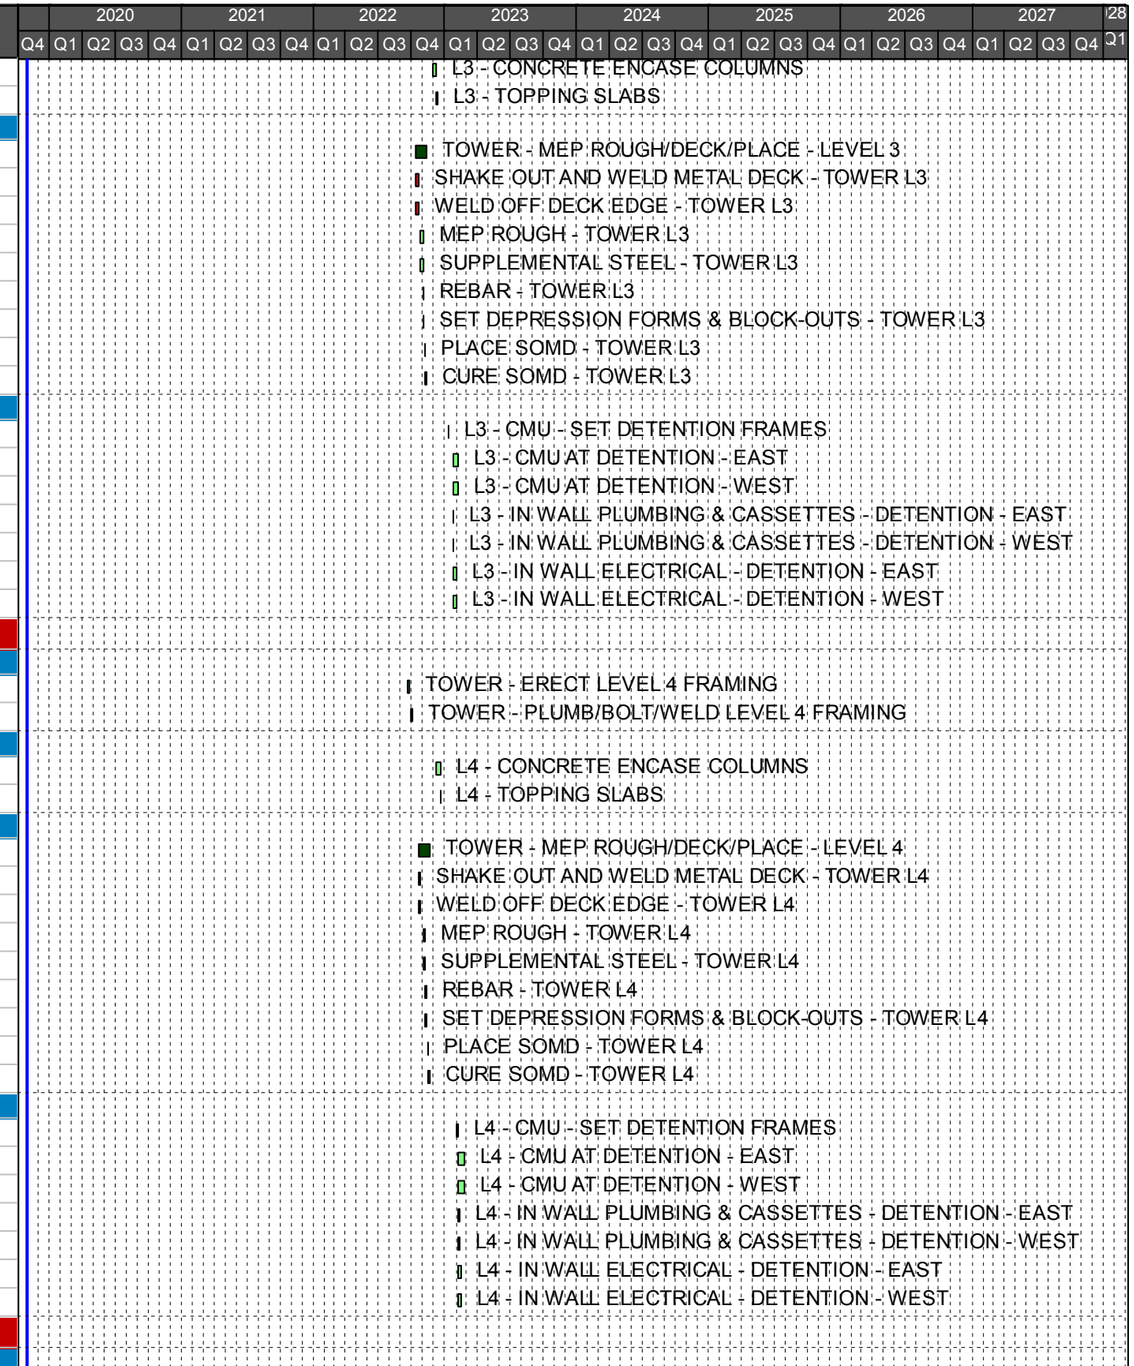

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TSTR5-1070	TOWER - ERECT LEVEL 5 FRAMING	5	27-Sep-22	03-Oct-22
TSTR5-1090	TOWER - PLUMB/BOLT/WELD LEVEL 5 FRAMING	5	06-Oct-22	12-Oct-22
COLUMNS AND TOPPING SLABS				
TTSCOL5-1080	L5 - CONCRETE ENCASE COLUMNS	7	20-Dec-22	29-Dec-22
TTSCOL5-1110	L5 - TOPPING SLABS	3	30-Dec-22	04-Jan-23
SLAB ON METAL DECK				
TSOMD5-1040	TOWER - MEP ROUGH/DECK/PLACE - LEVEL 5	18	27-Oct-22	21-Nov-22
TSOMD2-1260	SHAKE OUT AND WELD METAL DECK - TOWER L5	5	27-Oct-22	02-Nov-22
TSOMD2-1270	WELD OFF DECK EDGE - TOWER L5	4	28-Oct-22	02-Nov-22
TSOMD2-1280	MEP ROUGH - TOWER L5	4	04-Nov-22	09-Nov-22
TSOMD2-1290	SUPPLEMENTAL STEEL - TOWER L5	5	04-Nov-22	10-Nov-22
TSOMD2-1300	REBAR - TOWER L5	4	09-Nov-22	14-Nov-22
TSOMD2-1310	SET DEPRESSION FORMS & BLOCK-OUTS - TOWER L5	4	09-Nov-22	14-Nov-22
TSOMD2-1320	PLACE SOMD - TOWER L5	1	15-Nov-22	15-Nov-22
TSOMD2-1330	CURE SOMD - TOWER L5	7	15-Nov-22	21-Nov-22
TOWER CMU				
TCMU5-1000	L5 - CMU - SET DETENTION FRAMES	2	07-Feb-23	08-Feb-23
TCMU5-1010	L5 - CMU AT DETENTION - EAST	10	23-Feb-23	08-Mar-23
TCMU5-1020	L5 - CMU AT DETENTION - WEST	10	23-Feb-23	08-Mar-23
TCMU2-1150	L5 - IN WALL PLUMBING & CASSETTES - DETENTION - EAST	2	24-Feb-23	27-Feb-23
TCMU2-1160	L5 - IN WALL PLUMBING & CASSETTES - DETENTION - WEST	2	24-Feb-23	27-Feb-23
TCMU2-1170	L5 - IN WALL ELECTRICAL - DETENTION - EAST	5	27-Feb-23	03-Mar-23
TCMU2-1180	L5 - IN WALL ELECTRICAL - DETENTION - WEST	5	27-Feb-23	03-Mar-23
LEVEL 6				
EXTERIOR FRAMING				
TSTR6-1100	TOWER - ERECT LEVEL 6 FRAMING	5	04-Oct-22	10-Oct-22
TSTR6-1110	TOWER - PLUMB/BOLT/WELD LEVEL 6 FRAMING	5	13-Oct-22	19-Oct-22
COLUMNS AND TOPPING SLABS				
TTSCOL6-1100	L6 - CONCRETE ENCASE COLUMNS	7	30-Dec-22	10-Jan-23
TTSCOL6-1130	L6 - TOPPING SLABS	3	11-Jan-23	13-Jan-23
SLAB ON METAL DECK				
TSOMD6-1050	TOWER - MEP ROUGH/DECK/PLACE - LEVEL 6	30	03-Nov-22	16-Dec-22
TSOMD2-1340	SHAKE OUT AND WELD METAL DECK - TOWER L6	5	03-Nov-22	09-Nov-22
TSOMD2-1350	WELD OFF DECK EDGE - TOWER L6	4	04-Nov-22	09-Nov-22
TSOMD2-1360	MEP ROUGH - TOWER L6	4	01-Dec-22	06-Dec-22
TSOMD2-1370	SUPPLEMENTAL STEEL - TOWER L6	5	01-Dec-22	07-Dec-22
TSOMD2-1380	REBAR - TOWER L6	4	06-Dec-22	09-Dec-22
TSOMD2-1390	SET DEPRESSION FORMS & BLOCK-OUTS - TOWER L6	4	06-Dec-22	09-Dec-22
TSOMD2-1400	PLACE SOMD - TOWER L6	1	12-Dec-22	12-Dec-22
TSOMD2-1410	CURE SOMD - TOWER L6	7	12-Dec-22	18-Dec-22
CMU				
TCMU4-1030	L6 - CMU - SET DETENTION FRAMES	2	17-Jan-23	18-Jan-23
TCMU6-1000	L6 - CMU AT H1/H2	10	09-Mar-23	22-Mar-23
TCMU4-1040	L6 - CMU AT DETENTION - EAST	10	09-Mar-23	22-Mar-23
TCMU4-1050	L6 - CMU AT DETENTION - WEST	10	09-Mar-23	22-Mar-23
TCMU2-1270	L6 - IN WALL PLUMBING & CASSETTES - DETENTION - EAST	2	10-Mar-23	13-Mar-23
TCMU2-1280	L6 - IN WALL PLUMBING & CASSETTES - DETENTION - WEST	2	10-Mar-23	13-Mar-23
TCMU2-1290	L6 - IN WALL ELECTRICAL - DETENTION - EAST	5	13-Mar-23	17-Mar-23

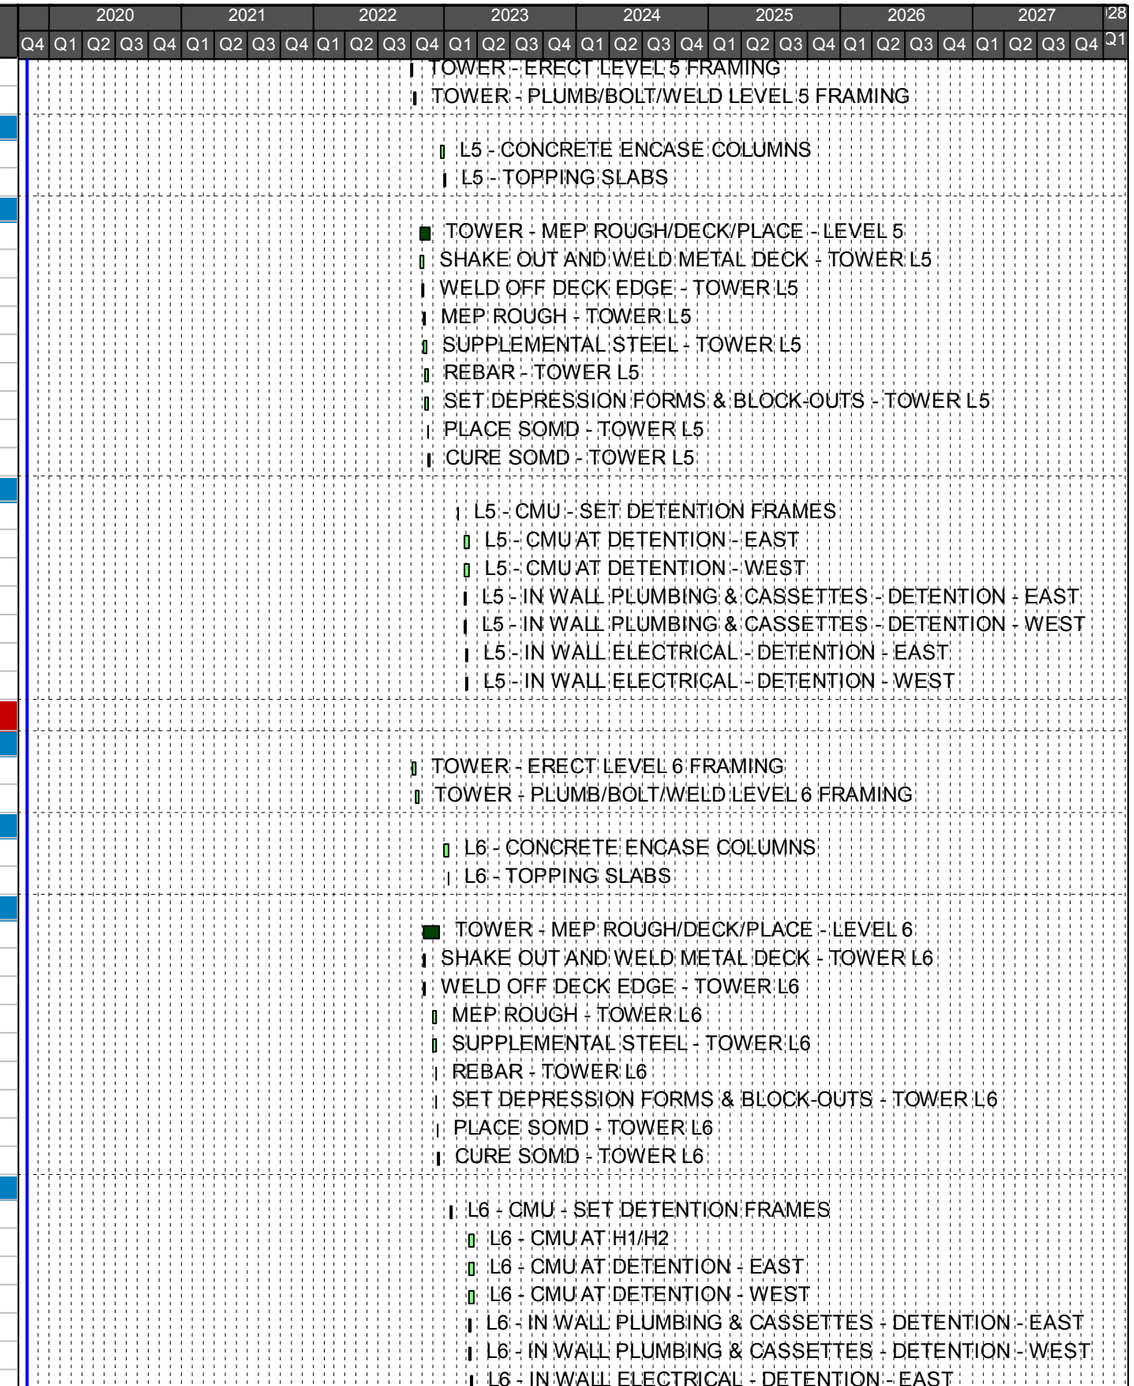

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development

PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19

Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TCMU2-1300	L6 - IN WALL ELECTRICAL - DETENTION - WEST	5	13-Mar-23	17-Mar-23
LEVEL 7				
EXTERIOR FRAMING				
TSTR7-1120	TOWER - ERECT LEVEL 7 FRAMING	5	08-Nov-22	14-Nov-22
TSTR7-1130	TOWER - PLUMB/BOLT/WELD LEVEL 7 FRAMING	5	15-Nov-22	21-Nov-22
COLUMNS AND TOPPING SLABS				
TTSCOL7-1120	L7 - CONCRETE ENCASE COLUMNS	7	11-Jan-23	20-Jan-23
TTSCOL7-1150	L7 - TOPPING SLABS	3	23-Jan-23	25-Jan-23
SLAB ON METAL DECK				
TSOMD7-1060	TOWER - MEP ROUGH/DECK/PLACE - LEVEL 7	22	22-Nov-22	23-Dec-22
TSOMD2-1420	SHAKE OUT AND WELD METAL DECK - TOWER L7	5	22-Nov-22	30-Nov-22
TSOMD2-1430	WELD OFF DECK EDGE - TOWER L7	4	23-Nov-22	30-Nov-22
TSOMD2-1440	MEP ROUGH - TOWER L7	4	08-Dec-22	13-Dec-22
TSOMD2-1450	SUPPLEMENTAL STEEL - TOWER L7	5	08-Dec-22	14-Dec-22
TSOMD2-1460	REBAR - TOWER L7	4	13-Dec-22	16-Dec-22
TSOMD2-1470	SET DEPRESSION FORMS & BLOCK-OUTS - TOWER L7	4	13-Dec-22	16-Dec-22
TSOMD2-1480	PLACE SOMD - TOWER L7	1	19-Dec-22	19-Dec-22
TSOMD2-1490	CURE SOMD - TOWER L7	7	19-Dec-22	25-Dec-22
CMU				
TCMU7-1000	L7 - CMU - SET DETENTION FRAMES	2	09-Feb-23	10-Feb-23
TCMU7-1010	L7 - CMU AT DETENTION - EAST	10	23-Mar-23	05-Apr-23
TCMU7-1020	L7 - CMU AT DETENTION - WEST	10	23-Mar-23	05-Apr-23
TCMU2-1190	L7 - IN WALL PLUMBING & CASSETTES - DETENTION - EAST	2	24-Mar-23	27-Mar-23
TCMU2-1200	L7 - IN WALL PLUMBING & CASSETTES - DETENTION - WEST	2	24-Mar-23	27-Mar-23
TCMU2-1210	L7 - IN WALL ELECTRICAL - DETENTION - EAST	5	27-Mar-23	31-Mar-23
TCMU2-1220	L7 - IN WALL ELECTRICAL - DETENTION - WEST	5	27-Mar-23	31-Mar-23
LEVEL 8				
EXTERIOR FRAMING				
TSTR8-1140	TOWER - ERECT LEVEL 8 FRAMING	5	15-Nov-22	21-Nov-22
TSTR8-1150	TOWER - PLUMB/BOLT/WELD LEVEL 8 FRAMING	5	22-Nov-22	30-Nov-22
COLUMNS AND TOPPING SLABS				
TTSCOL8-1140	L8 - CONCRETE ENCASE COLUMNS	7	23-Jan-23	31-Jan-23
TTSCOL8-1160	L8 - TOPPING SLABS	3	01-Feb-23	03-Feb-23
SLAB ON METAL DECK				
TSOMD8-1070	TOWER - MEP ROUGH/DECK/PLACE - LEVEL 8	20	01-Dec-22	29-Dec-22
TSOMD2-1500	SHAKE OUT AND WELD METAL DECK - TOWER L8	5	01-Dec-22	07-Dec-22
TSOMD2-1510	WELD OFF DECK EDGE - TOWER L8	4	02-Dec-22	07-Dec-22
TSOMD2-1520	MEP ROUGH - TOWER L8	4	14-Dec-22	19-Dec-22
TSOMD2-1530	SUPPLEMENTAL STEEL - TOWER L8	5	14-Dec-22	20-Dec-22
TSOMD2-1540	REBAR - TOWER L8	4	19-Dec-22	22-Dec-22
TSOMD2-1550	SET DEPRESSION FORMS & BLOCK-OUTS - TOWER L8	4	19-Dec-22	22-Dec-22
TSOMD2-1560	PLACE SOMD - TOWER L8	1	23-Dec-22	23-Dec-22
TSOMD2-1570	CURE SOMD - TOWER L8	7	23-Dec-22	29-Dec-22
CMU				
TCMU8-1020	L8 - CMU AT DETENTION ELEVATOR H1 - WEST	5	06-Apr-23	12-Apr-23
LEVEL 9				
EXTERIOR FRAMING				
TSTRM-1160	TOWER - ERECT LEVEL 9 MECH ROOF FRAMING	5	22-Nov-22	30-Nov-22

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TSTRM-1170	TOWER - PLUMB/BOLT/WELD LEVEL 9 MECH ROOF FRAMING	5	01-Dec-22	07-Dec-22
TSTRR-1180	TOWER - ERECT LEVEL 9 PENTHOUSE FRAMING	7	01-Dec-22	09-Dec-22
TSTRR-1190	TOWER - PLUMB/BOLT/WELD LEVEL 9 PENTHOUSE FRAMING	5	12-Dec-22	16-Dec-22
SLAB ON METAL DECK				
MECHANICAL ROOF				
TSOMD9-1080	TOWER - MEP ROUGH/DECK/PLACE - LEVEL 9 - MECHANICAL ROOF	19	08-Dec-22	05-Jan-23
TSOMD2-1580	SHAKE OUT AND WELD METAL DECK - TOWER L9 MECHANICAL R(	5	08-Dec-22	14-Dec-22
TSOMD2-1590	WELD OFF DECK EDGE - TOWER L9 MECHANICAL ROOF	4	09-Dec-22	14-Dec-22
TSOMD2-1600	MEP ROUGH - TOWER L9 MECHANICAL ROOF	4	20-Dec-22	23-Dec-22
TSOMD2-1610	SUPPLEMENTAL STEEL - TOWER L9 MECHANICAL ROOF	5	20-Dec-22	27-Dec-22
TSOMD2-1620	REBAR - TOWER L9 MECHANICAL ROOF	4	23-Dec-22	29-Dec-22
TSOMD2-1630	SET DEPRESSION FORMS & BLOCK-OUTS - TOWER L9 MECHANIC	4	23-Dec-22	29-Dec-22
TSOMD2-1640	PLACE SOMD - TOWER L9 MECHANICAL ROOF	1	30-Dec-22	30-Dec-22
TSOMD2-1650	CURE SOMD - TOWER L9 MECHANICAL ROOF	7	30-Dec-22	05-Jan-23
PENTHOUSE				
TSOMDR-1090	TOWER - MEP ROUGH/DECK/PLACE - TOWER L9 PENTHOUSE	14	19-Dec-22	09-Jan-23
TSOMD2-1660	SHAKE OUT AND WELD METAL DECK - TOWER L9 PENTHOUSE	2	19-Dec-22	20-Dec-22
TSOMD2-1670	WELD OFF DECK EDGE - TOWER L9 PENTHOUSE	1	20-Dec-22	20-Dec-22
TSOMD2-1680	MEP ROUGH - TOWER L9 PENTHOUSE	1	27-Dec-22	27-Dec-22
TSOMD2-1690	SUPPLEMENTAL STEEL - TOWER L9 PENTHOUSE	2	27-Dec-22	28-Dec-22
TSOMD2-1700	REBAR - TOWER L9 PENTHOUSE	1	30-Dec-22	30-Dec-22
TSOMD2-1710	SET DEPRESSION FORMS & BLOCK-OUTS - TOWER L9 PENTHOUSE	1	30-Dec-22	30-Dec-22
TSOMD2-1720	PLACE SOMD - TOWER L9 PENTHOUSE	1	03-Jan-23	03-Jan-23
TSOMD2-1730	CURE SOMD - TOWER L9 PENTHOUSE	7	03-Jan-23	09-Jan-23
LOW-RISE				
LOW RISE STAIRS				
STAIR5-100	STAIR 5 (L1 TO L3)	7	08-Feb-23	16-Feb-23
STAIR5-110	STAIR 6 (L1 TO L3)	7	14-Feb-23	24-Feb-23
LEVEL 1 - LEVEL 4				
STRUCTURAL STEEL				
LSTR-1000	LOW RISE - ERECT STEEL	10	12-Dec-22	23-Dec-22
LSTR-1010	LOW RISE - PLUMB / BOLT / WELD STEEL	15	19-Dec-22	10-Jan-23
LPG2-1000	COMMUNICATING STAIR LOW RISE L2	15	09-Jan-23	30-Jan-23
LEVEL 2				
SLAB ON METAL DECK				
LSOMD2-100	SHAKE OUT AND WELD METAL DECK - LOW RISE L2	5	27-Dec-22	03-Jan-23
LSOMD2-110	WELD OFF DECK EDGE - LOW RISE L2	4	28-Dec-22	03-Jan-23
LSOMD2-120	MEP ROUGH - LOW RISE L2	5	04-Jan-23	10-Jan-23
LSOMD2-130	REBAR - LOW RISE L2	5	09-Jan-23	13-Jan-23
LSOMD2-140	SET DEPRESSION FORMS & BLOCK-OUTS - LOW RISE L2	4	10-Jan-23	13-Jan-23
LSOMD2-150	SUPPLEMENTAL STEEL - LOW RISE L2	5	31-Jan-23	06-Feb-23
LSOMD2-160	PLACE SOMD - LOW RISE L2	1	07-Feb-23	07-Feb-23
LSOMD2-170	CURE SOMD - LOW RISE L2	7	08-Feb-23	14-Feb-23
LEVEL 3				
SLAB ON METAL DECK				
LSOMD3-100	SHAKE OUT AND WELD METAL DECK - LOW RISE L3	5	17-Jan-23	23-Jan-23
LSOMD3-110	WELD OFF DECK EDGE - LOW RISE L3	4	18-Jan-23	23-Jan-23

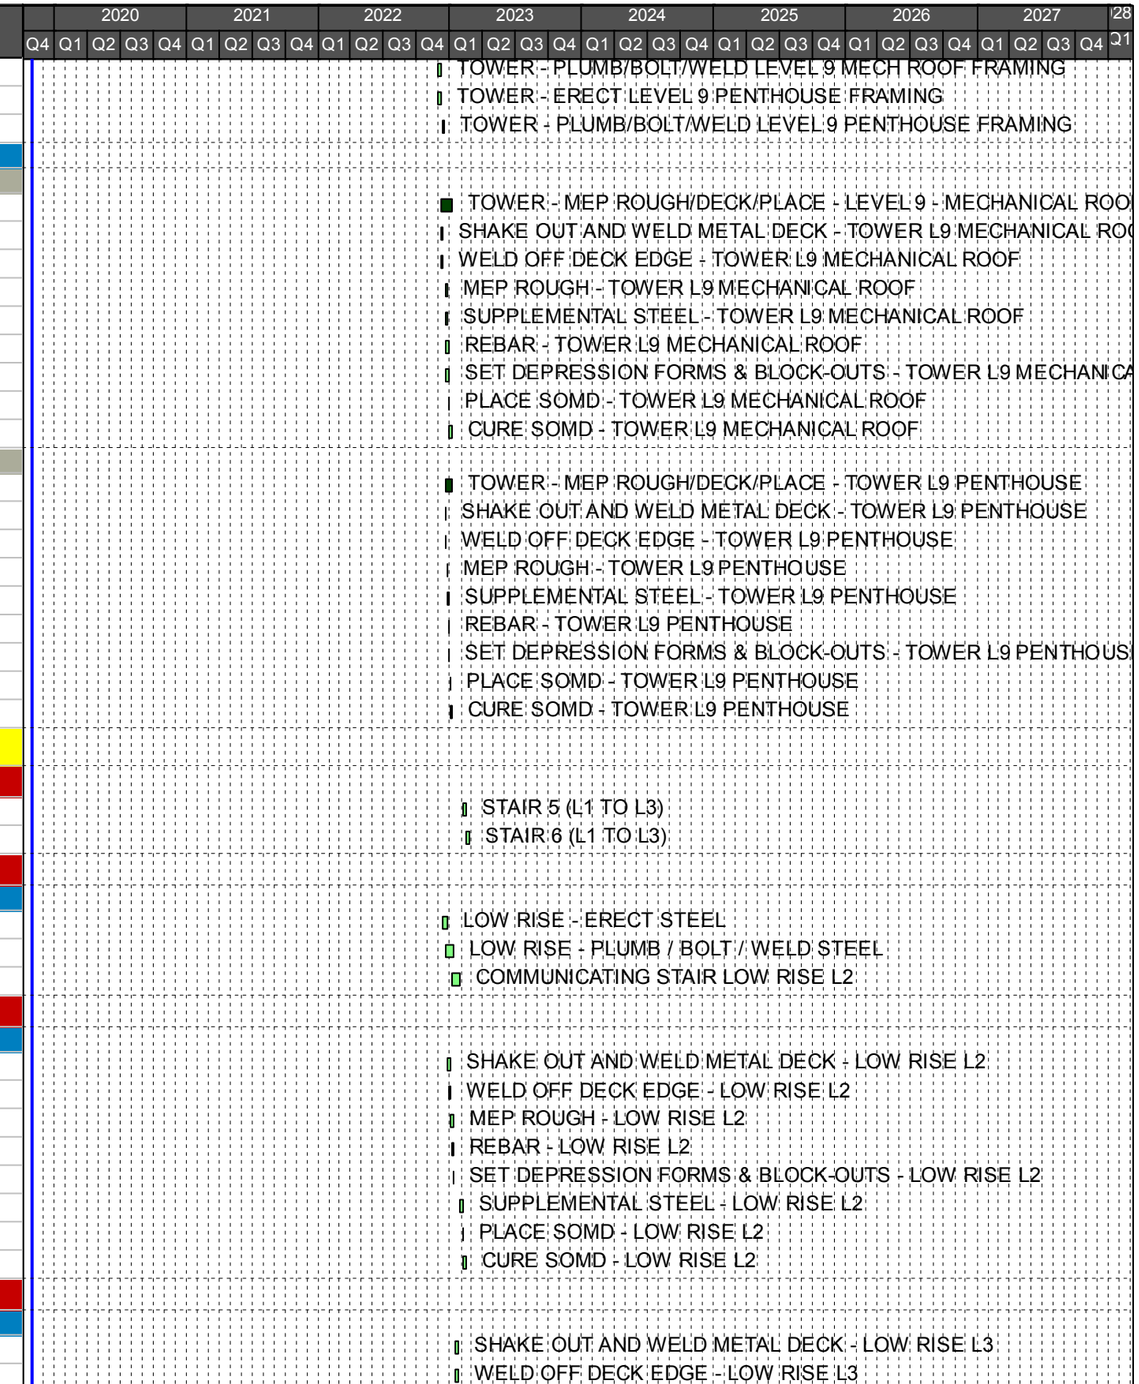

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
LSOMD3-120	MEP ROUGH - LOW RISE L3	5	24-Jan-23	30-Jan-23
LSOMD3-130	REBAR - LOW RISE L3	5	27-Jan-23	02-Feb-23
LSOMD3-140	SET DEPRESSION FORMS & BLOCK-OUTS - LOW RISE L3	4	30-Jan-23	02-Feb-23
LSOMD3-150	SUPPLEMENTAL STEEL - LOW RISE L3	5	31-Jan-23	06-Feb-23
LSOMD3-160	PLACE SOMD - LOW RISE L3	1	07-Feb-23	07-Feb-23
LSOMD3-170	CURE SOMD - LOW RISE L3	7	07-Feb-23	13-Feb-23
LEVEL 4				
SLAB ON METAL DECK				
LSOMD4-100	SHAKE OUT AND WELD METAL DECK - LOW RISE L4	5	03-Feb-23	09-Feb-23
LSOMD4-110	WELD OFF DECK EDGE - LOW RISE L4	4	06-Feb-23	09-Feb-23
LSOMD4-120	MEP ROUGH - LOW RISE L4	5	10-Feb-23	16-Feb-23
LSOMD4-130	REBAR - LOW RISE L4	5	15-Feb-23	23-Feb-23
LSOMD4-140	SET DEPRESSION FORMS & BLOCK-OUTS - LOW RISE L4	4	16-Feb-23	23-Feb-23
LSOMD4-150	SUPPLEMENTAL STEEL - LOW RISE L4	5	21-Feb-23	27-Feb-23
LSOMD4-160	PLACE SOMD - LOW RISE L4	1	28-Feb-23	28-Feb-23
LROOF-1090	SOMD CURE - LOW RISE L4	10	01-Mar-23	10-Mar-23
SALLYPORT				
LEVEL 1				
SPSTR-1010	MASONRY AT EXTERIOR WALLS - SALLYPORT	10	17-Apr-23	28-Apr-23
SSTR1-100	FORM STAIRS - SALLYPORT	2	24-Apr-23	25-Apr-23
SSTR1-110	REBAR STAIRS - SALLYPORT	1	26-Apr-23	26-Apr-23
SSTR1-140	PRE - POUR INSPECTION - STAIRS SALLYPORT	1	26-Apr-23	26-Apr-23
SSTR1-120	POUR STAIRS - SALLYPORT	1	27-Apr-23	27-Apr-23
SSTR1-130	CURE STAIRS - SALLYPORT	3	28-Apr-23	30-Apr-23
SWP1-100	BACKFILL & A/B FOR RAMPS AND WALLS - SALLYPORT	3	28-Apr-23	02-May-23
SWP1-110	STRIP STAIRS - SALLYPORT	1	01-May-23	01-May-23
SWP1-120	FORM RAMPS AND WALLS - SALLYPORT	5	03-May-23	09-May-23
SWP1-130	REBAR RAMPS AND WALLS - SALLYPORT	6	10-May-23	17-May-23
SWP1-170	PRE - POUR INSPECTION - RAMPS AND WALLS SALLYPORT	1	17-May-23	17-May-23
SWP1-140	POUR RAMPS AND WALLS - SALLYPORT	1	18-May-23	18-May-23
SWP1-150	STRIP RAMPS AND WALLS - SALLYPORT	1	19-May-23	19-May-23
SWP1-160	CURE RAMPS AND WALLS - SALLYPORT	3	20-May-23	22-May-23
MECHANICAL BUILDING				
LEVEL 1				
MBSTR-1010	PILASTERS & CMU WALLS (TO ROOF STEEL) - MECH. BUILDING	40	23-Jan-23	21-Mar-23
MBSTR-1020	SET EMERGENCY GENERATOR - MECH. BUILDING	3	22-Mar-23	24-Mar-23
MBSTR-1050	ROOF FRAMING AND METAL DECK - MECH. BUILDING	10	27-Mar-23	07-Apr-23
MECHRI-1000	FIRE SUPPRESSION INSERTS - MECHANICAL BUILDING	1	10-Apr-23	10-Apr-23
MECHRI-1010	ELECTRICAL INSERTS - MECHANICAL BUILDING	1	10-Apr-23	10-Apr-23
MECHRI-1020	MECHANICAL INSERTS - MECHANICAL BUILDING	1	10-Apr-23	10-Apr-23
MECHSOMD-1000	REBAR ROOF DECK - MECHANICAL BUILDING	2	11-Apr-23	12-Apr-23
MBSTR-1060	PLACE ROOF CONCRETE - MECH. BUILDING	1	13-Apr-23	13-Apr-23
MBSTR-1030	CMU PARAPET (ABOVE ROOF STEEL) - NORTH WALLS - MECH. BU	10	14-Apr-23	27-Apr-23
MBSTR-1070	ROOF DECK CURE - MECH. BUILDING	10	14-Apr-23	23-Apr-23
TMROOF-1140	APPLY ROOFING MEMBRANE	5	24-Apr-23	28-Apr-23
MBSTR-1040	PLATFORMS AND STAIRS - MECH. BUILDING	2	28-Apr-23	01-May-23

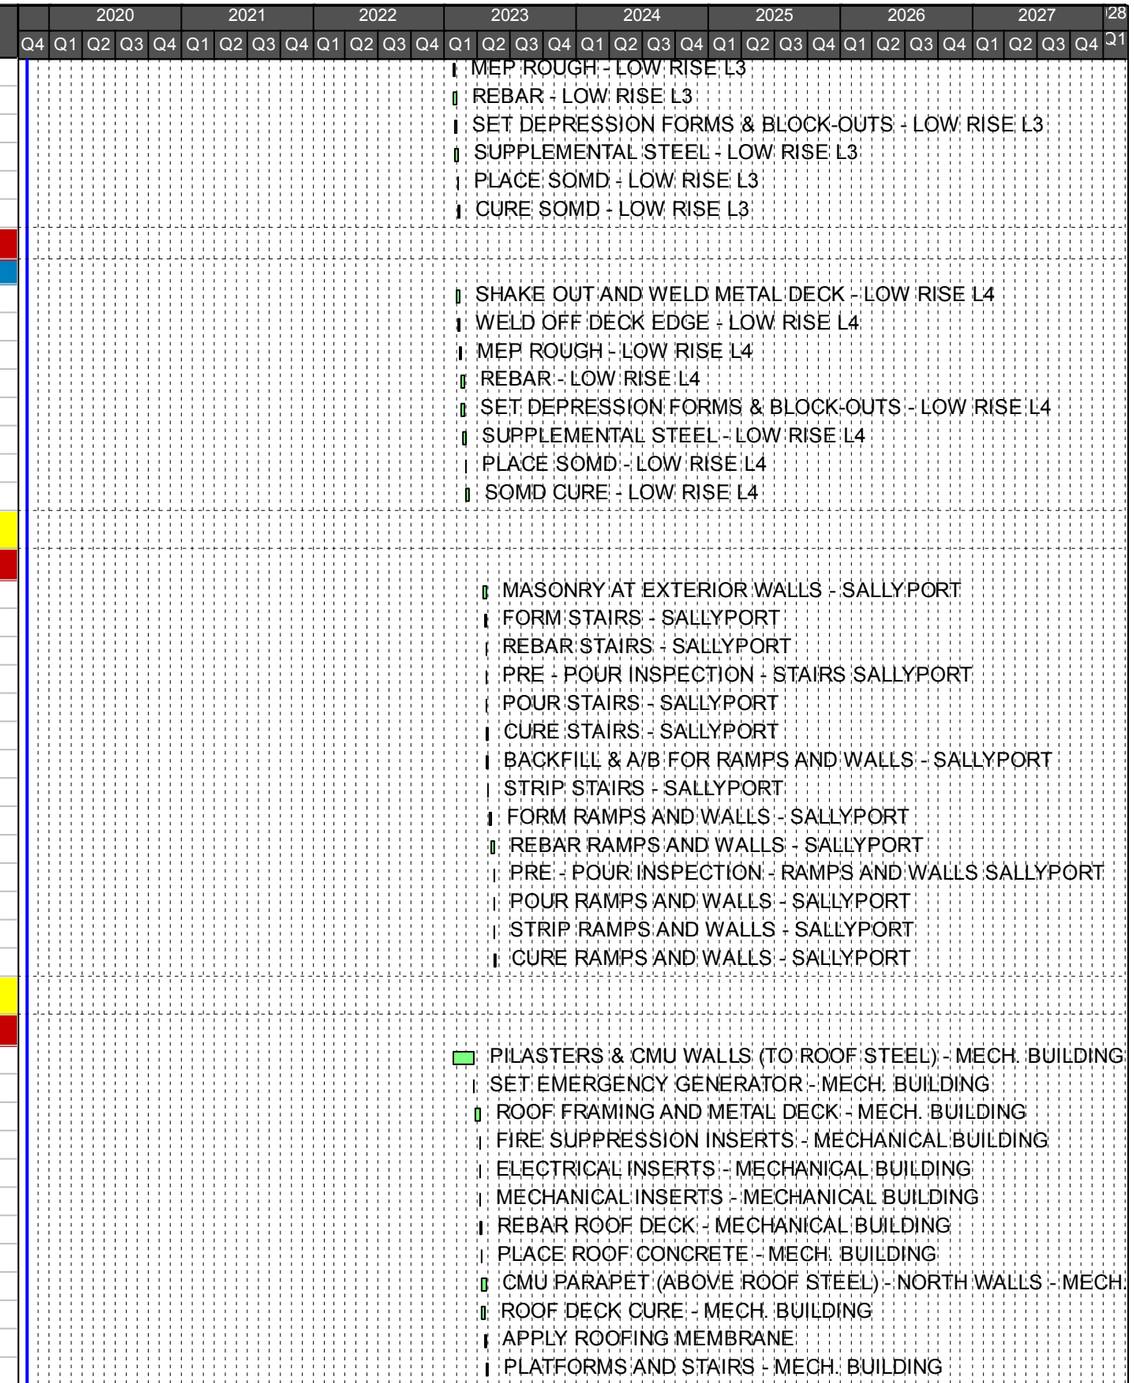

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
BUILDING ENCLOSURE				
TOWER				
TOWER LEVELS 1-2				
TENCL12-1000	ERECT PRECAST	12	21-Dec-22	09-Jan-23
TENCL12-1010	ALIGN/WELD PRECAST	14	30-Dec-22	20-Jan-23
TEXT-1000	INSTALL GLAZING TOWER LEVELS 1-2	7	03-Jan-23	11-Jan-23
TENCLN-1000	CURTAINWALL NORTH 1-2	5	23-Jan-23	27-Jan-23
TENCLS-1000	CURTAINWALL SOUTH 1-2	5	30-Jan-23	03-Feb-23
TOWER LEVELS 3-4				
TENCL34-1000	ERECT PRECAST	12	18-Jan-23	02-Feb-23
TENCL34-1010	ALIGN/WELD PRECAST	14	26-Jan-23	14-Feb-23
TEXT-1010	INSTALL GLAZING TOWER LEVELS 3-4	7	27-Jan-23	06-Feb-23
TENCLN-1010	CURTAINWALL NORTH 3-4	5	15-Feb-23	23-Feb-23
TENCLS-1010	CURTAINWALL SOUTH 3-4	5	24-Feb-23	02-Mar-23
TOWER LEVELS 5-6				
TENCL56-1000	ERECT PRECAST	12	07-Feb-23	24-Feb-23
TENCL56-1010	ALIGN/WELD PRECAST	14	15-Feb-23	08-Mar-23
TEXT-1020	INSTALL GLAZING TOWER LEVELS 5-6	7	16-Feb-23	28-Feb-23
TENCLN-1020	CURTAINWALL NORTH 5-6	5	09-Mar-23	15-Mar-23
TENCLS-1020	CURTAINWALL SOUTH 5-6	5	16-Mar-23	22-Mar-23
TOWER LEVELS 7-R				
TENCL7R-1000	ERECT PRECAST	12	01-Mar-23	16-Mar-23
TENCL7R-1010	ALIGN/WELD PRECAST	14	09-Mar-23	28-Mar-23
TEXT-1030	INSTALL GLAZING TOWER LEVELS 7-8	7	10-Mar-23	20-Mar-23
TENCLN-1030	CURTAINWALL NORTH 7-8	5	29-Mar-23	04-Apr-23
TENCLS-1030	CURTAINWALL SOUTH 7-8	5	05-Apr-23	11-Apr-23
TOWER ROOFING				
MAIN ROOF				
TMROOF-1000	PADS AND CURBS	15	06-Jan-23	27-Jan-23
TMROOF-1070	GUARDRAILS	10	06-Jan-23	20-Jan-23
TMROOF-1010	CURE PADS AND CURBS	10	28-Jan-23	06-Feb-23
TRF-1000	INSTALL MISC METALS - TOWER ROOF	3	30-Jan-23	01-Feb-23
TMROOF-1020	ROOF SCREEN TUBE STEEL FRAMING	15	07-Feb-23	01-Mar-23
TMROOF-1100	FIELD MEASURE SHEET METAL FLASHING - TOWER ROOF	1	07-Feb-23	07-Feb-23
LRF-100	INSTALL TROLLEY SYSTEM - TOWER ROOF	3	02-Mar-23	06-Mar-23
TRF-1010	APPLY ROOFING MEMBRANE ON PENTHOUSE WALLS - TOWER R(	7	20-Mar-23	28-Mar-23
TMROOF-1040	SET MECHANICAL EQUIPMENT - TOWER ROOF	10	29-Mar-23	11-Apr-23
TMROOF-1030	APPLY ROOFING MEMBRANE	12	29-Mar-23	13-Apr-23
TRF-1020	SET PLUMBING EQUIPMENT - TOWER ROOF	5	05-Apr-23	11-Apr-23
TMROOF-1060	INSTALL MECHANICAL SCREEN	15	12-Apr-23	02-May-23
TMROOF-1080	SET MECHANICAL DUCTWORK - TOWER ROOF	30	12-Apr-23	23-May-23
TRD-100	TOWER TEMPORARY DRY-IN	0		13-Apr-23
TMROOF-1050	WALK PADS	5	14-Apr-23	20-Apr-23
TMROOF-1110	ROOF MEMBRANE AT PARAPET NEAR PRECAST AND METAL PANE	5	14-Apr-23	20-Apr-23
TRF-1030	PLUMBING/ PIPING - TOWER ROOF	30	19-Apr-23	01-Jun-23
TMROOF-1130	INSTALL SHEET METAL FLASHING - TOWER ROOF	4	21-Apr-23	26-Apr-23

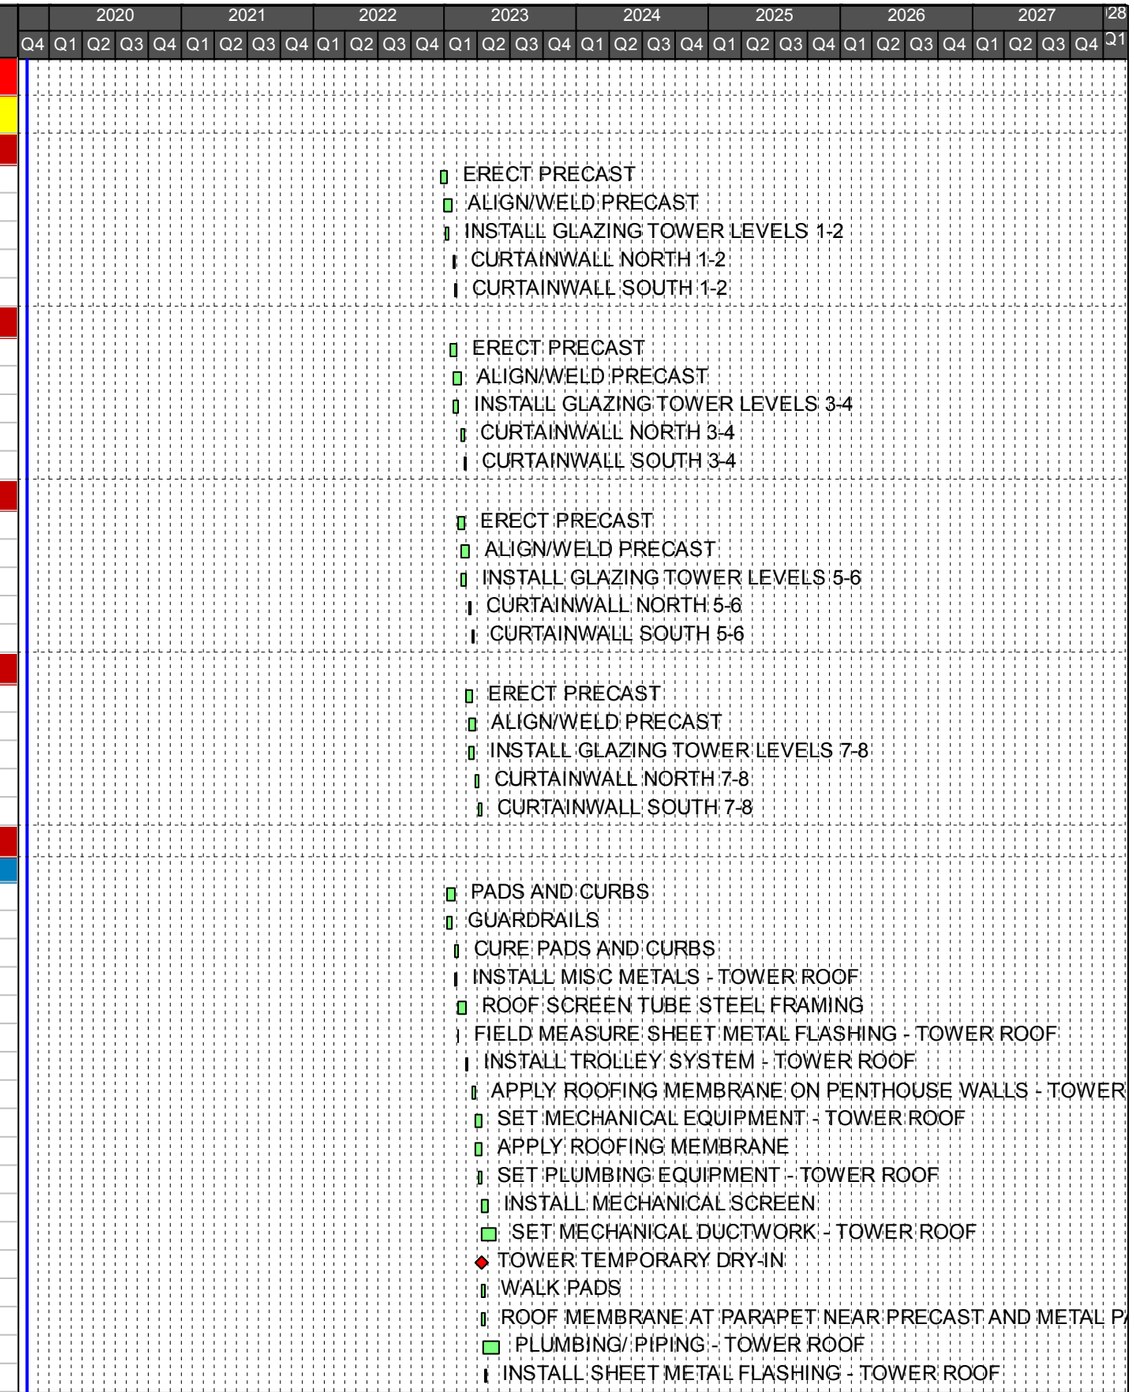

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TRF-1040	ROOF EXTERIOR ELECTRICAL - TOWER ROOF	10	10-May-23	23-May-23
TMROOF-1090	MECHANICAL EQUIPMENT CONNECTIONS & CONTROLS - TOWER	25	24-May-23	29-Jun-23
TRD-110	TOWER DRY-IN	0		19-Sep-23
PENTHOUSE ROOF				
THROOF-1000	ROOFING	5	29-Mar-23	04-Apr-23
THROOF-1010	GUTTERS AND DOWNSPOUTS	5	14-Apr-23	20-Apr-23
THROOF-1020	MISC. SPECIALTIES INCLUDING ROOF LADDERS	10	21-Apr-23	04-May-23
TOWER CAULK/SEALANTS				
TCAULK-1000	NORTH 1ST PASS	20	29-Mar-23	25-Apr-23
TCAULK-1010	EAST 1ST PASS	10	26-Apr-23	09-May-23
TCAULK-1020	SOUTH 1ST PASS	20	10-May-23	08-Jun-23
TCAULK-1030	WEST 1ST PASS	10	09-Jun-23	22-Jun-23
TCAULK-1040	NORTH 2ND PASS	20	23-Jun-23	21-Jul-23
TCAULK-1050	EAST 2ND PASS	10	24-Jul-23	04-Aug-23
TCAULK-1060	SOUTH 2ND PASS	20	07-Aug-23	05-Sep-23
TCAULK-1070	WEST 2ND PASS	10	06-Sep-23	19-Sep-23
MANLIFT BAY CLOSE-UP				
MLENCL-1000	ERECT MANLIFT BAY PANELS	2	21-Jul-23	24-Jul-23
MLENCL-1010	CAULK MANLIFT BAY PANELS	8	25-Jul-23	03-Aug-23
LOW-RISE				
LOW-RISE LEVEL 1				
LENCL1-1000	ERECT/ALIGN/WELD PRECAST - LOW RISE L1	5	07-Mar-23	13-Mar-23
LENCL23-1000	ERECT SCAFFOLD FOR CLEAR STORY - LOW RISE L1	10	14-Mar-23	27-Mar-23
LENCL23-1010	FRAME EXTERIOR - LOW RISE L1	10	14-Mar-23	27-Mar-23
LEXTRI1-100	ROUGH-IN ELECTRICAL AT EXTERIOR- LOW RISE L1	5	28-Mar-23	03-Apr-23
LENCL23-1180	STAIR 5 & STAIR 6 FRAMING - LOW RISE L1	3	28-Mar-23	30-Mar-23
LEXTRI1-110	ROUGH-IN FIRE SUPPRESSION AT EXTERIOR - LOW RISE L1	5	04-Apr-23	10-Apr-23
LENCL23-1020	SHEATH - LOW RISE L1	10	11-Apr-23	24-Apr-23
LENCL23-1030	WATERPROOFING - LOW RISE L1	10	18-Apr-23	01-May-23
LENCL23-1040	CURTAINWALLS/PUNCHED WINDOWS - LOW RISE L1	15	26-Apr-23	16-May-23
LENCL23-1050	METAL PANELS - LOW RISE L1	12	01-May-23	16-May-23
LENCL1-1040	PLASTER SOFFIT - LOW RISE L1	20	02-May-23	31-May-23
LENCL23-1060	FINS - LOW RISE L1	10	17-May-23	01-Jun-23
LENCL1-1050	STOREFRONT GLAZING - LOW RISE L1	15	01-Jun-23	21-Jun-23
LENCL23-1190	INSTALL STAIR 5 & STAIR 6 EXTERIOR SKIN - LOW RISE L1	10	01-Jun-23	14-Jun-23
LENCL23-1070	DISMANTLE SCAFFOLD - LOW RISE L1	5	11-Jul-23	17-Jul-23
LOW-RISE LEVELS 2				
LEXT2-100	FRAME EXTERIOR - LOW RISE L2	10	28-Mar-23	10-Apr-23
LEXTRI2-100	ROUGH-IN ELECTRICAL AT EXTERIOR - LOW RISE L2	5	11-Apr-23	17-Apr-23
LEXTRI2-110	ROUGH-IN FIRE SUPPRESSION AT EXTERIOR - LOW RISE L2	5	18-Apr-23	24-Apr-23
LENCL23-1080	SHEATH - LOW RISE L2	10	25-Apr-23	08-May-23
LENCL23-1090	WATERPROOFING - LOW RISE L2	10	02-May-23	15-May-23
LENCL1-1060	STOREFRONT GLAZING - LOW RISE L2	20	16-May-23	14-Jun-23
LENCL23-1100	CURTAINWALLS/PUNCHED WINDOWS - LOW RISE L2	13	17-May-23	06-Jun-23
LENCL23-1110	METAL PANELS - LOW RISE L2	12	22-May-23	08-Jun-23
LENCL23-1120	FINS - LOW RISE L2	10	02-Jun-23	15-Jun-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
LOW-RISE LEVELS 3				
LEXT3-100	FRAME AT EXTERIOR - LOW RISE L3	10	11-Apr-23	24-Apr-23
LEXTRI3-100	ROUGH-IN ELECTRICAL AT EXTERIOR - LOW RISE L3	5	25-Apr-23	01-May-23
LEXTRI3-110	ROUGH-IN FIRE SUPPRESSION AT EXTERIOR - LOW RISE L3	5	02-May-23	08-May-23
LENCL23-1130	SHEATH - LOW RISE L3	10	09-May-23	22-May-23
LENCL23-1140	WATERPROOFING - LOW RISE L3	10	23-May-23	07-Jun-23
LENCL23-1150	CURTAINWALLS/PUNCHED WINDOWS - LOW RISE L3	13	07-Jun-23	23-Jun-23
LENCL1-1070	STOREFRONT GLAZING - LOW RISE L3	20	08-Jun-23	06-Jul-23
LENCL23-1160	METAL PANELS - LOW RISE L3	12	12-Jun-23	27-Jun-23
LENCL23-1170	FINS - LOW RISE L3	10	26-Jun-23	10-Jul-23
LOW-RISE ROOFING				
LROOF-1000	PADS, CURBS, AND WALLS - LOW RISE ROOF	5	13-Mar-23	17-Mar-23
LROOF-1010	CURE PADS, CURBS, AND WALLS - LOW RISE ROOF	5	18-Mar-23	22-Mar-23
LROOF-1020	ROOF SCREEN TUBE STEEL FRAMING - LOW RISE ROOF	5	23-Mar-23	29-Mar-23
LROOF-1040	ROOFING AND WALK PADS - LOW RISE ROOF	15	30-Mar-23	19-Apr-23
LROOF-1030	SET MECHANICAL EQUIPMENT - LOW RISE ROOF	5	20-Apr-23	26-Apr-23
LROOF-1060	GUARDRAILS - LOW RISE ROOF	15	20-Apr-23	10-May-23
LEXT4-100	FRAME AT EXTERIOR - LOW RISE ROOF	10	25-Apr-23	08-May-23
LROOF-1050	CORRUGATED METAL PANELS - LOW RISE ROOF	5	27-Apr-23	03-May-23
LRF-110	INSTALL SEISMIC JOINT - - LOW RISE ROOF	10	09-May-23	22-May-23
LROOF-1070	SET MECHANICAL DUCTWORK - LOW RISE ROOF	10	11-May-23	24-May-23
LROOF-1080	MECHANICAL EQUIPMENT CONNECTIONS & CONTROLS - LOW RIS	10	25-May-23	09-Jun-23
LOW-RISE CAULK/SEALANTS				
LCAULK-1000	SOUTH CAULKING - LOW RISE	5	07-Jul-23	13-Jul-23
LCAULK-1020	NORTH CAULKING - LOW RISE	20	07-Jul-23	03-Aug-23
LCAULK-1010	EAST CAULKING - LOW RISE	10	04-Aug-23	17-Aug-23
LCAULK-1030	WEST CAULKING - LOW RISE	10	18-Aug-23	31-Aug-23
SALLYPORT				
SPENCL-1000	FRAME/SHEATH PARAPETS - SALLYPORT	5	24-May-23	01-Jun-23
MECHANICAL BUILDING				
MBENCL-1000	LOUVERS - MECHANICAL BUILDING	3	22-Mar-23	24-Mar-23
MBENCL-1030	ROOFING - MECHANICAL BUILDING	6	24-Apr-23	01-May-23
MBENCL-1020	DOORS AND HARDWARE - MECHANICAL BUILDING	3	28-Apr-23	02-May-23
SPENCL-1010	ROOFING AND PARAPETS - SALLYPORT (JOIN TO MECH. BLDG)	4	05-Jun-23	08-Jun-23
INTERIOR BUILDOUT				
TOWER				
BASEMENT				
BASEMENT FULL FLOOR				
MSB-1000	LEVEL 2 METAL DECK IN PLACE	0		07-Nov-22
TRFB-1000	SET SUMP SOI PIT EQUIPMENT - TOWER BASEMENT	10	15-Nov-22	30-Nov-22
TRFB-1020	LAYOUT WALLS AND EQUIP PADS - TOWER BASEMENT	2	21-Nov-22	22-Nov-22
TRFB-1030	CONCRETE CURBS AND EQUIP PADS - TOWER BASEMENT	5	23-Nov-22	01-Dec-22
TRFB-1050	PRE-WELD CLIPS AND HANGERS - TOWER BASEMENT	5	23-Nov-22	01-Dec-22
TRFB-1120	INSTALL TOP TRACK - TOWER BASEMENT	5	23-Nov-22	01-Dec-22
TRFB-1040	PLACE SUMP_SOI CONCRETE PIT LID - TOWER BASEMENT	2	01-Dec-22	02-Dec-22

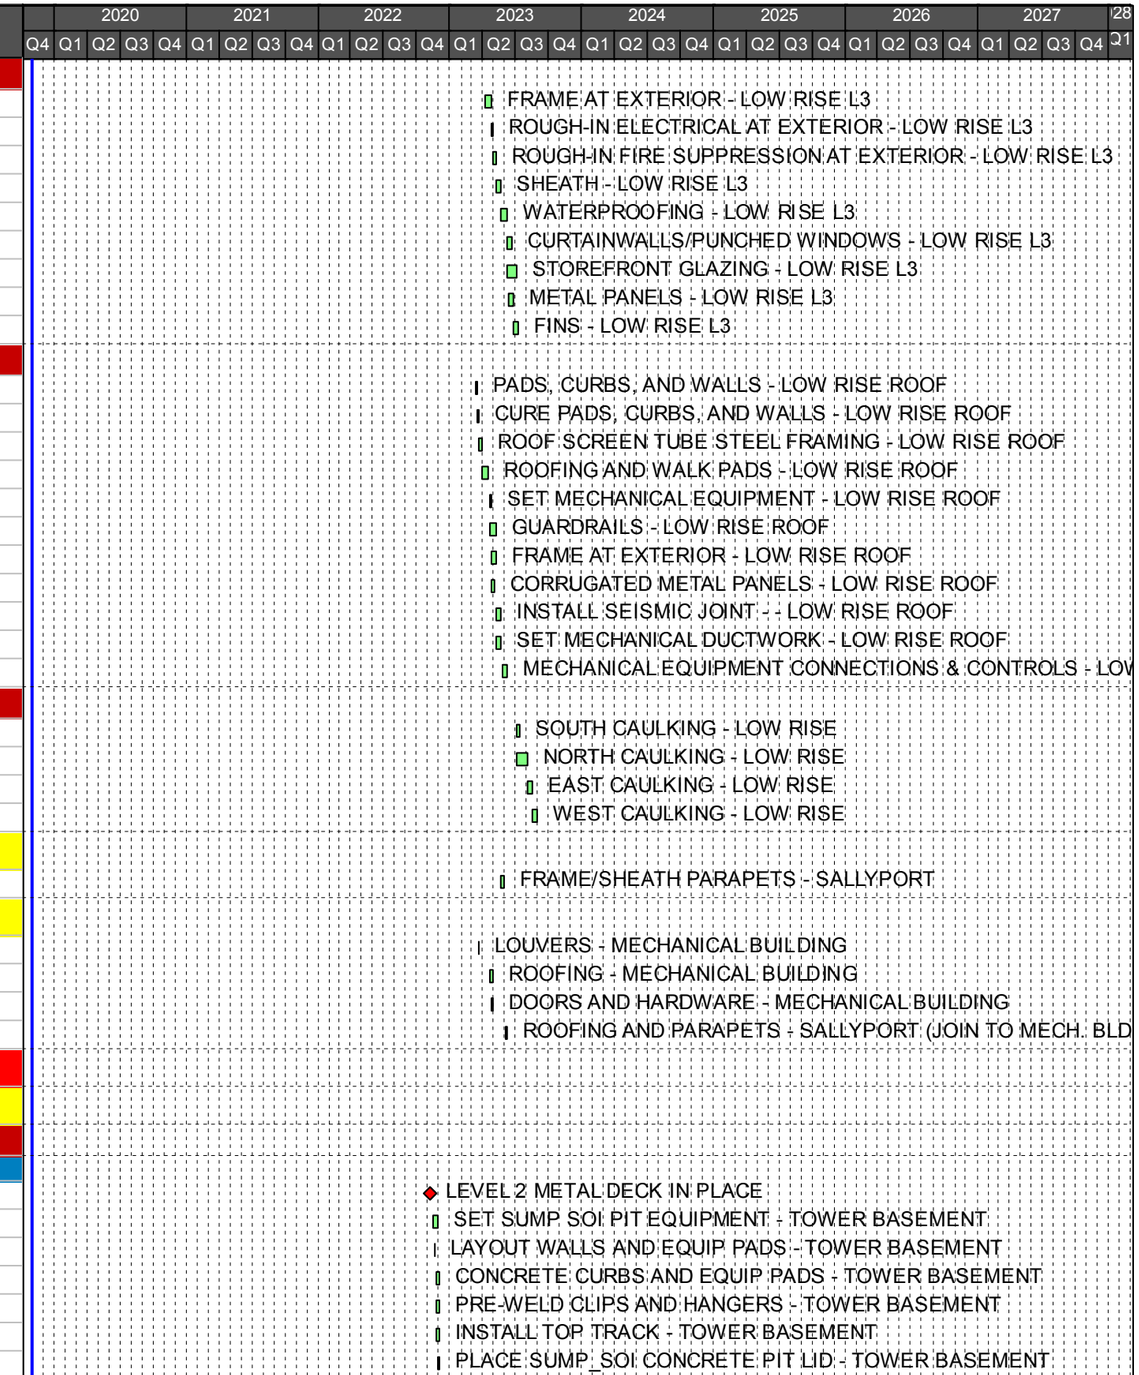

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TRFB-1070	FIREPROOFING (EXCEPT AT FIRE WATER STORAGE TANK) - TOWI	5	02-Dec-22	08-Dec-22
TRFB-1060	FIREPROOFING AT FIRE WATER STORAGE TANK - TOWER BASEM	3	09-Dec-22	13-Dec-22
TRIB-140	ROUGH-IN OVERHEAD FIRE SUPPRESSION- TOWER BASEMENT	5	09-Dec-22	15-Dec-22
TRIB-100	ROUGH-IN OVERHEAD MECHANICAL - TOWER BASEMENT	5	21-Dec-22	28-Dec-22
TRIB-130	ROUGH-IN OVERHEAD ELECTRICAL - TOWER BASEMENT	5	29-Dec-22	05-Jan-23
TRIB-120	ROUGH-IN OVERHEAD PLUMBING - TOWER BASEMENT	6	06-Jan-23	13-Jan-23
TRIB-160	ROUGH-IN OVERHEAD BRANCHES MECHANICAL - TOWER BASEMI	5	03-Feb-23	09-Feb-23
TRIB-170	ROUGH-IN OVERHEAD BRANCHES ELECTRICAL - TOWER BASEME	5	10-Feb-23	16-Feb-23
TRIB-180	ROUGH-IN OVERHEAD BRANCHES PLUMBING - TOWER BASEMENT	5	15-Feb-23	23-Feb-23
PRIORITY WALLS (IDF/ ELEC/ SHAFT/ STAIRS)				
IDF/ ELECTRICAL ROOM/ CENTRAL CONTROL				
TRFB-1220	ELECTRICAL AND IDF, PANELS AND RACKS - TOWER BASEMENT	15	08-May-23	30-May-23
INTERIOR BUILDOUT				
TRFB-1080	FRAME PRIORITY WALLS - TOWER BASEMENT	5	09-Dec-22	15-Dec-22
TRFB-1110	TOP DOWN PRIORITY WALLS - TOWER BASEMENT	3	16-Dec-22	20-Dec-22
TRFB-1100	FRAME WALLS - TOWER BASEMENT	10	17-Jan-23	30-Jan-23
TRIB-110	ROUGH-IN PLUMBING WALLS - TOWER BASEMENT	7	31-Jan-23	08-Feb-23
TRIB-150	ROUGH-IN OVERHEAD BRANCHES FIRE SUPPRESSION- TOWER B	3	31-Jan-23	02-Feb-23
TRIB-200	IN WALL INSPECTION	1	31-Jan-23	31-Jan-23
TRIB-190	ROUGH-IN ELECTRICAL WALLS - TOWER BASEMENT	7	09-Feb-23	21-Feb-23
TRFB-1130	DRYWALL WALLS - TOWER BASEMENT	5	07-Apr-23	13-Apr-23
TRFB-1240	TAPE & FINISH WALLS - TOWER BASEMENT	7	11-Apr-23	19-Apr-23
TRFB-1140	DOORS/HARDWARE - TOWER BASEMENT	5	20-Apr-23	26-Apr-23
TRFB-1170	PAINT WALLS - TOWER BASEMENT	7	27-Apr-23	05-May-23
TRFB-1190	CEILINGS AT FMU, BMS, SHOWERS, AND EVIDENCE STORAGE - T	5	08-May-23	12-May-23
TRFB-1090	STRIPING, BOLLARDS, AND SIGNAGE - TOWER BASEMENT	10	08-May-23	19-May-23
TRFB-1200	TILE AT SHOWERS - TOWER BASEMENT	15	08-May-23	30-May-23
TRFB-1210	FF&E INSTALLATION- TOWER BASEMENT	5	08-May-23	12-May-23
TRFB-1180	MECHANICAL TRIM- TOWER BASEMENT	5	15-May-23	19-May-23
TRFB-1260	ELECTRICAL TRIM- TOWER BASEMENT	5	15-May-23	19-May-23
TRFB-1270	PLUMBING TRIM- TOWER BASEMENT	5	15-May-23	19-May-23
TRFB-1280	FIRE SUPPRESSION TRIM - TOWER BASEMENT	5	15-May-23	19-May-23
TRFB-1230	MEP FINISH IN SHOWERS - TOWER BASEMENT	10	31-May-23	13-Jun-23
TRFB-1150	PAINT STAIR 1 - TOWER BASEMENT	3	19-Dec-23	21-Dec-23
TRFB-1160	PAINT STAIR 2 - TOWER BASEMENT	3	22-Dec-23	27-Dec-23
LEVEL 1				
LEVEL 1 FULL FLOOR				
MS1-1010	PRE-WELD EXTERIOR & PARTITION CLIPS - TOWER L1	7	21-Nov-22	01-Dec-22
T1-G-110	FIREPROOF PRIORITY WALLS/PERIMETER - TOWER L1	5	06-Dec-22	12-Dec-22
MS1-1030	FIREPROOF BALANCE OF FLOORS - TOWER L1	5	20-Dec-22	27-Dec-22
T1-G-100	EDGE OF SLAB FIRE SAFE - TOWER L1	5	23-Jan-23	27-Jan-23
TFING1-1220	FIELD MEASURE FOR WINDOW COVERINGS - TOWER L1	1	30-May-23	30-May-23
TFING1-1230	FABRICATE WINDOW COVERINGS - TOWER L1	10	29-Dec-23	12-Jan-24
T1-G-860	FINAL PAINT - TOWER L1	7	04-Jan-24	12-Jan-24
TFING1-1170	WINDOW COVERINGS PUBLIC GALLERY & OFFICE SPACES - TOW	4	16-Jan-24	19-Jan-24
TFING1-1160	INSTALL SIGNAGE - TOWER L1	5	16-Jan-24	22-Jan-24
TFING1-1210	INT. CERTIFICATION & READY FOR PUNCH - TOWER L1	1	23-Jan-24	23-Jan-24

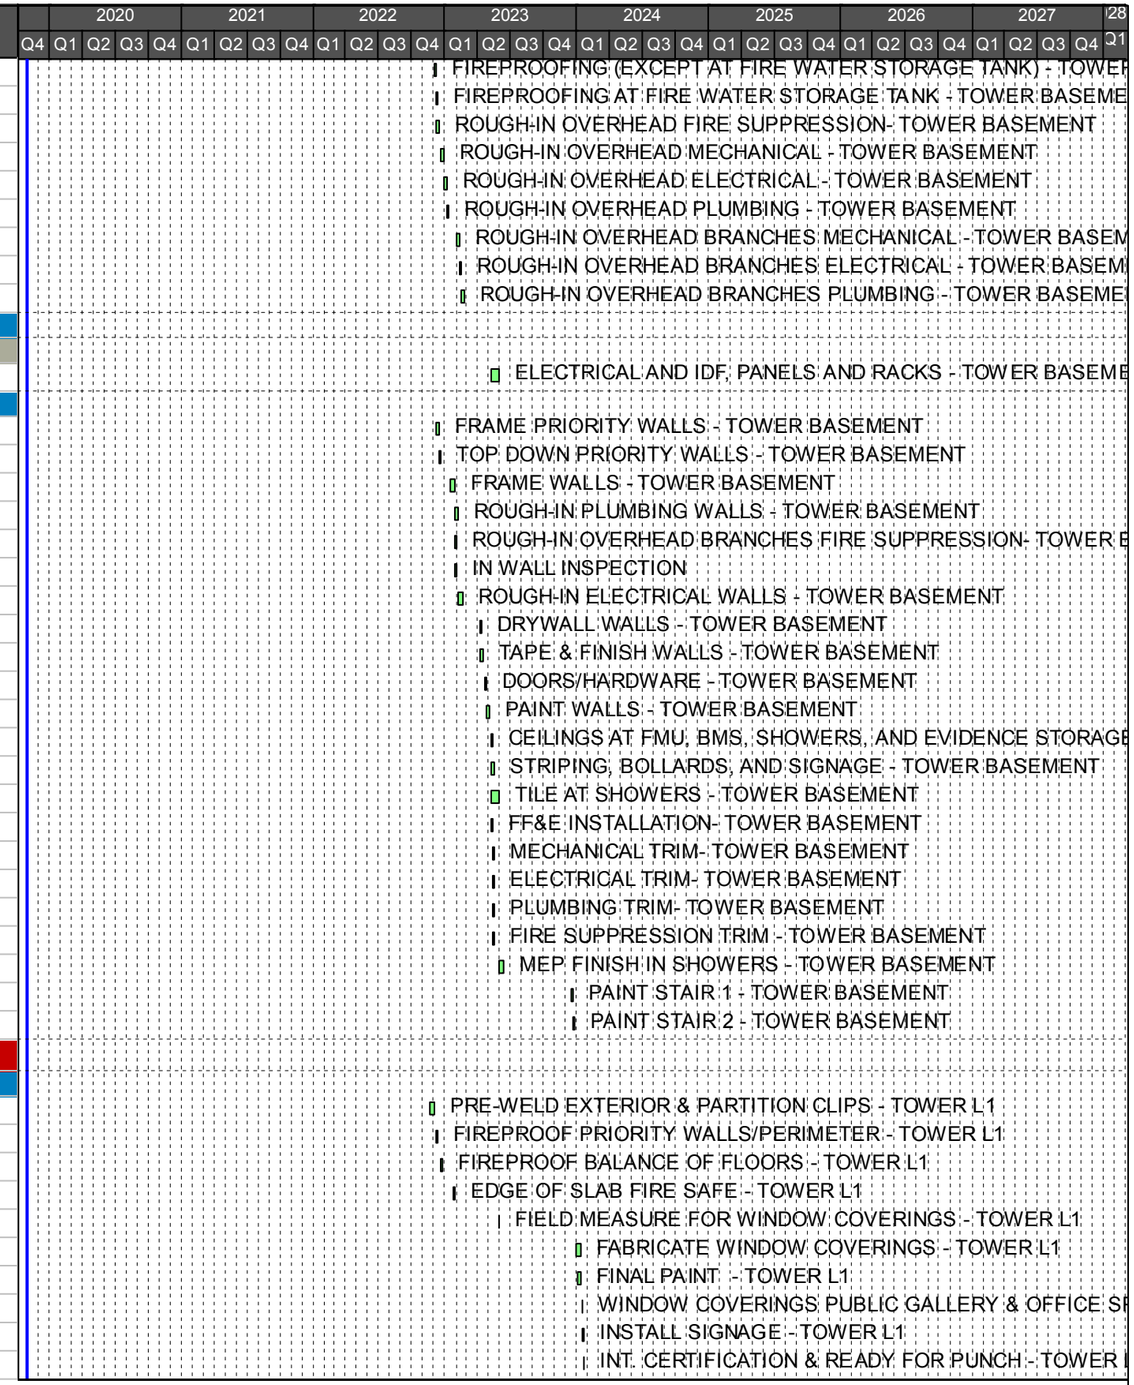

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
OVERHEAD ROUGH-INS				
TFING1-100	LAYOUT FOR CLIPS AND TRACK - TOWER L1	3	13-Dec-22	15-Dec-22
TFING1-150	INSTALL TOP TRACK - TOWER L1	4	14-Dec-22	19-Dec-22
TFING1-140	INSTALL FIRE SUPPRESSION HANGERS - TOWER L1	4	16-Dec-22	21-Dec-22
TFING1-170	FIRE SUPPRESSION MAINS - TOWER L1	5	22-Dec-22	29-Dec-22
TFING1-130	INSTALL ELECTRICAL HANGERS - TOWER L1	4	22-Dec-22	28-Dec-22
TFING1-8260	INSTALL LOW VOLTAGE HANGERS - TOWER L1	4	22-Dec-22	28-Dec-22
TFING1-110	INSTALL PLUMBING HANGERS - TOWER L1	5	29-Dec-22	05-Jan-23
TFING1-120	INSTALL MECHANICAL HANGERS - TOWER L1	5	29-Dec-22	05-Jan-23
TOHG1-120	O/H WASTE & VENT - TOWER L1	7	06-Jan-23	17-Jan-23
TOHG1-100	O/H ELECTRICAL MAINS - TOWER L1	5	10-Jan-23	17-Jan-23
TOHG1-1530	O/H LOW VOLTAGE MAINS - TOWER L1	8	10-Jan-23	20-Jan-23
TOHG1-130	O/H PLUMBING MAINS - TOWER L1	6	18-Jan-23	25-Jan-23
TOHG1-1690	O/H PLUMBING BRANCHES - TOWER L1	7	26-Jan-23	03-Feb-23
TOHG1-110	O/H MECHANICAL MAINS - TOWER L1	10	06-Feb-23	21-Feb-23
TFING1-250	HANG VAV'S - TOWER L1	8	08-Feb-23	21-Feb-23
TOHG1-190	O/H MECHANICAL BRANCHES - TOWER L1	15	22-Feb-23	14-Mar-23
TOHG1-150	O/H HYDRONIC PIPING - TOWER L1	8	22-Feb-23	03-Mar-23
TFING1-320	FIRE SUPPRESSION BRANCHES - TOWER L1	10	02-Mar-23	15-Mar-23
TOHG1-170	O/H ELECTRICAL BRANCHES - TOWER L1	5	09-Mar-23	15-Mar-23
TOHG1-1540	O/H LOW VOLTAGE BRANCHES - TOWER L1	5	09-Mar-23	15-Mar-23
TOHG1-210	O/H SECURITY WIRING - TOWER L1	5	15-Mar-23	21-Mar-23
TFING1-700	O/H HVAC CONTROLS - TOWER L1	5	16-Mar-23	22-Mar-23
TOHG1-180	O/H LOW VOLTAGE - TOWER L1	5	16-Mar-23	22-Mar-23
PRIORITY WALLS (IDF/ ELEC/ SHAFT/ STAIRS)				
IDF/ ELECTRICAL ROOM/ CENTRAL CONTROL				
TPR1-2140	FRAME IDF ROOM, ELECTRICAL ROOM, STAIRS - TOWER L1	5	16-Dec-22	22-Dec-22
TELECRI1-100	ROUGH-IN IDF / ELECTRICAL ROOMS - TOWER L1	5	23-Dec-22	30-Dec-22
TELECRI1-110	ROUGH-IN PLUMBING IDF / ELECTRICAL ROOMS - TOWER L1	2	23-Dec-22	27-Dec-22
TELECRI1-120	ROUGH-IN ELECTRICAL IDF / ELECTRICAL ROOMS - TOWER L1	4	27-Dec-22	30-Dec-22
TELECRI1-130	ROUGH-IN MECHANICAL IDF / ELECTRICAL ROOMS - TOWER L1	3	28-Dec-22	30-Dec-22
TPR1-1070	DRYWALL IDF/ ELECTRICAL ROOMS - TOWER L1	3	03-Jan-23	05-Jan-23
TPR1-2130	TAPE & FINISH IDF/ELECTRICAL ROOMS - TOWER L1	7	06-Jan-23	17-Jan-23
TELEC1-130	PAINT IDF / ELECTRICAL ROOMS - TOWER L1	3	18-Jan-23	20-Jan-23
TELEC1-140	SEAL FLOORS IDF / ELECTRICAL ROOMS - TOWER L1	2	23-Jan-23	24-Jan-23
TPR1-1150	DOORS & HARDWARE IDF/ ELECTRICAL ROOMS - TOWER L1	2	25-Jan-23	26-Jan-23
TPR1-1130	IDF/ ELECTRICAL ROOMS/ RACKS AND PANELS - TOWER L1	15	06-Feb-23	28-Feb-23
MEP SHAFTS				
TPR1-1060	INSTALL MEPF IN SHAFTS - TOWER L1	8	13-Dec-22	22-Dec-22
TPR1-1050	FRAME HVAC SHAFTS & DRYWALL C/R SIDE - TOWER L1	3	27-Dec-22	29-Dec-22
TPR1-1140	DRYWALL HVAC SHAFTS - TOWER L1	6	14-Apr-23	21-Apr-23
TPR1-2120	TAPE & FINISH HVAC SHAFTS - TOWER L1	6	24-Apr-23	01-May-23
ELEVATOR/ STAIR SHAFTS				
TPR1-1000	FRAME PASSENGER ELEVATOR HOISTWAYS - TOWER L1	3	30-Dec-22	04-Jan-23
TDR1-1000	FRAME AT H1/H2 - ELEVATOR FRAMES DETENTION AREA - TOWEF	4	30-Dec-22	05-Jan-23
TPR1-1040	FRAME J1/J2 ELEVATOR WALLS - TOWER L1	3	05-Jan-23	09-Jan-23
TPR1-2150	DRYWALL PASSENGER ELEVATOR - TOWER L1	2	06-Jan-23	09-Jan-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TPR1-2160	DRYWALL J1/J2 ELEVATOR WALLS - TOWER L1	2	10-Jan-23	11-Jan-23
TPR1-2170	TAPE & FINISH PASSENGER ELEVATOR - TOWER L1	6	10-Jan-23	18-Jan-23
TPR1-2180	TAPE & FINISH J1/J2 ELEVATOR WALLS - TOWER L1	6	19-Jan-23	26-Jan-23
TPR1-1080	DRYWALL STAIR 1-2 - TOWER L1	2	24-Apr-23	25-Apr-23
TPR1-1090	DRYWALL STAIR 3-4 - TOWER L1	2	26-Apr-23	27-Apr-23
TPR1-1100	TAPE & FINISH STAIR 1-2 - TOWER L1	6	26-Apr-23	03-May-23
TPR1-1110	TAPE & FINISH STAIR 3-4 - TOWER L1	6	04-May-23	11-May-23
TPR1-1120	FINISHES STAIR 1-2 - TOWER L1	4	04-May-23	09-May-23
TSTR1-100	PRIME AND FIRST COAT PAINT STAIR 1-2 - TOWER L1	5	04-May-23	10-May-23
TSTR1-110	PRIME AND FIRST COAT PAINT STAIR 3-4 - TOWER L1	5	12-May-23	18-May-23
TPR1-1160	FINISHES STAIR 3-4 - TOWER L1	4	04-Jan-24	09-Jan-24
DETENTION AREA				
TFIND1-100	FRAME PARTITION WALLS DETENTION AREA - TOWER L1	4	30-Dec-22	05-Jan-23
TRID1-120	ROUGH-IN OVERHEAD MECHANICAL DETENTION AREA - TOWER L1	8	06-Jan-23	18-Jan-23
TRID1-130	ROUGH-IN OVERHEAD PLUMBING DETENTION AREA - TOWER L1	5	19-Jan-23	25-Jan-23
TRID1-160	ROUGH-IN OVERHEAD FIRE SUPPRESSION DETENTION AREA - TC	5	19-Jan-23	25-Jan-23
TRID1-140	ROUGH-IN OVERHEAD ELECTRICAL DETENTION AREA - TOWER L1	5	20-Jan-23	26-Jan-23
TRID1-150	ROUGH-IN OVERHEAD LOW VOLTAGE DETENTION AREA - TOWEF	5	20-Jan-23	26-Jan-23
TRID1-100	ROUGH-IN IN-WALL PLUMBING DETENTION AREA - TOWER L1	5	03-Feb-23	09-Feb-23
TRID1-110	ROUGH-IN IN WALL ELECTRICAL DETENTION AREA - TOWER L1	2	08-Feb-23	09-Feb-23
TFIND2-1330	INSULATE WALLS - TOWER L1	1	10-Feb-23	10-Feb-23
TFIND2-1340	IN-WALL INSPECTION TOWER L1	1	13-Feb-23	13-Feb-23
TDR1-1020	DETENTION METAL CEILINGS AT DETENTION AREA - TOWER L1	10	14-Apr-23	27-Apr-23
TFIND1-160	DRYWALL PARTITION WALLS DETENTION AREA - TOWER L1	3	14-Apr-23	18-Apr-23
TFIND1-280	TAPE/ FINISH PARTITION WALLS DETENTION AREA - TOWER L1	7	19-Apr-23	27-Apr-23
TDR1-1050	DOORS AND HARDWARE DETENTION AREA - TOWER L1	10	28-Apr-23	11-May-23
TDR1-1070	PAINT DETENTION AREA - TOWER L1	10	12-May-23	25-May-23
TDR1-1090	CEILING GRID AND DEVICE TILES DETENTION AREA - TOWER L1	6	30-May-23	06-Jun-23
TDR1-1060	DETENTION FIXTURES DETENTION AREA - TOWER L1	10	30-May-23	12-Jun-23
TFIND1-170	CASEWORK & TOPS DETENTION AREA - TOWER L1	7	30-May-23	07-Jun-23
TFIND1-180	INSTALL PLUMBING COMBI UNITS DETENTION AREA - TOWER L1	5	30-May-23	05-Jun-23
TFIND1-190	PLUMBING FIXTURES DETENTION AREA - TOWER L1	5	06-Jun-23	12-Jun-23
TDR1-1100	COMPLETE MECHANICAL IN CEILING DETENTION AREA - TOWER I	5	07-Jun-23	13-Jun-23
TFIND1-220	COMPLETE OVERHEAD FIRE SUPPRESSION IN CEILING - L1	2	07-Jun-23	08-Jun-23
TFIND1-240	COMPLETE ELECTRICAL IN CEILING DETENTION AREA - TOWER L1	5	07-Jun-23	13-Jun-23
TFIND1-250	COMPLETE PLUMBING IN CEILING DETENTION AREA - TOWER L1	5	07-Jun-23	13-Jun-23
TFIND1-260	COMPLETE LOW VOLTAGE IN CEILING DETENTION AREA - TOWEF	5	07-Jun-23	13-Jun-23
TDR1-1080	TRIM DETENTION AREA - TOWER L1	3	08-Jun-23	12-Jun-23
TDR1-1130	ABOVE CEILING INSPECTION DETENTION AREA - TOWER L1	1	14-Jun-23	14-Jun-23
TFIND1-270	INSTALL SEISMIC BRACING DETENTION AREA - TOWER L1	10	14-Jun-23	27-Jun-23
TDR1-1110	DROP BALANCE OF TILES DETENTION AREA - TOWER L1	10	28-Jun-23	12-Jul-23
TDR1-1120	SEAL CONCRETE FLOORS DETENTION AREA - TOWER L1	4	13-Jul-23	18-Jul-23
TFIND1-200	INSTALL GRILLS & DIFFUSERS IN CEILING DETENTION AREA - TOV	3	13-Jul-23	17-Jul-23
TFIND1-210	INSTALL LIGHTING & TRIM DETENTION AREA - TOWER L1	2	13-Jul-23	14-Jul-23
TFIND1-290	INSTALL INTERIOR GLAZING - TOWER L1	10	13-Jul-23	26-Jul-23
RESTRICTED COORIDOR				
T1-G-260	FRAME RESTRICTED CORRIDOR WALLS - TOWER L1	5	22-Feb-23	28-Feb-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
T1-G-300	ELECTRICAL WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L	5	01-Mar-23	07-Mar-23
TRIG1-150	LOW-VOLTAGE WALL ROUGH-IN RESTRICTED CORRIDOR - TOWE	5	01-Mar-23	07-Mar-23
TRIG1-160	PLUMBING WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L1	5	01-Mar-23	07-Mar-23
T1-G-280	INSULATE WALLS RESTRICTED CORRIDOR WALLS - TOWER L1	1	08-Mar-23	08-Mar-23
T1-G-290	IN WALL INSPECTION RESTRICTED CORRIDOR WALLS - TOWER L1	1	09-Mar-23	09-Mar-23
T1-G-680	DRYWALL RESTRICTED CORRIDOR - TOWER L1	5	14-Apr-23	20-Apr-23
T1-G-1160	TAPE & FINISH RESTRICTED CORRIDOR - TOWER L1	7	04-May-23	12-May-23
T1-G-780	PRIME & PAINT RESTRICTED CORRIDOR - TOWER L1	5	15-May-23	19-May-23
T1-G-1520	PULL WIRE RESTRICTED CORRIDOR WALLS - TOWER L1	2	15-May-23	16-May-23
T1-G-830	CEILING GRID & DEVICE TILES RESTRICTED CORRIDOR - TOWER	4	22-May-23	25-May-23
T1-G-880	HVAC TRIM RESTRICTED CORRIDOR - TOWER L1	3	22-May-23	24-May-23
TFING1-660	ELECTRICAL TRIM RESTRICTED CORRIDOR - TOWER L1	2	22-May-23	23-May-23
TFING1-680	LOW VOLTAGE FINISHES RESTRICTED CORRIDOR - TOWER L1	2	30-May-23	31-May-23
TFING1-690	FIRE SUPPRESSION HEADS RESTRICTED CORRIDOR - TOWER L1	2	30-May-23	31-May-23
T1-G-840	INSTALL SEISMIC SUPPORTS RESTRICTED CORRIDOR - TOWER L	10	01-Jun-23	14-Jun-23
TFING1-730	ABOVE CEILING INSPECTION RESTRICTED CORRIDOR WALLS - T	1	15-Jun-23	15-Jun-23
T1-G-930	DROP BALANCE OF CEILING TILES RESTRICTED CORRIDOR - TOW	2	16-Jun-23	19-Jun-23
T1-G-270	INSTALL INTERIOR GLAZING RESTRICTED CORRIDOR WALLS - TC	10	20-Jun-23	03-Jul-23
T1-G-940	INSTALL FLOORING & BASE RESTRICTED CORRIDOR - TOWER L1	5	05-Jul-23	11-Jul-23
JUDGES CHAMBERS / JUDGES RR / FCC				
TJD1-1000	FRAME JURY DELIBERATION/JUDGE'S CHAMBERS & JUDGE R/R A	7	22-Feb-23	02-Mar-23
TFINJ1-110	INSTALL DOOR FRAMES AT JUDICIAL SPACES - TOWER L1	3	03-Mar-23	07-Mar-23
TOHJ1-100	MECHANICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L1	7	15-Mar-23	23-Mar-23
TOHJ1-110	PLUMBING ROUGH-IN AT JUDICIAL SPACES - TOWER L1	5	17-Mar-23	23-Mar-23
TOHJ1-120	ELECTRICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L1	6	24-Mar-23	31-Mar-23
TOHJ1-130	LOW VOLTAGE ROUGH-IN AT JUDICIAL SPACES - TOWER L1	6	24-Mar-23	31-Mar-23
TOHJ1-140	INSULATE WALLS AT JUDICIAL SPACES - TOWER L1	1	03-Apr-23	03-Apr-23
TOHJ1-150	IN WALL INSPECTION AT JUDICIAL SPACES - TOWER L1	1	04-Apr-23	04-Apr-23
TFINJ1-140	DRYWALL WALLS AT JUDICIAL SPACES - TOWER L1	6	21-Apr-23	28-Apr-23
TFINJ1-210	TAPE & FINISH WALLS AT JUDICIAL SPACES - TOWER L1	7	25-Apr-23	03-May-23
TFINJ1-150	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT JUDICIAL SPA	3	04-May-23	08-May-23
TFINJ1-160	CEILING GRID & DEVICE TILES AT JUDICIAL SPACES - TOWER L1	6	09-May-23	16-May-23
TJD1-1030	MECHANICAL TRIM AT JUDICIAL SPACES - TOWER L1	5	17-May-23	23-May-23
TJD1-1040	ELECTRICAL TRIM AT JUDICIAL SPACES - TOWER L1	5	17-May-23	23-May-23
TJD1-1050	PLUMBING TRIM AT JUDICIAL SPACES - TOWER L1	5	17-May-23	23-May-23
TJD1-1060	FIRE SUPPRESSION TRIM AT JUDICIAL SPACES - TOWER L1	5	17-May-23	23-May-23
TJD1-1070	LOW VOLTAGE TRIM AT JUDICIAL SPACES - TOWER L1	5	17-May-23	23-May-23
TJD1-1130	INSTALL SEISMIC BRACING JUDICIAL SPACES - TOWER L1	10	24-May-23	08-Jun-23
TJD1-1120	ABOVE CEILING INSPECTION AT JUDICIAL SPACES - TOWER L1	1	09-Jun-23	09-Jun-23
TFINJ1-190	DROP CEILING TILE AT JUDICIAL SPACES - TOWER L1	2	12-Jun-23	13-Jun-23
TFINJ1-220	INSTALL INTERIOR GLAZING AT JUDICIAL SPACES - TOWER L1	10	14-Jun-23	27-Jun-23
TJD1-1080	INSTALL CASEWORK AT JUDICIAL SPACES - TOWER L1	5	23-Jun-23	29-Jun-23
TFINJ1-170	FLOOR PREP AT JUDICIAL SPACES - TOWER L1	1	30-Jun-23	30-Jun-23
TFINJ1-180	INSTALL CARPET & BASE AT JUDICIAL SPACES - TOWER L1	4	03-Jul-23	07-Jul-23
TFINJ1-200	DOORS & HARDWARE AT JUDICIAL SPACES - TOWER L1	5	10-Jul-23	14-Jul-23
COURTROOMS				
TCR1-1000	FRAME PERIMETER WALLS AT COURTROOMS - TOWER L1	5	01-Mar-23	07-Mar-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TCR1-1020	FLOOR LEVEL AT COURTROOMS - TOWER L1	3	08-Mar-23	10-Mar-23
TOHC1-130	MECHANICAL ROUGH-IN DROPS AT COURTROOMS - TOWER L1	7	24-Mar-23	03-Apr-23
TOHC1-110	PLUMBING ROUGH-IN DROPS AT COURTROOMS - TOWER L1	5	04-Apr-23	10-Apr-23
TOHC1-200	FIRE SUPPRESSION ROUGH-IN DROPS AT COURTROOMS - TOWEI	5	04-Apr-23	10-Apr-23
TOHC1-120	ELECTRICAL ROUGH-IN DROPS AT COURTROOMS - TOWER L1	6	06-Apr-23	13-Apr-23
TOHC1-190	LOW VOLTAGE ROUGH-IN DROPS AT COURTROOMS - TOWER L1	6	06-Apr-23	13-Apr-23
TOHC1-230	ELECTRICAL ROUGH-IN DROPS AT COURTROOMS - TOWER L1	6	06-Apr-23	13-Apr-23
TOHC1-210	INSTALL WALL BACKING - TOWER L1	2	14-Apr-23	17-Apr-23
TCR1-1050	FRAME CEILINGS AT COURTROOMS - TOWER L1	5	18-Apr-23	24-Apr-23
TCR1-1130	INSULATE WALLS AT COURTROOMS - TOWER L1	3	18-Apr-23	20-Apr-23
TCR1-1440	IN WALL INSPECTION AT COURTROOMS - TOWER L1	1	21-Apr-23	21-Apr-23
TCR1-1060	CEILING FIXTURES PRE-DRYWALL AT COURTROOMS - TOWER L1	5	25-Apr-23	01-May-23
TCR1-1100	FRAME LOW WALLS AT COURTROOMS - TOWER L1	3	25-Apr-23	27-Apr-23
TFINC1-130	INSTALL DOOR FRAMES AT COURTROOMS - TOWER L1	3	28-Apr-23	02-May-23
TCR1-1070	DRYWALL COURTROOMS - TOWER L1	6	02-May-23	09-May-23
TCR1-1110	TAPE & FINISH COURTROOMS - TOWER L1	7	10-May-23	18-May-23
TFINC1-140	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT COURTROOM:	3	19-May-23	23-May-23
TCR1-1080	CEILING GRID & DEVICE TILES AT COURTROOMS - TOWER L1	7	24-May-23	05-Jun-23
TCR1-1170	DOORS & HARDWARE AT COURTROOMS - TOWER L1	3	24-May-23	30-May-23
TFINC1-180	ELECTRICAL COMPLETE CEILING CONNECTIONS AT COURTROOM	2	24-May-23	25-May-23
TFINC1-210	FIRE SUPPRESSION COMPLETE CEILING CONNECTIONS AT COUI	2	24-May-23	25-May-23
TCR1-1180	FABRIC WALL PANELS AT COURTROOMS - TOWER L1	3	25-May-23	31-May-23
TCR1-1140	ACCESS FLOORING AT COURTROOMS - TOWER L1	5	02-Jun-23	08-Jun-23
TCR1-1200	MECHANICAL COMPLETE CEILING CONNECTIONS AT COURTROOI	2	06-Jun-23	07-Jun-23
TFINC1-190	PLUMBING COMPLETE CEILING CONNECTIONS AT COURTROOMS	2	06-Jun-23	07-Jun-23
TFINC1-200	LOW VOLTAGE COMPLETE CEILING CONNECTIONS AT COURTROC	2	06-Jun-23	07-Jun-23
TCR1-1030	INSTALL SEISMIC SUPPORTS AT COURTROOMS - TOWER L1	10	08-Jun-23	21-Jun-23
TFINC1-150	ABOVE CEILING INSPECTION AT COURTROOMS - TOWER L1	1	22-Jun-23	22-Jun-23
TCR1-1090	DROP CEILING TILE AT COURTROOMS - TOWER L1	2	23-Jun-23	26-Jun-23
TCR1-1120	INSTALL INTERIOR GLAZING AT COURTROOMS - TOWER L1	10	27-Jun-23	11-Jul-23
TCR1-1150	CASEWORK AT COURTROOMS - TOWER L1	10	30-Jun-23	14-Jul-23
TCR1-1430	INSTALL RAILING - TOWER L1	10	17-Jul-23	28-Jul-23
TCR1-1160	INSTALL CARPET & BASE AT COURTROOMS - TOWER L1	4	31-Jul-23	03-Aug-23
TCR1-1190	FF & E AT COURTROOMS - TOWER L1	4	04-Aug-23	09-Aug-23
TCR1-1210	CLOSE-UP CASEWORK ELEC/LV TRIM & ACCESSORIES	2	10-Aug-23	11-Aug-23
PUBLIC GALLERY / OFFICE SPACES				
TFING1-1080	INSTALL SEISMIC SUPPORTS PUBLIC GALLERY & OFFICE SPACES	10	11-Jul-23	24-Jul-23
TFING1-1020	ABOVE CEILING INSPECTION AT T-BAR PUBLIC GALLERY & OFFIC	1	25-Jul-23	25-Jul-23
IN-WALL ROUGH-INS				
TFING1-310	FRAME INTERIOR WALLS PUBLIC GALLERY & OFFICE SPACES - T	10	03-Mar-23	16-Mar-23
TFING1-330	IN WALL COUNTERTOP SUPPORTS PUBLIC GALLERY & OFFICE SF	3	07-Mar-23	09-Mar-23
TRIG1-100	ROUGH-IN WALL PLUMBING PUBLIC GALLERY & OFFICE SPACES -	8	09-Mar-23	20-Mar-23
TFING1-350	HM DOOR FRAMES PUBLIC GALLERY & OFFICE SPACES - TOWER	5	10-Mar-23	16-Mar-23
TRIG1-110	ROUGH-IN WALL LOW VOLTAGE PUBLIC GALLERY & OFFICE SPAC	8	16-Mar-23	27-Mar-23
TRIG1-120	ROUGH-IN WALL ELECTRICAL PUBLIC GALLERY & OFFICE SPACES	8	16-Mar-23	27-Mar-23
TFING1-210	INSTALL ELEVATOR DOOR FRAMES & ELEVATOR FRONTS PUBLIC	8	17-Mar-23	28-Mar-23
TRIG1-130	ROUGH-IN MECHANICAL CONTROLS PUBLIC GALLERY & OFFICE S	8	20-Mar-23	29-Mar-23

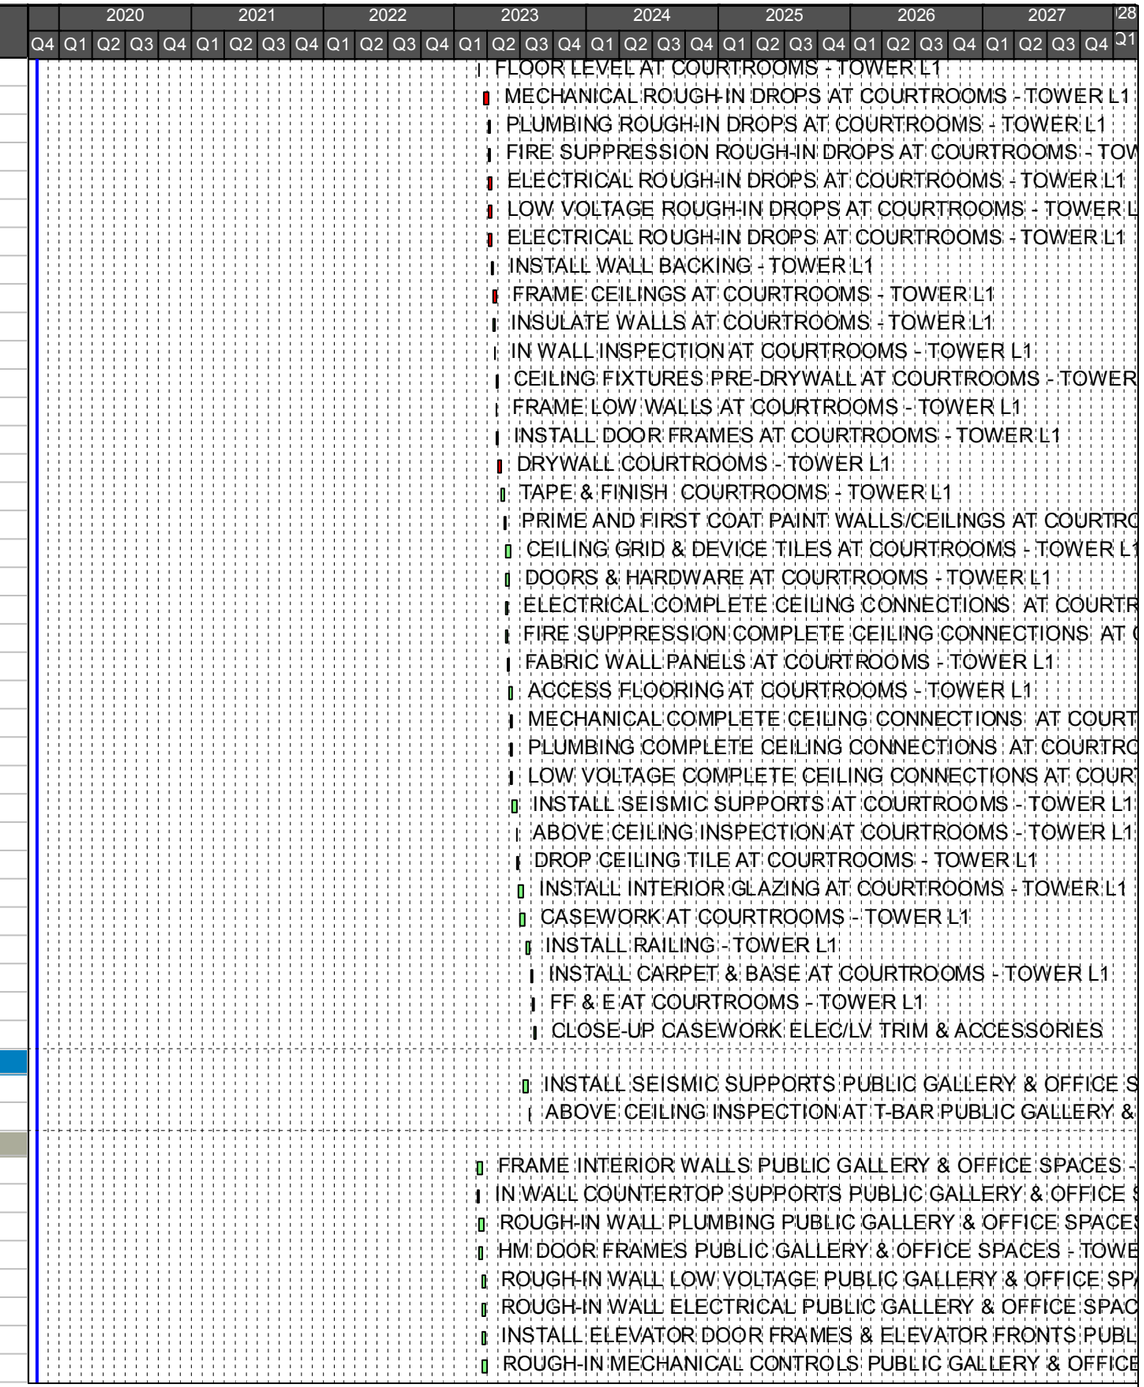

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TFING1-460	WALL BACKING PUBLIC GALLERY & OFFICE SPACES - TOWER L1	8	23-Mar-23	03-Apr-23
TFING1-560	INSULATE WALLS PUBLIC GALLERY & OFFICE SPACES - TOWER L1	4	04-Apr-23	07-Apr-23
TFING1-480	IN-WALL INSPECTION PUBLIC GALLERY & OFFICE SPACES - TOWE	1	10-Apr-23	10-Apr-23
OVERHEAD ROUGH-INS				
T1-G-670	FRAME GYP CEILING PUBLIC GALLERY & OFFICE SPACES - TOWE	7	23-Mar-23	31-Mar-23
TRIG1-180	ROUGH-IN MECHANICAL AT HARDLIDS PUBLIC GALLERY & OFFICE	3	03-Apr-23	05-Apr-23
TRIG1-190	ROUGH-IN ELECTRICAL AT HARDLIDS PUBLIC GALLERY & OFFICE	4	06-Apr-23	11-Apr-23
TFING1-540	ABOVE CEILING INSPECTION AT HARDLIDS PUBLIC GALLERY & OI	1	12-Apr-23	12-Apr-23
FINISHES				
TFING1-610	INSTALL LOW VOLTAGE PUBLIC GALLERY & OFFICE SPACES - TO\	4	03-Apr-23	06-Apr-23
TFING1-570	DRYWALL WALLS PUBLIC GALLERY & OFFICE SPACES - TOWER L1	4	10-May-23	15-May-23
TFING1-630	MEASURE & FAB INTERIOR GLAZING FRAMES PUBLIC GALLERY &	1	16-May-23	16-May-23
TFING1-710	FURNISH MATERIAL FOR INTERIOR GLAZING FRAMES PUBLIC GA	10	17-May-23	01-Jun-23
TFING1-580	DRYWALL HARDLIDS & SOFFITS PUBLIC GALLERY & OFFICE SPAC	6	18-May-23	25-May-23
TFING1-640	TAPE & FINISH PUBLIC GALLERY & OFFICE SPACES - TOWER L1	11	30-May-23	13-Jun-23
TFING1-650	PRIME & PAINT 1ST COAT PUBLIC GALLERY & OFFICE SPACES - T	7	09-Jun-23	19-Jun-23
TFING1-860	CEILING GRID PUBLIC GALLERY & OFFICE SPACES - TOWER L1	10	14-Jun-23	27-Jun-23
T1-G-730	INSTALL LIGHT FIXTURES AT HARDLIDS PUBLIC GALLERY & OFFIC	4	20-Jun-23	23-Jun-23
T1-G-1140	DOORS & HARDWARE PUBLIC GALLERY & OFFICE SPACES - TOW	5	20-Jun-23	26-Jun-23
TFING1-1110	MOBILE STORAGE SHELVING PUBLIC GALLERY & OFFICE SPACES	4	20-Jun-23	23-Jun-23
TFING1-1190	ELECTRICAL COVER PLATES PUBLIC GALLERY & OFFICE SPACES	3	20-Jun-23	22-Jun-23
TFING1-1130	SEAL CONCRETE FLOORS AT MAINTANANCE ROOMS - TOWER L1	3	20-Jun-23	22-Jun-23
TFING1-620	FIRE SUPPRESSION HEADS AT HARDLIDS PUBLIC GALLERY & OFI	4	20-Jun-23	23-Jun-23
TFING1-720	INSTALL HVAC CONTROLS PUBLIC GALLERY & OFFICE SPACES - T	5	20-Jun-23	26-Jun-23
TFING1-1150	INSTALL GLAZING PUBLIC GALLERY & OFFICE SPACES - TOWER L1	8	23-Jun-23	05-Jul-23
MS1-1040	EXPANSION JOINT AT TOWER CONNECTION - TOWER L1	2	28-Jun-23	29-Jun-23
TFING1-960	CASEWORK & TOPS PUBLIC GALLERY & OFFICE SPACES - TOWE	10	28-Jun-23	12-Jul-23
TOHG1-220	LIGHT FIXTURES IN T-BAR CEILING PUBLIC GALLERY & OFFICE SI	5	28-Jun-23	05-Jul-23
TFING1-890	FIRE SUPPRESSION HEADS AT GRID PUBLIC GALLERY & OFFICE S	8	28-Jun-23	10-Jul-23
TFING1-900	MECHANICAL DIFFUSERS & REGISTERS PUBLIC GALLERY & OFFI	7	28-Jun-23	07-Jul-23
TFING1-970	LOW VOLTAGE FINISH/DEVICES PUBLIC GALLERY & OFFICE SPAC	7	28-Jun-23	07-Jul-23
TFING1-980	FIRE ALARM DEVICES PUBLIC GALLERY & OFFICE SPACES - TOW	7	28-Jun-23	07-Jul-23
TFING1-990	INSTALL SERVICE COUNTER/WINDOW PUBLIC GALLERY & OFFICE	5	30-Jun-23	07-Jul-23
TFING1-870	INSTALL DEVICE TILES PUBLIC GALLERY & OFFICE SPACES - TOV	3	06-Jul-23	10-Jul-23
TFING1-750	FLOOR PREP AT LOBBY & PUBLIC GALLERY & OFFICE SPACES - T	4	11-Jul-23	14-Jul-23
TFING1-1060	INSTALL EDGE GUARDS PUBLIC GALLERY & OFFICE SPACES - TO	7	13-Jul-23	21-Jul-23
TFING1-850	INSTALL FLOOR TILE IN PUBLIC GALLERY & OFFICE SPACES - TO\	12	17-Jul-23	01-Aug-23
TFING1-1030	DROP CEILING TILE PUBLIC GALLERY & OFFICE SPACES - TOWEF	8	26-Jul-23	04-Aug-23
TFING1-1010	INSTALL FLOOR BASE AT TILE WALLS PUBLIC GALLERY & OFFICE	5	02-Aug-23	08-Aug-23
TFING1-1100	FIRE EXTINGUISHERS CABINETS PUBLIC GALLERY & OFFICE SPA	2	07-Aug-23	08-Aug-23
TFING1-1040	INSTALL WALL TILE PUBLIC GALLERY & OFFICE SPACES - TOWER	5	09-Aug-23	15-Aug-23
TFING1-840	INSTALL METAL WALL PANELS/ TRIM PUBLIC GALLERY & OFFICE S	3	09-Aug-23	11-Aug-23
T1-G-1130	BENCHES FF&E PUBLIC GALLERY & OFFICE SPACES- TOWER L1	2	14-Aug-23	15-Aug-23
TFING1-1070	PLUMBING FIXTURES PUBLIC GALLERY & OFFICE SPACES - TOWI	5	16-Aug-23	22-Aug-23
TFING1-1120	OFOI VISUAL DISPLAY SURFACES PUBLIC GALLERY & OFFICE SP	2	16-Jan-24	17-Jan-24
PUBLIC / STAFF RESTROOMS/ SHERIFF LOCKER ROOM				
ROUGH-INS AND FINISHES				

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
T1-R-100	FRAME PUBLIC / STAFF RR - TOWER L1	4	13-Mar-23	16-Mar-23
TRIR1-100	ROUGH-IN WALL PLUMBING PUBLIC / STAFF RR - TOWER L1	5	17-Mar-23	23-Mar-23
TRIR1-110	ROUGH-IN WALL ELECTRICAL PUBLIC / STAFF RR - TOWER L1	5	21-Mar-23	27-Mar-23
TFINR1-130	WALL BACKING PUBLIC / STAFF RR - TOWER L1	2	28-Mar-23	29-Mar-23
TFINR1-140	INSULATE WALLS PUBLIC / STAFF RR - TOWER L1	1	30-Mar-23	30-Mar-23
TFINR1-150	DRYWALL WALLS PUBLIC / STAFF RR - TOWER L1	2	12-May-23	15-May-23
TFINR1-160	FRAME HARDLID CEILINGS & SOFFITS PUBLIC / STAFF RR - TOWE	4	16-May-23	19-May-23
TFINR1-170	OVERHEAD MEP CEILING DROPS PUBLIC / STAFF RR - TOWER L1	4	22-May-23	25-May-23
TFINR1-220	DRYWALL HARDLIDS & SOFFITS PUBLIC / STAFF RR - TOWER L1	3	30-May-23	01-Jun-23
TFINR1-230	TAPE & FINISH PUBLIC / STAFF RR - TOWER L1	7	05-Jun-23	13-Jun-23
TFINR1-240	PRIME & PAINT 1ST COAT PUBLIC / STAFF RR - TOWER L1	3	15-Jun-23	19-Jun-23
TFINR1-250	FLOOR PREP AT PUBLIC / STAFF RR - TOWER L1	2	20-Jun-23	21-Jun-23
TFINR1-260	PULL & TERMINATE ELECTRICAL/ LOW VOLTAGE WIRE - TOWER L1	2	20-Jun-23	21-Jun-23
TFINR1-270	ELECTRICAL/FIRE ALARM FINISH/DEVICES PUBLIC / STAFF RR - T	4	22-Jun-23	27-Jun-23
TFINR1-280	INSTALL FLOOR & WALL TILE IN PUBLIC / STAFF RR - TOWER L1	9	22-Jun-23	05-Jul-23
TFINR1-290	CASEWORK & TOPS PUBLIC / STAFF RR - TOWER L1	3	10-Jul-23	12-Jul-23
TFINR1-300	FIRE SUPPRESSION HEADS PUBLIC / STAFF RR - TOWER L1	1	13-Jul-23	13-Jul-23
TFINR1-310	MECHANICAL DIFFUSERS & REGISTERS PUBLIC / STAFF RR - TOW	2	13-Jul-23	14-Jul-23
TFINR1-320	PLUMBING FIXTURES PUBLIC / STAFF RR - TOWER L1	4	17-Jul-23	20-Jul-23
TFINR1-330	DOORS & HARDWARE PUBLIC / STAFF RR - TOWER L1	7	21-Jul-23	31-Jul-23
TFINR1-340	INSTALL PARTITIONS AND ACCESSORIES PUBLIC / STAFF RR - TO	7	07-Sep-23	15-Sep-23
SALLYPORT				
SFIN1-100	FIRE SUPPRESSION HANGERS SALLYPORT - TOWER L1	1	14-Apr-23	14-Apr-23
SFIN1-110	ELECTRICAL HANGERS SALLYPORT - TOWER L1	1	14-Apr-23	14-Apr-23
SFIN1-120	MECHANICAL HANGERS SALLYPORT - TOWER L1	1	14-Apr-23	14-Apr-23
SFIN1-130	INSTALL FIRE SUPPRESSION MAINS AND BRANCHES SALLYPORT	3	17-Apr-23	19-Apr-23
SFIN1-140	INSTALL ELECTRICAL MAINS AND BRANCHES SALLYPORT - TOWE	5	20-Apr-23	26-Apr-23
SFIN1-150	INSTALL MECHANICAL MAINS AND BRANCHES SALLYPORT - TOWI	5	27-Apr-23	03-May-23
SPSTR-1020	FRAMING, ROOF, AND ROLLUP DOOR SUPPORTS SALLYPORT - TC	5	01-May-23	05-May-23
SFIN1-160	SHEATHING SALLYPORT - TOWER L1	2	08-May-23	09-May-23
SPSTR-1030	DECK/MEP ROUGH/PLACE - SALLYPORT	10	10-May-23	23-May-23
SFIN1-170	INSTALL DOOR FRAMES SALLYPORT - TOWER L1	4	10-May-23	15-May-23
SFIN1-180	PRIME AND FIRST COAT SALLYPORT - TOWER L1	3	16-May-23	18-May-23
SFIN1-190	INSTALL DOORS AND HARDWARE - TOWER L1	1	16-May-23	16-May-23
SPSTR-1040	ROOF DECK CURE SALLYPORT - TOWER L1	10	24-May-23	02-Jun-23
SPENCL-1020	OVERHEAD ROLL-UP DOORS SALLYPORT - TOWER L1	10	09-Jun-23	22-Jun-23
TSP1-1000	FINAL PAINT SALLYPORT - TOWER L1	3	16-Jan-24	18-Jan-24
SFIN1-200	INSTALL FIRE SUPPRESSION HEADS SALLYPORT - TOWER L1	1	19-Jan-24	19-Jan-24
SFIN1-210	INSTALL MECHANICAL TRIM SALLYPORT - TOWER L1	1	22-Jan-24	22-Jan-24
SFIN1-220	INSTALL ELECTRICAL WIRE AND TRIM SALLYPORT - TOWER L1	3	23-Jan-24	25-Jan-24
TSP1-1010	WORK COMPLETION LIST SALLYPORT - TOWER L1	0	26-Jan-24	26-Jan-24
MECHANICAL BUILDING				
MB-100	SEAL CONCRETE FLOOR	4	01-May-23	04-May-23
MB-120	INSTALL & TEST SWITCHGEAR	10	05-May-23	18-May-23
MB-130	TERMINATE SWITCHGEAR	12	09-May-23	24-May-23
MB-140	INSTALL O/H FIRE SUPPRESSION	3	09-May-23	11-May-23
MB-150	INSTALL HVAC	4	12-May-23	17-May-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
MB-160	INSTALL PLUMBING	4	18-May-23	23-May-23
MB-170	INSTALL ELECTRICAL & LOW VOLTAGE	6	24-May-23	02-Jun-23
MB-190	CONNECT MEP TO GENERATOR	10	25-May-23	09-Jun-23
MB-200	INSTALL STAIRS & HANDRAILS	3	12-Jun-23	14-Jun-23
MB-210	PAINT INTERIOR	3	15-Jun-23	19-Jun-23
MB-220	INSTALL O/H COILING DOORS	3	20-Jun-23	22-Jun-23
MB-110	INSTALL (MID) TRANSFORMER	10	23-Jun-23	07-Jul-23
MB-240	(MID) PULL ELECTRICAL FEEDER	3	23-Jun-23	27-Jun-23
MB-180	INSTALL (MID) METER	3	10-Jul-23	12-Jul-23
MANLIFT BAY				
LOB1-100	FRAME MANLIFT BAY - TOWER L1	3	25-Jul-23	27-Jul-23
LOB1-110	ROUGH-IN MEP MANLIFT BAY - TOWER L1	5	28-Jul-23	03-Aug-23
LOB1-120	FINISHES MANLIFT BAY - TOWER L1	15	04-Aug-23	24-Aug-23
LOB1-130	TRIM MANLIFT BAY - TOWER L1	5	25-Aug-23	31-Aug-23
LEVEL 2				
LEVEL 2 FULL FLOOR				
MS2-1000	PRE-WELD EXTERIOR & PARTITION CLIPS	7	22-Nov-22	02-Dec-22
MS3-1040	FIREPROOF PRIORITY WALLS/PERIMETER - TOWER L2	5	13-Dec-22	19-Dec-22
MS2-1020	FIREPROOF BALANCE OF FLOORS - TOWER L2	5	28-Dec-22	04-Jan-23
MS2-1030	EDGE OF SLAB FIRE SAFE	5	23-Jan-23	27-Jan-23
TFING1-2040	FIELD MEASURE FOR WINDOW COVERINGS - TOWER L2	1	20-Jun-23	20-Jun-23
TFING1-2050	FABRICATE WINDOW COVERINGS - TOWER L2	10	16-Jan-24	29-Jan-24
TPG2-1170	FINAL PAINT - TOWER L2	7	19-Jan-24	29-Jan-24
TFING1-1450	WINDOW COVERINGS PUBLIC GALLERY - TOWER L2	4	30-Jan-24	02-Feb-24
TFING1-1680	INSTALL SIGNAGE - TOWER L2	5	30-Jan-24	05-Feb-24
TFING1-1690	INT. CERTIFICATION & READY FOR PUNCH - TOWER L2	1	06-Feb-24	06-Feb-24
OVERHEAD ROUGH-INS				
TFING1-1430	LAYOUT FOR CLIPS AND TRACK - TOWER L2	3	16-Dec-22	20-Dec-22
TFING1-1420	INSTALL TOP TRACK - TOWER L2	2	21-Dec-22	22-Dec-22
TFING1-2010	INSTALL FIRE SUPPRESSION HANGERS - TOWER L2	4	06-Jan-23	11-Jan-23
TFING1-2000	INSTALL ELECTRICAL HANGERS - TOWER L2	4	12-Jan-23	18-Jan-23
TFING1-8270	INSTALL LOW VOLTAGE HANGERS - TOWER L2	4	12-Jan-23	18-Jan-23
TFING1-1520	INSTALL PLUMBING HANGERS - TOWER L2	5	19-Jan-23	25-Jan-23
TFING1-1990	INSTALL MECHANICAL HANGERS - TOWER L2	5	19-Jan-23	25-Jan-23
TFING1-1700	FIRE SUPPRESSION MAINS - TOWER L2	5	26-Jan-23	01-Feb-23
TOHG1-280	O/H WASTE & VENT - TOWER L2	7	26-Jan-23	03-Feb-23
TPG2-1000	ONE SIDE TIE INTO EXTERIOR - TOWER L2	2	30-Jan-23	31-Jan-23
TOHG1-230	O/H ELECTRICAL MAINS - TOWER L2	8	30-Jan-23	08-Feb-23
TOHG1-1550	O/H LOW VOLTAGE MAINS - TOWER L2	8	30-Jan-23	08-Feb-23
TOHG1-240	O/H PLUMBING MAINS - TOWER L2	6	06-Feb-23	13-Feb-23
TOHG1-1700	O/H PLUMBING BRANCHES - TOWER L2	7	14-Feb-23	24-Feb-23
TOHG1-270	O/H MECHANICAL MAINS - TOWER L2	10	27-Feb-23	10-Mar-23
TFING1-1710	HANG VAV'S - TOWER L2	8	01-Mar-23	10-Mar-23
TOHG1-300	O/H HYDRONIC PIPING - TOWER L2	5	10-Mar-23	16-Mar-23
TOHG1-290	O/H MECHANICAL BRANCHES - TOWER L2	15	13-Mar-23	31-Mar-23
TFING1-1530	FIRE SUPPRESSION BRANCHES - TOWER L2	10	20-Mar-23	31-Mar-23
TOHG1-310	O/H ELECTRICAL BRANCHES - TOWER L2	3	27-Mar-23	29-Mar-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

Activity ID	Activity Name	Original Duration	Start	Finish
TOHG1-1560	O/H LOW VOLTAGE BRANCHES - TOWER L2	3	27-Mar-23	29-Mar-23
TFING1-1470	O/H HVAC CONTROLS - TOWER L2	2	30-Mar-23	31-Mar-23
TOHG1-250	O/H LOW VOLTAGE - TOWER L2	2	30-Mar-23	31-Mar-23
TOHG1-260	O/H SECURITY - TOWER L2	2	03-Apr-23	04-Apr-23
PRIORITY WALLS (IDF/ ELEC/ SHAFT/ STAIRS)				
IDF/ ELECTRICAL ROOM/ CENTRAL CONTROL				
TPR2-1050	FRAME IDF ROOM, ELECTRICAL ROOM, STAIRS - TOWER L2	5	06-Jan-23	12-Jan-23
TPR2-1060	ROUGH-IN IDF / ELECTRICAL ROOMS - TOWER L2	5	13-Jan-23	20-Jan-23
TELECRI2-100	ROUGH-IN PLUMBING IDF / ELECTRICAL ROOMS - TOWER L2	2	13-Jan-23	17-Jan-23
TELECRI2-110	ROUGH-IN IDF / ELECTRICAL ROOMS - TOWER L2	4	17-Jan-23	20-Jan-23
TELECRI2-120	ROUGH-IN MECHANICAL IDF / ELECTRICAL ROOMS - TOWER L2	3	18-Jan-23	20-Jan-23
TPR2-1070	DRYWALL IDF/ ELECTRICAL ROOMS - TOWER L2	7	23-Jan-23	31-Jan-23
TPR2-1340	TAPE & FINISH IDF/ELECTRICAL ROOMS - TOWER L2	7	28-Apr-23	08-May-23
TELEC2-130	PAINT IDF/ELECTRICAL ROOMS - TOWER L2	3	09-May-23	11-May-23
TELEC2-140	SEAL FLOORS IDF/ELECTRICAL ROOMS - TOWER L2	2	12-May-23	15-May-23
TPR2-1120	DOORS & HARDWARE - TOWER L2	2	16-May-23	17-May-23
TPR2-1100	ELECTRICAL AND IDF, PANELS AND RACKS - TOWER L2	15	30-May-23	19-Jun-23
MEP SHAFTS				
TPR2-1040	INSTALL MEPF IN SHAFTS - TOWER L2	8	23-Dec-22	05-Jan-23
TPR2-1020	FRAME HVAC SHAFTS & DRYWALL C/R SIDE - TOWER L2	3	06-Jan-23	10-Jan-23
TPR2-1110	DRYWALL HVAC SHAFTS - TOWER L2	3	28-Apr-23	02-May-23
TPR2-1350	TAPE & FINISH HVAC SHAFTS - TOWER L2	7	03-May-23	11-May-23
ELEVATOR/ STAIR SHAFTS				
TPR2-1000	FRAME PASSENGER ELEVATOR HOISTWAYS - TOWER L2	3	11-Jan-23	13-Jan-23
TPR2-1010	FRAME J1/J2 ELEVATOR WALLS - TOWER L2	3	11-Jan-23	13-Jan-23
TPR1-2190	DRYWALL PASSENGER ELEVATOR - TOWER L2	2	17-Jan-23	18-Jan-23
TPR1-2200	DRYWALL J1/J2 ELEVATOR WALLS - TOWER L2	2	19-Jan-23	20-Jan-23
TPR1-2210	TAPE & FINISH PASSENGER ELEVATOR - TOWER L2	6	19-Jan-23	26-Jan-23
TDR2-1000	FRAME AT H1/H2 - ELEVATOR FRAMES DETENTION AREA - TOWEF	2	24-Jan-23	25-Jan-23
TPR1-2220	TAPE & FINISH J1/J2 ELEVATOR WALLS - TOWER L2	6	27-Jan-23	03-Feb-23
TPR2-1080	DRYWALL STAIR 1-2 - TOWER L2	2	03-May-23	04-May-23
TPR2-1090	DRYWALL STAIR 3-4 - TOWER L2	2	05-May-23	08-May-23
TPR2-1130	TAPE & FINISH STAIR 1-2 - TOWER L2	6	02-Aug-23	09-Aug-23
TPR2-1150	TAPE & FINISH STAIR 3-4 - TOWER L2	6	10-Aug-23	17-Aug-23
TPR2-1140	FINISHES STAIR 1-2 - TOWER L2	4	10-Aug-23	15-Aug-23
TELEC2-150	PRIME AND FIRST COAT PAINT STAIR 1-2 - TOWER L2	5	10-Aug-23	16-Aug-23
TPR2-1160	FINISHES STAIR 3-4 - TOWER L2	4	18-Aug-23	23-Aug-23
TELEC2-160	PRIME AND FIRST COAT PAINT STAIR 3-4 - TOWER L2	5	18-Aug-23	24-Aug-23
DETENTION AREA				
TFIND2-100	FRAME PARTITION WALLS DETENTION AREA - TOWER L2	2	24-Jan-23	25-Jan-23
TOHD2-100	ROUGH-IN OVERHEAD MECHANICAL DETENTION AREA - TOWER L2	5	26-Jan-23	01-Feb-23
TRID2-110	ROUGH-IN IN-WALL PLUMBING DETENTION AREA - TOWER L2	2	10-Feb-23	13-Feb-23
TRID2-130	ROUGH-IN - IN WALL ELECTRICAL DETENTION AREA - TOWER L2	2	13-Feb-23	14-Feb-23
TOHD2-110	ROUGH-IN OVERHEAD PLUMBING DETENTION AREA - TOWER L2	2	11-Apr-23	12-Apr-23
TOHD2-240	ROUGH-IN OVERHEAD FIRE SUPPRESSION DETENTION AREA - TC	2	11-Apr-23	12-Apr-23
TOHD3-100	ROUGH-IN OVERHEAD ELECTRICAL DETENTION AREA - TOWER L2	3	12-Apr-23	14-Apr-23
TOHD3-170	ROUGH-IN OVERHEAD LOW VOLTAGE DETENTION AREA - TOWER	3	12-Apr-23	14-Apr-23

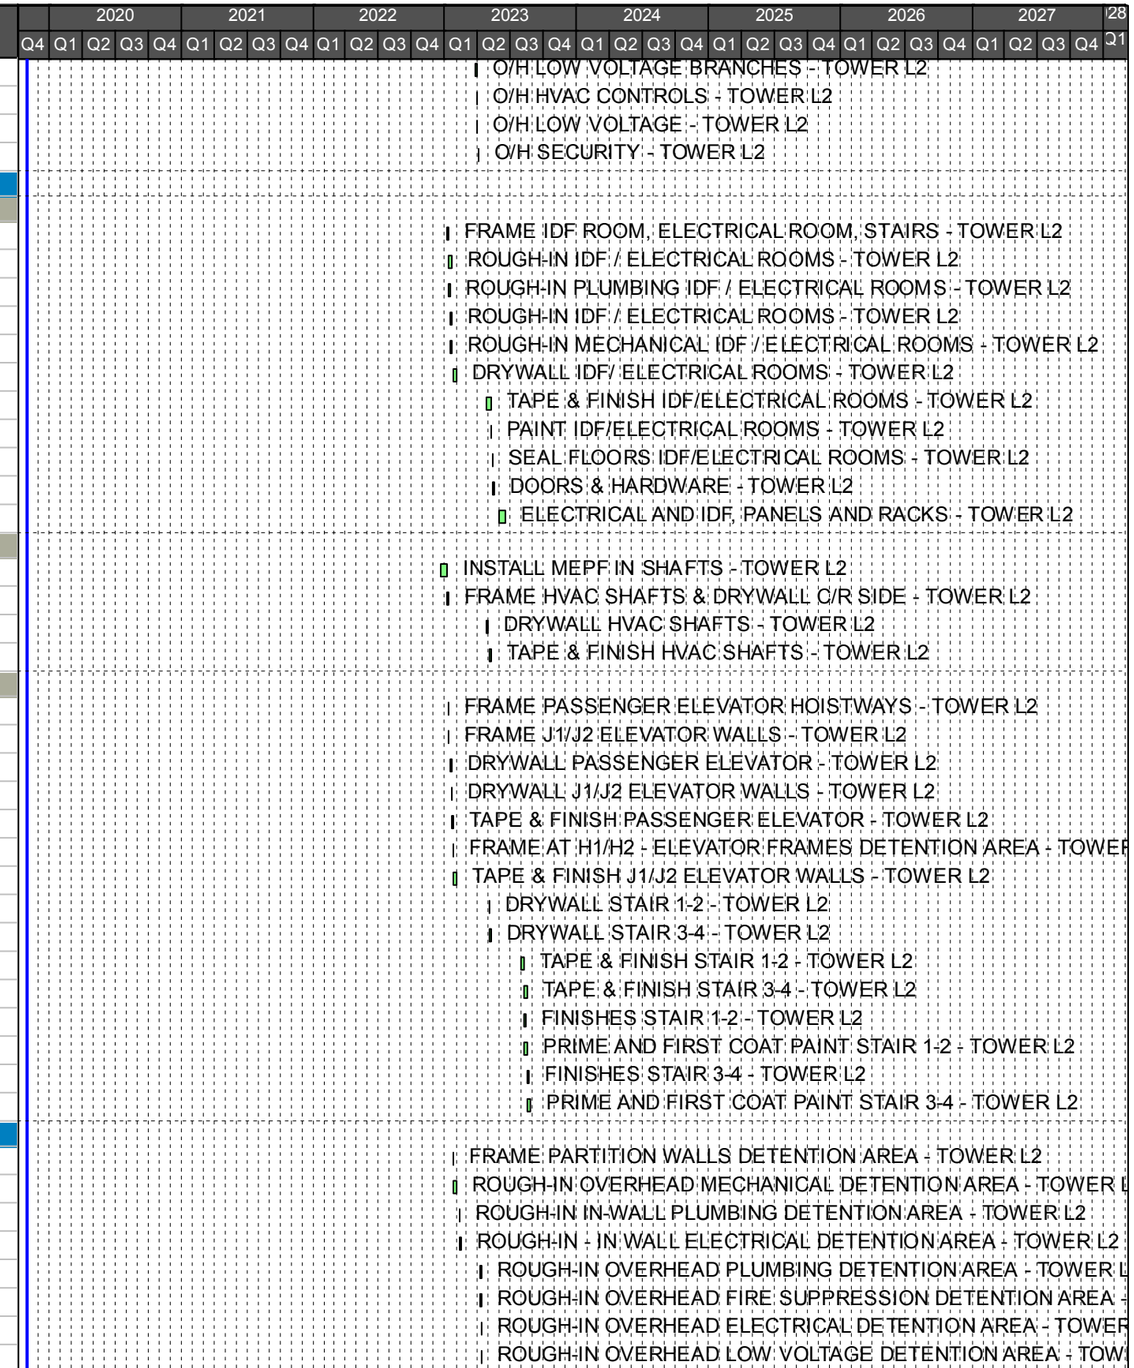

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TDR2-1010	DETENTION METAL CEILINGS DETENTION AREA - TOWER L2	5	17-Apr-23	21-Apr-23
TFIND2-1350	INSULATE WALLS - TOWER L2	1	17-Apr-23	17-Apr-23
TFIND2-1360	IN-WALL INSPECTION TOWER L2	1	18-Apr-23	18-Apr-23
TFIND2-160	DRYWALL PARTITION WALLS DETENTION AREA - TOWER L2	3	19-Apr-23	21-Apr-23
TFIND2-310	TAPE/ FINISH PARTITION WALLS DETENTION AREA - TOWER L2	7	20-Apr-23	28-Apr-23
TFIND2-180	PAINT DETENTION AREA - TOWER L2	5	01-May-23	05-May-23
TFIND2-170	DOORS AND HARDWARE DETENTION AREA - TOWER L2	4	08-May-23	11-May-23
TFIND2-200	DETENTION FIXTURES DETENTION AREA - TOWER L2	10	08-May-23	19-May-23
TFIND2-220	INSTALL PLUMBING COMBI UNITS DETENTION AREA - TOWER L2	5	08-May-23	12-May-23
TFIND2-230	PLUMBING FIXTURES DETENTION AREA - TOWER L2	5	15-May-23	19-May-23
TDR1-1140	CEILING GRID AND DEVICE TILES DETENTION AREA - TOWER L2	6	30-May-23	06-Jun-23
TFIND2-250	INSTALL GRILLS & DIFFUSERS IN CEILING DETENTION AREA - TOV	3	07-Jun-23	09-Jun-23
TFIND2-260	INSTALL LIGHTING & TRIM DETENTION AREA - TOWER L2	2	07-Jun-23	08-Jun-23
TDR1-1150	COMPLETE MECHANICAL IN CEILING DETENTION AREA - TOWER I	5	07-Jun-23	13-Jun-23
TFIND1-300	COMPLETE OVERHEAD FIRE SUPPRESSION IN CEILING - L2	2	07-Jun-23	08-Jun-23
TFIND1-310	COMPLETE ELECTRICAL IN CEILING DETENTION AREA - TOWER L2	5	07-Jun-23	13-Jun-23
TFIND1-320	COMPLETE PLUMBING IN CEILING DETENTION AREA - TOWER L2	5	07-Jun-23	13-Jun-23
TFIND1-330	COMPLETE LOW VOLTAGE IN CEILING DETENTION AREA - TOWEF	5	07-Jun-23	13-Jun-23
TFIND2-360	ABOVE CEILING INSPECTION DETENTION AREA - TOWER L2	1	14-Jun-23	14-Jun-23
TFIND1-550	INSTALL SEISMIC BRACING DETENTION AREA - TOWER L2	10	14-Jun-23	27-Jun-23
TFIND2-290	DROP BALANCE OF TILES DETENTION AREA - TOWER L2	3	28-Jun-23	30-Jun-23
TFIND2-300	SEAL CONCRETE FLOORS DETENTION AREA - TOWER L2	10	03-Jul-23	17-Jul-23
TFIND2-410	INSTALL INTERIOR GLAZING - TOWER L2	10	03-Jul-23	17-Jul-23
TFIND2-210	CASEWORK & TOPS DETENTION AREA - TOWER L2	7	13-Jul-23	21-Jul-23
TDR2-1040	TRIM DETENTION AREA - TOWER L2	3	24-Jul-23	26-Jul-23
RESTRICTED CORRIDOR				
TPG2-1010	FRAME RESTRICTED CORRIDOR WALLS - TOWER L2	3	13-Mar-23	15-Mar-23
T1-G-1170	ELECTRICAL WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L	5	16-Mar-23	22-Mar-23
TRIG1-980	LOW-VOLTAGE WALL ROUGH-IN RESTRICTED CORRIDOR - TOWEI	5	16-Mar-23	22-Mar-23
TRIG1-990	PLUMBING WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L2	5	16-Mar-23	22-Mar-23
T1-G-1380	INSULATE WALLS RESTRICTED CORRIDOR WALLS - TOWER L2	1	23-Mar-23	23-Mar-23
T1-G-1390	IN WALL INSPECTION RESTRICTED CORRIDOR WALLS - TOWER L2	1	24-Mar-23	24-Mar-23
TPG2-1060	DRYWALL RESTRICTED CORRIDOR - TOWER L2	5	16-May-23	22-May-23
TPG2-2140	TAPE & FINISH RESTRICTED CORRIDOR - TOWER L2	7	23-May-23	02-Jun-23
T1-G-1240	PRIME & PAINT RESTRICTED CORRIDOR - TOWER L2	5	05-Jun-23	09-Jun-23
T1-G-1530	PULL WIRE RESTRICTED CORRIDOR WALLS - TOWER L2	2	05-Jun-23	06-Jun-23
TPG2-1080	CEILING GRID & DEVICE TILES RESTRICTED CORRIDOR - TOWER	4	12-Jun-23	15-Jun-23
T1-G-1250	HVAC TRIM RESTRICTED CORRIDOR - TOWER L2	3	12-Jun-23	14-Jun-23
TFING1-8040	ELECTRICAL TRIM RESTRICTED CORRIDOR - TOWER L2	2	12-Jun-23	13-Jun-23
TFING1-8050	LOW VOLTAGE FINISHES RESTRICTED CORRIDOR - TOWER L2	2	16-Jun-23	19-Jun-23
TFING1-8060	FIRE SUPPRESSION HEADS RESTRICTED CORRIDOR - TOWER L2	2	16-Jun-23	19-Jun-23
TPG2-2160	INSTALL SEISMIC SUPPORTS RESTRICTED CORRIDOR - TOWER I	10	20-Jun-23	03-Jul-23
TPG2-1030	ABOVE CEILING INSPECTION RESTRICTED CORRIDOR WALLS - T	1	05-Jul-23	05-Jul-23
TPG2-1120	DROP BALANCE OF CEILING TILES RESTRICTED CORRIDOR - TOW	4	06-Jul-23	11-Jul-23
TPG2-1020	INSTALL INTERIOR GLAZING RESTRICTED CORRIDOR WALLS - TC	10	12-Jul-23	25-Jul-23
TPG2-1090	INSTALL FLOORING & BASE RESTRICTED CORRIDOR - TOWER L2	5	26-Jul-23	01-Aug-23
JURY DELIBERATION / JUDGES CHAMBERS / JUDGES RESTROOMS				

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TJD2-1000	METAL PANELS & SOUND CAP TIE-IN TO EXTERIOR AT JUDICIAL S	3	05-Jan-23	09-Jan-23
TJD2-1010	FRAME JURY DELIBERATION/JUDGE'S CHAMBERS & JUDGE R/R -	7	17-Mar-23	27-Mar-23
TOHJ2-100	MECHANICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L2	7	28-Mar-23	05-Apr-23
TFINJ2-110	INSTALL DOOR FRAMES AT JUDICIAL SPACES - TOWER L2	3	28-Mar-23	30-Mar-23
TOHJ2-110	PLUMBING ROUGH-IN AT JUDICIAL SPACES - TOWER L2	5	13-Apr-23	19-Apr-23
TOHJ2-120	ELECTRICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L2	6	17-Apr-23	24-Apr-23
TOHJ2-130	LOW VOLTAGE ROUGH-IN AT JUDICIAL SPACES - TOWER L2	6	17-Apr-23	24-Apr-23
TOHJ1-160	INSULATE WALLS AT JUDICIAL SPACES - TOWER L2	1	25-Apr-23	25-Apr-23
TOHJ1-170	IN WALL INSPECTION AT JUDICIAL SPACES - TOWER L2	1	26-Apr-23	26-Apr-23
TFINJ2-140	DRYWALL WALLS AT JUDICIAL SPACES - TOWER L2	6	23-May-23	01-Jun-23
TFINJ2-240	TAPE & FINISH WALLS AT JUDICIAL SPACES - TOWER L2	7	05-Jun-23	13-Jun-23
TFINJ2-170	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT JUDICIAL SPA	3	14-Jun-23	16-Jun-23
TFINJ2-180	CEILING GRID & DEVICE TILES AT JUDICIAL SPACES - TOWER L2	6	19-Jun-23	26-Jun-23
TJD2-1040	MECHANICAL TRIM AT JUDICIAL SPACES - TOWER L2	5	27-Jun-23	03-Jul-23
TJD2-1350	ELECTRICAL TRIM AT JUDICIAL SPACES - TOWER L2	5	27-Jun-23	03-Jul-23
TJD2-1360	PLUMBING TRIM AT JUDICIAL SPACES - TOWER L2	5	27-Jun-23	03-Jul-23
TJD2-1370	FIRE SUPPRESSION TRIM AT JUDICIAL SPACES - TOWER L2	5	27-Jun-23	03-Jul-23
TJD2-1380	LOW VOLTAGE TRIM AT JUDICIAL SPACES - TOWER L2	5	27-Jun-23	03-Jul-23
TFINJ2-230	INSTALL SEISMIC BRACING JUDICIAL SPACES - TOWER L2	10	05-Jul-23	18-Jul-23
TJD1-1085	INSTALL CASEWORK AT JUDICIAL SPACES - TOWER L2	5	17-Jul-23	21-Jul-23
TJD2-1050	ABOVE CEILING INSPECTION AT JUDICIAL SPACES - TOWER L2	1	19-Jul-23	19-Jul-23
TFINJ2-210	DROP CEILING TILE AT JUDICIAL SPACES - TOWER L2	2	20-Jul-23	21-Jul-23
TJD2-1030	INSTALL INTERIOR GLAZING AT JUDICIAL SPACES - TOWER L2	10	24-Jul-23	04-Aug-23
TFINJ2-190	FLOOR PREP AT JUDICIAL SPACES - TOWER L2	1	07-Aug-23	07-Aug-23
TFINJ2-200	INSTALL BASE AT JUDICIAL SPACES - TOWER L2	4	08-Aug-23	11-Aug-23
TFINJ2-220	DOORS & HARDWARE AT JUDICIAL SPACES - TOWER L2	5	14-Aug-23	18-Aug-23
COURTROOMS				
TCR2-1000	FRAME PERIMETER WALLS AT COURTROOMS - TOWER L2	10	16-Mar-23	29-Mar-23
TCR2-1020	FLOOR LEVEL AT COURTROOMS - TOWER L2	8	30-Mar-23	10-Apr-23
TRIC2-100	MECHANICAL ROUGH-IN DROPS AT COURTROOMS - TOWER L2	8	11-Apr-23	20-Apr-23
TRIC2-110	PLUMBING ROUGH-IN DROPS AT COURTROOMS - TOWER L2	6	20-Apr-23	27-Apr-23
TRIC2-300	FIRE SUPPRESSION ROUGH-IN DROPS AT COURTROOMS - TOWEI	6	20-Apr-23	27-Apr-23
TRIC2-120	ELECTRICAL ROUGH-IN DROPS AT COURTROOMS - TOWER L2	8	25-Apr-23	04-May-23
TRIC2-290	LOW VOLTAGE ROUGH-IN DROPS AT COURTROOMS - TOWER L2	8	25-Apr-23	04-May-23
TCR2-1010	INSTALL WALL BACKING - TOWER L2	2	05-May-23	08-May-23
TCR2-1050	FRAME CEILINGS AT COURTROOMS - TOWER L2	8	09-May-23	18-May-23
TCR1-1450	INSULATE WALLS AT COURTROOMS - TOWER L2	3	09-May-23	11-May-23
TCR1-1460	IN WALL INSPECTION AT COURTROOMS - TOWER L2	1	12-May-23	12-May-23
TCR2-1060	CEILING FIXTURES PRE-DRYWALL AT COURTROOMS - TOWER L2	5	19-May-23	25-May-23
TCR2-1090	FRAME LOW WALLS AT COURTROOMS - TOWER L2	6	19-May-23	30-May-23
TCR2-1070	DRYWALL GYP CEILINGS AT COURTROOMS - TOWER L2	8	30-May-23	08-Jun-23
TCR2-1130	ACCESS FLOORING LAYOUT AT COURTROOMS - TOWER L2	3	31-May-23	02-Jun-23
TFINC2-130	INSTALL DOOR FRAMES AT COURTROOMS - TOWER L2	3	31-May-23	02-Jun-23
TCR2-1030	DRYWALL WALLS AT COURTROOMS - TOWER L2	5	02-Jun-23	08-Jun-23
TCR2-1240	TAPE & FINISH GYP CEILINGS AT COURTROOMS - TOWER L2	7	09-Jun-23	19-Jun-23
TCR2-1040	TAPE & FINISH WALLS AT COURTROOMS - TOWER L2	6	14-Jun-23	21-Jun-23
TCR2-1120	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT COURTROOM	3	20-Jun-23	22-Jun-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TCR2-1080	CEILING GRID & DEVICE TILES AT COURTROOMS - TOWER L2	7	23-Jun-23	03-Jul-23
TCR2-1150	ACCESS FLOORING AT COURTROOMS - TOWER L2	12	23-Jun-23	11-Jul-23
TCR2-1100	MECHANICAL COMPLETE CEILING CONNECTIONS AT COURTROOM	5	05-Jul-23	11-Jul-23
TCR2-1260	ELECTRICAL COMPLETE CEILING CONNECTIONS AT COURTROOM	5	05-Jul-23	11-Jul-23
TCR2-1270	PLUMBING COMPLETE CEILING CONNECTIONS AT COURTROOMS	5	05-Jul-23	11-Jul-23
TCR2-1280	FIRE SUPPRESSION COMPLETE CEILING CONNECTIONS AT COUR	5	05-Jul-23	11-Jul-23
TCR2-1290	LOW VOLTAGE COMPLETE CEILING CONNECTIONS AT COURTROC	5	05-Jul-23	11-Jul-23
TCR2-1220	INSTALL SEISMIC SUPPORTS AT COURTROOMS - TOWER L2	10	12-Jul-23	25-Jul-23
TFINC1-310	ABOVE CEILING INSPECTION AT COURTROOMS - TOWER L2	1	26-Jul-23	26-Jul-23
TCR2-1110	DROP BALANCE OF CEILING TILES AT COURTROOMS - TOWER L2	4	27-Jul-23	01-Aug-23
TCR2-1160	CASEWORK AT COURTROOMS - TOWER L2	12	02-Aug-23	17-Aug-23
TCR2-1140	INSTALL INTERIOR GLAZING AT COURTROOMS - TOWER L2	10	02-Aug-23	15-Aug-23
TCR2-1250	INSTALL RAILING - TOWER L2	10	18-Aug-23	31-Aug-23
TCR2-1180	FINISH FLOORING & BASE AT COURTROOMS - TOWER L2	8	05-Sep-23	14-Sep-23
TCR2-1190	DOORS & HARDWARE AT COURTROOMS - TOWER L2	4	05-Sep-23	08-Sep-23
TCR2-1200	FABRIC WALL PANELS AT COURTROOMS - TOWER L2	4	11-Sep-23	14-Sep-23
TCR2-1210	FF & E AT COURTROOMS - TOWER L2	5	11-Sep-23	15-Sep-23
TCR2-1170	JURY SEATING AT COURTROOMS - TOWER L2	4	15-Sep-23	20-Sep-23
TCR2-1230	CLOSE-UP CASEWORK ELEC/LV TRIM & ACCESSORIES - TOWER L2	4	21-Sep-23	26-Sep-23
PUBLIC GALLERY				
IN-WALL ROUGH-INS				
TFING1-1720	FRAME INTERIOR WALLS PUBLIC GALLERY - TOWER L2	5	03-Apr-23	07-Apr-23
TFING1-1600	IN WALL COUNTERTOP SUPPORTS PUBLIC GALLERY - TOWER L2	2	05-Apr-23	06-Apr-23
TFING1-1860	HM DOOR FRAMES PUBLIC GALLERY - TOWER L2	2	06-Apr-23	07-Apr-23
TRIG1-220	ROUGH-IN WALL PLUMBING PUBLIC GALLERY - TOWER L2	2	07-Apr-23	10-Apr-23
TFING1-1910	INSTALL ELEVATOR DOOR FRAMES & ELEVATOR FRONTS PUBLIC	8	10-Apr-23	19-Apr-23
TFING1-1970	INSTALL STORE FRONT FRAMES PUBLIC GALLERY - TOWER L2	2	10-Apr-23	11-Apr-23
TRIG1-210	ROUGH-IN WALL LOW VOLTAGE PUBLIC GALLERY - TOWER L2	8	11-Apr-23	20-Apr-23
TRIG1-230	ROUGH-IN WALL ELECTRICAL PUBLIC GALLERY - TOWER L2	2	11-Apr-23	12-Apr-23
TRIG1-200	ROUGH-IN MECHANICAL CONTROLS PUBLIC GALLERY - TOWER L2	2	13-Apr-23	14-Apr-23
TFING1-1730	WALL BACKING PUBLIC GALLERY - TOWER L2	1	18-Apr-23	18-Apr-23
TFING1-1560	IN-WALL INSPECTION PUBLIC GALLERY - TOWER L2	1	21-Apr-23	21-Apr-23
OVERHEAD ROUGH-INS				
TPG2-1140	FRAME GYP CEILING PUBLIC GALLERY - TOWER L2	7	10-Apr-23	18-Apr-23
TRIG1-250	ROUGH-IN MECHANICAL AT HARDLIDS PUBLIC GALLERY - TOWER	2	19-Apr-23	20-Apr-23
TRIG1-240	ROUGH-IN ELECTRICAL AT HARDLIDS PUBLIC GALLERY - TOWER L	2	21-Apr-23	24-Apr-23
TFING1-1760	ABOVE CEILING INSPECTION AT HARDLIDS PUBLIC GALLERY - TO	1	25-Apr-23	25-Apr-23
FINISHES				
TFING1-1580	INSULATE WALLS PUBLIC GALLERY - TOWER L2	4	24-Apr-23	27-Apr-23
TFING1-1610	DRYWALL WALLS PUBLIC GALLERY - TOWER L2	4	09-Jun-23	14-Jun-23
TPG2-1160	DRYWALL CEILINGS PUBLIC GALLERY - TOWER L2	3	15-Jun-23	19-Jun-23
TFING1-1500	MEASURE & FAB INTERIOR GLAZING FRAMES PUBLIC GALLERY -	1	15-Jun-23	15-Jun-23
TFING1-1510	FURNISH MATERIAL FOR INTERIOR GLAZING FRAMES PUBLIC GAL	10	16-Jun-23	29-Jun-23
TFING1-1620	TAPE & FINISH PUBLIC GALLERY - TOWER L2	6	22-Jun-23	29-Jun-23
TFING1-1590	PRIME & PAINT 1ST COAT PUBLIC GALLERY - TOWER L2	3	05-Jul-23	07-Jul-23
TPG2-1150	INSTALL LIGHT FIXTURES AT HARDLIDS PUBLIC GALLERY - TOWE	4	10-Jul-23	13-Jul-23
TPG2-1180	CEILING GRID PUBLIC GALLERY - TOWER L2	4	10-Jul-23	13-Jul-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development

PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19

Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TPG2-1250	DOORS & HARDWARE PUBLIC GALLERY - TOWER L2	2	10-Jul-23	11-Jul-23
TFING1-1570	ELECTRICAL COVER PLATES PUBLIC GALLERY - TOWER L2	3	10-Jul-23	12-Jul-23
TFING1-1980	INSTALL STORE FRONT GLAZING PUBLIC GALLERY - TOWER L2	5	10-Jul-23	14-Jul-23
TFING1-2030	FIRE SUPPRESSION HEADS AT HARDLIDS PUBLIC GALLERY - TOV	4	10-Jul-23	13-Jul-23
TFING1-2060	INSTALL HVAC CONTROLS PUBLIC GALLERY - TOWER L2	5	10-Jul-23	14-Jul-23
TFING1-1670	INSTALL GLAZING PUBLIC GALLERY - TOWER L2	8	13-Jul-23	24-Jul-23
TPG2-1220	MECHANICAL DIFFUSERS & REGISTERS PUBLIC GALLERY - TOWE	3	14-Jul-23	18-Jul-23
TPG2-1200	INSTALL DEVICE TILES PUBLIC GALLERY - TOWER L2	3	14-Jul-23	18-Jul-23
TFING1-1780	CASEWORK PUBLIC GALLERY - TOWER L2	10	14-Jul-23	27-Jul-23
TOHG1-320	LIGHT FIXTURES IN T-BAR CEILING PUBLIC GALLERY - TOWER L2	2	14-Jul-23	17-Jul-23
TFING1-1810	FIRE SUPPRESSION HEADS AT GRID PUBLIC GALLERY - TOWER L2	2	14-Jul-23	17-Jul-23
TFING1-1820	MECHANICAL DIFFUSERS & REGISTERS AT GRID PUBLIC GALLER	2	14-Jul-23	17-Jul-23
TFING1-1900	FIRE ALARM DEVICES PUBLIC GALLERY - TOWER L2	2	14-Jul-23	17-Jul-23
TFING1-1630	INSTALL SEISMIC SUPPORTS PUBLIC GALLERY - TOWER L2	10	18-Jul-23	31-Jul-23
TFING1-1950	FLOOR PREP AT LOBBY & PUBLIC GALLERY - TOWER L2	4	19-Jul-23	24-Jul-23
TFING1-1960	INSTALL FLOOR TILE IN PUBLIC GALLERY - TOWER L2	7	25-Jul-23	02-Aug-23
TFING1-1750	INSTALL EDGE GUARDS PUBLIC GALLERY - TOWER L2	2	28-Jul-23	31-Jul-23
TFING1-1830	ABOVE CEILING INSPECTION AT T-BAR PUBLIC GALLERY - TOWEF	1	01-Aug-23	01-Aug-23
TPG2-1210	DROP CEILING TILE PUBLIC GALLERY - TOWER L2	4	02-Aug-23	07-Aug-23
TFING1-1940	INSTALL FLOOR BASE AT TILE WALLS PUBLIC GALLERY - TOWER	5	03-Aug-23	09-Aug-23
TFING1-1770	FIRE EXTINGUISHERS CABINETS PUBLIC GALLERY - TOWER L2	2	08-Aug-23	09-Aug-23
TPG2-1190	INSTALL WALL TILE PUBLIC GALLERY - TOWER L2	5	10-Aug-23	16-Aug-23
TFING1-1930	INSTALL METAL WALL PANELS/ TRIM PUBLIC GALLERY - TOWER L2	3	10-Aug-23	14-Aug-23
TPG2-1240	BENCHES FF&E PUBLIC GALLERY - TOWER L2	2	15-Aug-23	16-Aug-23
TFING1-1850	PLUMBING FIXTURES PUBLIC GALLERY - TOWER L2	2	17-Aug-23	18-Aug-23
TFING1-1490	OFOI VISUAL DISPLAY SURFACES PUBLIC GALLERY - TOWER L2	2	30-Jan-24	31-Jan-24
TFING1-2020	INSTALL LOW VOLTAGE PUBLIC GALLERY - TOWER L2	4	30-Jan-24	02-Feb-24
PUBLIC / STAFF RESTROOMS				
TRR2-1000	FRAME PUBLIC / STAFF RR - TOWER L2	4	10-Apr-23	13-Apr-23
TRIR2-100	ROUGH-IN WALL PLUMBING PUBLIC / STAFF RR - TOWER L2	3	14-Apr-23	18-Apr-23
TFINR2-110	FIELD MEASURE FOR TOILET PARTITIONS PUBLIC / STAFF RR - TC	1	14-Apr-23	14-Apr-23
TFINR2-120	FABRICATE TOILET PARTITIONS PUBLIC / STAFF RR - TOWER L2	30	17-Apr-23	30-May-23
TRIR2-110	ROUGH-IN WALL ELECTRICAL PUBLIC / STAFF RR - TOWER L2	3	18-Apr-23	20-Apr-23
TRIR2-120	ROUGH-IN MECHANICAL AT HARDLIDS PUBLIC / STAFF RR - TOWE	3	20-Apr-23	24-Apr-23
TRR2-1020	FINISHES PUBLIC / STAFF RR - TOWER L2	12	25-Apr-23	10-May-23
TFINR2-150	WALL BACKING PUBLIC / STAFF RR - TOWER L2	2	25-Apr-23	26-Apr-23
TFINR2-160	INSULATE WALLS PUBLIC / STAFF RR - TOWER L2	1	27-Apr-23	27-Apr-23
TFINR2-170	DRYWALL WALLS PUBLIC / STAFF RR - TOWER L2	2	13-Jun-23	14-Jun-23
TFINR2-190	FRAME HARDLID CEILINGS & SOFFITS PUBLIC / STAFF RR - TOWE	4	15-Jun-23	20-Jun-23
TFINR1-380	OVERHEAD MEP CEILING DROPS PUBLIC / STAFF RR - TOWER L2	4	21-Jun-23	26-Jun-23
TFINR2-180	DRYWALL HARDLIDS & SOFFITS PUBLIC / STAFF RR - TOWER L2	3	27-Jun-23	29-Jun-23
TFINR2-200	TAPE & FINISH PUBLIC / STAFF RR - TOWER L2	7	30-Jun-23	11-Jul-23
TFINR2-210	PRIME & PAINT 1ST COAT PUBLIC / STAFF RR - TOWER L2	3	13-Jul-23	17-Jul-23
TFINR2-220	FLOOR PREP PUBLIC / STAFF RR - TOWER L2	2	18-Jul-23	19-Jul-23
TFINR2-230	PULL & TERMINATE ELECTRICAL/ LOW VOLTAGE WIRE PUBLIC / S	2	18-Jul-23	19-Jul-23
TFINR2-240	ELECTRICAL/FIRE ALARM FINISH/DEVICES PUBLIC / STAFF RR - T	4	20-Jul-23	25-Jul-23
TFINR2-250	INSTALL FLOOR & WALL TILE PUBLIC / STAFF RR - TOWER L2	9	20-Jul-23	01-Aug-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

Activity ID	Activity Name	Original Duration	Start	Finish
TRR2-1030	MEP TRIM PUBLIC / STAFF RR - TOWER L2	7	26-Jul-23	03-Aug-23
TFINR2-260	CASEWORK & TOPS PUBLIC / STAFF RR - TOWER L2	3	02-Aug-23	04-Aug-23
TFINR2-280	MECHANICAL DIFFUSERS & REGISTERS PUBLIC / STAFF RR - TOW	2	04-Aug-23	07-Aug-23
TFINR2-270	FIRE SUPPRESSION HEADS PUBLIC / STAFF RR - TOWER L2	1	07-Aug-23	07-Aug-23
TFINR2-290	PLUMBING FIXTURES PUBLIC / STAFF RR - TOWER L2	4	08-Aug-23	11-Aug-23
TFINR2-300	DOORS & HARDWARE PUBLIC / STAFF RR - TOWER L2	7	14-Aug-23	22-Aug-23
TFINR2-310	INSTALL PARTITIONS AND ACCESSORIES PUBLIC / STAFF RR - TO	7	07-Sep-23	15-Sep-23
MANLIFT BAY				
LOB2-100	FRAME MANLIFT BAY - TOWER L2	3	25-Jul-23	27-Jul-23
LOB2-110	ROUGH-IN MEP MANLIFT BAY - TOWER L2	5	28-Jul-23	03-Aug-23
LOB2-120	FINISHES MANLIFT BAY - TOWER L2	15	04-Aug-23	24-Aug-23
LOB2-130	TRIM MANLIFT BAY - TOWER L2	5	25-Aug-23	31-Aug-23
LEVEL 3				
LEVEL 3 FULL FLOOR				
MS3-1000	PRE-WELD EXTERIOR & PARTITION CLIPS	7	19-Dec-22	28-Dec-22
MS3-1010	FIREPROOF PRIORITY WALLS/PERIMETER - TOWER L3	5	29-Dec-22	05-Jan-23
MS3-1020	FIREPROOF BALANCE OF FLOORS	5	05-Jan-23	11-Jan-23
MS3-1030	EDGE OF SLAB FIRE SAFE	5	15-Feb-23	23-Feb-23
TFING1-5540	FIELD MEASURE FOR WINDOW COVERINGS - TOWER L3	1	19-Jul-23	19-Jul-23
TFING1-5550	FABRICATE WINDOW COVERINGS - TOWER L3	10	25-Jan-24	07-Feb-24
TPG3-1170	FINAL PAINT - TOWER L3	7	30-Jan-24	07-Feb-24
TFING1-5090	WINDOW COVERINGS PUBLIC GALLERY - TOWER L3	4	08-Feb-24	13-Feb-24
TFING1-5260	INSTALL SIGNAGE - TOWER L3	5	08-Feb-24	14-Feb-24
TFING1-5270	INT. CERTIFICATION & READY FOR PUNCH - TOWER L3	1	15-Feb-24	15-Feb-24
OVERHEAD ROUGH-INS				
TFING1-5080	LAYOUT FOR CLIPS AND TRACK - TOWER L3	3	21-Dec-22	23-Dec-22
TFING1-5070	INSTALL TOP TRACK - TOWER L3	2	23-Dec-22	27-Dec-22
TFING1-5510	INSTALL FIRE SUPPRESSION HANGERS - TOWER L3	4	12-Jan-23	18-Jan-23
TFING1-5500	INSTALL ELECTRICAL HANGERS - TOWER L3	4	19-Jan-23	24-Jan-23
TFING1-8280	INSTALL LOW VOLTAGE HANGERS - TOWER L3	4	19-Jan-23	24-Jan-23
TFING1-5140	INSTALL PLUMBING HANGERS - TOWER L3	5	26-Jan-23	01-Feb-23
TFING1-5490	INSTALL MECHANICAL HANGERS - TOWER L3	5	26-Jan-23	01-Feb-23
TFING1-5280	FIRE SUPPRESSION MAINS - TOWER L3	5	02-Feb-23	08-Feb-23
TOHG1-980	O/H WASTE & VENT - TOWER L3	7	06-Feb-23	14-Feb-23
TOHG1-930	O/H ELECTRICAL MAINS - TOWER L3	5	09-Feb-23	15-Feb-23
TOHG1-1570	O/H LOW VOLTAGE MAINS - TOWER L3	8	09-Feb-23	22-Feb-23
TOHG1-940	O/H PLUMBING MAINS - TOWER L3	6	27-Feb-23	06-Mar-23
TOHG1-1710	O/H PLUMBING BRANCHES - TOWER L3	7	07-Mar-23	15-Mar-23
TOHG1-970	O/H MECHANICAL MAINS - TOWER L3	10	16-Mar-23	29-Mar-23
TFING1-5290	HANG VAV'S - TOWER L3	8	20-Mar-23	29-Mar-23
TOHG1-1000	O/H HYDRONIC PIPING - TOWER L3	5	29-Mar-23	04-Apr-23
TFING1-5150	FIRE SUPPRESSION BRANCHES - TOWER L3	10	06-Apr-23	19-Apr-23
TOHG1-990	O/H MECHANICAL BRANCHES - TOWER L3	15	26-Apr-23	16-May-23
TOHG1-1010	O/H ELECTRICAL BRANCHES - TOWER L3	3	01-May-23	03-May-23
TOHG1-1580	O/H LOW VOLTAGE BRANCHES - TOWER L3	3	01-May-23	03-May-23
TFING1-5100	O/H HVAC CONTROLS - TOWER L3	2	04-May-23	05-May-23
TOHG1-950	O/H LOW VOLTAGE - TOWER L3	2	04-May-23	05-May-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TPG3-1000	ONE SIDE TIE INTO EXTERIOR - TOWER L3	2	05-May-23	08-May-23
TOHG1-960	O/H SECURITY - TOWER L3	2	17-May-23	18-May-23
PRIORITY WALLS (IDF/ ELEC/ SHAFT/ STAIRS)				
IDF/ ELECTRICAL ROOM/ CENTRAL CONTROL				
TPR3-1050	FRAME IDF ROOM, ELECTRICAL ROOM, STAIRS - TOWER L3	5	26-Jan-23	01-Feb-23
TPR3-1060	ROUGH-IN IDF / ELECTRICAL ROOMS - TOWER L3	5	02-Feb-23	08-Feb-23
TELECRI3-100	ROUGH-IN PLUMBING IDF / ELECTRICAL ROOMS - TOWER L3	2	02-Feb-23	03-Feb-23
TELECRI3-110	ROUGH-IN ELECTRICAL IDF / ELECTRICAL ROOMS - TOWER L3	4	03-Feb-23	08-Feb-23
TELECRI3-120	ROUGH-IN MECHANICAL IDF / ELECTRICAL ROOMS - TOWER L3	3	06-Feb-23	08-Feb-23
TPR3-1070	DRYWALL IDF/ ELECTRICAL ROOMS - TOWER L3	5	12-May-23	18-May-23
TPR3-1170	TAPE & FINISH IDF/ELECTRICAL ROOMS - TOWER L3	7	15-May-23	23-May-23
TELEC3-130	PAINT IDF/ELECTRICAL ROOMS - TOWER L3	3	24-May-23	30-May-23
TELEC3-140	SEAL FLOORS IDF/ELECTRICAL ROOMS - TOWER L3	2	31-May-23	01-Jun-23
TPR3-1120	DOORS & HARDWARE IDF / ELECTRICAL ROOMS - TOWER L3	2	02-Jun-23	05-Jun-23
TPR3-1100	ELECTRICAL AND IDF, PANELS AND RACKS - TOWER L3	15	14-Jun-23	05-Jul-23
MEP SHAFTS				
TPR3-1040	INSTALL MEPF IN SHAFTS - TOWER L3	8	06-Jan-23	18-Jan-23
TPR3-1020	FRAME HVAC SHAFTS & DRYWALL C/R SIDE - TOWER L3	3	26-Jan-23	30-Jan-23
TPR3-1110	DRYWALL HVAC SHAFTS - TOWER L3	3	09-May-23	11-May-23
TPR3-1180	TAPE & FINISH HVAC SHAFTS - TOWER L3	7	12-May-23	22-May-23
ELEVATOR/ STAIR SHAFTS				
TPR3-1000	FRAME PASSENGER ELEVATOR HOISTWAYS - TOWER L3	3	31-Jan-23	02-Feb-23
TPR3-1010	FRAME J1/J2 ELEVATOR WALLS - TOWER L3	3	03-Feb-23	07-Feb-23
TPR1-2230	DRYWALL PASSENGER ELEVATOR - TOWER L1	2	03-Feb-23	06-Feb-23
TDR3-1010	FRAME AT H1/H2 ELEVATOR FRAMES DETENTION AREA - TOWER	4	07-Feb-23	10-Feb-23
TPR1-2250	TAPE & FINISH PASSENGER ELEVATOR - TOWER L3	6	07-Feb-23	14-Feb-23
TPR1-2240	DRYWALL J1/J2 ELEVATOR WALLS - TOWER L3	2	08-Feb-23	09-Feb-23
TPR1-2260	TAPE & FINISH J1/J2 ELEVATOR WALLS - TOWER L3	6	15-Feb-23	24-Feb-23
TPR3-1080	DRYWALL STAIR 1-2 - TOWER L3	2	12-May-23	15-May-23
TPR3-1090	DRYWALL STAIR 3-4 - TOWER L3	2	16-May-23	17-May-23
TPR3-1130	TAPE & FINISH STAIR 1-2 - TOWER L3	6	30-Aug-23	08-Sep-23
TPR3-1150	TAPE & FINISH STAIR 3-4 - TOWER L3	6	11-Sep-23	18-Sep-23
TPR3-1140	FINISHES STAIR 1-2 - TOWER L3	4	11-Sep-23	14-Sep-23
TELEC3-150	PRIME AND FIRST COAT PAINT STAIR 1-2 - TOWER L3	5	11-Sep-23	15-Sep-23
TPR3-1160	FINISHES STAIR 3-4 - TOWER L3	4	19-Sep-23	22-Sep-23
TELEC3-160	PRIME AND FIRST COAT PAINT STAIR 3-4 - TOWER L3	5	19-Sep-23	25-Sep-23
DETENTION AREA				
TFIND2-320	FRAME PARTITION WALLS DETENTION AREA - TOWER L3	2	09-Feb-23	10-Feb-23
TRID2-140	ROUGH-IN IN-WALL PLUMBING DETENTION AREA - TOWER L3	2	14-Feb-23	15-Feb-23
TRID2-150	ROUGH-IN - IN WALL ELECTRICAL DETENTION AREA - TOWER L3	2	15-Feb-23	16-Feb-23
TOHD2-120	ROUGH-IN OVERHEAD MECHANICAL DETENTION AREA - TOWER L3	5	13-Mar-23	17-Mar-23
TOHD2-250	ROUGH-IN OVERHEAD FIRE SUPPRESSION DETENTION AREA - TC	2	13-Apr-23	14-Apr-23
TOHD2-130	ROUGH-IN OVERHEAD PLUMBING DETENTION AREA - TOWER L3	2	28-Apr-23	01-May-23
TOHD3-110	ROUGH-IN OVERHEAD ELECTRICAL DETENTION AREA - TOWER L3	3	01-May-23	03-May-23
TOHD3-180	ROUGH-IN OVERHEAD LOW VOLTAGE DETENTION AREA - TOWER	3	01-May-23	03-May-23
TFIND2-430	INSTALL LIGHTING & TRIM DETENTION AREA - TOWER L3	2	04-May-23	05-May-23
TFIND2-1370	INSULATE WALLS - TOWER L3	1	04-May-23	04-May-23

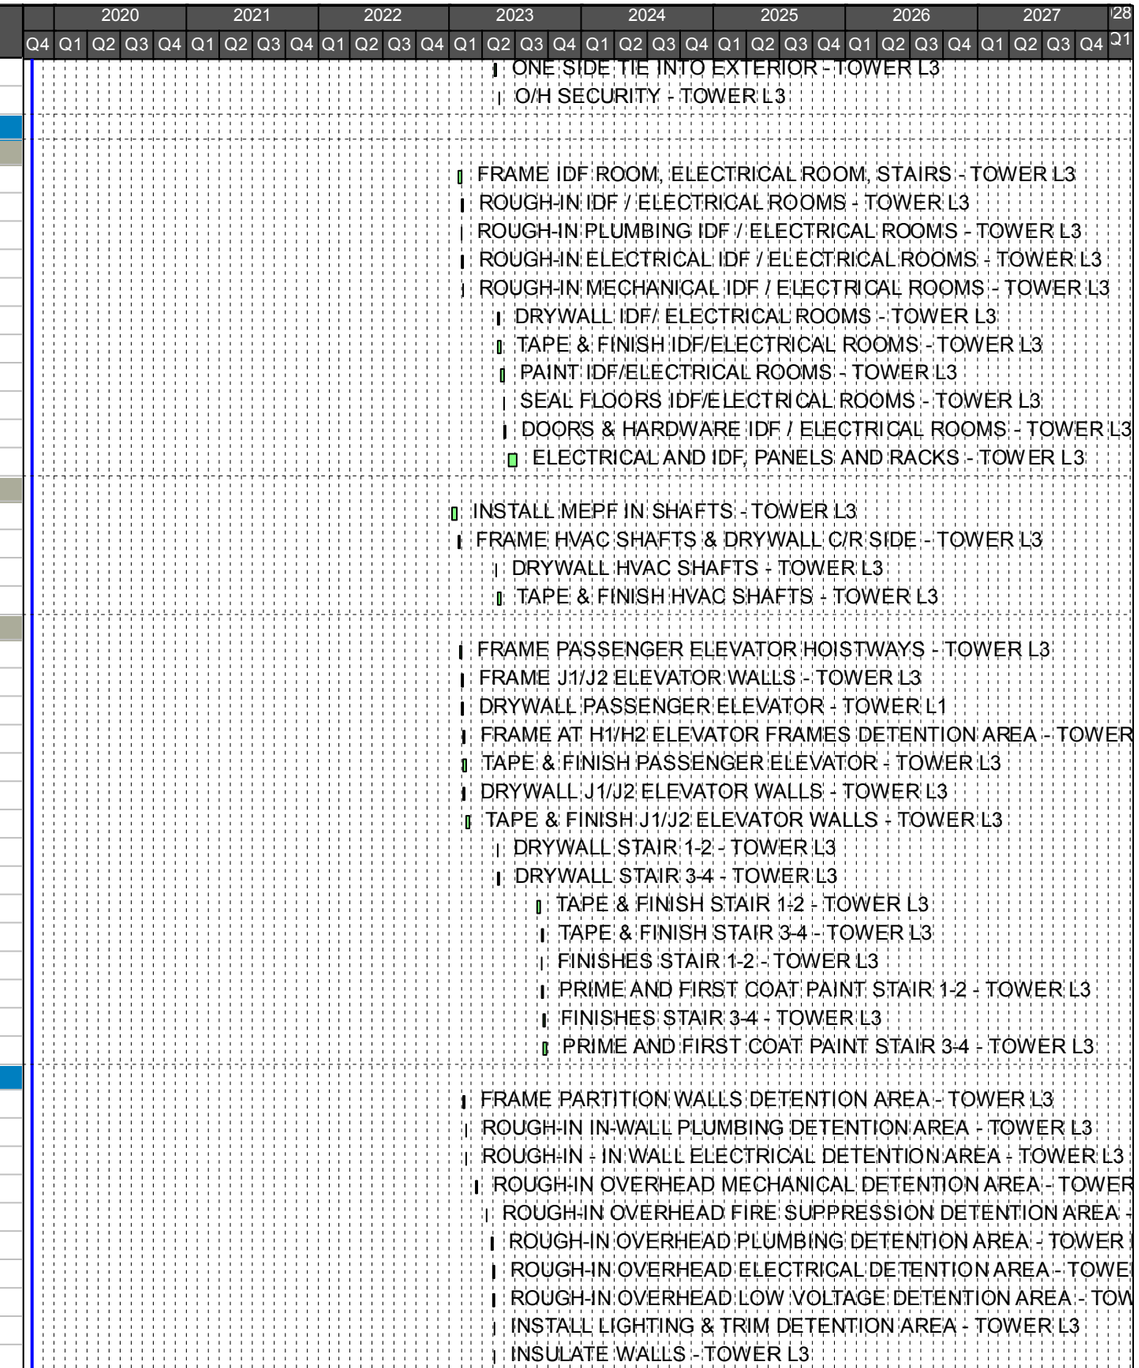

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TFIND2-1380	IN-WALL INSPECTION TOWER L3	1	05-May-23	05-May-23
TFIND2-330	DRYWALL PARTITION WALLS DETENTION AREA - TOWER L3	3	15-Jun-23	19-Jun-23
TFIND2-340	TAPE & FINISH PARTITION WALLS DETENTION AREA - TOWER L3	7	16-Jun-23	26-Jun-23
TFIND2-350	PAINT DETENTION AREA - TOWER L3	5	27-Jun-23	03-Jul-23
TFIND2-390	INSTALL PLUMBING COMBI UNITS DETENTION AREA - TOWER L3	5	05-Jul-23	11-Jul-23
TDR1-1160	CEILING GRID AND DEVICE TILES DETENTION AREA - TOWER L3	6	05-Jul-23	12-Jul-23
TDR3-1000	DETENTION METAL CEILINGS DETENTION AREA - TOWER L3	5	11-Jul-23	17-Jul-23
TFIND2-400	PLUMBING FIXTURES DETENTION AREA - TOWER L3	5	12-Jul-23	18-Jul-23
TFIND2-420	INSTALL GRILLS & DIFFUSERS IN CEILING DETENTION AREA - TOV	3	13-Jul-23	17-Jul-23
TDR1-1170	COMPLETE MECHANICAL IN CEILING DETENTION AREA - TOWER I	5	13-Jul-23	19-Jul-23
TFIND1-340	COMPLETE OVERHEAD FIRE SUPPRESSION IN CEILING - L3	2	13-Jul-23	14-Jul-23
TFIND1-350	COMPLETE ELECTRICAL IN CEILING DETENTION AREA - TOWER L3	5	13-Jul-23	19-Jul-23
TFIND1-360	COMPLETE PLUMBING IN CEILING DETENTION AREA - TOWER L3	5	13-Jul-23	19-Jul-23
TFIND1-370	COMPLETE LOW VOLTAGE IN CEILING DETENTION AREA - TOWEF	5	13-Jul-23	19-Jul-23
TFIND2-370	DOORS AND HARDWARE DETENTION AREA - TOWER L3	4	18-Jul-23	21-Jul-23
TFIND2-380	DETENTION FIXTURES DETENTION AREA - TOWER L3	10	18-Jul-23	31-Jul-23
TFIND2-460	ABOVE CEILING INSPECTION DETENTION AREA - TOWER L3	10	20-Jul-23	02-Aug-23
TDR1-1300	INSTALL SEISMIC BRACING DETENTION AREA - TOWER L3	10	20-Jul-23	02-Aug-23
TDR3-1050	DROP BALANCE OF TILES DETENTION AREA - TOWER L3	3	03-Aug-23	07-Aug-23
TFIND2-480	CASEWORK & TOPS DETENTION AREA - TOWER L3	7	07-Aug-23	15-Aug-23
TFIND2-470	SEAL CONCRETE FLOORS DETENTION AREA - TOWER L3	10	08-Aug-23	21-Aug-23
TOHD3-150	INSTALL INTERIOR GLAZING - TOWER L3	10	08-Aug-23	21-Aug-23
TDR3-1040	TRIM DETENTION AREA - TOWER L3	3	16-Aug-23	18-Aug-23
RESTRICTED CORRIDOR				
TPG3-1010	FRAME RESTRICTED CORRIDOR WALLS - TOWER L3	3	30-Mar-23	03-Apr-23
T1-G-1180	ELECTRICAL WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L	5	04-Apr-23	10-Apr-23
TRIG1-1000	LOW-VOLTAGE WALL ROUGH-IN RESTRICTED CORRIDOR - TOWEI	5	04-Apr-23	10-Apr-23
TRIG1-1010	PLUMBING WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L3	5	04-Apr-23	10-Apr-23
T1-G-1400	INSULATE WALLS RESTRICTED CORRIDOR WALLS - TOWER L3	1	11-Apr-23	11-Apr-23
T1-G-1410	IN WALL INSPECTION RESTRICTED CORRIDOR WALLS - TOWER L3	1	12-Apr-23	12-Apr-23
TPG3-1060	DRYWALL RESTRICTED CORRIDOR - TOWER L3	5	15-Jun-23	21-Jun-23
TPG3-1260	TAPE & FINISH RESTRICTED CORRIDOR - TOWER L3	7	22-Jun-23	30-Jun-23
T1-G-1270	PRIME & PAINT RESTRICTED CORRIDOR - TOWER L3	5	03-Jul-23	10-Jul-23
T1-G-1540	PULL WIRE RESTRICTED CORRIDOR WALLS - TOWER L3	2	03-Jul-23	05-Jul-23
TPG3-1100	CEILING GRID & DEVICE TILES RESTRICTED CORRIDOR - TOWER	4	11-Jul-23	14-Jul-23
T1-G-1260	HVAC TRIM RESTRICTED CORRIDOR - TOWER L3	3	11-Jul-23	13-Jul-23
TFING1-8070	ELECTRICAL TRIM RESTRICTED CORRIDOR - TOWER L3	2	11-Jul-23	12-Jul-23
TFING1-8080	LOW VOLTAGE FINISHES RESTRICTED CORRIDOR - TOWER L3	2	17-Jul-23	18-Jul-23
TFING1-8090	FIRE SUPPRESSION HEADS RESTRICTED CORRIDOR - TOWER L3	2	17-Jul-23	18-Jul-23
TFING1-8340	INSTALL SEISMIC SUPPORTS RESTRICTED CORRIDOR - TOWER I	10	19-Jul-23	01-Aug-23
TPG3-1030	ABOVE CEILING INSPECTION RESTRICTED CORRIDOR WALLS - T	1	02-Aug-23	02-Aug-23
TPG2-2150	DROP BALANCE OF CEILING TILES RESTRICTED CORRIDOR - TOW	4	03-Aug-23	08-Aug-23
TPG3-1020	INSTALL INTERIOR GLAZING RESTRICTED CORRIDOR WALLS - TC	10	09-Aug-23	22-Aug-23
TPG3-1120	INSTALL FLOORING & BASE RESTRICTED CORRIDOR - TOWER L3	5	23-Aug-23	29-Aug-23
JURY DELIBERATION / JUDGES CHAMBERS / JUDGES RESTROOMS				
TJD3-1000	METAL PANELS & SOUND CAP TIE-IN TO EXTERIOR AT JUDICIAL S	3	12-Jan-23	17-Jan-23
TJD3-1010	FRAME JURY DELIBERATION/JUDGE'S CHAMBERS & JUDGE R/R A	7	10-Apr-23	18-Apr-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development

PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19

Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TOHJ3-100	MECHANICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L3	7	19-Apr-23	27-Apr-23
TFINJ3-110	INSTALL DOOR FRAMES AT JUDICIAL SPACES - TOWER L3	3	19-Apr-23	21-Apr-23
TOHJ3-110	PLUMBING ROUGH-IN AT JUDICIAL SPACES - TOWER L3	5	02-May-23	08-May-23
TOHJ3-120	ELECTRICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L3	6	04-May-23	11-May-23
TOHJ3-130	LOW VOLTAGE ROUGH-IN AT JUDICIAL SPACES - TOWER L3	6	04-May-23	11-May-23
TOHJ1-180	INSULATE WALLS AT JUDICIAL SPACES - TOWER L3	1	12-May-23	12-May-23
TOHJ1-190	IN WALL INSPECTION AT JUDICIAL SPACES - TOWER L3	1	15-May-23	15-May-23
TJD3-1030	FINISHES AT JUDICIAL SPACES - TOWER L3	61	22-Jun-23	19-Sep-23
TFINJ3-150	DRYWALL WALLS AT JUDICIAL SPACES - TOWER L3	6	22-Jun-23	29-Jun-23
TFINJ3-240	TAPE & FINISH WALLS AT JUDICIAL SPACES - TOWER L3	7	03-Jul-23	12-Jul-23
TFINJ3-170	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT JUDICIAL SPA	3	13-Jul-23	17-Jul-23
TFINJ3-180	CEILING GRID & DEVICE TILES AT JUDICIAL SPACES - TOWER L3	6	18-Jul-23	25-Jul-23
TJD3-1040	MECHANICAL TRIM AT JUDICIAL SPACES - TOWER L3	5	26-Jul-23	01-Aug-23
TJD3-1050	ELECTRICAL TRIM AT JUDICIAL SPACES - TOWER L3	5	26-Jul-23	01-Aug-23
TJD3-1060	PLUMBING TRIM AT JUDICIAL SPACES - TOWER L3	5	26-Jul-23	01-Aug-23
TJD3-1070	FIRE SUPPRESSION TRIM AT JUDICIAL SPACES - TOWER L3	5	26-Jul-23	01-Aug-23
TJD3-1080	LOW VOLTAGE TRIM AT JUDICIAL SPACES - TOWER L3	5	26-Jul-23	01-Aug-23
TJD3-1110	INSTALL SEISMIC BRACING JUDICIAL SPACES - TOWER L3	10	02-Aug-23	15-Aug-23
TJD3-1100	ABOVE CEILING INSPECTION AT JUDICIAL SPACES - TOWER L3	1	16-Aug-23	16-Aug-23
TFINJ3-210	DROP CEILING TILE AT JUDICIAL SPACES - TOWER L3	2	17-Aug-23	18-Aug-23
TJD1-1090	INSTALL CASEWORK AT JUDICIAL SPACES - TOWER L3	5	18-Aug-23	24-Aug-23
TJD3-1090	INSTALL INTERIOR GLAZING AT JUDICIAL SPACES - TOWER L3	10	21-Aug-23	05-Sep-23
TFINJ3-190	FLOOR PREP AT JUDICIAL SPACES - TOWER L3	1	06-Sep-23	06-Sep-23
TFINJ3-200	INSTALL CARPET & BASE AT JUDICIAL SPACES - TOWER L3	4	07-Sep-23	12-Sep-23
TFINJ3-220	DOORS & HARDWARE AT JUDICIAL SPACES - TOWER L3	5	13-Sep-23	19-Sep-23
COURTROOMS				
TCR3-1000	FRAME PERIMETER WALLS AT COURTROOMS - TOWER L3	10	04-Apr-23	17-Apr-23
TCR3-1020	FLOOR LEVEL AT COURTROOMS - TOWER L3	8	18-Apr-23	27-Apr-23
TRIC2-130	MECHANICAL ROUGH-IN DROPS AT COURTROOMS - TOWER L3	8	28-Apr-23	09-May-23
TRIC2-140	PLUMBING ROUGH-IN DROPS AT COURTROOMS - TOWER L3	6	09-May-23	16-May-23
TRIC2-320	FIRE SUPPRESSION ROUGH-IN DROPS AT COURTROOMS - TOWEI	6	09-May-23	16-May-23
TRIC2-150	ELECTRICAL ROUGH-IN DROPS AT COURTROOMS - TOWER L3	8	12-May-23	23-May-23
TRIC2-310	LOW VOLTAGE ROUGH-IN DROPS AT COURTROOMS - TOWER L3	8	12-May-23	23-May-23
TCR3-1010	INSTALL WALL BACKING - TOWER L3	2	24-May-23	25-May-23
TCR3-1050	FRAME CEILINGS AT COURTROOMS - TOWER L3	8	30-May-23	08-Jun-23
TCR1-1470	INSULATE WALLS AT COURTROOMS - TOWER L3	3	30-May-23	01-Jun-23
TCR1-1480	IN WALL INSPECTION AT COURTROOMS - TOWER L3	1	02-Jun-23	02-Jun-23
TCR3-1060	CEILING FIXTURES PRE-DRYWALL AT COURTROOMS - TOWER L3	5	09-Jun-23	15-Jun-23
TCR3-1090	FRAME LOW WALLS AT COURTROOMS - TOWER L3	6	09-Jun-23	16-Jun-23
TCR3-1070	DRYWALL GYP CEILINGS AT COURTROOMS - TOWER L3	6	16-Jun-23	23-Jun-23
TCR3-1130	ACCESS FLOORING LAYOUT AT COURTROOMS - TOWER L3	3	19-Jun-23	21-Jun-23
TFINC3-100	INSTALL DOOR FRAMES AT COURTROOMS - TOWER L3	3	19-Jun-23	21-Jun-23
TCR3-1240	TAPE & FINISH GYP CEILINGS AT COURTROOMS - TOWER L3	7	26-Jun-23	05-Jul-23
TCR3-1030	DRYWALL WALLS AT COURTROOMS - TOWER L3	5	30-Jun-23	07-Jul-23
TCR3-1120	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT COURTROOM	3	06-Jul-23	10-Jul-23
TCR3-1080	CEILING GRID & DEVICE TILES AT COURTROOMS - TOWER L3	7	11-Jul-23	19-Jul-23
TCR3-1150	ACCESS FLOORING AT COURTROOMS - TOWER L3	12	11-Jul-23	26-Jul-23

Activity ID	Activity Name	Original Duration	Start	Finish
TCR3-1040	TAPE & FINISH WALLS AT COURTROOMS - TOWER L3	6	13-Jul-23	20-Jul-23
TCR3-1100	MECHANICAL COMPLETE CEILING CONNECTIONS AT COURTROOM	5	20-Jul-23	26-Jul-23
TCR3-1270	ELECTRICAL COMPLETE CEILING CONNECTIONS AT COURTROOM	5	20-Jul-23	26-Jul-23
TCR3-1280	PLUMBING COMPLETE CEILING CONNECTIONS AT COURTROOMS	5	20-Jul-23	26-Jul-23
TCR3-1290	FIRE PROTECTION COMPLETE CEILING CONNECTIONS AT COURT	5	20-Jul-23	26-Jul-23
TCR3-1300	LOW VOLTAGE COMPLETE CEILING CONNECTIONS AT COURTROC	5	20-Jul-23	26-Jul-23
TCR3-1220	INSTALL SEISMIC SUPPORTS AT COURTROOMS - TOWER L3	10	27-Jul-23	09-Aug-23
TFINC1-320	ABOVE CEILING INSPECTION AT COURTROOMS - TOWER L3	1	10-Aug-23	10-Aug-23
TCR3-1110	DROP BALANCE OF CEILING TILES AT COURTROOMS - TOWER L3	4	11-Aug-23	16-Aug-23
TCR3-1140	INSTALL INTERIOR GLAZING AT COURTROOMS - TOWER L3	10	17-Aug-23	30-Aug-23
TCR3-1160	CASEWORK AT COURTROOMS - TOWER L3	12	25-Aug-23	13-Sep-23
TCR3-1260	INSTALL RAILING - TOWER L3	10	14-Sep-23	27-Sep-23
TCR3-1180	FINISH FLOORING & BASE AT COURTROOMS - TOWER L3	8	28-Sep-23	09-Oct-23
TCR3-1190	DOORS & HARDWARE AT COURTROOMS - TOWER L3	4	28-Sep-23	03-Oct-23
TCR3-1200	FABRIC WALL PANELS AT COURTROOMS - TOWER L3	4	04-Oct-23	09-Oct-23
TCR3-1210	FF & E AT COURTROOMS - TOWER L3	5	04-Oct-23	10-Oct-23
TCR3-1170	JURY SEATING AT COURTROOMS - TOWER L3	4	10-Oct-23	13-Oct-23
TCR3-1230	CLOSE-UP CASEWORK ELEC/LV TRIM & ACCESSORIES - TOWER L3	4	16-Oct-23	19-Oct-23
PUBLIC GALLERY				
IN-WALL ROUGH-INS				
TFING1-5300	FRAME INTERIOR WALLS PUBLIC GALLERY - TOWER L3	5	19-Apr-23	25-Apr-23
TFING1-5200	IN WALL COUNTERTOP SUPPORTS PUBLIC GALLERY - TOWER L3	2	21-Apr-23	24-Apr-23
TFING1-5400	HM DOOR FRAMES PUBLIC GALLERY - TOWER L3	2	24-Apr-23	25-Apr-23
TRIG1-640	ROUGH-IN WALL PLUMBING PUBLIC GALLERY - TOWER L3	2	25-Apr-23	26-Apr-23
TFING1-5420	INSTALL ELEVATOR DOOR FRAMES & ELEVATOR FRONTS PUBLIC	8	26-Apr-23	05-May-23
TFING1-5470	INSTALL STORE FRONT FRAMES PUBLIC GALLERY - TOWER L3	2	26-Apr-23	27-Apr-23
TRIG1-630	ROUGH-IN WALL LOW VOLTAGE PUBLIC GALLERY - TOWER L3	8	27-Apr-23	08-May-23
TRIG1-650	ROUGH-IN WALL ELECTRICAL PUBLIC GALLERY - TOWER L3	2	27-Apr-23	28-Apr-23
TRIG1-620	ROUGH-IN MECHANICAL CONTROLS PUBLIC GALLERY - TOWER L3	2	01-May-23	02-May-23
TFING1-5310	WALL BACKING PUBLIC GALLERY - TOWER L3	1	04-May-23	04-May-23
TFING1-5160	IN-WALL INSPECTION PUBLIC GALLERY - TOWER L3	1	09-May-23	09-May-23
OVERHEAD ROUGH-INS				
TPG3-1090	FRAME GYP CEILING PUBLIC GALLERY - TOWER L3	7	17-May-23	25-May-23
TRIG1-670	ROUGH-IN MECHANICAL AT HARDLIDS PUBLIC GALLERY - TOWER	2	30-May-23	31-May-23
TRIG1-660	ROUGH-IN ELECTRICAL AT HARDLIDS PUBLIC GALLERY - TOWER L	2	01-Jun-23	02-Jun-23
TFING1-5330	ABOVE CEILING INSPECTION AT HARDLIDS PUBLIC GALLERY - TO	1	05-Jun-23	05-Jun-23
FINISHES				
TFING1-5180	INSULATE WALLS PUBLIC GALLERY - TOWER L3	4	10-May-23	15-May-23
TFING1-5210	DRYWALL WALLS PUBLIC GALLERY - TOWER L3	4	10-Jul-23	13-Jul-23
TPG3-1140	DRYWALL CEILINGS PUBLIC GALLERY - TOWER L3	3	14-Jul-23	18-Jul-23
TFING1-5120	MEASURE & FAB INTERIOR GLAZING FRAMES PUBLIC GALLERY -	1	14-Jul-23	14-Jul-23
TFING1-5130	FURNISH MATERIAL FOR INTERIOR GLAZING FRAMES PUBLIC GAL	10	17-Jul-23	28-Jul-23
TFING1-5220	TAPE & FINISH PUBLIC GALLERY - TOWER L3	6	21-Jul-23	28-Jul-23
TFING1-5190	PRIME & PAINT 1ST COAT PUBLIC GALLERY - TOWER L3	3	02-Aug-23	04-Aug-23
TPG3-1180	CEILING GRID / DEVICE TILES PUBLIC GALLERY - TOWER L3	4	07-Aug-23	10-Aug-23
TPG3-1110	INSTALL LIGHT FIXTURES AT HARDLIDS PUBLIC GALLERY - TOWE	4	07-Aug-23	10-Aug-23
TFING1-5170	ELECTRICAL COVER PLATES PUBLIC GALLERY - TOWER L3	3	07-Aug-23	09-Aug-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TFING1-5480	INSTALL STORE FRONT GLAZING PUBLIC GALLERY - TOWER L3	5	07-Aug-23	11-Aug-23
TFING1-5530	FIRE SUPPRESSION HEADS AT HARDLIDS PUBLIC GALLERY - TOV	4	07-Aug-23	10-Aug-23
TFING1-5560	INSTALL HVAC CONTROLS PUBLIC GALLERY - TOWER L3	5	07-Aug-23	11-Aug-23
TPG3-1200	FIRE ALARM DEVICES PUBLIC GALLERY - TOWER L3	2	11-Aug-23	14-Aug-23
TPG2-1570	MECHANICAL DIFFUSERS & REGISTERS PUBLIC GALLERY - TOWE	3	11-Aug-23	15-Aug-23
TPG2-1610	INSTALL DEVICE TILES PUBLIC GALLERY - TOWER L3	3	11-Aug-23	15-Aug-23
TFING1-5350	CASEWORK PUBLIC GALLERY - TOWER L3	10	11-Aug-23	24-Aug-23
TOHG1-1020	LIGHT FIXTURES IN T-BAR CEILING PUBLIC GALLERY - TOWER L3	2	11-Aug-23	14-Aug-23
TFING1-5360	FIRE SUPPRESSION HEADS AT GRID PUBLIC GALLERY - TOWER L3	2	11-Aug-23	14-Aug-23
TFING1-5370	MECHANICAL DIFFUSERS & REGISTERS AT GRID PUBLIC GALLER	2	11-Aug-23	14-Aug-23
TFING1-5230	INSTALL SEISMIC SUPPORTS PUBLIC GALLERY - TOWER L3	10	15-Aug-23	28-Aug-23
TFING1-5450	FLOOR PREP AT LOBBY & PUBLIC GALLERY - TOWER L3	4	16-Aug-23	21-Aug-23
TPG3-1230	INSTALL FLOOR TILE IN PUBLIC GALLERY - TOWER L3	7	22-Aug-23	30-Aug-23
TFING1-5320	INSTALL EDGE GUARDS PUBLIC GALLERY - TOWER L3	2	25-Aug-23	28-Aug-23
TFING1-5380	ABOVE CEILING INSPECTION AT T-BAR PUBLIC GALLERY - TOWE	1	29-Aug-23	29-Aug-23
TPG3-1210	DROP CEILING TILE PUBLIC GALLERY - TOWER L3	4	30-Aug-23	06-Sep-23
TPG3-1250	DOORS & HARDWARE - TOWER L3	2	31-Aug-23	05-Sep-23
TFING1-5440	INSTALL FLOOR BASE AT TILE WALLS PUBLIC GALLERY - TOWER	5	31-Aug-23	08-Sep-23
TFING1-5250	INSTALL GLAZING PUBLIC GALLERY - TOWER L3	8	07-Sep-23	18-Sep-23
TFING1-5340	FIRE EXTINGUISHERS CABINETS PUBLIC GALLERY - TOWER L3	2	07-Sep-23	08-Sep-23
TPG3-1190	INSTALL WALL TILE PUBLIC GALLERY - TOWER L3	5	11-Sep-23	15-Sep-23
TFING1-5430	INSTALL METAL WALL PANELS/ TRIM PUBLIC GALLERY - TOWER L3	3	11-Sep-23	13-Sep-23
TPG3-1240	BENCHES FF&E PUBLIC GALLERY - TOWER L3	2	14-Sep-23	15-Sep-23
TPG3-1220	PLUMBING FIXTURES PUBLIC GALLERY - TOWER L3	2	18-Sep-23	19-Sep-23
TFING1-5110	OFOI VISUAL DISPLAY SURFACES PUBLIC GALLERY - TOWER L3	2	08-Feb-24	09-Feb-24
TFING1-5520	INSTALL LOW VOLTAGE PUBLIC GALLERY - TOWER L3	4	08-Feb-24	13-Feb-24
PUBLIC / STAFF RESTROOMS				
TRR3-1000	FRAME PUBLIC / STAFF RR - TOWER L3	4	20-Apr-23	25-Apr-23
TRIR3-100	ROUGH-IN WALL PLUMBING PUBLIC / STAFF RR - TOWER L3	5	26-Apr-23	02-May-23
TFINR3-120	FIELD MEASURE FOR TOILET PARTITIONS PUBLIC / STAFF RR - TO	1	26-Apr-23	26-Apr-23
TFINR3-130	FABRICATE TOILET PARTITIONS PUBLIC / STAFF RR - TOWER L3	30	27-Apr-23	09-Jun-23
TRIR3-110	ROUGH-IN WALL ELECTRICAL PUBLIC / STAFF RR - TOWER L3	5	28-Apr-23	04-May-23
TRR3-1020	FINISHES PUBLIC / STAFF RR - TOWER L3	12	05-May-23	22-May-23
TRIR3-120	ROUGH-IN MECHANICAL AT HARDLIDS PUBLIC / STAFF RR - TOWE	5	05-May-23	11-May-23
TFINR3-150	WALL BACKING PUBLIC / STAFF RR - TOWER L3	2	05-May-23	08-May-23
TFINR3-160	INSULATE WALLS PUBLIC / STAFF RR - TOWER L3	1	09-May-23	09-May-23
TFINR3-170	DRYWALL WALLS PUBLIC / STAFF RR - TOWER L3	2	12-Jul-23	13-Jul-23
TFINR3-190	FRAME HARDLID CEILINGS & SOFFITS PUBLIC / STAFF RR - TOWE	4	14-Jul-23	19-Jul-23
TFINR1-390	OVERHEAD MEP CEILING DROPS PUBLIC / STAFF RR - TOWER L3	4	20-Jul-23	25-Jul-23
TFINR3-180	DRYWALL HARDLIDS & SOFFITS PUBLIC / STAFF RR - TOWER L3	3	26-Jul-23	28-Jul-23
TFINR3-200	TAPE & FINISH AND FINISH PUBLIC / STAFF RR - TOWER L3	7	31-Jul-23	08-Aug-23
TFINR3-220	PRIME & PAINT 1ST COAT PUBLIC / STAFF RR - TOWER L3	3	10-Aug-23	14-Aug-23
TFINR3-230	FINISHES PUBLIC / STAFF RR - TOWER L3	12	15-Aug-23	30-Aug-23
TFINR3-240	FLOOR PREP PUBLIC / STAFF RR - TOWER L3	2	15-Aug-23	16-Aug-23
TFINR3-250	PULL & TERMINATE ELECTRICAL/ LOW VOLTAGE WIRE PUBLIC / S	2	15-Aug-23	16-Aug-23
TFINR3-260	ELECTRICAL/FIRE ALARM FINISH/DEVICES PUBLIC / STAFF RR - T	4	17-Aug-23	22-Aug-23
TFINR3-270	INSTALL FLOOR & WALL TILE PUBLIC / STAFF RR - TOWER L3	9	17-Aug-23	29-Aug-23

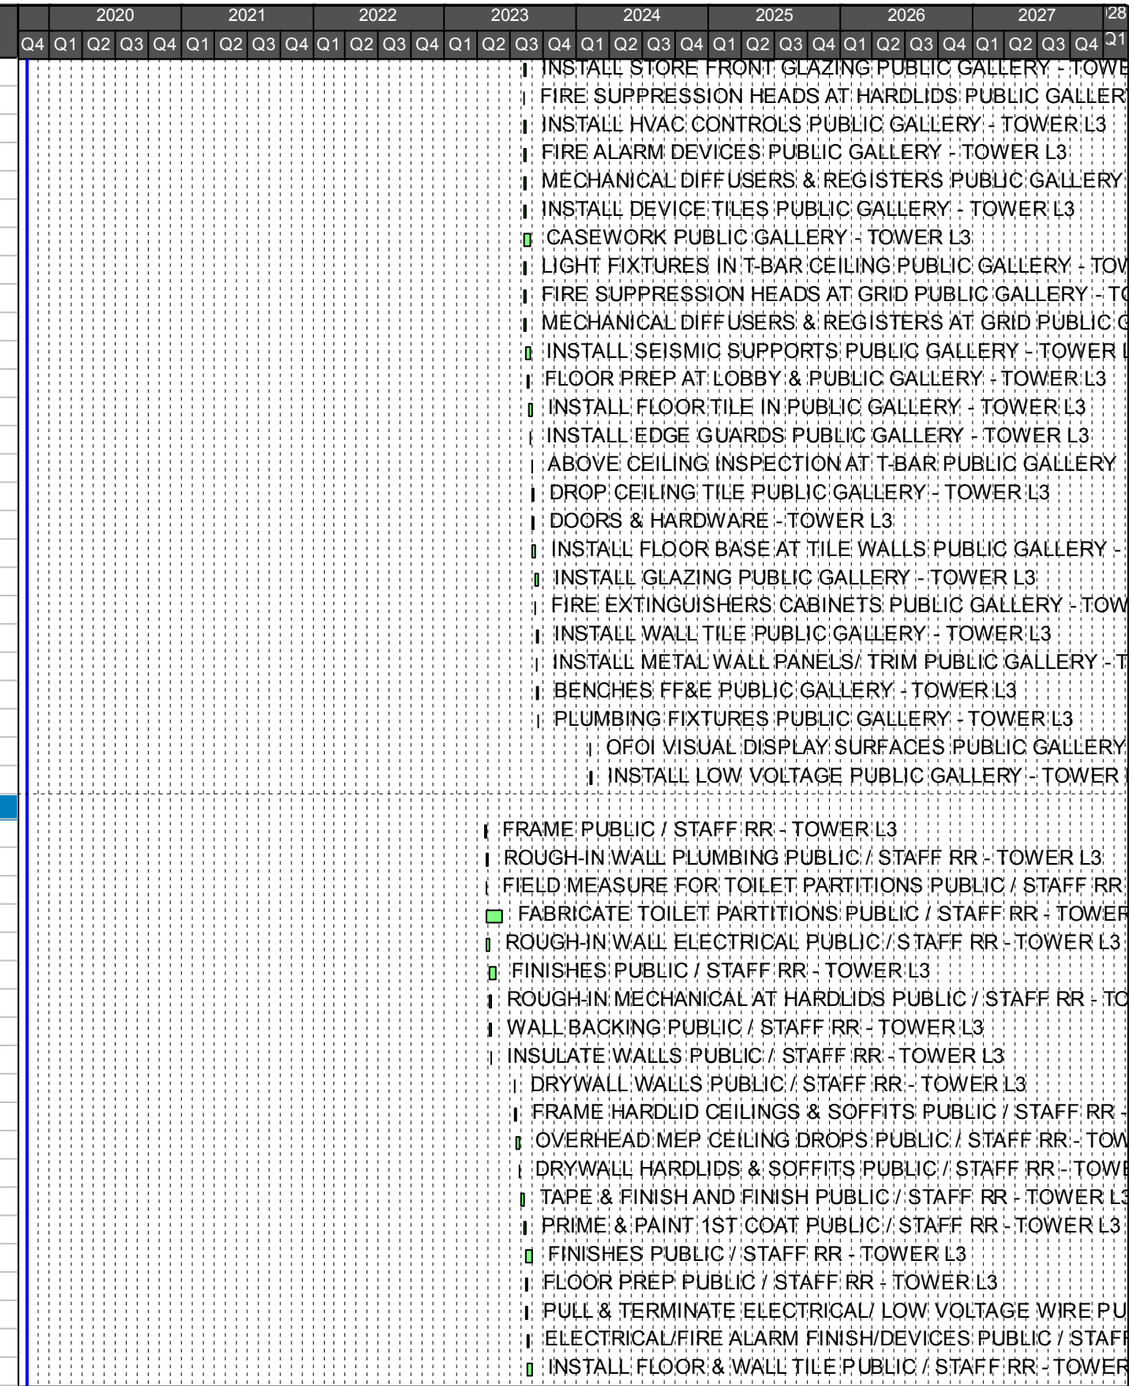

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TRR3-1030	MEP TRIM PUBLIC / STAFF PUBLIC / STAFF RR - TOWER L3	7	23-Aug-23	31-Aug-23
TFINR3-280	CASEWORK & TOPS PUBLIC / STAFF RR - TOWER L3	3	30-Aug-23	05-Sep-23
TFINR3-310	MECHANICAL DIFFUSERS & REGISTERS PUBLIC / STAFF RR - TOW	2	30-Aug-23	31-Aug-23
TFINR3-290	MEP TRIM PUBLIC / STAFF RR - TOWER L3	7	31-Aug-23	12-Sep-23
TFINR3-300	FIRE SUPPRESSION HEADS PUBLIC / STAFF RR - TOWER L3	1	06-Sep-23	06-Sep-23
TFINR3-320	PLUMBING FIXTURES PUBLIC / STAFF RR - TOWER L3	4	06-Sep-23	11-Sep-23
TFINR3-330	DOORS & HARDWARE PUBLIC / STAFF RR - TOWER L3	7	12-Sep-23	20-Sep-23
TFINR3-340	INSTALL PARTITIONS AND ACCESSORIES PUBLIC / STAFF RR - TO	7	15-Sep-23	25-Sep-23
TFINR3-350	FINAL PAINT PUBLIC / STAFF RR - TOWER L3	2	26-Sep-23	27-Sep-23
MANLIFT BAY				
LOB3-100	FRAME MANLIFT BAY - TOWER L3	3	25-Jul-23	27-Jul-23
LOB3-110	ROUGH-IN MEP MANLIFT BAY - TOWER L3	5	28-Jul-23	03-Aug-23
LOB3-120	FINISHES MANLIFT BAY - TOWER L3	15	04-Aug-23	24-Aug-23
LOB3-130	TRIM MANLIFT BAY - TOWER L3	5	25-Aug-23	31-Aug-23
LEVEL 4				
LEVEL 4 FULL FLOOR				
MS4-1000	PRE-WELD EXTERIOR & PARTITION CLIPS	7	29-Dec-22	09-Jan-23
MS4-1020	FIREPROOF PRIORITY WALLS/PERIMETER - TOWER L4	5	10-Jan-23	17-Jan-23
MS4-1030	FIREPROOF BALANCE OF FLOORS	5	12-Jan-23	19-Jan-23
MS4-1010	EDGE OF SLAB FIRE SAFE	5	15-Feb-23	23-Feb-23
TPG4-1000	ONE SIDE TIE INTO EXTERIOR - TOWER L4	5	24-Feb-23	02-Mar-23
TFING1-6040	FIELD MEASURE FOR WINDOW COVERINGS - TOWER L4	1	17-Jul-23	17-Jul-23
TFING1-6050	FABRICATE WINDOW COVERINGS - TOWER L4	10	05-Feb-24	20-Feb-24
TPG4-1160	FINAL PAINT - TOWER L4	7	08-Feb-24	20-Feb-24
TFING1-5590	WINDOW COVERINGS PUBLIC GALLERY - TOWER L4	4	21-Feb-24	26-Feb-24
TFING1-5760	INSTALL SIGNAGE - TOWER L4	5	21-Feb-24	27-Feb-24
TFING1-5770	INT. CERTIFICATION & READY FOR PUNCH - TOWER L4	1	28-Feb-24	28-Feb-24
OVERHEAD ROUGH-INS				
TFING1-5580	LAYOUT FOR CLIPS AND TRACK - TOWER L4	3	27-Dec-22	29-Dec-22
TFING1-5570	INSTALL TOP TRACK - TOWER L4	2	28-Dec-22	29-Dec-22
TFING1-6010	INSTALL FIRE SUPPRESSION HANGERS - TOWER L4	4	19-Jan-23	24-Jan-23
TFING1-6000	INSTALL ELECTRICAL HANGERS - TOWER L4	4	25-Jan-23	30-Jan-23
TFING1-8290	INSTALL LOW VOLTAGE HANGERS - TOWER L4	4	25-Jan-23	30-Jan-23
TFING1-5640	INSTALL PLUMBING HANGERS - TOWER L4	5	02-Feb-23	08-Feb-23
TFING1-5990	INSTALL MECHANICAL HANGERS - TOWER L4	5	02-Feb-23	08-Feb-23
TFING1-5780	FIRE SUPPRESSION MAINS - TOWER L4	5	09-Feb-23	15-Feb-23
TOHG1-1080	O/H WASTE & VENT - TOWER L4	7	15-Feb-23	27-Feb-23
TOHG1-1030	O/H ELECTRICAL MAINS - TOWER L4	5	21-Feb-23	27-Feb-23
TOHG1-1590	O/H LOW VOLTAGE MAINS - TOWER L4	8	21-Feb-23	02-Mar-23
TOHG1-1040	O/H PLUMBING MAINS - TOWER L4	6	16-Mar-23	23-Mar-23
TOHG1-1720	O/H PLUMBING BRANCHES - TOWER L4	7	24-Mar-23	03-Apr-23
TOHG1-1070	O/H MECHANICAL MAINS - TOWER L4	10	04-Apr-23	17-Apr-23
TFING1-5790	HANG VAV'S - TOWER L4	8	06-Apr-23	17-Apr-23
TOHG1-1100	O/H HYDRONIC PIPING - TOWER L4	5	17-Apr-23	21-Apr-23
TFING1-5650	FIRE SUPPRESSION BRANCHES - TOWER L4	10	25-Apr-23	08-May-23
TOHG1-1110	O/H ELECTRICAL BRANCHES - TOWER L4	3	02-May-23	04-May-23
TOHG1-1600	O/H LOW VOLTAGE BRANCHES - TOWER L4	3	02-May-23	04-May-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TFING1-5600	O/H HVAC CONTROLS - TOWER L4	2	05-May-23	08-May-23
TOHG1-1050	O/H LOW VOLTAGE - TOWER L4	2	05-May-23	08-May-23
TOHG1-1090	O/H MECHANICAL BRANCHES - TOWER L4	15	12-May-23	05-Jun-23
TPG2-1650	ONE SIDE TIE INTO EXTERIOR - TOWER L4	2	23-May-23	24-May-23
TOHG1-1060	O/H SECURITY - TOWER L4	2	06-Jun-23	07-Jun-23
PRIORITY WALLS (IDF/ ELEC/ SHAFT/ STAIRS)				
IDF/ ELECTRICAL ROOM/ CENTRAL CONTROL				
TPR4-1050	FRAME IDF ROOM, ELECTRICAL ROOM, STAIRS - TOWER L4	5	13-Feb-23	21-Feb-23
TELECRI4-100	ROUGH-IN PLUMBING IDF / ELECTRICAL ROOMS - TOWER L4	2	22-Feb-23	23-Feb-23
TELECRI4-110	ROUGH-IN ELECTRICAL IDF / ELECTRICAL ROOMS - TOWER L4	4	23-Feb-23	28-Feb-23
TELECRI4-120	ROUGH-IN MECHANICAL IDF / ELECTRICAL ROOMS - TOWER L4	3	24-Feb-23	28-Feb-23
TPR4-1070	DRYWALL IDF/ ELECTRICAL ROOMS - TOWER L4	5	31-May-23	06-Jun-23
TPR4-1170	TAPE & FINISH IDF / ELECTRICAL ROOMS - TOWER L4	7	27-Jun-23	06-Jul-23
TELEC4-130	PAINT IDF / ELECTRICAL ROOMS - TOWER L4	3	07-Jul-23	11-Jul-23
TELEC4-140	SEAL FLOORS IDF / ELECTRICAL ROOMS - TOWER L4	2	12-Jul-23	13-Jul-23
TPR4-1120	DOORS & HARDWARE IDF / ELECTRICAL ROOMS - TOWER L4	2	14-Jul-23	17-Jul-23
TPR4-1100	ELECTRICAL AND IDF, PANELS AND RACKS IDF / ELECTRICAL ROC	15	26-Jul-23	15-Aug-23
TELEC4-150	PRIME AND FIRST COAT PAINT STAIR 1-2 - TOWER L4	5	02-Oct-23	06-Oct-23
MEP SHAFTS				
TPR4-1040	INSTALL MEPF IN SHAFTS	8	19-Jan-23	30-Jan-23
TPR4-1020	FRAME HVAC SHAFTS & DRYWALL C/R SIDE	3	13-Feb-23	15-Feb-23
TPR4-1180	DRYWALL HVAC SHAFTS - TOWER L4	7	18-May-23	30-May-23
TPR4-1110	TAPE & FINISH HVAC SHAFTS - TOWER L4	3	19-Sep-23	21-Sep-23
ELEVATOR/ STAIR SHAFTS				
TPR4-1000	FRAME PASSENGER ELEVATOR HOISTWAYS	3	16-Feb-23	22-Feb-23
TPR4-1010	FRAME J1/J2 ELEVATOR WALLS	3	23-Feb-23	27-Feb-23
TDR4-1010	FRAME AT H1/H2 - ELEVATOR FRAMES - L4 DETENTION AREA	4	23-Feb-23	28-Feb-23
TPR1-2270	DRYWALL PASSENGER ELEVATOR - TOWER L4	2	23-Feb-23	24-Feb-23
TPR1-2290	TAPE & FINISH PASSENGER ELEVATOR - TOWER L4	6	27-Feb-23	06-Mar-23
TPR1-2280	DRYWALL J1/J2 ELEVATOR WALLS - TOWER L4	2	28-Feb-23	01-Mar-23
TPR1-2300	TAPE & FINISH J1/J2 ELEVATOR WALLS - TOWER L4	6	07-Mar-23	14-Mar-23
TPR4-1080	DRYWALL STAIR 1-2 - TOWER L4	2	31-May-23	01-Jun-23
TPR4-1090	DRYWALL STAIR 3-4 - TOWER L4	2	02-Jun-23	05-Jun-23
TPR4-1130	TAPE & FINISH STAIR 1-2 - TOWER L4	6	22-Sep-23	29-Sep-23
TPR4-1140	FINISHES STAIR 1-2 - TOWER L4	4	02-Oct-23	05-Oct-23
TPR4-1150	TAPE & FINISH STAIR 3-4 - TOWER L4	6	02-Oct-23	09-Oct-23
TPR4-1160	FINISHES STAIR 3-4 - TOWER L4	4	10-Oct-23	13-Oct-23
TELEC4-160	PRIME AND FIRST COAT PAINT STAIR 3-4 - TOWER L4	5	10-Oct-23	16-Oct-23
DETENTION AREA				
TFIND2-490	FRAME PARTITION WALLS DETENTION AREA - TOWER L4	2	28-Feb-23	01-Mar-23
TRID2-160	ROUGH-IN IN-WALL PLUMBING DETENTION AREA - TOWER L4	2	02-Mar-23	03-Mar-23
TRID2-170	ROUGH-IN - IN WALL ELECTRICAL DETENTION AREA - TOWER L4	2	03-Mar-23	06-Mar-23
TOHD2-140	ROUGH-IN OVERHEAD MECHANICAL DETENTION AREA - TOWER L4	5	20-Mar-23	24-Mar-23
TOHD2-260	ROUGH-IN OVERHEAD FIRE SUPPRESSION DETENTION AREA - TC	2	17-Apr-23	18-Apr-23
TOHD2-150	ROUGH-IN OVERHEAD PLUMBING DETENTION AREA - TOWER L4	2	17-May-23	18-May-23
TOHD3-120	ROUGH-IN OVERHEAD ELECTRICAL DETENTION AREA - TOWER L4	3	18-May-23	22-May-23
TOHD3-190	ROUGH-IN OVERHEAD LOW VOLTAGE DETENTION AREA - TOWER	3	18-May-23	22-May-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TDR4-1000	DETENTION METAL CEILINGS DETENTION AREA - TOWER L4	5	23-May-23	31-May-23
TFIND2-1390	INSULATE WALLS - TOWER L4	1	23-May-23	23-May-23
TFIND2-1400	IN-WALL INSPECTION TOWER L4	1	24-May-23	24-May-23
TFIND2-500	DRYWALL PARTITION WALLS DETENTION AREA - TOWER L4	3	20-Jun-23	22-Jun-23
TFIND2-510	TAPE & FINISH PARTITION WALLS DETENTION AREA - TOWER L4	7	27-Jun-23	06-Jul-23
TFIND2-520	PAINT DETENTION AREA - TOWER L4	5	07-Jul-23	13-Jul-23
TFIND2-540	DOORS AND HARDWARE DETENTION AREA - TOWER L4	4	14-Jul-23	19-Jul-23
TFIND2-550	DETENTION FIXTURES DETENTION AREA - TOWER L4	10	14-Jul-23	27-Jul-23
TFIND2-560	INSTALL PLUMBING COMBI UNITS DETENTION AREA - TOWER L4	5	14-Jul-23	20-Jul-23
TDR1-1180	CEILING GRID AND DEVICE TILES DETENTION AREA - TOWER L4	6	14-Jul-23	21-Jul-23
TFIND2-570	PLUMBING FIXTURES DETENTION AREA - TOWER L4	5	21-Jul-23	27-Jul-23
TDR1-1190	COMPLETE MECHANICAL IN CEILING DETENTION AREA - TOWER I	5	24-Jul-23	28-Jul-23
TFIND1-380	COMPLETE OVERHEAD FIRE SUPPRESSION IN CEILING - L4	2	24-Jul-23	25-Jul-23
TFIND1-390	COMPLETE ELECTRICAL IN CEILING DETENTION AREA - TOWER L4	5	24-Jul-23	28-Jul-23
TFIND1-400	COMPLETE PLUMBING IN CEILING DETENTION AREA - TOWER L4	5	24-Jul-23	28-Jul-23
TFIND1-410	COMPLETE LOW VOLTAGE IN CEILING DETENTION AREA - TOWEF	5	24-Jul-23	28-Jul-23
TDR1-1260	ABOVE CEILING INSPECTION DETENTION AREA - TOWER L4	1	31-Jul-23	31-Jul-23
TDR1-1310	INSTALL SEISMIC BRACING DETENTION AREA - TOWER L4	10	31-Jul-23	11-Aug-23
TFIND2-530	DROP BALANCE OF TILES DETENTION AREA - TOWER L4	3	14-Aug-23	16-Aug-23
TFIND2-580	INSTALL INTERIOR GLAZING - TOWER L4	10	17-Aug-23	30-Aug-23
TFIND2-640	SEAL CONCRETE FLOORS DETENTION AREA - TOWER L4	10	31-Aug-23	15-Sep-23
TFIND2-650	CASEWORK & TOPS DETENTION AREA - TOWER L4	7	06-Sep-23	14-Sep-23
TDR4-1040	TRIM - L4 DETENTION AREA	3	15-Sep-23	19-Sep-23
RESTRICTED CORRIDOR				
TPG4-1010	FRAME RESTRICTED CORRIDOR WALLS - TOWER L4	5	18-Apr-23	24-Apr-23
T1-G-1190	ELECTRICAL WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L	5	25-Apr-23	01-May-23
TRIG1-1020	LOW-VOLTAGE WALL ROUGH-IN RESTRICTED CORRIDOR - TOWEI	5	25-Apr-23	01-May-23
TRIG1-1030	PLUMBING WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L4	5	25-Apr-23	01-May-23
T1-G-1420	INSULATE WALLS RESTRICTED CORRIDOR WALLS - TOWER L4	1	02-May-23	02-May-23
T1-G-1430	IN WALL INSPECTION RESTRICTED CORRIDOR WALLS - TOWER L4	1	03-May-23	03-May-23
TPG3-1270	DRYWALL RESTRICTED CORRIDOR - TOWER L4	5	04-May-23	10-May-23
TPG3-1280	TAPE & FINISH RESTRICTED CORRIDOR - TOWER L4	7	11-May-23	19-May-23
T1-G-1280	PRIME & PAINT RESTRICTED CORRIDOR - TOWER L4	5	22-May-23	30-May-23
T1-G-1550	PULL WIRE RESTRICTED CORRIDOR WALLS - TOWER L4	2	22-May-23	23-May-23
TPG4-1080	CEILING GRID & DEVICE TILES RESTRICTED CORRIDOR - TOWER	4	31-May-23	05-Jun-23
T1-G-1290	HVAC TRIM RESTRICTED CORRIDOR - TOWER L4	3	31-May-23	02-Jun-23
TFING1-8120	ELECTRICAL TRIM RESTRICTED CORRIDOR - TOWER L4	2	31-May-23	01-Jun-23
TFING1-8100	LOW VOLTAGE FINISHES RESTRICTED CORRIDOR - TOWER L4	2	06-Jun-23	07-Jun-23
TFING1-8110	FIRE SUPPRESSION HEADS RESTRICTED CORRIDOR - TOWER L4	2	06-Jun-23	07-Jun-23
TFING1-8350	INSTALL SEISMIC SUPPORTS RESTRICTED CORRIDOR - TOWER I	10	08-Jun-23	21-Jun-23
TPG4-1020	ABOVE CEILING INSPECTION RESTRICTED CORRIDOR WALLS - T	1	22-Jun-23	22-Jun-23
TPG4-1260	DROP BALANCE OF CEILING TILES RESTRICTED CORRIDOR - TOW	4	23-Jun-23	28-Jun-23
TFING1-8250	INSTALL INTERIOR GLAZING RESTRICTED CORRIDOR WALLS - TC	10	29-Jun-23	13-Jul-23
TPG3-1290	INSTALL FLOORING & BASE RESTRICTED CORRIDOR - TOWER L4	5	14-Jul-23	20-Jul-23
JURY DELIBERATION / JUDGES CHAMBERS / JUDGES RESTROOMS				
TJD4-1000	METAL PANELS & SOUND CAP TIE-IN TO EXTERIOR AT JUDICIAL S	3	03-Mar-23	07-Mar-23
TJD4-1010	FRAME JURY DELIBERATION/JUDGE'S CHAMBERS & JUDGE R/R -	7	26-Apr-23	04-May-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development

PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19

Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TOHJ4-100	MECHANICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L4	7	05-May-23	15-May-23
TFINJ4-110	INSTALL DOOR FRAMES AT JUDICIAL SPACES - TOWER L4	3	05-May-23	09-May-23
TOHJ4-110	PLUMBING ROUGH-IN AT JUDICIAL SPACES - TOWER L4	5	19-May-23	25-May-23
TOHJ4-120	ELECTRICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L4	6	23-May-23	01-Jun-23
TOHJ4-160	LOW VOLTAGE ROUGH-IN AT JUDICIAL SPACES - TOWER L4	6	23-May-23	01-Jun-23
TOHJ1-200	INSULATE WALLS AT JUDICIAL SPACES - TOWER L4	1	02-Jun-23	02-Jun-23
TOHJ1-210	IN WALL INSPECTION AT JUDICIAL SPACES - TOWER L4	1	05-Jun-23	05-Jun-23
TJD4-1030	FINISHES AT JUDICIAL SPACES - TOWER L4	84	06-Jun-23	04-Oct-23
TFINJ4-150	DRYWALL WALLS AT JUDICIAL SPACES - TOWER L4	6	06-Jun-23	13-Jun-23
TFINJ4-240	TAPE & FINISH WALLS AT JUDICIAL SPACES - TOWER L4	7	13-Jul-23	21-Jul-23
TFINJ4-170	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT JUDICIAL SPA	3	24-Jul-23	26-Jul-23
TFINJ4-180	CEILING GRID & DEVICE TILES AT JUDICIAL SPACES - TOWER L4	6	27-Jul-23	03-Aug-23
TJD4-1040	MECHANICAL TRIM AT JUDICIAL SPACES - TOWER L4	5	04-Aug-23	10-Aug-23
TJD4-1100	ELECTRICAL TRIM AT JUDICIAL SPACES - TOWER L4	5	04-Aug-23	10-Aug-23
TJD4-1110	PLUMBING TRIM AT JUDICIAL SPACES - TOWER L4	5	04-Aug-23	10-Aug-23
TJD4-1120	FIRE SUPPRESSION TRIM AT JUDICIAL SPACES - TOWER L4	5	04-Aug-23	10-Aug-23
TJD4-1130	LOW VOLTAGE TRIM AT JUDICIAL SPACES - TOWER L4	5	04-Aug-23	10-Aug-23
TJD4-1220	INSTALL SEISMIC SUPPORTS JUDICIAL SPACES - TOWER L4	10	11-Aug-23	24-Aug-23
TJD4-1200	ABOVE CEILING INSPECTION AT JUDICIAL SPACES - TOWER L4	1	25-Aug-23	25-Aug-23
TFINJ4-210	DROP CEILING TILE AT JUDICIAL SPACES - TOWER L4	2	28-Aug-23	29-Aug-23
TJD4-1180	INSTALL INTERIOR GLAZING AT JUDICIAL SPACES - TOWER L4	10	30-Aug-23	14-Sep-23
TJD1-1095	INSTALL CASEWORK AT JUDICIAL SPACES - TOWER L4	5	14-Sep-23	20-Sep-23
TFINJ4-190	FLOOR PREP AT JUDICIAL SPACES - TOWER L4	1	21-Sep-23	21-Sep-23
TFINJ4-200	INSTALL CARPET & BASE AT JUDICIAL SPACES - TOWER L4	4	22-Sep-23	27-Sep-23
TFINJ4-220	DOORS & HARDWARE AT JUDICIAL SPACES - TOWER L4	5	28-Sep-23	04-Oct-23
COURTROOMS				
TCR4-1000	FRAME PERIMETER WALLS AT COURTROOMS - TOWER L4	10	25-Apr-23	08-May-23
TCR4-1020	FLOOR LEVEL AT COURTROOMS - TOWER L4	8	09-May-23	18-May-23
TRIC2-160	MECHANICAL ROUGH-IN DROPS AT COURTROOMS - TOWER L4	8	19-May-23	01-Jun-23
TRIC2-170	PLUMBING ROUGH-IN DROPS AT COURTROOMS - TOWER L4	6	30-May-23	06-Jun-23
TRIC2-330	FIRE SUPPRESSION ROUGH-IN DROPS AT COURTROOMS - TOWEI	6	30-May-23	06-Jun-23
TRIC2-180	ELECTRICAL ROUGH-IN DROPS AT COURTROOMS - TOWER L4	8	02-Jun-23	13-Jun-23
TRIC2-340	LOW VOLTAGE ROUGH-IN DROPS AT COURTROOMS - TOWER L4	8	02-Jun-23	13-Jun-23
TCR4-1140	INSTALL WALL BACKING	2	14-Jun-23	15-Jun-23
TCR4-1050	FRAME CEILINGS AT COURTROOMS - TOWER L4	8	16-Jun-23	27-Jun-23
TCR1-1490	INSULATE WALLS AT COURTROOMS - TOWER L4	3	16-Jun-23	20-Jun-23
TCR1-1500	IN WALL INSPECTION AT COURTROOMS - TOWER L4	1	21-Jun-23	21-Jun-23
TCR4-1030	DRYWALL WALLS AT COURTROOMS - TOWER L4	5	28-Jun-23	05-Jul-23
TCR4-1060	CEILING FIXTURES PRE-DRYWALL AT COURTROOMS - TOWER L4	5	28-Jun-23	05-Jul-23
TCR4-1100	FRAME LOW WALLS AT COURTROOMS - TOWER L4	6	28-Jun-23	06-Jul-23
TCR4-1130	ACCESS FLOORING LAYOUT AT COURTROOMS - TOWER L4	3	07-Jul-23	11-Jul-23
TFINC4-110	INSTALL DOOR FRAMES AT COURTROOMS - TOWER L4	3	07-Jul-23	11-Jul-23
TCR4-1070	DRYWALL GYP CEILINGS AT COURTROOMS - TOWER L4	6	11-Jul-23	18-Jul-23
TCR4-1240	TAPE & FINISH GYP CEILINGS AT COURTROOMS - TOWER L4	7	19-Jul-23	27-Jul-23
TCR4-1040	TAPE & FINISH WALLS AT COURTROOMS - TOWER L4	6	24-Jul-23	31-Jul-23
TCR4-1120	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT COURTROOM	3	28-Jul-23	01-Aug-23
TCR4-1080	CEILING GRID & DEVICE TILES AT COURTROOMS - TOWER L4	7	02-Aug-23	10-Aug-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TCR4-1150	ACCESS FLOORING AT COURTROOMS - TOWER L4	12	02-Aug-23	17-Aug-23
TCR4-1090	MECHANICAL COMPLETE CEILING CONNECTIONS AT COURTROOM	5	11-Aug-23	17-Aug-23
TCR4-1490	ELECTRICAL COMPLETE CEILING CONNECTIONS AT COURTROOM	5	11-Aug-23	17-Aug-23
TCR4-1500	PLUMBING COMPLETE CEILING CONNECTIONS AT COURTROOMS	5	11-Aug-23	17-Aug-23
TCR4-1510	FIRE SUPPRESSION COMPLETE CEILING CONNECTIONS AT COUR	5	11-Aug-23	17-Aug-23
TCR4-1520	LOW VOLTAGE COMPLETE CEILING CONNECTIONS AT COURTROC	5	11-Aug-23	17-Aug-23
TCR4-1220	INSTALL SEISMIC SUPPORTS AT COURTROOMS - TOWER L4	10	18-Aug-23	31-Aug-23
TFINC1-330	ABOVE CEILING INSPECTION AT COURTROOMS - TOWER L4	1	05-Sep-23	05-Sep-23
TCR4-1110	DROP BALANCE OF CEILING TILES AT COURTROOMS - TOWER L4	4	06-Sep-23	11-Sep-23
TCR4-1010	INSTALL INTERIOR GLAZING AT COURTROOMS - TOWER L4	10	12-Sep-23	25-Sep-23
TCR4-1160	CASEWORK AT COURTROOMS - TOWER L4	12	21-Sep-23	06-Oct-23
TCR4-1480	INSTALL RAILING - TOWER L4	10	09-Oct-23	20-Oct-23
TCR4-1180	FINISH FLOORING & BASE AT COURTROOMS - TOWER L4	8	23-Oct-23	01-Nov-23
TCR4-1190	DOORS & HARDWARE AT COURTROOMS - TOWER L4	4	23-Oct-23	26-Oct-23
TCR4-1200	FABRIC WALL PANELS AT COURTROOMS - TOWER L4	4	27-Oct-23	01-Nov-23
TCR4-1210	FF & E AT COURTROOMS - TOWER L4	5	27-Oct-23	02-Nov-23
TCR4-1170	JURY SEATING AT COURTROOMS - TOWER L4	4	02-Nov-23	07-Nov-23
TCR4-1230	CLOSE-UP CASEWORK ELEC/LV TRIM & ACCESSORIES - TOWER L4	4	08-Nov-23	13-Nov-23
PUBLIC GALLERY				
IN-WALL ROUGH-INS				
TFING1-5800	FRAME INTERIOR WALLS PUBLIC GALLERY - TOWER L4	5	05-May-23	11-May-23
TFING1-5700	IN WALL COUNTERTOP SUPPORTS PUBLIC GALLERY - TOWER L4	2	09-May-23	10-May-23
TFING1-5900	HM DOOR FRAMES PUBLIC GALLERY - TOWER L4	2	10-May-23	11-May-23
TRIG1-700	ROUGH-IN WALL PLUMBING PUBLIC GALLERY - TOWER L4	2	11-May-23	12-May-23
TFING1-5920	INSTALL ELEVATOR DOOR FRAMES & ELEVATOR FRONTS PUBLIC	8	12-May-23	23-May-23
TFING1-5970	INSTALL STORE FRONT FRAMES PUBLIC GALLERY - TOWER L4	2	12-May-23	15-May-23
TRIG1-690	ROUGH-IN WALL LOW VOLTAGE PUBLIC GALLERY - TOWER L4	8	15-May-23	24-May-23
TRIG1-710	ROUGH-IN WALL ELECTRICAL PUBLIC GALLERY - TOWER L4	2	15-May-23	16-May-23
TRIG1-680	ROUGH-IN MECHANICAL CONTROLS PUBLIC GALLERY - TOWER L4	2	17-May-23	18-May-23
TFING1-5810	WALL BACKING PUBLIC GALLERY - TOWER L4	1	22-May-23	22-May-23
TFING1-5660	IN-WALL INSPECTION PUBLIC GALLERY - TOWER L4	1	25-May-23	25-May-23
OVERHEAD ROUGH-INS				
TPG4-1130	FRAME GYP CEILING PUBLIC GALLERY - TOWER L4	7	06-Jun-23	14-Jun-23
TRIG1-730	ROUGH-IN MECHANICAL AT HARDLIDS PUBLIC GALLERY - TOWER	2	15-Jun-23	16-Jun-23
TRIG1-720	ROUGH-IN ELECTRICAL AT HARDLIDS PUBLIC GALLERY - TOWER L	2	19-Jun-23	20-Jun-23
TFING1-5830	ABOVE CEILING INSPECTION AT HARDLIDS PUBLIC GALLERY - TO	1	21-Jun-23	21-Jun-23
FINISHES				
TFING1-5680	INSULATE WALLS PUBLIC GALLERY - TOWER L4	4	30-May-23	02-Jun-23
TPG4-1100	FINISHES RESTRICTED CORRIDOR PUBLIC GALLERY - TOWER L4	5	06-Jun-23	12-Jun-23
TPG4-1140	F2 LIGHT FIXTURES CEILINGS/MEP DROPS PUBLIC GALLERY - TO	4	15-Jun-23	20-Jun-23
TFING1-5710	DRYWALL WALLS PUBLIC GALLERY - TOWER L4	4	06-Jul-23	11-Jul-23
TPG4-1150	DRYWALL CEILINGS PUBLIC GALLERY - TOWER L4	3	12-Jul-23	14-Jul-23
TFING1-5620	MEASURE & FAB INTERIOR GLAZING FRAMES PUBLIC GALLERY -	1	12-Jul-23	12-Jul-23
TFING1-5630	FURNISH MATERIAL FOR INTERIOR GLAZING FRAMES PUBLIC GAI	10	13-Jul-23	26-Jul-23
TFING1-5720	TAPE & FINISH AND FINISH PUBLIC GALLERY - TOWER L4	6	01-Aug-23	08-Aug-23
TFING1-5690	PRIME & PAINT 1ST COAT PUBLIC GALLERY - TOWER L4	3	11-Aug-23	15-Aug-23
TPG4-1170	CEILING GRID / DEVICE TILES PUBLIC GALLERY - TOWER L4	4	16-Aug-23	21-Aug-23

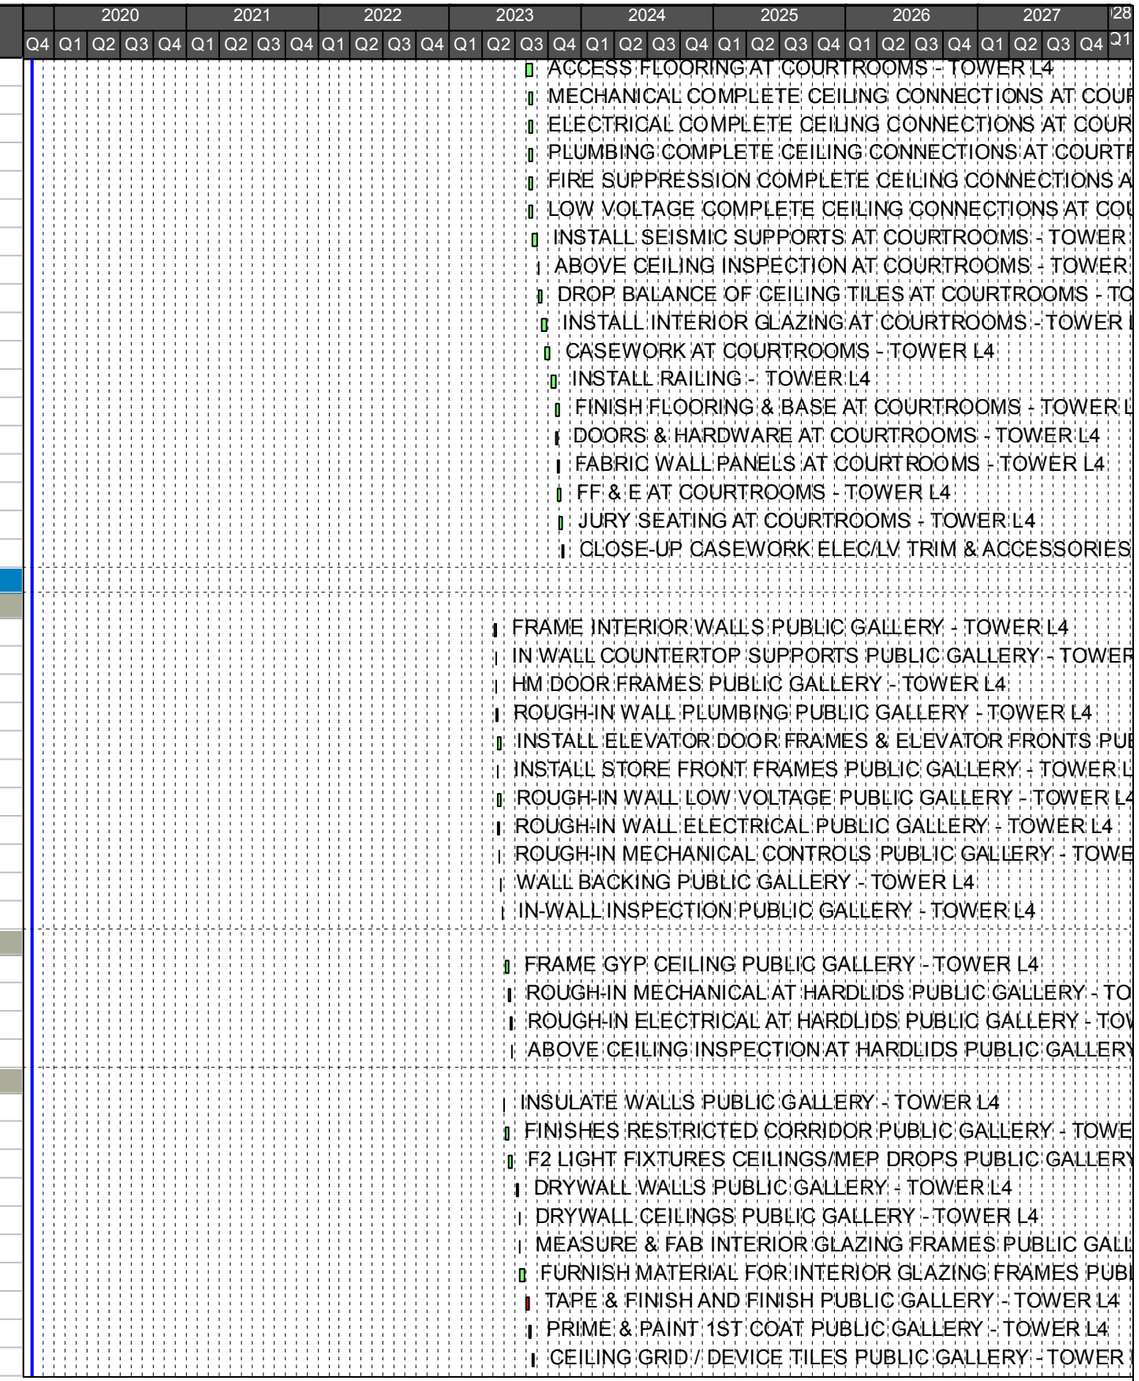

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TPG2-1630	INSTALL LIGHT FIXTURES AT HARDLIDS PUBLIC GALLERY - TOWE	4	16-Aug-23	21-Aug-23
TFING1-5670	ELECTRICAL COVER PLATES PUBLIC GALLERY - TOWER L4	3	16-Aug-23	18-Aug-23
TFING1-5980	INSTALL STORE FRONT GLAZING PUBLIC GALLERY - TOWER L4	5	16-Aug-23	22-Aug-23
TFING1-6030	FIRE SUPPRESSION HEADS AT HARDLIDS PUBLIC GALLERY - TOV	4	16-Aug-23	21-Aug-23
TFING1-6060	INSTALL HVAC CONTROLS PUBLIC GALLERY - TOWER L4	5	16-Aug-23	22-Aug-23
TPG4-1190	FIRE ALARM DEVICES PUBLIC GALLERY - TOWER L4	2	22-Aug-23	23-Aug-23
TPG2-1690	MECHANICAL DIFFUSERS & REGISTERS PUBLIC GALLERY - TOWE	3	22-Aug-23	24-Aug-23
TPG2-1730	INSTALL DEVICE TILES PUBLIC GALLERY - TOWER L4	3	22-Aug-23	24-Aug-23
TOHG1-1120	LIGHT FIXTURES IN T-BAR CEILING PUBLIC GALLERY - TOWER L4	2	22-Aug-23	23-Aug-23
TFING1-5860	FIRE SUPPRESSION HEADS AT GRID PUBLIC GALLERY - TOWER L4	2	22-Aug-23	23-Aug-23
TFING1-5870	MECHANICAL DIFFUSERS & REGISTERS AT GRID PUBLIC GALLER	2	22-Aug-23	23-Aug-23
TFING1-5730	INSTALL SEISMIC SUPPORTS PUBLIC GALLERY - TOWER L4	10	24-Aug-23	08-Sep-23
TFING1-5850	CASEWORK PUBLIC GALLERY - TOWER L4	10	25-Aug-23	11-Sep-23
TFING1-5950	FLOOR PREP AT LOBBY & PUBLIC GALLERY - TOWER L4	4	25-Aug-23	30-Aug-23
TPG4-1220	INSTALL FLOOR TILE IN PUBLIC GALLERY - TOWER L4	7	31-Aug-23	12-Sep-23
TFING1-5880	ABOVE CEILING INSPECTION AT T-BAR PUBLIC GALLERY - TOWEF	1	11-Sep-23	11-Sep-23
TPG4-1200	DROP CEILING TILE PUBLIC GALLERY - TOWER L4	4	12-Sep-23	15-Sep-23
TFING1-5820	INSTALL EDGE GUARDS PUBLIC GALLERY - TOWER L4	2	12-Sep-23	13-Sep-23
TPG4-1240	DOOR/HARDWARE PUBLIC GALLERY - TOWER L4	5	13-Sep-23	19-Sep-23
TPG4-1250	DOORS & HARDWARE PUBLIC GALLERY - TOWER L4	2	13-Sep-23	14-Sep-23
TFING1-5940	INSTALL FLOOR BASE AT TILE WALLS PUBLIC GALLERY - TOWER	5	13-Sep-23	19-Sep-23
TFING1-5750	INSTALL GLAZING PUBLIC GALLERY - TOWER L4	8	18-Sep-23	27-Sep-23
TFING1-5840	FIRE EXTINGUISHERS CABINETS PUBLIC GALLERY - TOWER L4	2	18-Sep-23	19-Sep-23
TPG4-1180	INSTALL WALL TILE PUBLIC GALLERY - TOWER L4	5	20-Sep-23	26-Sep-23
TFING1-5930	INSTALL METAL WALL PANELS/ TRIM PUBLIC GALLERY - TOWER L4	3	20-Sep-23	22-Sep-23
TPG4-1230	BENCHES FF&E PUBLIC GALLERY - TOWER L4	2	25-Sep-23	26-Sep-23
TPG4-1210	PLUMBING FIXTURES PUBLIC GALLERY - TOWER L4	2	27-Sep-23	28-Sep-23
TFING1-5610	OFOI VISUAL DISPLAY SURFACES PUBLIC GALLERY - TOWER L4	2	21-Feb-24	22-Feb-24
TFING1-6020	INSTALL LOW VOLTAGE PUBLIC GALLERY - TOWER L4	4	21-Feb-24	26-Feb-24
PUBLIC / STAFF RESTROOMS				
TRR4-1000	FRAME PUBLIC / STAFF RR - TOWER L4	4	08-May-23	11-May-23
TRIR4-100	ROUGH-IN WALL PLUMBING PUBLIC / STAFF RR - TOWER L4	5	12-May-23	18-May-23
TFINR4-100	FIELD MEASURE FOR TOILET PARTITIONS PUBLIC / STAFF RR - TC	1	12-May-23	12-May-23
TFINR4-110	FABRICATE TOILET PARTITIONS PUBLIC / STAFF RR - TOWER L4	30	15-May-23	27-Jun-23
TRIR4-110	ROUGH-IN WALL ELECTRICAL PUBLIC / STAFF RR - TOWER L4	5	16-May-23	22-May-23
TRIR4-120	ROUGH-IN MECHANICAL AT HARDLIDS PUBLIC / STAFF RR - TOWE	5	23-May-23	31-May-23
TFINR4-140	WALL BACKING PUBLIC / STAFF RR - TOWER L4	2	23-May-23	24-May-23
TFINR4-150	INSULATE WALLS PUBLIC / STAFF RR - TOWER L4	1	25-May-23	25-May-23
TFINR4-170	DRYWALL WALLS PUBLIC / STAFF RR - TOWER L4	2	14-Jul-23	17-Jul-23
TFINR4-190	FRAME HARDLID CEILINGS & SOFFITS PUBLIC / STAFF RR - TOWE	4	18-Jul-23	21-Jul-23
TFINR1-400	OVERHEAD MEP CEILING DROPS PUBLIC / STAFF RR - TOWER L4	4	24-Jul-23	27-Jul-23
TFINR4-180	DRYWALL HARDLIDS & SOFFITS PUBLIC / STAFF RR - TOWER L4	3	28-Jul-23	01-Aug-23
TFINR4-200	TAPE AND FINISH PUBLIC / STAFF RR - TOWER L4	7	09-Aug-23	17-Aug-23
TFINR4-210	PRIME & PAINT 1ST COAT PUBLIC / STAFF RR - TOWER L4	3	21-Aug-23	23-Aug-23
TFINR4-220	FLOOR PREP AT PUBLIC / STAFF RR - TOWER L4	2	24-Aug-23	25-Aug-23
TFINR4-230	PULL & TERMINATE ELECTRICAL/ LOW VOLTAGE WIRE PUBLIC / S	2	24-Aug-23	25-Aug-23
TFINR4-240	ELECTRICAL/FIRE ALARM FINISH/DEVICES PUBLIC / STAFF RR - T	4	28-Aug-23	31-Aug-23

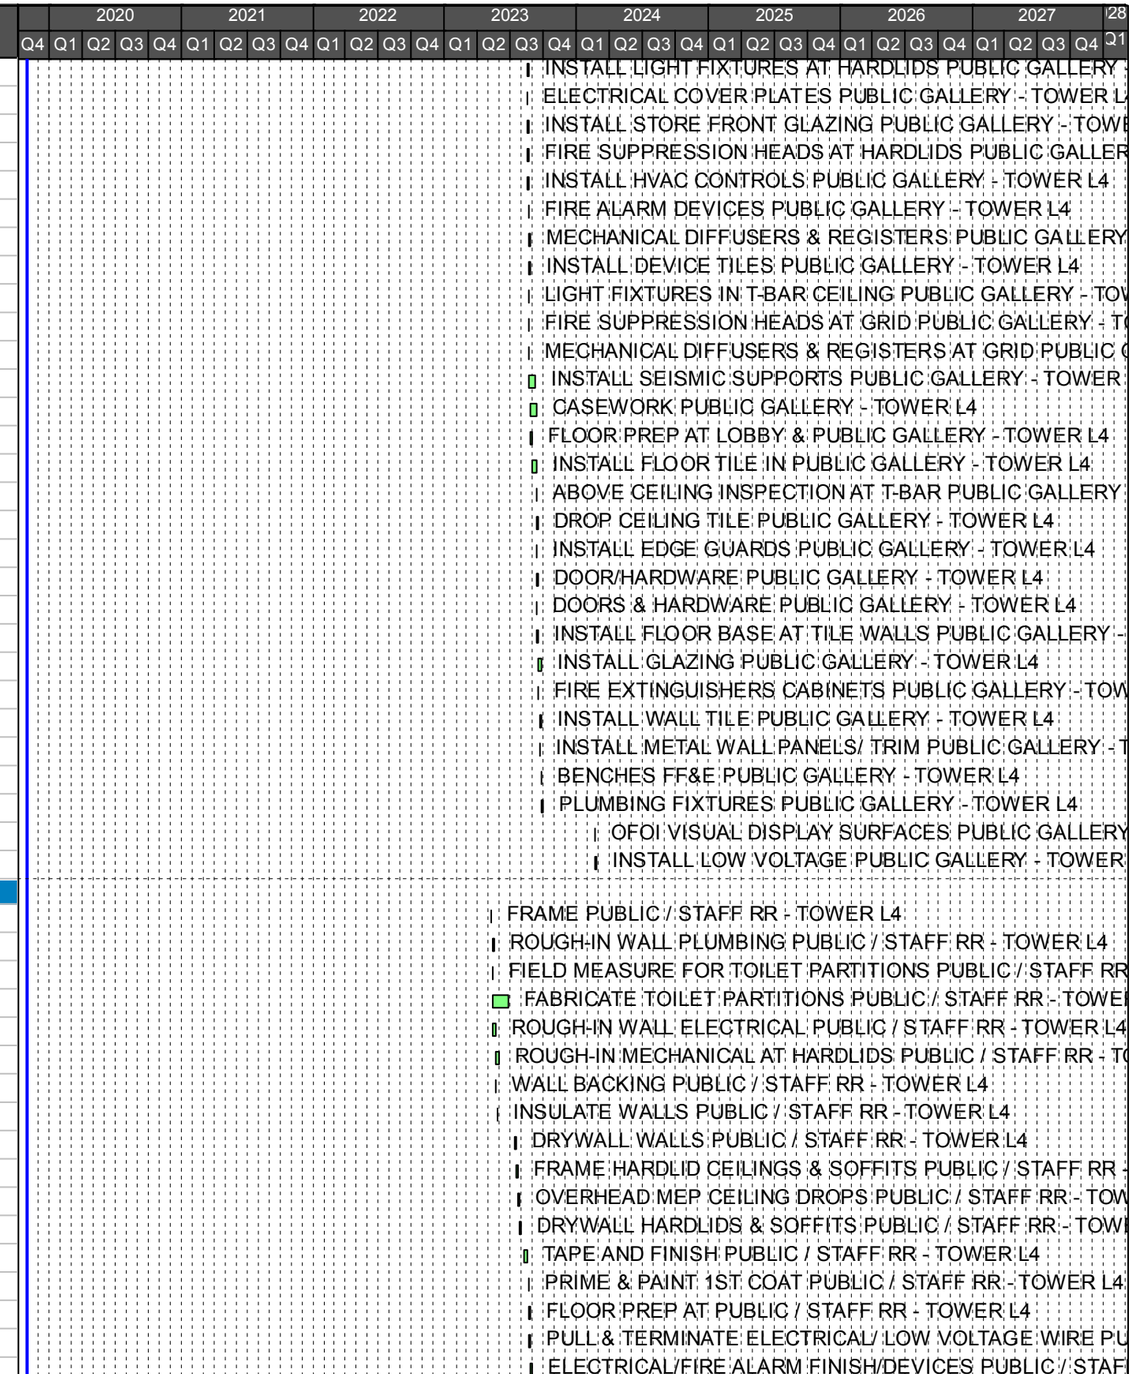

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TFINR4-250	INSTALL FLOOR & WALL TILE IN PUBLIC / STAFF RR - TOWER L4	9	28-Aug-23	11-Sep-23
TRR4-1030	MEP TRIM PUBLIC / STAFF PUBLIC / STAFF RR - TOWER L4	7	05-Sep-23	13-Sep-23
TFINR4-260	CASEWORK & TOPS PUBLIC / STAFF RR - TOWER L4	3	12-Sep-23	14-Sep-23
TFINR4-280	MECHANICAL DIFFUSERS & REGISTERS PUBLIC / STAFF RR - TOW	2	12-Sep-23	13-Sep-23
TFINR4-270	FIRE SUPPRESSION HEADS PUBLIC / STAFF RR - TOWER L4	1	15-Sep-23	15-Sep-23
TFINR4-290	PLUMBING FIXTURES PUBLIC / STAFF RR - TOWER L4	4	15-Sep-23	20-Sep-23
TFINR4-300	DOORS & HARDWARE PUBLIC / STAFF RR - TOWER L4	7	21-Sep-23	29-Sep-23
TFINR4-310	INSTALL PARTITIONS AND ACCESSORIES PUBLIC / STAFF RR - TO	7	26-Sep-23	04-Oct-23
TFINR4-320	FINAL PAINT PUBLIC / STAFF RR - TOWER L4	2	05-Oct-23	06-Oct-23
MANLIFT BAY				
ML4-1000	FRAME MANLIFT BAY - TOWER L4	3	25-Jul-23	27-Jul-23
ML4-1010	ROUGH-IN MEP MANLIFT BAY - TOWER L4	5	28-Jul-23	03-Aug-23
ML4-1020	FINISHES MANLIFT BAY - TOWER L4	15	04-Aug-23	24-Aug-23
ML4-1030	TRIM MANLIFT BAY - TOWER L4	5	25-Aug-23	31-Aug-23
LEVEL 5				
LEVEL 5 FULL FLOOR				
MS5-1000	PRE-WELD EXTERIOR & PARTITION CLIPS	7	10-Jan-23	19-Jan-23
MS5-1030	FIREPROOF BALANCE OF FLOORS	5	20-Jan-23	26-Jan-23
MS5-1020	FIREPROOF PRIORITY WALLS/PERIMETER - TOWER L5	5	20-Jan-23	26-Jan-23
MS5-1010	EDGE OF SLAB FIRE SAFE	5	09-Mar-23	15-Mar-23
TPG5-1000	ONE SIDE TIE INTO EXTERIOR - TOWER L5	5	16-Mar-23	22-Mar-23
TFING1-6540	FIELD MEASURE FOR WINDOW COVERINGS - TOWER L5	1	23-Aug-23	23-Aug-23
TFING1-6550	FABRICATE WINDOW COVERINGS - TOWER L5	10	14-Feb-24	29-Feb-24
TPG5-1160	FINAL PAINT - TOWER L5	7	21-Feb-24	29-Feb-24
TFING1-6090	WINDOW COVERINGS PUBLIC GALLERY - TOWER L5	4	01-Mar-24	06-Mar-24
TFING1-6260	INSTALL SIGNAGE - TOWER L5	5	01-Mar-24	07-Mar-24
TFING1-6270	INT. CERTIFICATION & READY FOR PUNCH - TOWER L5	1	08-Mar-24	08-Mar-24
OVERHEAD ROUGH-INS				
TFING1-6080	LAYOUT FOR CLIPS AND TRACK - TOWER L5	3	30-Dec-22	04-Jan-23
TFING1-6070	INSTALL TOP TRACK - TOWER L5	2	03-Jan-23	04-Jan-23
TFING1-6510	INSTALL FIRE SUPPRESSION HANGERS - TOWER L5	4	25-Jan-23	30-Jan-23
TFING1-6500	INSTALL ELECTRICAL HANGERS - TOWER L5	4	31-Jan-23	03-Feb-23
TFING1-8300	INSTALL LOW VOLTAGE HANGERS - TOWER L5	4	31-Jan-23	03-Feb-23
TFING1-6140	INSTALL PLUMBING HANGERS - TOWER L5	5	09-Feb-23	15-Feb-23
TFING1-6490	INSTALL MECHANICAL HANGERS - TOWER L5	5	09-Feb-23	15-Feb-23
TFING1-6280	FIRE SUPPRESSION MAINS - TOWER L5	5	16-Feb-23	24-Feb-23
TOHG1-1180	O/H WASTE & VENT - TOWER L5	7	28-Feb-23	08-Mar-23
TOHG1-1130	O/H ELECTRICAL MAINS - TOWER L5	5	02-Mar-23	08-Mar-23
TOHG1-1610	O/H LOW VOLTAGE MAINS - TOWER L5	8	02-Mar-23	13-Mar-23
TOHG1-1140	O/H PLUMBING MAINS - TOWER L5	6	04-Apr-23	11-Apr-23
TOHG1-1730	O/H PLUMBING BRANCHES - TOWER L5	7	12-Apr-23	20-Apr-23
TOHG1-1170	O/H MECHANICAL MAINS - TOWER L5	10	21-Apr-23	04-May-23
TFING1-6290	HANG VAV'S - TOWER L5	8	25-Apr-23	04-May-23
TOHG1-1200	O/H HYDRONIC PIPING - TOWER L5	5	04-May-23	10-May-23
TFING1-6150	FIRE SUPPRESSION BRANCHES - TOWER L5	10	12-May-23	25-May-23
TOHG1-1210	O/H ELECTRICAL BRANCHES - TOWER L5	3	19-May-23	23-May-23
TOHG1-1620	O/H LOW VOLTAGE BRANCHES - TOWER L5	3	19-May-23	23-May-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TFING1-6100	O/H HVAC CONTROLS - TOWER L5	2	24-May-23	25-May-23
TOHG1-1150	O/H LOW VOLTAGE - TOWER L5	2	24-May-23	25-May-23
TOHG1-1190	O/H MECHANICAL BRANCHES - TOWER L5	15	01-Jun-23	21-Jun-23
TPG2-1770	ONE SIDE TIE INTO EXTERIOR - TOWER L5	2	12-Jun-23	13-Jun-23
TOHG1-1160	O/H SECURITY - TOWER L5	2	22-Jun-23	23-Jun-23
PRIORITY WALLS (IDF/ ELEC/ SHAFT/ STAIRS)				
IDF/ ELECTRICAL ROOM/ CENTRAL CONTROL				
TPR5-1050	FRAME IDF ROOM, ELECTRICAL ROOM, STAIRS - TOWER L5	5	02-Mar-23	08-Mar-23
TPR5-1060	ROUGH-IN IDF / ELECTRICAL ROOMS - TOWER L5	5	09-Mar-23	15-Mar-23
TELECRI5-100	ROUGH-IN PLUMBING IDF / ELECTRICAL ROOMS - TOWER L5	2	09-Mar-23	10-Mar-23
TELECRI5-110	ROUGH-IN ELECTRICAL IDF / ELECTRICAL ROOMS - TOWER L5	4	10-Mar-23	15-Mar-23
TELECRI5-120	ROUGH-IN MECHANICAL IDF / ELECTRICAL ROOMS - TOWER L5	3	13-Mar-23	15-Mar-23
TPR5-1070	DRYWALL IDF/ ELECTRICAL ROOMS - TOWER L5	5	07-Jun-23	13-Jun-23
TPR5-1170	TAPE & FINISH IDF / ELECTRICAL ROOMS - TOWER L5 - TOWER L5	7	27-Jul-23	04-Aug-23
TELEC5-130	PAINT IDF / ELECTRICAL ROOMS - TOWER L5	3	07-Aug-23	09-Aug-23
TELEC5-140	SEAL FLOORS IDF/ELECTRICAL ROOMS - TOWER L5	2	10-Aug-23	11-Aug-23
TPR5-1120	DOORS & HARDWARE - TOWER L5	2	14-Aug-23	15-Aug-23
TPR5-1100	ELECTRICAL AND IDF, PANELS AND RACKS - TOWER L5	15	24-Aug-23	15-Sep-23
MEP SHAFTS				
TPR5-1040	INSTALL MEPF IN SHAFTS - TOWER L5	8	31-Jan-23	09-Feb-23
TPR5-1020	FRAME HVAC SHAFTS & DRYWALL C/R SIDE - TOWER L5	3	02-Mar-23	06-Mar-23
TPR5-1110	DRYWALL HVAC SHAFTS - TOWER L5	3	06-Jun-23	08-Jun-23
TPR5-1180	TAPE & FINISH HVAC SHAFTS - TOWER L5	7	22-Sep-23	02-Oct-23
ELEVATOR/ STAIR SHAFTS				
TPR5-1000	FRAME PASSENGER ELEVATOR HOISTWAYS - TOWER L5	3	07-Mar-23	09-Mar-23
TDR5-1010	FRAME AT H1/H2 - ELEVATOR FRAMES DETENTION AREA - TOWEF	4	09-Mar-23	14-Mar-23
TPR5-1010	FRAME J1/J2 ELEVATOR WALLS - TOWER L5	3	10-Mar-23	14-Mar-23
TPR1-2310	DRYWALL PASSENGER ELEVATOR - TOWER L5	2	10-Mar-23	13-Mar-23
TPR1-2330	TAPE & FINISH PASSENGER ELEVATOR - TOWER L5	6	14-Mar-23	21-Mar-23
TPR1-2320	DRYWALL J1/J2 ELEVATOR WALLS - TOWER L5	2	15-Mar-23	16-Mar-23
TPR1-2340	TAPE & FINISH J1/J2 ELEVATOR WALLS - TOWER L5	6	22-Mar-23	29-Mar-23
TPR5-1080	DRYWALL STAIR 1-2 - TOWER L5	2	09-Jun-23	12-Jun-23
TPR5-1090	DRYWALL STAIR 3-4 - TOWER L5	2	13-Jun-23	14-Jun-23
TPR5-1130	TAPE & FINISH STAIR 1-2 - TOWER L5	6	10-Oct-23	17-Oct-23
TPR5-1150	TAPE & FINISH STAIR 3-4 - TOWER L5	6	18-Oct-23	25-Oct-23
TPR5-1140	FINISHES STAIR 1-2 - TOWER L5	4	18-Oct-23	23-Oct-23
TELEC5-150	PRIME AND FIRST COAT PAINT STAIR 1-2 - TOWER L5	5	18-Oct-23	24-Oct-23
TPR5-1160	FINISHES STAIR 3-4 - TOWER L5	4	26-Oct-23	31-Oct-23
TELEC5-160	PRIME AND FIRST COAT PAINT STAIR 3-4 - TOWER L5	5	26-Oct-23	01-Nov-23
DETENTION AREA				
TFIND2-660	FRAME PARTITION WALLS DETENTION AREA - TOWER L5	2	15-Mar-23	16-Mar-23
TRID2-180	ROUGH-IN IN-WALL PLUMBING DETENTION AREA - TOWER L5	2	17-Mar-23	20-Mar-23
TRID2-190	ROUGH-IN - IN WALL ELECTRICAL DETENTION AREA - TOWER L5	2	20-Mar-23	21-Mar-23
TRID2-260	ROUGH-IN - IN WALL LOW VOLTAGE DETENTION AREA - TOWER L5	2	20-Mar-23	21-Mar-23
TOHD2-160	ROUGH-IN OVERHEAD MECHANICAL DETENTION AREA - TOWER L5	5	27-Mar-23	31-Mar-23
TFIND2-1430	INSULATE WALLS - TOWER L6	1	06-Apr-23	06-Apr-23
TFIND2-1440	IN-WALL INSPECTION TOWER L6	1	07-Apr-23	07-Apr-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

Activity ID	Activity Name	Original Duration	Start	Finish
TOHD2-270	ROUGH-IN OVERHEAD FIRE SUPPRESSION DETENTION AREA - TC	2	19-May-23	22-May-23
TOHD2-170	ROUGH-IN OVERHEAD PLUMBING DETENTION AREA - TOWER L5	2	07-Jun-23	08-Jun-23
TOHD3-130	ROUGH-IN OVERHEAD ELECTRICAL DETENTION AREA - TOWER L5	3	08-Jun-23	12-Jun-23
TFIND2-670	DRYWALL PARTITION WALLS DETENTION AREA - TOWER L5	3	23-Jun-23	27-Jun-23
TFIND2-680	TAPE/ FINISH PARTITION WALLS DETENTION AREA - TOWER L5	7	07-Jul-23	17-Jul-23
TFIND2-690	PAINT DETENTION AREA - TOWER L5	5	18-Jul-23	24-Jul-23
TFIND2-730	INSTALL PLUMBING COMBI UNITS DETENTION AREA - TOWER L5	5	25-Jul-23	31-Jul-23
TDR1-1200	CEILING GRID AND DEVICE TILES DETENTION AREA - TOWER L5	6	25-Jul-23	01-Aug-23
TDR5-1000	DETENTION METAL CEILINGS DETENTION AREA - TOWER L5	5	31-Jul-23	04-Aug-23
TFIND2-740	PLUMBING FIXTURES DETENTION AREA - TOWER L5	5	01-Aug-23	07-Aug-23
TFIND2-760	INSTALL GRILLS & DIFFUSERS IN CEILING DETENTION AREA - TOV	3	02-Aug-23	04-Aug-23
TDR1-1210	COMPLETE MECHANICAL IN CEILING DETENTION AREA - TOWER I	5	02-Aug-23	08-Aug-23
TFIND1-420	COMPLETE OVERHEAD FIRE SUPPRESSION IN CEILING - L5	2	02-Aug-23	03-Aug-23
TFIND1-430	COMPLETE ELECTRICAL IN CEILING DETENTION AREA - TOWER L5	5	02-Aug-23	08-Aug-23
TFIND1-440	COMPLETE PLUMBING IN CEILING DETENTION AREA - TOWER L5	5	02-Aug-23	08-Aug-23
TFIND1-450	COMPLETE LOW VOLTAGE IN CEILING DETENTION AREA - TOWEF	5	02-Aug-23	08-Aug-23
TFIND2-710	DOORS AND HARDWARE DETENTION AREA - TOWER L5	4	07-Aug-23	10-Aug-23
TFIND2-720	DETENTION FIXTURES DETENTION AREA - TOWER L5	10	07-Aug-23	18-Aug-23
TDR1-1270	ABOVE CEILING INSPECTION DETENTION AREA - TOWER L5	1	09-Aug-23	09-Aug-23
TDR1-1320	INSTALL SEISMIC BRACING DETENTION AREA - TOWER L5	10	09-Aug-23	22-Aug-23
TDR5-1050	DROP BALANCE OF TILES DETENTION AREA - TOWER L5	10	23-Aug-23	07-Sep-23
TFIND2-750	INSTALL INTERIOR GLAZING - TOWER L5	10	08-Sep-23	21-Sep-23
TFIND2-820	CASEWORK & TOPS DETENTION AREA - TOWER L5	7	15-Sep-23	25-Sep-23
TFIND2-810	SEAL CONCRETE FLOORS DETENTION AREA - TOWER L5	10	22-Sep-23	05-Oct-23
TDR5-1040	TRIM DETENTION AREA - TOWER L5	3	26-Sep-23	28-Sep-23
RESTRICTED CORRIDOR				
TPG5-1010	FRAME RESTRICTED CORRIDOR WALLS - TOWER L5	5	09-May-23	15-May-23
T1-G-1200	ELECTRICAL WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L	5	16-May-23	22-May-23
TRIG1-1040	LOW-VOLTAGE WALL ROUGH-IN RESTRICTED CORRIDOR - TOWEI	5	16-May-23	22-May-23
TRIG1-1050	PLUMBING WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L5	5	16-May-23	22-May-23
T1-G-1440	INSULATE WALLS RESTRICTED CORRIDOR WALLS - TOWER L5	1	23-May-23	23-May-23
T1-G-1450	IN WALL INSPECTION RESTRICTED CORRIDOR WALLS - TOWER L5	1	24-May-23	24-May-23
TPG5-1070	DRYWALL RESTRICTED CORRIDOR - TOWER L5	5	12-Jul-23	18-Jul-23
TPG5-1270	TAPE & FINISH RESTRICTED CORRIDOR - TOWER L5	5	09-Aug-23	15-Aug-23
TPG5-1090	MEP ROUGH-IN RESTRICTED CORRIDOR - TOWER L5	5	16-Aug-23	22-Aug-23
T1-G-1300	PRIME & PAINT RESTRICTED CORRIDOR - TOWER L5	5	16-Aug-23	22-Aug-23
T1-G-1560	PULL WIRE RESTRICTED CORRIDOR WALLS - TOWER L5	2	16-Aug-23	17-Aug-23
TPG5-1110	CEILING GRID & DEVICE TILES RESTRICTED CORRIDOR - TOWER	4	23-Aug-23	28-Aug-23
T1-G-1310	HVAC TRIM RESTRICTED CORRIDOR - TOWER L5	3	23-Aug-23	25-Aug-23
TFING1-8130	ELECTRICAL TRIM RESTRICTED CORRIDOR - TOWER L5	2	23-Aug-23	24-Aug-23
TFING1-8140	LOW VOLTAGE FINISHES RESTRICTED CORRIDOR - TOWER L5	2	29-Aug-23	30-Aug-23
TFING1-8150	FIRE SUPPRESSION HEADS RESTRICTED CORRIDOR - TOWER L5	2	29-Aug-23	30-Aug-23
TPG5-1040	INSTALL SEISMIC SUPPORTS RESTRICTED CORRIDOR - TOWER L	10	31-Aug-23	15-Sep-23
TPG5-1030	ABOVE CEILING INSPECTION RESTRICTED CORRIDOR WALLS - T	1	18-Sep-23	18-Sep-23
TPG5-1170	DROP BALANCE OF CEILING TILES RESTRICTED CORRIDOR - TOW	4	19-Sep-23	22-Sep-23
TPG5-1020	INSTALL INTERIOR GLAZING RESTRICTED CORRIDOR WALLS - TC	10	25-Sep-23	06-Oct-23
TPG5-1130	INSTALL FLOORING & BASE RESTRICTED CORRIDOR - TOWER L5	5	09-Oct-23	13-Oct-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
JURY DELIBERATION / JUDGES CHAMBERS / JUDGES RESTROOMS				
TJD5-1000	METAL PANELS & SOUND CAP TIE-IN TO EXTERIOR AT JUDICIAL S	3	23-Mar-23	27-Mar-23
TJD5-1010	FRAME JURY DELIBERATION/JUDGE'S CHAMBERS & JUDGE R/R -	7	12-May-23	22-May-23
TOHJ5-100	MECHANICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L5	7	23-May-23	02-Jun-23
TFINJ5-110	INSTALL DOOR FRAMES AT JUDICIAL SPACES - TOWER L5	3	23-May-23	25-May-23
TOHJ5-110	PLUMBING ROUGH-IN AT JUDICIAL SPACES - TOWER L5	5	09-Jun-23	15-Jun-23
TOHJ5-120	ELECTRICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L5	6	13-Jun-23	20-Jun-23
TOHJ5-130	LOW VOLTAGE ROUGH-IN AT JUDICIAL SPACES - TOWER L5	6	13-Jun-23	20-Jun-23
TOHJ1-220	INSULATE WALLS AT JUDICIAL SPACES - TOWER L5	1	21-Jun-23	21-Jun-23
TOHJ1-230	IN WALL INSPECTION AT JUDICIAL SPACES - TOWER L5	1	22-Jun-23	22-Jun-23
TFINJ5-150	DRYWALL WALLS AT JUDICIAL SPACES - TOWER L5	6	19-Jul-23	26-Jul-23
TFINJ5-240	TAPE & FINISH WALLS AT JUDICIAL SPACES - TOWER L5	7	16-Aug-23	24-Aug-23
TFINJ5-170	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT JUDICIAL SPA	3	25-Aug-23	29-Aug-23
TFINJ5-180	CEILING GRID & DEVICE TILES AT JUDICIAL SPACES - TOWER L5	6	30-Aug-23	08-Sep-23
TJD5-1040	MECHANICAL TRIM AT JUDICIAL SPACES - TOWER L5	5	11-Sep-23	15-Sep-23
TJD5-1050	ELECTRICAL TRIM AT JUDICIAL SPACES - TOWER L5	5	11-Sep-23	15-Sep-23
TJD5-1060	PLUMBING TRIM AT JUDICIAL SPACES - TOWER L5	5	11-Sep-23	15-Sep-23
TJD5-1070	FIRE SUPPRESSION TRIM AT JUDICIAL SPACES - TOWER L5	5	11-Sep-23	15-Sep-23
TJD5-1080	LOW VOLTAGE TRIM AT JUDICIAL SPACES - TOWER L5	5	11-Sep-23	15-Sep-23
TJD5-1110	INSTALL SEISMIC SUPPORTS JUDICIAL SPACES - TOWER L5	10	18-Sep-23	29-Sep-23
TJD5-1100	ABOVE CEILING INSPECTION AT JUDICIAL SPACES - TOWER L5	1	02-Oct-23	02-Oct-23
TFINJ5-210	DROP CEILING TILE AT JUDICIAL SPACES - TOWER L5	2	03-Oct-23	04-Oct-23
TJD5-1090	INSTALL INTERIOR GLAZING AT JUDICIAL SPACES - TOWER L5	10	05-Oct-23	18-Oct-23
TJD1-1100	INSTALL CASEWORK AT JUDICIAL SPACES - TOWER 5	5	09-Oct-23	13-Oct-23
TFINJ5-190	FLOOR PREP AT JUDICIAL SPACES - TOWER L5	1	19-Oct-23	19-Oct-23
TFINJ5-200	INSTALL CARPET & BASE AT JUDICIAL SPACES - TOWER L5	4	20-Oct-23	25-Oct-23
TFINJ5-220	DOORS & HARDWARE AT JUDICIAL SPACES - TOWER L5	5	26-Oct-23	01-Nov-23
COURTROOMS				
TCR5-1000	FRAME PERIMETER WALLS AT COURTROOMS - TOWER L5	10	16-May-23	31-May-23
TCR5-1020	FLOOR LEVEL AT COURTROOMS - TOWER L5	8	01-Jun-23	12-Jun-23
TRIC2-190	MECHANICAL ROUGH-IN DROPS AT COURTROOMS - TOWER L5	8	13-Jun-23	22-Jun-23
TRIC2-200	PLUMBING ROUGH-IN DROPS AT COURTROOMS - TOWER L5	6	13-Jul-23	20-Jul-23
TRIC2-360	FIRE SUPPRESSION ROUGH-IN DROPS AT COURTROOMS - TOWEI	6	13-Jul-23	20-Jul-23
TRIC2-210	ELECTRICAL ROUGH-IN DROPS AT COURTROOMS - TOWER L5	8	18-Jul-23	27-Jul-23
TRIC2-350	LOW VOLTAGE ROUGH-IN DROPS AT COURTROOMS - TOWER L5	8	18-Jul-23	27-Jul-23
TRIC2-280	INSTALL WALL BACKING - TOWER L5	2	28-Jul-23	31-Jul-23
TCR5-1050	FRAME CEILINGS AT COURTROOMS - TOWER L5	8	01-Aug-23	10-Aug-23
TCR1-1510	INSULATE WALLS AT COURTROOMS - TOWER L5	3	01-Aug-23	03-Aug-23
TCR1-1520	IN WALL INSPECTION AT COURTROOMS - TOWER L5	1	04-Aug-23	04-Aug-23
TCR5-1030	DRYWALL WALLS AT COURTROOMS - TOWER L5	5	11-Aug-23	17-Aug-23
TCR5-1060	CEILING FIXTURES PRE-DRYWALL AT COURTROOMS - TOWER L5	5	11-Aug-23	17-Aug-23
TCR5-1090	FRAME LOW WALLS AT COURTROOMS - TOWER L5	6	11-Aug-23	18-Aug-23
TCR5-1070	DRYWALL GYP CEILINGS AT COURTROOMS - TOWER L5	6	18-Aug-23	25-Aug-23
TCR5-1130	ACCESS FLOORING LAYOUT AT COURTROOMS - TOWER L5	3	21-Aug-23	23-Aug-23
TFINC5-100	INSTALL DOOR FRAMES AT COURTROOMS - TOWER L5	3	21-Aug-23	23-Aug-23
TCR5-1040	TAPE & FINISH WALLS AT COURTROOMS - TOWER L5	6	25-Aug-23	05-Sep-23
TCR5-1240	TAPE & FINISH GYP CEILINGS AT COURTROOMS - TOWER L5	7	28-Aug-23	07-Sep-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TCR5-1120	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT COURTROOM	3	08-Sep-23	12-Sep-23
TCR5-1080	CEILING GRID & DEVICE TILES AT COURTROOMS - TOWER L5	7	13-Sep-23	21-Sep-23
TCR5-1150	ACCESS FLOORING AT COURTROOMS - TOWER L5	12	13-Sep-23	28-Sep-23
TCR5-1100	MECHANICAL COMPLETE CEILING CONNECTIONS AT COURTROOM	5	22-Sep-23	28-Sep-23
TCR5-1260	ELECTRICAL COMPLETE CEILING CONNECTIONS AT COURTROOM	5	22-Sep-23	28-Sep-23
TCR5-1270	PLUMBING COMPLETE CEILING CONNECTIONS AT COURTROOMS	5	22-Sep-23	28-Sep-23
TCR5-1280	FIRE SUPPRESSION COMPLETE CEILING CONNECTIONS AT COUR	5	22-Sep-23	28-Sep-23
TCR5-1290	LOW VOLTAGE COMPLETE CEILING CONNECTIONS AT COURTROC	5	22-Sep-23	28-Sep-23
TRIC2-390	INSTALL SEISMIC SUPPORTS AT COURTROOMS - TOWER L5	10	29-Sep-23	12-Oct-23
TFINC1-340	ABOVE CEILING INSPECTION AT COURTROOMS - TOWER L5	1	13-Oct-23	13-Oct-23
TCR5-1110	DROP BALANCE OF CEILING TILES AT COURTROOMS - TOWER L5	4	16-Oct-23	19-Oct-23
TCR5-1160	CASEWORK AT COURTROOMS - TOWER L5	12	20-Oct-23	06-Nov-23
TCR5-1010	INSTALL INTERIOR GLAZING AT COURTROOMS - TOWER L5	10	20-Oct-23	02-Nov-23
TCR5-1250	INSTALL RAILING - TOWER L5	10	07-Nov-23	20-Nov-23
TCR5-1180	FINISH FLOORING & BASE AT COURTROOMS - TOWER L5	8	21-Nov-23	04-Dec-23
TCR5-1190	DOORS & HARDWARE AT COURTROOMS - TOWER L5	4	21-Nov-23	28-Nov-23
TCR5-1200	FABRIC WALL PANELS AT COURTROOMS - TOWER L5	4	29-Nov-23	04-Dec-23
TCR5-1210	FF & E AT COURTROOMS - TOWER L5	5	29-Nov-23	05-Dec-23
TCR5-1170	JURY SEATING AT COURTROOMS - TOWER L5	4	05-Dec-23	08-Dec-23
TCR5-1230	CLOSE-UP CASEWORK ELEC/LV TRIM & ACCESSORIES - TOWER L5	4	11-Dec-23	14-Dec-23
PUBLIC GALLERY				
TPG5-1100	F2 LIGHT FIXTURES AT PUBLIC GALLERY CEILINGS/MEP DROPS	4	03-Jul-23	07-Jul-23
IN-WALL ROUGH-INS				
TFING1-6300	FRAME INTERIOR WALLS PUBLIC GALLERY - TOWER L5	5	23-May-23	31-May-23
TFING1-6200	IN WALL COUNTERTOP SUPPORTS PUBLIC GALLERY - TOWER L5	2	25-May-23	30-May-23
TFING1-6400	HM DOOR FRAMES PUBLIC GALLERY - TOWER L5	2	30-May-23	31-May-23
TRIG1-760	ROUGH-IN WALL PLUMBING PUBLIC GALLERY - TOWER L5	2	31-May-23	01-Jun-23
TFING1-6420	INSTALL ELEVATOR DOOR FRAMES & ELEVATOR FRONTS PUBLIC	8	01-Jun-23	12-Jun-23
TFING1-6470	INSTALL STORE FRONT FRAMES PUBLIC GALLERY - TOWER L5	2	01-Jun-23	02-Jun-23
TRIG1-750	ROUGH-IN WALL LOW VOLTAGE PUBLIC GALLERY - TOWER L5	8	02-Jun-23	13-Jun-23
TRIG1-770	ROUGH-IN WALL ELECTRICAL PUBLIC GALLERY - TOWER L5	2	02-Jun-23	05-Jun-23
TRIG1-740	ROUGH-IN MECHANICAL CONTROLS PUBLIC GALLERY - TOWER L5	2	06-Jun-23	07-Jun-23
TFING1-6310	WALL BACKING PUBLIC GALLERY - TOWER L5	1	09-Jun-23	09-Jun-23
TFING1-6160	IN-WALL INSPECTION PUBLIC GALLERY - TOWER L5	1	14-Jun-23	14-Jun-23
OVERHEAD ROUGH-INS				
TPG5-1080	FRAME GYP CEILING PUBLIC GALLERY - TOWER L5	7	22-Jun-23	30-Jun-23
TRIG1-790	ROUGH-IN MECHANICAL AT HARDLIDS PUBLIC GALLERY - TOWER	2	03-Jul-23	05-Jul-23
TRIG1-780	ROUGH-IN ELECTRICAL AT HARDLIDS PUBLIC GALLERY - TOWER L	2	06-Jul-23	07-Jul-23
TFING1-6330	ABOVE CEILING INSPECTION AT HARDLIDS PUBLIC GALLERY - TO	1	10-Jul-23	10-Jul-23
FINISHES				
TFING1-6180	INSULATE WALLS PUBLIC GALLERY - TOWER L5	4	15-Jun-23	20-Jun-23
TFING1-6210	DRYWALL WALLS PUBLIC GALLERY - TOWER L5	4	14-Aug-23	17-Aug-23
TPG5-1120	DRYWALL CEILINGS PUBLIC GALLERY - TOWER L5	3	18-Aug-23	22-Aug-23
TFING1-6120	MEASURE & FAB INTERIOR GLAZING FRAMES PUBLIC GALLERY -	1	18-Aug-23	18-Aug-23
TFING1-6130	FURNISH MATERIAL FOR INTERIOR GLAZING FRAMES PUBLIC GAL	10	21-Aug-23	05-Sep-23
TFING1-6220	TAPE & FINISH PUBLIC GALLERY - TOWER L5	6	06-Sep-23	13-Sep-23
TFING1-6190	PRIME & PAINT 1ST COAT PUBLIC GALLERY - TOWER L5	3	18-Sep-23	20-Sep-23

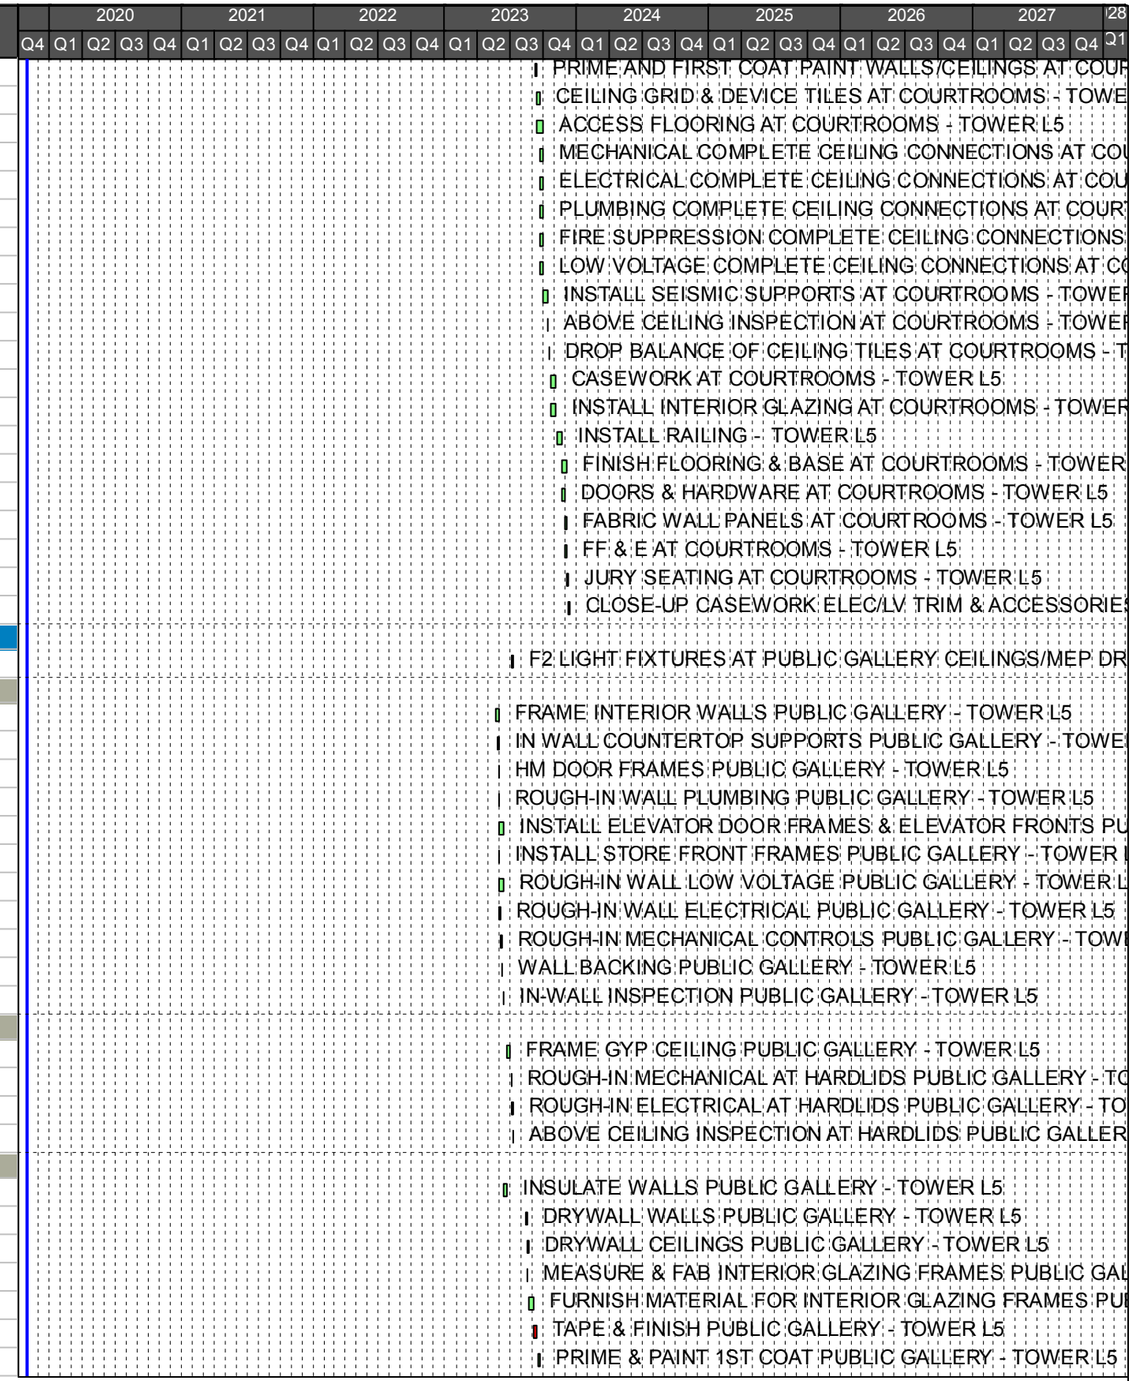

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TPG5-1190	CEILING GRID / DEVICE TILES PUBLIC GALLERY - TOWER L5	4	21-Sep-23	26-Sep-23
TPG2-1750	INSTALL LIGHT FIXTURES AT HARDLIDS PUBLIC GALLERY - TOWE	4	21-Sep-23	26-Sep-23
TFING1-6170	ELECTRICAL COVER PLATES PUBLIC GALLERY - TOWER L5	3	21-Sep-23	25-Sep-23
TFING1-6480	INSTALL STORE FRONT GLAZING PUBLIC GALLERY - TOWER L5	5	21-Sep-23	27-Sep-23
TFING1-6530	FIRE SUPPRESSION HEADS AT HARDLIDS PUBLIC GALLERY - TOV	4	21-Sep-23	26-Sep-23
TFING1-6560	INSTALL HVAC CONTROLS PUBLIC GALLERY - TOWER L5	5	21-Sep-23	27-Sep-23
TPG5-1210	FIRE ALARM DEVICES PUBLIC GALLERY - TOWER L5	2	27-Sep-23	28-Sep-23
TPG2-1810	MECHANICAL DIFFUSERS & REGISTERS PUBLIC GALLERY - TOWE	3	27-Sep-23	29-Sep-23
TPG2-1850	INSTALL DEVICE TILES PUBLIC GALLERY - TOWER L5	3	27-Sep-23	29-Sep-23
TFING1-6350	CASEWORK PUBLIC GALLERY - TOWER L5	10	27-Sep-23	10-Oct-23
TOHG1-1220	LIGHT FIXTURES IN T-BAR CEILING PUBLIC GALLERY - TOWER L5	2	27-Sep-23	28-Sep-23
TFING1-6360	FIRE SUPPRESSION HEADS AT GRID PUBLIC GALLERY - TOWER L5	2	27-Sep-23	28-Sep-23
TFING1-6370	MECHANICAL DIFFUSERS & REGISTERS AT GRID PUBLIC GALLER	2	27-Sep-23	28-Sep-23
TFING1-6230	INSTALL SEISMIC SUPPORTS PUBLIC GALLERY - TOWER L5	10	29-Sep-23	12-Oct-23
TFING1-6450	FLOOR PREP AT LOBBY & PUBLIC GALLERY - TOWER L5	4	02-Oct-23	05-Oct-23
TPG5-1240	INSTALL FLOOR TILE IN PUBLIC GALLERY - TOWER L5	7	06-Oct-23	16-Oct-23
TFING1-6320	INSTALL EDGE GUARDS PUBLIC GALLERY - TOWER L5	2	11-Oct-23	12-Oct-23
TFING1-6380	ABOVE CEILING INSPECTION AT T-BAR PUBLIC GALLERY - TOWE	1	13-Oct-23	13-Oct-23
TPG5-1220	DROP CEILING TILE PUBLIC GALLERY - TOWER L5	4	16-Oct-23	19-Oct-23
TPG5-1260	DOORS & HARDWARE PUBLIC GALLERY - TOWER L5	2	17-Oct-23	18-Oct-23
TFING1-6440	INSTALL FLOOR BASE AT TILE WALLS PUBLIC GALLERY - TOWER	5	17-Oct-23	23-Oct-23
TFING1-6250	INSTALL GLAZING PUBLIC GALLERY - TOWER L5	8	20-Oct-23	31-Oct-23
TFING1-6340	FIRE EXTINGUISHERS CABINETS PUBLIC GALLERY - TOWER L5	2	20-Oct-23	23-Oct-23
TPG5-1200	INSTALL WALL TILE PUBLIC GALLERY - TOWER L5	5	24-Oct-23	30-Oct-23
TFING1-6430	INSTALL METAL WALL PANELS/ TRIM PUBLIC GALLERY - TOWER L5	3	24-Oct-23	26-Oct-23
TPG5-1250	BENCHES FF&E PUBLIC GALLERY - TOWER L5	2	27-Oct-23	30-Oct-23
TPG5-1230	PLUMBING FIXTURES PUBLIC GALLERY - TOWER L5	2	31-Oct-23	01-Nov-23
TFING1-6110	OFOI VISUAL DISPLAY SURFACES PUBLIC GALLERY - TOWER L5	2	01-Mar-24	04-Mar-24
TFING1-6520	INSTALL LOW VOLTAGE PUBLIC GALLERY - TOWER L5	4	01-Mar-24	06-Mar-24
PUBLIC / STAFF RESTROOMS				
TRR5-1000	FRAME PUBLIC / STAFF RR - TOWER L5	4	01-Jun-23	06-Jun-23
TRIR5-100	ROUGH-IN WALL PLUMBING PUBLIC / STAFF RR - TOWER L5	5	07-Jun-23	13-Jun-23
TFINR5-110	FIELD MEASURE FOR TOILET PARTITIONS PUBLIC / STAFF RR - TO	1	07-Jun-23	07-Jun-23
TFINR5-120	FABRICATE TOILET PARTITIONS PUBLIC / STAFF RR - TOWER L5	30	08-Jun-23	20-Jul-23
TRIR5-110	ROUGH-IN WALL ELECTRICAL PUBLIC / STAFF RR - TOWER L5	5	14-Jun-23	20-Jun-23
TRIR5-120	ROUGH-IN MECHANICAL AT HARDLIDS PUBLIC / STAFF RR - TOWE	5	21-Jun-23	27-Jun-23
TRR5-1020	FINISHES PUBLIC / STAFF RR - TOWER L5	12	28-Jun-23	14-Jul-23
TFINR5-150	WALL BACKING PUBLIC / STAFF RR - TOWER L5	2	28-Jun-23	29-Jun-23
TFINR5-160	INSULATE WALLS PUBLIC / STAFF RR - TOWER L5	1	30-Jun-23	30-Jun-23
TFINR5-170	DRYWALL WALLS PUBLIC / STAFF RR - TOWER L5	2	16-Aug-23	17-Aug-23
TFINR5-190	FRAME HARDLID CEILINGS & SOFFITS PUBLIC / STAFF RR - TOWE	4	18-Aug-23	23-Aug-23
TFINR1-410	OVERHEAD MEP CEILING DROPS PUBLIC / STAFF RR - TOWER L5	4	24-Aug-23	29-Aug-23
TFINR5-180	DRYWALL HARDLIDS & SOFFITS PUBLIC / STAFF RR - TOWER L5	3	29-Sep-23	03-Oct-23
TFINR5-200	TAPE & FINISH AND FINISH PUBLIC / STAFF RR - TOWER L5	7	04-Oct-23	12-Oct-23
TFINR5-210	PRIME & PAINT 1ST COAT PUBLIC / STAFF RR - TOWER L5	3	16-Oct-23	18-Oct-23
TFINR5-220	FINISHES PUBLIC / STAFF RR - TOWER L5	12	19-Oct-23	03-Nov-23
TFINR5-230	FLOOR PREP AT PUBLIC / STAFF RR - TOWER L5	2	19-Oct-23	20-Oct-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TFINR5-240	PULL & TERMINATE ELECTRICAL/ LOW VOLTAGE WIRE	2	19-Oct-23	20-Oct-23
TRR5-1030	MEP TRIM PUBLIC / STAFF RR - TOWER L5	7	23-Oct-23	31-Oct-23
TFINR5-250	ELECTRICAL/FIRE ALARM FINISH/DEVICES PUBLIC / STAFF RR - T	4	23-Oct-23	26-Oct-23
TFINR5-260	INSTALL FLOOR & WALL TILE IN PUBLIC / STAFF RR - TOWER L5	9	23-Oct-23	02-Nov-23
TFINR5-300	MECHANICAL DIFFUSERS & REGISTERS PUBLIC / STAFF RR - TOW	2	30-Oct-23	31-Oct-23
TFINR5-270	CASEWORK & TOPS PUBLIC / STAFF RR - TOWER L5	3	03-Nov-23	07-Nov-23
TFINR5-280	MEP TRIM PUBLIC / STAFF RR - TOWER L5	7	06-Nov-23	14-Nov-23
TFINR5-290	FIRE SUPPRESSION HEADS PUBLIC / STAFF RR - TOWER L5	1	08-Nov-23	08-Nov-23
TFINR5-310	PLUMBING FIXTURES PUBLIC / STAFF RR - TOWER L5	4	08-Nov-23	13-Nov-23
TFINR5-320	DOORS & HARDWARE PUBLIC / STAFF RR - TOWER L5	7	14-Nov-23	22-Nov-23
TFINR5-330	INSTALL PARTITIONS AND ACCESSORIES PUBLIC / STAFF RR - TO	7	17-Nov-23	29-Nov-23
MANLIFT BAY				
LOB5-100	FRAME MANLIFT BAY - TOWER L5	3	25-Jul-23	27-Jul-23
LOB5-110	ROUGH-IN MEP MANLIFT BAY - TOWER L5	5	28-Jul-23	03-Aug-23
LOB5-120	FINISHES MANLIFT BAY - TOWER L5	15	04-Aug-23	24-Aug-23
LOB5-130	TRIM MANLIFT BAY - TOWER L5	5	25-Aug-23	31-Aug-23
LEVEL 6				
PRIORITY WALLS (IDF/ ELEC/ SHAFT/ STAIRS)				
TCR4-1250	FRAME PERIMETER WALLS AT COURTROOMS - TOWER L6	10	08-Jun-23	21-Jun-23
TCR4-1260	FLOOR LEVEL AT COURTROOMS - TOWER L6	8	22-Jun-23	03-Jul-23
TFINC4-120	INSTALL DOOR FRAMES AT COURTROOMS - TOWER L6	3	22-Jun-23	26-Jun-23
TOHC4-110	O/H & I/W ROUGH-IN DROPS AT COURTROOMS - TOWER L6	15	28-Jun-23	19-Jul-23
TRIC2-250	MECHANICAL ROUGH-IN DROPS AT COURTROOMS - TOWER L6	8	28-Jun-23	10-Jul-23
TRIC2-260	PLUMBING ROUGH-IN DROPS AT COURTROOMS - TOWER L6	6	05-Jul-23	12-Jul-23
TRIC2-270	ELECTRICAL ROUGH-IN DROPS AT COURTROOMS - TOWER L6	8	10-Jul-23	19-Jul-23
TCR4-1270	DRYWALL WALLS AT COURTROOMS - TOWER L6	5	06-Sep-23	12-Sep-23
TCR4-1280	TAPE & FINISH WALLS AT COURTROOMS - TOWER L6	6	02-Oct-23	09-Oct-23
TCR4-1290	FRAME CEILINGS AT COURTROOMS - TOWER L6	8	10-Oct-23	19-Oct-23
TCR4-1300	CEILING FIXTURES PRE-DRYWALL AT COURTROOMS - TOWER L6	5	20-Oct-23	26-Oct-23
TCR4-1330	FRAME LOW WALLS AT COURTROOMS - TOWER L6	6	20-Oct-23	27-Oct-23
TCR4-1310	DRYWALL GYP CEILINGS AT COURTROOMS - TOWER L6	6	27-Oct-23	03-Nov-23
TCR4-1350	ACCESS FLOORING LAYOUT AT COURTROOMS - TOWER L6	3	30-Oct-23	01-Nov-23
TCR4-1470	TAPE & FINISH GYP CEILINGS AT COURTROOMS - TOWER L6	7	06-Nov-23	14-Nov-23
TCR4-1340	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT COURTROOM	3	15-Nov-23	17-Nov-23
TCR4-1320	CEILING GRID & DEVICE TILES AT COURTROOMS - TOWER L6	7	20-Nov-23	30-Nov-23
TCR4-1360	ACCESS FLOORING AT COURTROOMS - TOWER L6	12	20-Nov-23	07-Dec-23
TCR4-1460	MEP COMPLETE CEILING CONNECTIONS AT COURTROOMS - TOW	5	01-Dec-23	07-Dec-23
TCR4-1370	DROP BALANCE OF CEILING TILES AT COURTROOMS - TOWER L6	4	08-Dec-23	13-Dec-23
TCR4-1390	CASEWORK AT COURTROOMS - TOWER L6	12	14-Dec-23	02-Jan-24
TCR4-1400	FINISH FLOORING & BASE AT COURTROOMS - TOWER L6	8	28-Dec-23	09-Jan-24
TCR4-1410	DOORS & HARDWARE AT COURTROOMS - TOWER L6	4	28-Dec-23	03-Jan-24
TCR4-1420	FABRIC WALL PANELS AT COURTROOMS - TOWER L6	4	04-Jan-24	09-Jan-24
TCR4-1430	FF & E AT COURTROOMS - TOWER L6	5	04-Jan-24	10-Jan-24
TCR4-1380	JURY SEATING AT COURTROOMS - TOWER L6	4	10-Jan-24	16-Jan-24
TCR4-1440	MEP TRIM AT COURTROOMS - TOWER L6	4	17-Jan-24	22-Jan-24
TCR4-1450	CLOSE-UP CASEWORK MEP ACCESSORIES AT COURTROOMS - T(	4	23-Jan-24	26-Jan-24
MEP SHAFTS				

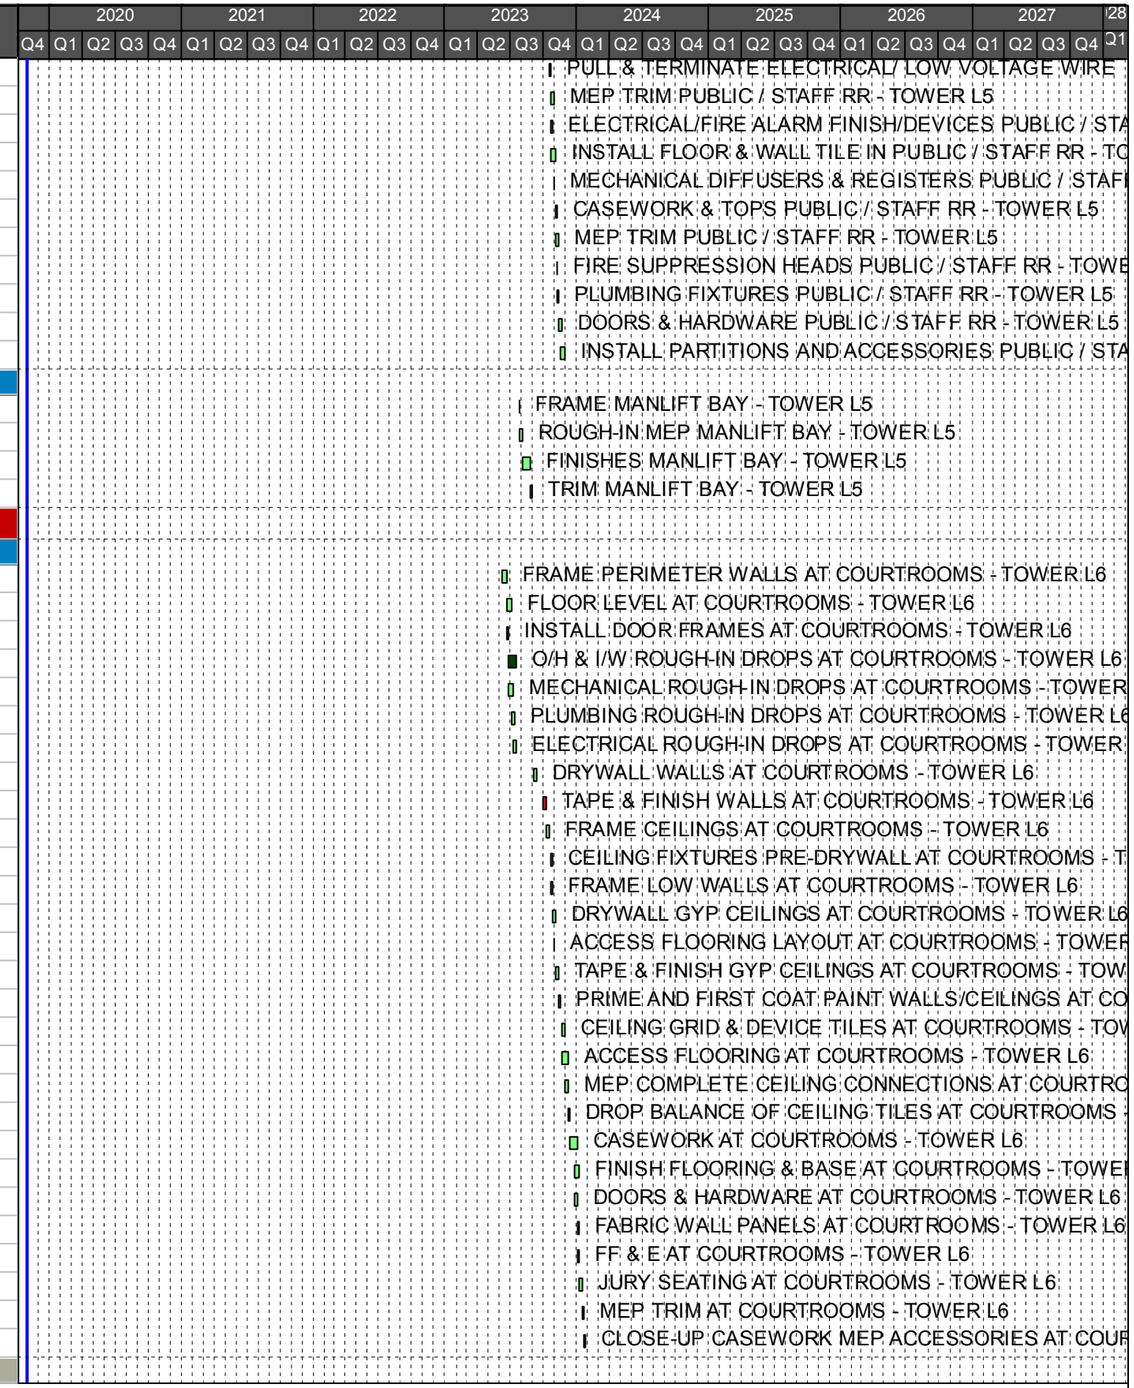

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TPR6-1140	TAPE & FINISH HVAC SHAFTS - TOWER L6	6	03-Oct-23	10-Oct-23
LEVEL 6 FULL FLOOR				
MS6-1000	PRE-WELD EXTERIOR & PARTITION CLIPS	5	29-Dec-22	05-Jan-23
MS6-1030	FIREPROOF BALANCE OF FLOORS	5	27-Jan-23	02-Feb-23
MS6-1020	FIREPROOF PRIORITY WALLS/PERIMETER - TOWER L6	5	27-Jan-23	02-Feb-23
MS6-1010	EDGE OF SLAB FIRE SAFE	5	15-Feb-23	23-Feb-23
TFING1-8010	FIELD MEASURE FOR WINDOW COVERINGS - TOWER L6	1	22-Sep-23	22-Sep-23
TFING1-8020	FABRICATE WINDOW COVERINGS - TOWER L6	10	27-Feb-24	11-Mar-24
TPG4-1380	FINAL PAINT - TOWER L6	7	01-Mar-24	11-Mar-24
TFING1-7590	WINDOW COVERINGS PUBLIC GALLERY - TOWER L6	4	12-Mar-24	15-Mar-24
TFING1-7760	INSTALL SIGNAGE - TOWER L6	5	12-Mar-24	18-Mar-24
TFING1-7770	INT. CERTIFICATION & READY FOR PUNCH - TOWER L6	1	19-Mar-24	19-Mar-24
OVERHEAD ROUGH-INS				
TFING1-7580	LAYOUT FOR CLIPS AND TRACK - TOWER L6	3	05-Jan-23	09-Jan-23
TFING1-7570	INSTALL TOP TRACK - TOWER L6	2	06-Jan-23	09-Jan-23
TFING1-7980	INSTALL FIRE SUPPRESSION HANGERS - TOWER L6	4	31-Jan-23	03-Feb-23
TFING1-7970	INSTALL ELECTRICAL HANGERS - TOWER L6	4	06-Feb-23	09-Feb-23
TFING1-8310	INSTALL LOW VOLTAGE HANGERS - TOWER L6	4	06-Feb-23	09-Feb-23
TFING1-7640	INSTALL PLUMBING HANGERS - TOWER L6	5	16-Feb-23	24-Feb-23
TFING1-7960	INSTALL MECHANICAL HANGERS - TOWER L6	5	16-Feb-23	24-Feb-23
TFING1-7780	FIRE SUPPRESSION MAINS - TOWER L6	5	27-Feb-23	03-Mar-23
TOHG1-1480	O/H WASTE & VENT - TOWER L6	7	09-Mar-23	17-Mar-23
TOHG1-1430	O/H ELECTRICAL MAINS - TOWER L6	5	13-Mar-23	17-Mar-23
TOHG1-1630	O/H LOW VOLTAGE MAINS - TOWER L6	8	13-Mar-23	22-Mar-23
TPR4-1220	FRAME IDF ROOM, ELECTRICAL ROOM, STAIRS - TOWER L6	5	17-Mar-23	23-Mar-23
TELECRI4-150	ROUGH-IN PLUMBING IDF / ELECTRICAL ROOMS - TOWER L6	2	24-Mar-23	27-Mar-23
TELECRI4-140	ROUGH-IN ELECTRICAL IDF / ELECTRICAL ROOMS - TOWER L6	4	27-Mar-23	30-Mar-23
TELECRI4-130	ROUGH-IN MECHANICAL IDF / ELECTRICAL ROOMS - TOWER L6	3	28-Mar-23	30-Mar-23
TOHG1-1440	O/H PLUMBING MAINS - TOWER L6	6	21-Apr-23	28-Apr-23
TOHG1-1740	O/H PLUMBING BRANCHES - TOWER L6	7	01-May-23	09-May-23
TOHG1-1470	O/H MECHANICAL MAINS - TOWER L6	10	10-May-23	23-May-23
TFING1-7790	HANG VAV'S - TOWER L6	8	12-May-23	23-May-23
TOHG1-1500	O/H HYDRONIC PIPING - TOWER L6	5	23-May-23	31-May-23
TFING1-7650	FIRE SUPPRESSION BRANCHES - TOWER L6	10	02-Jun-23	15-Jun-23
TOHG1-1510	O/H ELECTRICAL BRANCHES - TOWER L6	3	09-Jun-23	13-Jun-23
TOHG1-1640	O/H LOW VOLTAGE BRANCHES - TOWER L6	3	09-Jun-23	13-Jun-23
TFING1-7600	O/H HVAC CONTROLS - TOWER L6	2	14-Jun-23	15-Jun-23
TOHG1-1450	O/H LOW VOLTAGE - TOWER L6	2	14-Jun-23	15-Jun-23
TPR4-1250	DRYWALL IDF/ ELECTRICAL ROOMS - TOWER L6	5	26-Jun-23	30-Jun-23
TOHG1-1490	O/H MECHANICAL BRANCHES - TOWER L6	15	26-Jun-23	17-Jul-23
TPG2-2110	ONE SIDE TIE INTO EXTERIOR - TOWER L6	2	06-Jul-23	07-Jul-23
TOHG1-1460	O/H SECURITY - TOWER L6	2	18-Jul-23	19-Jul-23
TPR4-1340	TAPE & FINISH IDF / ELECTRICAL ROOMS - TOWER L6	7	07-Aug-23	15-Aug-23
TELEC4-190	PAINT IDF / ELECTRICAL ROOMS - TOWER L6	3	16-Aug-23	18-Aug-23
TELEC4-200	SEAL FLOORS IDF / ELECTRICAL ROOMS - TOWER L6	2	21-Aug-23	22-Aug-23
TPR4-1320	DOORS & HARDWARE IDF / ELECTRICAL ROOMS - TOWER L6	2	23-Aug-23	24-Aug-23
TPR4-1330	ELECTRICAL AND IDF, PANELS AND RACKS IDF / ELECTRICAL ROC	15	06-Sep-23	26-Sep-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TELEC4-210	PRIME AND FIRST COAT PAINT STAIR 1-2 - TOWER L6	5	08-Nov-23	14-Nov-23
MEP SHAFTS				
TPR4-1230	INSTALL MEPF IN SHAFTS	8	10-Feb-23	23-Feb-23
TPR4-1210	FRAME HVAC SHAFTS & DRYWALL C/R SIDE	3	17-Mar-23	21-Mar-23
TPR4-1350	DRYWALL HVAC SHAFTS - TOWER L6	7	15-Jun-23	23-Jun-23
TPR4-1240	TAPE & FINISH HVAC SHAFTS - TOWER L6	3	26-Oct-23	30-Oct-23
ELEVATOR/ STAIR SHAFTS				
TPR4-1190	FRAME PASSENGER ELEVATOR HOISTWAYS	3	22-Mar-23	24-Mar-23
TDR4-1050	FRAME AT H1/H2 - ELEVATOR FRAMES - L6 DETENTION AREA	4	23-Mar-23	28-Mar-23
TPR4-1200	FRAME J1/J2 ELEVATOR WALLS	3	27-Mar-23	29-Mar-23
TPR1-2450	DRYWALL PASSENGER ELEVATOR - TOWER L6	2	27-Mar-23	28-Mar-23
TPR1-2460	TAPE & FINISH PASSENGER ELEVATOR - TOWER L6	6	29-Mar-23	05-Apr-23
TPR1-2430	DRYWALL J1/J2 ELEVATOR WALLS - TOWER L6	2	30-Mar-23	31-Mar-23
TPR1-2440	TAPE & FINISH J1/J2 ELEVATOR WALLS - TOWER L6	6	06-Apr-23	13-Apr-23
TPR4-1260	DRYWALL STAIR 1-2 - TOWER L6	2	26-Jun-23	27-Jun-23
TPR4-1290	DRYWALL STAIR 3-4 - TOWER L6	2	28-Jun-23	29-Jun-23
TPR4-1270	TAPE & FINISH STAIR 1-2 - TOWER L6	6	31-Oct-23	07-Nov-23
TPR4-1280	FINISHES STAIR 1-2 - TOWER L6	4	08-Nov-23	13-Nov-23
TPR4-1300	TAPE & FINISH STAIR 3-4 - TOWER L6	6	08-Nov-23	15-Nov-23
TPR4-1310	FINISHES STAIR 3-4 - TOWER L6	4	16-Nov-23	21-Nov-23
TELEC4-220	PRIME AND FIRST COAT PAINT STAIR 3-4 - TOWER L6	5	16-Nov-23	22-Nov-23
DETENTION AREA				
TFIND2-1250	FRAME PARTITION WALLS DETENTION AREA - TOWER L6	2	30-Mar-23	31-Mar-23
TOHD2-220	ROUGH-IN OVERHEAD MECHANICAL DETENTION AREA - TOWER L6	5	03-Apr-23	07-Apr-23
TRID2-240	ROUGH-IN IN-WALL PLUMBING DETENTION AREA - TOWER L6	2	03-Apr-23	04-Apr-23
TRID2-250	ROUGH-IN - IN WALL ELECTRICAL DETENTION AREA - TOWER L6	2	04-Apr-23	05-Apr-23
TRID2-270	ROUGH-IN - OVERHEAD LOW VOLTAGE DETENTION AREA - TOWEI	2	04-Apr-23	05-Apr-23
TFIND2-1310	INSULATE WALLS - TOWER L6	1	06-Apr-23	06-Apr-23
TFIND2-1320	IN-WALL INSPECTION TOWER L6	1	07-Apr-23	07-Apr-23
TFIND2-1210	INSTALL GRILLS & DIFFUSERS IN CEILING DETENTION AREA - TOV	3	10-Apr-23	12-Apr-23
TOHD2-280	ROUGH-IN OVERHEAD FIRE SUPPRESSION DETENTION AREA - TC	2	10-Apr-23	11-Apr-23
TFIND2-1260	DRYWALL PARTITION WALLS DETENTION AREA - TOWER L6	3	28-Jun-23	30-Jun-23
TFIND2-1300	TAPE & FINISH PARTITION WALLS DETENTION AREA - TOWER L6	7	18-Jul-23	26-Jul-23
TOHD2-230	ROUGH-IN OVERHEAD PLUMBING DETENTION AREA - TOWER L6	2	21-Jul-23	24-Jul-23
TOHD3-160	ROUGH-IN OVERHEAD ELECTRICAL DETENTION AREA - TOWER L6	3	24-Jul-23	26-Jul-23
TDR4-1060	DETENTION METAL CEILINGS DETENTION AREA - TOWER L6	5	27-Jul-23	02-Aug-23
TFIND2-1170	PAINT DETENTION AREA - TOWER L6	5	03-Aug-23	09-Aug-23
TFIND2-1180	DOORS AND HARDWARE DETENTION AREA - TOWER L6	4	10-Aug-23	15-Aug-23
TFIND2-1190	DETENTION FIXTURES DETENTION AREA - TOWER L6	10	10-Aug-23	23-Aug-23
TFIND2-1290	INSTALL PLUMBING COMBI UNITS DETENTION AREA - TOWER L6	5	10-Aug-23	16-Aug-23
TDR1-1220	CEILING GRID AND DEVICE TILES DETENTION AREA - TOWER L6	6	10-Aug-23	17-Aug-23
TFIND2-1280	PLUMBING FIXTURES DETENTION AREA - TOWER L6	5	17-Aug-23	23-Aug-23
TDR1-1230	COMPLETE MECHANICAL IN CEILING DETENTION AREA - TOWER I	5	18-Aug-23	24-Aug-23
TFIND1-460	COMPLETE OVERHEAD FIRE SUPPRESSION IN CEILING - L6	2	18-Aug-23	21-Aug-23
TFIND1-470	COMPLETE ELECTRICAL IN CEILING DETENTION AREA - TOWER L6	5	18-Aug-23	24-Aug-23
TFIND1-480	COMPLETE PLUMBING IN CEILING DETENTION AREA - TOWER L6	5	18-Aug-23	24-Aug-23
TFIND1-490	COMPLETE LOW VOLTAGE IN CEILING DETENTION AREA - TOWEF	5	18-Aug-23	24-Aug-23

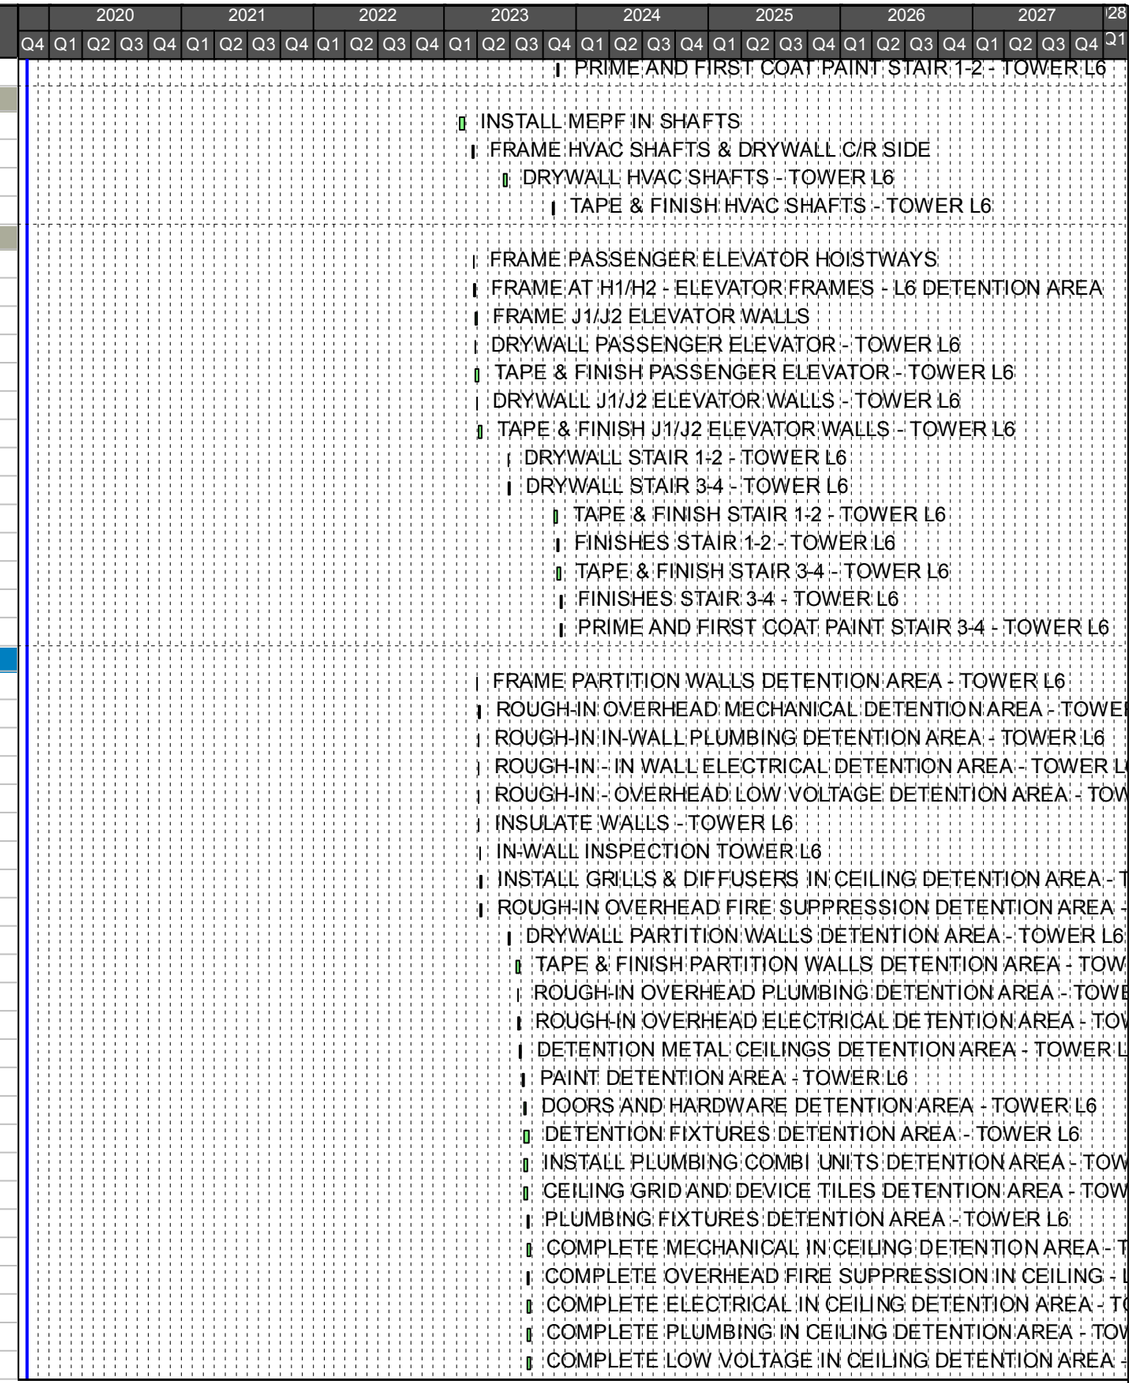

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TDR1-1280	ABOVE CEILING INSPECTION DETENTION AREA - TOWER L6	1	25-Aug-23	25-Aug-23
TFIND1-560	INSTALL SEISMIC BRACING DETENTION AREA - TOWER L6	10	25-Aug-23	11-Sep-23
TFIND1-540	DROP BALANCE OF TILES DETENTION AREA - TOWER L6	3	12-Sep-23	14-Sep-23
TFIND2-1220	INSTALL INTERIOR GLAZING - TOWER L6	10	15-Sep-23	28-Sep-23
TFIND2-1200	SEAL CONCRETE FLOORS DETENTION AREA - TOWER L6	10	29-Sep-23	12-Oct-23
TFIND2-1270	CASEWORK & TOPS DETENTION AREA - TOWER L6	7	08-Nov-23	16-Nov-23
TDR4-1080	TRIM - L6 DETENTION AREA	3	17-Nov-23	21-Nov-23
RESTRICTED CORRIDOR				
TPG4-1270	FRAME RESTRICTED CORRIDOR WALLS - TOWER L6	5	01-Jun-23	07-Jun-23
T1-G-1210	ELECTRICAL WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L	5	08-Jun-23	14-Jun-23
TRIG1-1060	LOW-VOLTAGE WALL ROUGH-IN RESTRICTED CORRIDOR - TOWE	5	08-Jun-23	14-Jun-23
TRIG1-1070	PLUMBING WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L6	5	08-Jun-23	14-Jun-23
T1-G-1460	INSULATE WALLS RESTRICTED CORRIDOR WALLS - TOWER L6	1	15-Jun-23	15-Jun-23
T1-G-1470	IN WALL INSPECTION RESTRICTED CORRIDOR WALLS - TOWER L6	1	16-Jun-23	16-Jun-23
TPG4-1300	DRYWALL RESTRICTED CORRIDOR - TOWER L6	5	18-Aug-23	24-Aug-23
TPG4-1510	TAPE & FINISH RESTRICTED CORRIDOR - TOWER L6	5	14-Sep-23	20-Sep-23
T1-G-1320	PRIME & PAINT RESTRICTED CORRIDOR - TOWER L6	5	21-Sep-23	27-Sep-23
T1-G-1570	PULL WIRE RESTRICTED CORRIDOR WALLS - TOWER L6	2	21-Sep-23	22-Sep-23
TPG4-1320	CEILING GRID & DEVICE TILES RESTRICTED CORRIDOR - TOWER	4	28-Sep-23	03-Oct-23
T1-G-1330	HVAC TRIM RESTRICTED CORRIDOR - TOWER L6	3	28-Sep-23	02-Oct-23
TFING1-8160	ELECTRICAL TRIM RESTRICTED CORRIDOR - TOWER L6	2	28-Sep-23	29-Sep-23
TFING1-8170	LOW VOLTAGE FINISHES RESTRICTED CORRIDOR - TOWER L6	2	04-Oct-23	05-Oct-23
TFING1-8180	FIRE SUPPRESSION HEADS RESTRICTED CORRIDOR - TOWER L6	2	04-Oct-23	05-Oct-23
T1-G-1600	INSTALL SEISMIC SUPPORTS RESTRICTED CORRIDOR - TOWER L	10	06-Oct-23	19-Oct-23
TPG4-1310	ABOVE CEILING INSPECTION RESTRICTED CORRIDOR WALLS - T	1	20-Oct-23	20-Oct-23
TPG4-1480	DROP BALANCE OF CEILING TILES RESTRICTED CORRIDOR - TOW	4	23-Oct-23	26-Oct-23
TPG4-1280	INSTALL INTERIOR GLAZING RESTRICTED CORRIDOR WALLS - TC	10	27-Oct-23	09-Nov-23
TPG5-1280	INSTALL FLOORING & BASE RESTRICTED CORRIDOR - TOWER L6	5	10-Nov-23	16-Nov-23
JURY DELIBERATION / JUDGES CHAMBERS / JUDGES RESTROOMS				
TJD4-1050	METAL PANELS & SOUND CAP TIE-IN TO EXTERIOR AT JUDICIAL S	3	31-Jan-23	02-Feb-23
TJD4-1060	FRAME JURY DELIBERATION/JUDGE'S CHAMBERS & JUDGE R/R -	7	08-Jun-23	16-Jun-23
TOHJ4-130	MECHANICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L6	7	19-Jun-23	27-Jun-23
TFINJ4-320	INSTALL DOOR FRAMES AT JUDICIAL SPACES - TOWER L6	3	19-Jun-23	21-Jun-23
TOHJ4-140	PLUMBING ROUGH-IN AT JUDICIAL SPACES - TOWER L6	5	25-Jul-23	31-Jul-23
TOHJ4-150	ELECTRICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L6	6	27-Jul-23	03-Aug-23
TOHJ4-170	LOW VOLTAGE ROUGH-IN AT JUDICIAL SPACES - TOWER L6	6	27-Jul-23	03-Aug-23
TOHJ1-240	INSULATE WALLS AT JUDICIAL SPACES - TOWER L6	1	04-Aug-23	04-Aug-23
TOHJ1-250	IN WALL INSPECTION AT JUDICIAL SPACES - TOWER L6	1	07-Aug-23	07-Aug-23
TJD4-1080	FINISHES AT JUDICIAL SPACES - TOWER L6	71	25-Aug-23	07-Dec-23
TFINJ4-260	DRYWALL WALLS AT JUDICIAL SPACES - TOWER L6	6	25-Aug-23	05-Sep-23
TFINJ4-360	TAPE & FINISH WALLS AT JUDICIAL SPACES - TOWER L6	7	21-Sep-23	29-Sep-23
TFINJ4-300	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT JUDICIAL SPA	3	02-Oct-23	04-Oct-23
TFINJ4-250	CEILING GRID & DEVICE TILES AT JUDICIAL SPACES - TOWER L6	6	05-Oct-23	12-Oct-23
TJD4-1090	MECHANICAL TRIM AT JUDICIAL SPACES - TOWER L6	5	13-Oct-23	19-Oct-23
TJD4-1140	ELECTRICAL TRIM AT JUDICIAL SPACES - TOWER L6	5	13-Oct-23	19-Oct-23
TJD4-1150	PLUMBING TRIM AT JUDICIAL SPACES - TOWER L6	5	13-Oct-23	19-Oct-23
TJD4-1160	FIRE SUPPRESSION TRIM AT JUDICIAL SPACES - TOWER L6	5	13-Oct-23	19-Oct-23

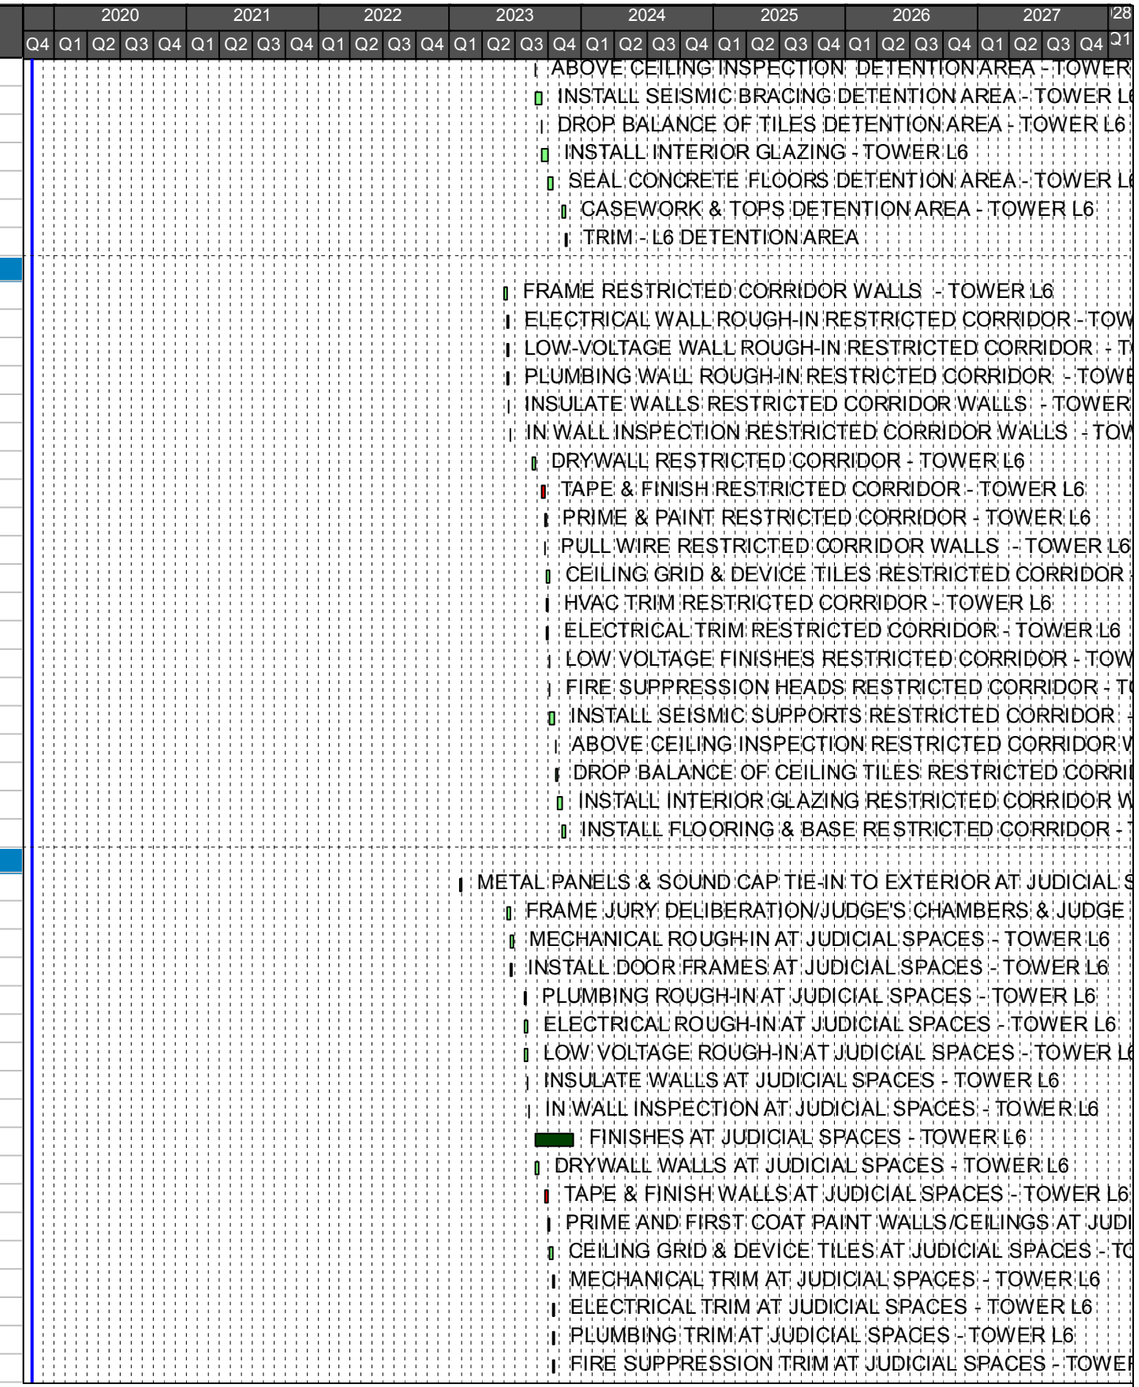

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TJD4-1170	LOW VOLTAGE TRIM AT JUDICIAL SPACES - TOWER L6	5	13-Oct-23	19-Oct-23
TJD4-1230	SEISMIC SUPPORTS JUDICIAL SPACES - TOWER L6	10	20-Oct-23	02-Nov-23
TJD4-1210	ABOVE CEILING INSPECTION AT JUDICIAL SPACES - TOWER L6	1	03-Nov-23	03-Nov-23
TFINJ4-270	DROP CEILING TILE AT JUDICIAL SPACES - TOWER L6	2	06-Nov-23	07-Nov-23
TJD1-1105	INSTALL CASEWORK AT JUDICIAL SPACES - TOWER L6	5	07-Nov-23	13-Nov-23
TJD4-1190	INSTALL INTERIOR GLAZING AT JUDICIAL SPACES - TOWER L	10	08-Nov-23	21-Nov-23
TFINJ4-310	FLOOR PREP AT JUDICIAL SPACES - TOWER L6	1	22-Nov-23	22-Nov-23
TFINJ4-280	INSTALL CARPET & BASE AT JUDICIAL SPACES - TOWER L6	4	27-Nov-23	30-Nov-23
TFINJ4-290	DOORS & HARDWARE AT JUDICIAL SPACES - TOWER L6	5	01-Dec-23	07-Dec-23
FULL FLOOR ORIGINAL				
TPG6-1000	FRAME ELEVATOR LOBBY AND H1/H2/J1/J2 VESTIBULES - TOWER	5	30-Oct-23	03-Nov-23
TPG6-1010	MEP ROUGH-IN ELEVATOR LOBBY AND J1/J2 VESTIBULES - TOWE	5	06-Nov-23	10-Nov-23
TPG6-1020	DRYWALL ELEVATOR LOBBY AND J1/J2 VESTIBULES - TOWER L6	3	13-Nov-23	15-Nov-23
TPG6-1050	TAPE & FINISH ELEVATOR LOBBY AND J1/J2 VESTIBULES - TOWE	7	14-Nov-23	22-Nov-23
TPG6-1030	PAINT ELEVATOR LOBBY AND J1/J2 VESTIBULES - TOWER L6	5	27-Nov-23	01-Dec-23
TPG6-1040	MEP TRIM ELEVATOR LOBBY AND J1/J2 VESTIBULES - TOWER L6	3	04-Dec-23	06-Dec-23
PUBLIC GALLERY				
TPG4-1360	F2 LIGHT FIXTURES CEILINGS/MEP DROPS PUBLIC GALLERY - TO	4	27-Jul-23	01-Aug-23
TPG4-1330	FINISHES RESTRICTED CORRIDOR PUBLIC GALLERY - TOWER L6	5	04-Oct-23	10-Oct-23
TPG4-1450	DOOR/HARDWARE PUBLIC GALLERY - TOWER L6	5	20-Nov-23	28-Nov-23
IN-WALL ROUGH-INS				
TFING1-7800	FRAME INTERIOR WALLS PUBLIC GALLERY - TOWER L6	5	19-Jun-23	23-Jun-23
TFING1-7700	IN WALL COUNTERTOP SUPPORTS PUBLIC GALLERY - TOWER L6	2	21-Jun-23	22-Jun-23
TFING1-7890	HM DOOR FRAMES PUBLIC GALLERY - TOWER L6	2	22-Jun-23	23-Jun-23
TRIG1-940	ROUGH-IN WALL PLUMBING PUBLIC GALLERY - TOWER L6	2	23-Jun-23	26-Jun-23
TFING1-7900	INSTALL ELEVATOR DOOR FRAMES & ELEVATOR FRONTS PUBLIC	8	26-Jun-23	06-Jul-23
TFING1-7940	INSTALL STORE FRONT FRAMES PUBLIC GALLERY - TOWER L6	2	26-Jun-23	27-Jun-23
TRIG1-930	ROUGH-IN WALL LOW VOLTAGE PUBLIC GALLERY - TOWER L6	8	27-Jun-23	07-Jul-23
TRIG1-950	ROUGH-IN WALL ELECTRICAL PUBLIC GALLERY - TOWER L6	2	27-Jun-23	28-Jun-23
TRIG1-920	ROUGH-IN MECHANICAL CONTROLS PUBLIC GALLERY - TOWER L6	2	29-Jun-23	30-Jun-23
TFING1-7810	WALL BACKING PUBLIC GALLERY - TOWER L6	1	05-Jul-23	05-Jul-23
TFING1-7660	IN-WALL INSPECTION PUBLIC GALLERY - TOWER L6	1	10-Jul-23	10-Jul-23
OVERHEAD ROUGH-INS				
TPG4-1350	FRAME GYP CEILING PUBLIC GALLERY - TOWER L6	7	18-Jul-23	26-Jul-23
TRIG1-970	ROUGH-IN MECHANICAL AT HARDLIDS PUBLIC GALLERY - TOWER	2	27-Jul-23	28-Jul-23
TRIG1-960	ROUGH-IN ELECTRICAL AT HARDLIDS PUBLIC GALLERY - TOWER L	2	31-Jul-23	01-Aug-23
TFING1-7830	ABOVE CEILING INSPECTION AT HARDLIDS PUBLIC GALLERY - TO	1	02-Aug-23	02-Aug-23
FINISHES				
TFING1-7680	INSULATE WALLS PUBLIC GALLERY - TOWER L6	4	11-Jul-23	14-Jul-23
TFING1-7710	DRYWALL WALLS PUBLIC GALLERY - TOWER L6	4	13-Sep-23	18-Sep-23
TPG4-1370	DRYWALL CEILINGS PUBLIC GALLERY - TOWER L6	3	19-Sep-23	21-Sep-23
TFING1-7620	MEASURE & FAB INTERIOR GLAZING FRAMES PUBLIC GALLERY -	1	19-Sep-23	19-Sep-23
TFING1-7630	FURNISH MATERIAL FOR INTERIOR GLAZING FRAMES PUBLIC GAL	10	20-Sep-23	03-Oct-23
TFING1-7720	TAPE & FINISH PUBLIC GALLERY - TOWER L6	6	10-Oct-23	17-Oct-23
TFING1-7690	PRIME & PAINT 1ST COAT PUBLIC GALLERY - TOWER L6	3	20-Oct-23	24-Oct-23
TPG4-1390	CEILING GRID / DEVICE TILES PUBLIC GALLERY - TOWER L6	4	25-Oct-23	30-Oct-23
TPG2-2100	INSTALL LIGHT FIXTURES AT HARDLIDS PUBLIC GALLERY - TOWE	4	25-Oct-23	30-Oct-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development

PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19

Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TFING1-7670	ELECTRICAL COVER PLATES PUBLIC GALLERY - TOWER L6	3	25-Oct-23	27-Oct-23
TFING1-7950	INSTALL STORE FRONT GLAZING PUBLIC GALLERY - TOWER L6	5	25-Oct-23	31-Oct-23
TFING1-8000	FIRE SUPPRESSION HEADS AT HARDLIDS PUBLIC GALLERY - TOV	4	25-Oct-23	30-Oct-23
TFING1-8030	INSTALL HVAC CONTROLS PUBLIC GALLERY - TOWER L6	5	25-Oct-23	31-Oct-23
TPG4-1500	FIRE ALARM DEVICES PUBLIC GALLERY - TOWER L6	2	31-Oct-23	01-Nov-23
TPG2-2120	MECHANICAL DIFFUSERS & REGISTERS PUBLIC GALLERY - TOWE	3	31-Oct-23	02-Nov-23
TPG2-2130	INSTALL DEVICE TILES PUBLIC GALLERY - TOWER L6	3	31-Oct-23	02-Nov-23
TFING1-7850	CASEWORK PUBLIC GALLERY - TOWER L6	10	31-Oct-23	13-Nov-23
TOHG1-1520	LIGHT FIXTURES IN T-BAR CEILING PUBLIC GALLERY - TOWER L6	2	31-Oct-23	01-Nov-23
TFING1-7860	FIRE SUPPRESSION HEADS AT GRID PUBLIC GALLERY - TOWER L6	2	31-Oct-23	01-Nov-23
TFING1-7870	MECHANICAL DIFFUSERS & REGISTERS AT GRID PUBLIC GALLER	2	31-Oct-23	01-Nov-23
TFING1-7730	INSTALL SEISMIC SUPPORTS PUBLIC GALLERY - TOWER L6	10	02-Nov-23	15-Nov-23
TFING1-7930	FLOOR PREP AT LOBBY & PUBLIC GALLERY - TOWER L6	4	03-Nov-23	08-Nov-23
TPG4-1420	INSTALL FLOOR TILE IN PUBLIC GALLERY - TOWER L6	7	09-Nov-23	17-Nov-23
TFING1-7820	INSTALL EDGE GUARDS PUBLIC GALLERY - TOWER L6	2	14-Nov-23	15-Nov-23
TFING1-7880	ABOVE CEILING INSPECTION AT T-BAR PUBLIC GALLERY - TOWEF	1	16-Nov-23	16-Nov-23
TPG4-1490	DROP CEILING TILE PUBLIC GALLERY - TOWER L6	4	17-Nov-23	22-Nov-23
TPG4-1460	DOORS & HARDWARE PUBLIC GALLERY - TOWER L6	2	20-Nov-23	21-Nov-23
TFING1-7920	INSTALL FLOOR BASE AT TILE WALLS PUBLIC GALLERY - TOWER	5	20-Nov-23	28-Nov-23
TFING1-7750	INSTALL GLAZING PUBLIC GALLERY - TOWER L6	8	27-Nov-23	06-Dec-23
TFING1-7840	FIRE EXTINGUISHERS CABINETS PUBLIC GALLERY - TOWER L6	2	27-Nov-23	28-Nov-23
TPG4-1400	INSTALL WALL TILE PUBLIC GALLERY - TOWER L6	5	29-Nov-23	05-Dec-23
TFING1-7910	INSTALL METAL WALL PANELS/ TRIM PUBLIC GALLERY - TOWER L6	3	29-Nov-23	01-Dec-23
TPG4-1430	BENCHES FF&E PUBLIC GALLERY - TOWER L6	2	04-Dec-23	05-Dec-23
TPG4-1410	PLUMBING FIXTURES PUBLIC GALLERY - TOWER L6	2	06-Dec-23	07-Dec-23
TFING1-7610	OFOI VISUAL DISPLAY SURFACES PUBLIC GALLERY - TOWER L6	2	12-Mar-24	13-Mar-24
TFING1-7990	INSTALL LOW VOLTAGE PUBLIC GALLERY - TOWER L6	4	12-Mar-24	15-Mar-24
PUBLIC / STAFF RESTROOMS				
TRR4-1040	FRAME PUBLIC / STAFF RR - TOWER L6	4	20-Jun-23	23-Jun-23
TRIR4-130	ROUGH-IN WALL PLUMBING PUBLIC / STAFF RR - TOWER L6	5	26-Jun-23	30-Jun-23
TFINR4-550	FIELD MEASURE FOR TOILET PARTITIONS PUBLIC / STAFF RR - TC	1	26-Jun-23	26-Jun-23
TFINR4-560	FABRICATE TOILET PARTITIONS PUBLIC / STAFF RR - TOWER L6	30	27-Jun-23	08-Aug-23
TRIR4-140	ROUGH-IN WALL ELECTRICAL PUBLIC / STAFF RR - TOWER L6	5	28-Jun-23	05-Jul-23
TRIR4-150	ROUGH-IN MECHANICAL AT HARDLIDS PUBLIC / STAFF RR - TOWE	5	06-Jul-23	12-Jul-23
TFINR4-450	WALL BACKING PUBLIC / STAFF RR - TOWER L6	2	06-Jul-23	07-Jul-23
TRR4-1060	FINISHES PUBLIC / STAFF RR - TOWER L6	12	10-Jul-23	25-Jul-23
TFINR4-350	INSULATE WALLS PUBLIC / STAFF RR - TOWER L6	1	10-Jul-23	10-Jul-23
TFINR4-370	SHEETDRYWALL WALLS PUBLIC / STAFF RR - TOWER L6	2	15-Sep-23	18-Sep-23
TFINR4-470	FRAME HARDLID CEILINGS & SOFFITS PUBLIC / STAFF RR - TOWE	4	19-Sep-23	22-Sep-23
TFINR1-420	OVERHEAD MEP CEILING DROPS PUBLIC / STAFF RR - TOWER L6	4	25-Sep-23	28-Sep-23
TFINR4-480	SHEETDRYWALL HARDLIDS & SOFFITS PUBLIC / STAFF RR - TOW	3	29-Sep-23	03-Oct-23
TFINR4-380	TAPE & FINISH PUBLIC / STAFF RR - TOWER L6	7	09-Oct-23	17-Oct-23
TFINR4-360	PRIME & PAINT 1ST COAT PUBLIC / STAFF RR - TOWER L6	3	19-Oct-23	23-Oct-23
TFINR4-520	FLOOR PREP AT PUBLIC / STAFF RR - TOWER L6	2	24-Oct-23	25-Oct-23
TFINR4-540	PULL & TERMINATE ELECTRICAL/ LOW VOLTAGE WIRE PUBLIC / S	2	24-Oct-23	25-Oct-23
TFINR4-420	ELECTRICAL/FIRE ALARM FINISH/DEVICES PUBLIC / STAFF RR - T	4	26-Oct-23	31-Oct-23
TFINR4-530	INSTALL FLOOR & WALL TILE IN PUBLIC / STAFF RR - TOWER L6	9	26-Oct-23	07-Nov-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

Activity ID	Activity Name	Original Duration	Start	Finish
TRR4-1070	MEP TRIM PUBLIC / STAFF PUBLIC / STAFF RR - TOWER L6	7	01-Nov-23	09-Nov-23
TFINR4-500	MECHANICAL DIFFUSERS & REGISTERS PUBLIC / STAFF RR - TOW	2	08-Nov-23	09-Nov-23
TFINR4-460	CASEWORK & TOPS PUBLIC / STAFF RR - TOWER L6	3	09-Nov-23	13-Nov-23
TFINR4-490	FIRE SUPPRESSION HEADS PUBLIC / STAFF RR - TOWER L6	1	14-Nov-23	14-Nov-23
TFINR4-510	PLUMBING FIXTURES PUBLIC / STAFF RR - TOWER L6	4	14-Nov-23	17-Nov-23
TFINR4-400	DOORS & HARDWARE PUBLIC / STAFF RR - TOWER L6	7	20-Nov-23	30-Nov-23
TFINR4-410	INSTALL PARTITIONS AND ACCESSORIES PUBLIC / STAFF RR - TO	7	27-Nov-23	05-Dec-23
MANLIFT BAY				
ML4-1040	FRAME MANLIFT BAY - TOWER L6	3	25-Jul-23	27-Jul-23
ML4-1050	ROUGH-IN MEP MANLIFT BAY - TOWER L6	5	28-Jul-23	03-Aug-23
ML4-1060	FINISHES MANLIFT BAY - TOWER L6	15	04-Aug-23	24-Aug-23
ML4-1070	TRIM MANLIFT BAY - TOWER L6	5	25-Aug-23	31-Aug-23
LEVEL 7				
LEVEL 7 FULL FLOOR				
MS7-1030	FIREPROOF BALANCE OF FLOORS	5	13-Jan-23	20-Jan-23
MS7-1000	PRE-WELD EXTERIOR & PARTITION CLIPS	7	20-Jan-23	30-Jan-23
MS7-1020	FIREPROOF PRIORITY WALLS/PERIMETER - TOWER L7	5	31-Jan-23	06-Feb-23
MS7-1010	EDGE OF SLAB FIRE SAFE	5	29-Mar-23	04-Apr-23
TPG7-1000	ONE SIDE TIE INTO EXTERIOR - TOWER L7	5	05-Apr-23	11-Apr-23
TFING1-7040	FIELD MEASURE FOR WINDOW COVERINGS - TOWER L7	1	25-Oct-23	25-Oct-23
TFING1-7050	FABRICATE WINDOW COVERINGS - TOWER L7	10	07-Mar-24	20-Mar-24
TPG7-1150	FINAL PAINT - TOWER L7	7	12-Mar-24	20-Mar-24
TFING1-6590	WINDOW COVERINGS PUBLIC GALLERY - TOWER L7	4	21-Mar-24	26-Mar-24
TFING1-6760	INSTALL SIGNAGE - TOWER L7	5	21-Mar-24	27-Mar-24
TFING1-6770	INT. CERTIFICATION & READY FOR PUNCH - TOWER L7	1	28-Mar-24	28-Mar-24
OVERHEAD ROUGH-INS				
TFING1-6580	LAYOUT FOR CLIPS AND TRACK - TOWER L7	3	10-Jan-23	12-Jan-23
TFING1-6570	INSTALL TOP TRACK - TOWER L7	2	11-Jan-23	12-Jan-23
TFING1-7010	INSTALL FIRE SUPPRESSION HANGERS - TOWER L7	4	06-Feb-23	09-Feb-23
TFING1-7000	INSTALL ELECTRICAL HANGERS - TOWER L7	4	10-Feb-23	15-Feb-23
TFING1-8320	INSTALL LOW VOLTAGE HANGERS - TOWER L7	4	10-Feb-23	15-Feb-23
TFING1-6640	INSTALL PLUMBING HANGERS - TOWER L7	5	27-Feb-23	03-Mar-23
TFING1-6990	INSTALL MECHANICAL HANGERS - TOWER L7	5	27-Feb-23	03-Mar-23
TFING1-6780	FIRE SUPPRESSION MAINS - TOWER L7	5	06-Mar-23	10-Mar-23
TOHG1-1280	O/H WASTE & VENT - TOWER L7	7	09-Mar-23	17-Mar-23
TOHG1-1230	O/H ELECTRICAL MAINS - TOWER L7	5	23-Mar-23	29-Mar-23
TOHG1-1650	O/H LOW VOLTAGE MAINS - TOWER L7	8	23-Mar-23	03-Apr-23
TOHG1-1240	O/H PLUMBING MAINS - TOWER L7	6	10-May-23	17-May-23
TOHG1-1750	O/H PLUMBING BRANCHES - TOWER L7	7	18-May-23	30-May-23
TOHG1-1270	O/H MECHANICAL MAINS - TOWER L7	10	31-May-23	13-Jun-23
TFING1-6790	HANG VAV'S - TOWER L7	8	02-Jun-23	13-Jun-23
TOHG1-1300	O/H HYDRONIC PIPING - TOWER L7	5	13-Jun-23	19-Jun-23
TFING1-6650	FIRE SUPPRESSION BRANCHES - TOWER L7	10	21-Jun-23	05-Jul-23
TOHG1-1310	O/H ELECTRICAL BRANCHES - TOWER L7	3	28-Jun-23	30-Jun-23
TOHG1-1660	O/H LOW VOLTAGE BRANCHES - TOWER L7	3	28-Jun-23	30-Jun-23
TFING1-6600	O/H HVAC CONTROLS - TOWER L7	2	03-Jul-23	05-Jul-23
TOHG1-1250	O/H LOW VOLTAGE - TOWER L7	2	03-Jul-23	05-Jul-23

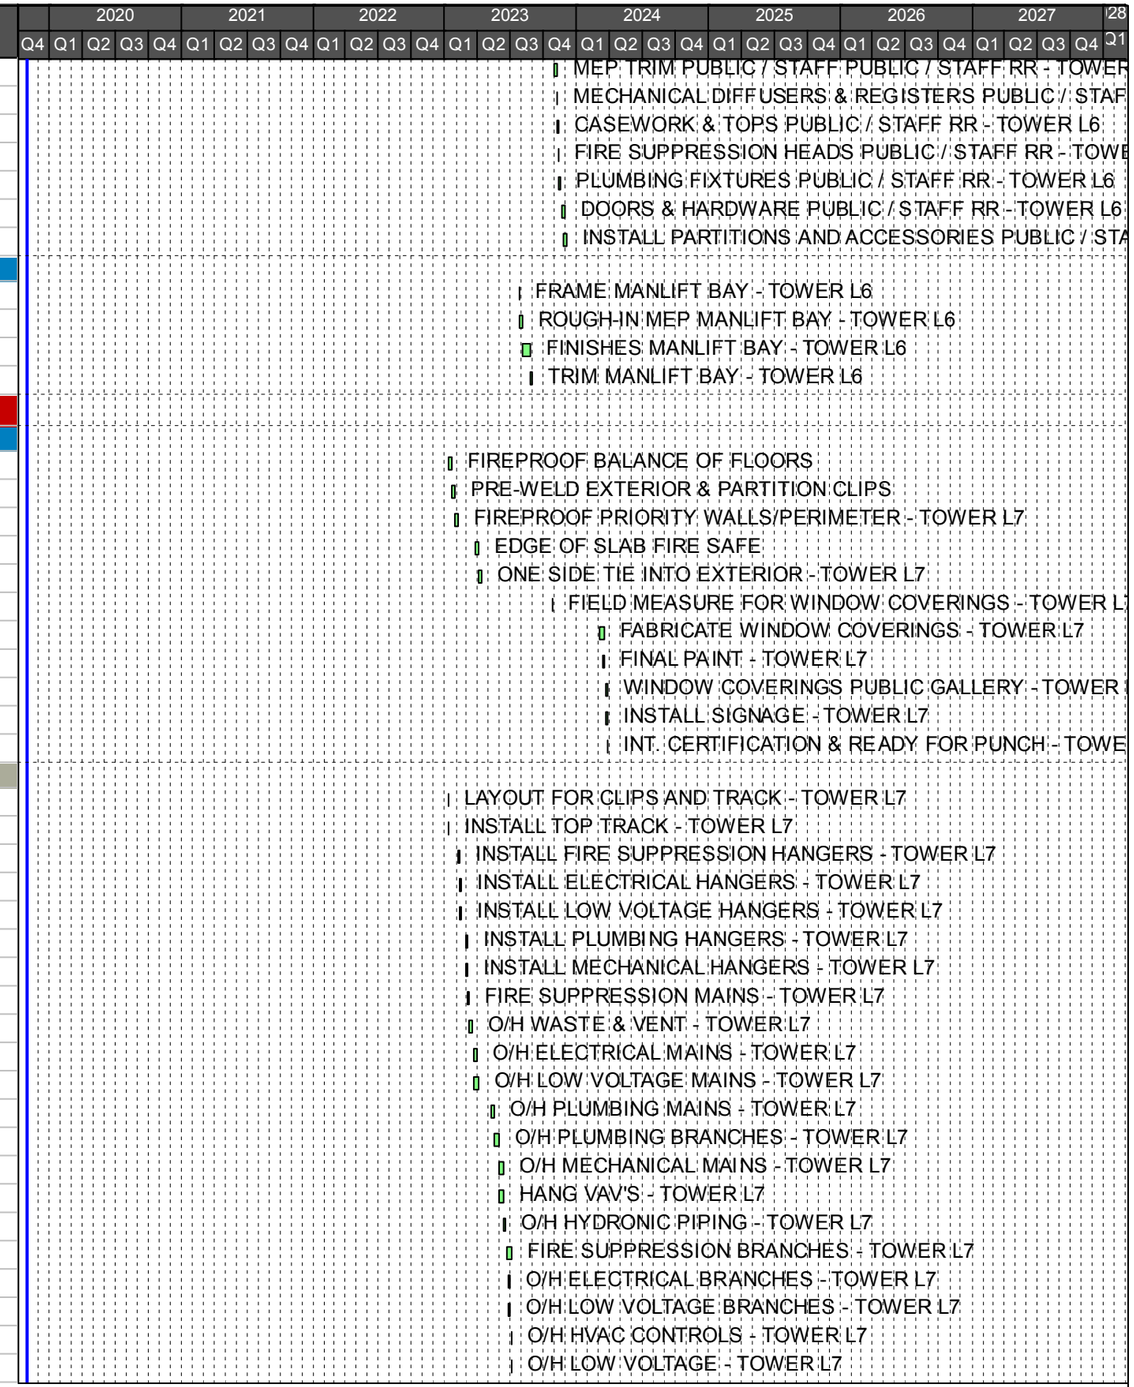

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TOHG1-1290	O/H MECHANICAL BRANCHES - TOWER L7	15	12-Jul-23	01-Aug-23
TPG2-1890	ONE SIDE TIE INTO EXTERIOR - TOWER L7	2	21-Jul-23	24-Jul-23
TOHG1-1260	O/H SECURITY - TOWER L7	2	02-Aug-23	03-Aug-23
PRIORITY WALLS (IDF/ ELEC/ SHAFT/ STAIRS)				
IDF/ ELECTRICAL ROOM/ CENTRAL CONTROL				
TPR7-1050	FRAME IDF ROOM, ELECTRICAL ROOM, STAIRS - TOWER L7	5	03-Apr-23	07-Apr-23
TPR7-1060	ROUGH-IN IDF / ELECTRICAL ROOMS - TOWER L7	5	10-Apr-23	14-Apr-23
TELECRI7-100	ROUGH-IN PLUMBING IDF / ELECTRICAL ROOMS - TOWER L7	2	10-Apr-23	11-Apr-23
TELECRI7-110	ROUGH-IN ELECTRICAL IDF / ELECTRICAL ROOMS - TOWER L7	4	11-Apr-23	14-Apr-23
TELECRI7-120	ROUGH-IN MECHANICAL IDF / ELECTRICAL ROOMS - TOWER L7	3	12-Apr-23	14-Apr-23
TPR7-1070	DRYWALL IDF/ ELECTRICAL ROOMS - TOWER L7	3	03-Jul-23	06-Jul-23
TPR7-1170	TAPE & FINISH IDF/ELECTRICAL ROOMS - TOWER L7	5	16-Aug-23	22-Aug-23
TELEC7-130	PAINT IDF/ELECTRICAL ROOMS - TOWER L7	3	23-Aug-23	25-Aug-23
TELEC7-140	SEAL FLOORS IDF/ELECTRICAL ROOMS - TOWER L7	2	28-Aug-23	29-Aug-23
TPR7-1120	DOORS & HARDWARE - TOWER L7	2	30-Aug-23	31-Aug-23
TPR7-1100	ELECTRICAL AND IDF, PANELS AND RACKS - TOWER L7	15	13-Sep-23	03-Oct-23
MEP SHAFTS				
TPR7-1040	INSTALL MEPF IN SHAFTS - TOWER L7	8	24-Feb-23	07-Mar-23
TPR7-1020	FRAME HVAC SHAFTS & DRYWALL C/R SIDE - TOWER L7	3	03-Apr-23	05-Apr-23
TPR7-1110	DRYWALL HVAC SHAFTS - TOWER L7	3	23-Aug-23	25-Aug-23
TPR7-1180	TAPE & FINISH HVAC SHAFTS - TOWER L7	7	31-Oct-23	08-Nov-23
ELEVATOR/ STAIR SHAFTS				
TPR7-1000	FRAME PASSENGER ELEVATOR HOISTWAYS - TOWER L7	3	06-Apr-23	10-Apr-23
TDR7-1010	FRAME AT H1/H2 DETENTION AREA - TOWER L7	4	06-Apr-23	11-Apr-23
TPR7-1010	FRAME J1/J2 ELEVATOR WALLS - TOWER L7	3	11-Apr-23	13-Apr-23
TPR1-2350	DRYWALL PASSENGER ELEVATOR - TOWER L7	2	11-Apr-23	12-Apr-23
TPR1-2360	DRYWALL J1/J2 ELEVATOR WALLS - TOWER L7	2	13-Apr-23	14-Apr-23
TPR1-2370	TAPE & FINISH PASSENGER ELEVATOR - TOWER L7	6	13-Apr-23	20-Apr-23
TPR1-2380	TAPE & FINISH J1/J2 ELEVATOR WALLS - TOWER L7	6	21-Apr-23	28-Apr-23
TPR7-1080	DRYWALL STAIR 1-2 - TOWER L7	2	28-Aug-23	29-Aug-23
TPR7-1090	DRYWALL STAIR 3-4 - TOWER L7	2	30-Aug-23	31-Aug-23
TPR7-1130	TAPE & FINISH STAIR 1-2 - TOWER L7	6	16-Nov-23	27-Nov-23
TPR7-1150	TAPE & FINISH STAIR 3-4 - TOWER L7	6	28-Nov-23	05-Dec-23
TPR7-1140	FINISHES STAIR 1-2 - TOWER L7	4	28-Nov-23	01-Dec-23
TELEC7-150	PRIME AND FIRST COAT PAINT STAIR 1-2 - TOWER L7	5	28-Nov-23	04-Dec-23
TPR7-1160	FINISHES STAIR 3-4 - TOWER L7	4	06-Dec-23	11-Dec-23
TELEC7-170	PRIME AND FIRST COAT PAINT STAIR 3-4 - TOWER L7	5	06-Dec-23	12-Dec-23
DETENTION AREA				
TFIND2-830	FRAME PARTITION WALLS DETENTION AREA - TOWER L7	2	14-Apr-23	17-Apr-23
TRID2-200	ROUGH-IN IN-WALL PLUMBING DETENTION AREA - TOWER L7	2	18-Apr-23	19-Apr-23
TRID2-210	ROUGH-IN - IN WALL ELECTRICAL DETENTION AREA - TOWER L7	2	19-Apr-23	20-Apr-23
TOHD2-180	ROUGH-IN OVERHEAD MECHANICAL DETENTION AREA - TOWER L7	5	05-May-23	11-May-23
TFIND2-930	INSTALL GRILLS & DIFFUSERS IN CEILING DETENTION AREA - TOV	3	12-May-23	16-May-23
TOHD2-190	ROUGH-IN OVERHEAD PLUMBING DETENTION AREA - TOWER L7	2	25-Jul-23	26-Jul-23
TOHD2-290	ROUGH-IN OVERHEAD FIRE SUPPRESSION DETENTION AREA - TC	2	25-Jul-23	26-Jul-23
TOHD3-140	ROUGH-IN OVERHEAD ELECTRICAL DETENTION AREA - TOWER L7	3	26-Jul-23	28-Jul-23
TOHD3-200	ROUGH-IN OVERHEAD LOW VOLTAGE DETENTION AREA - TOWER	3	26-Jul-23	28-Jul-23

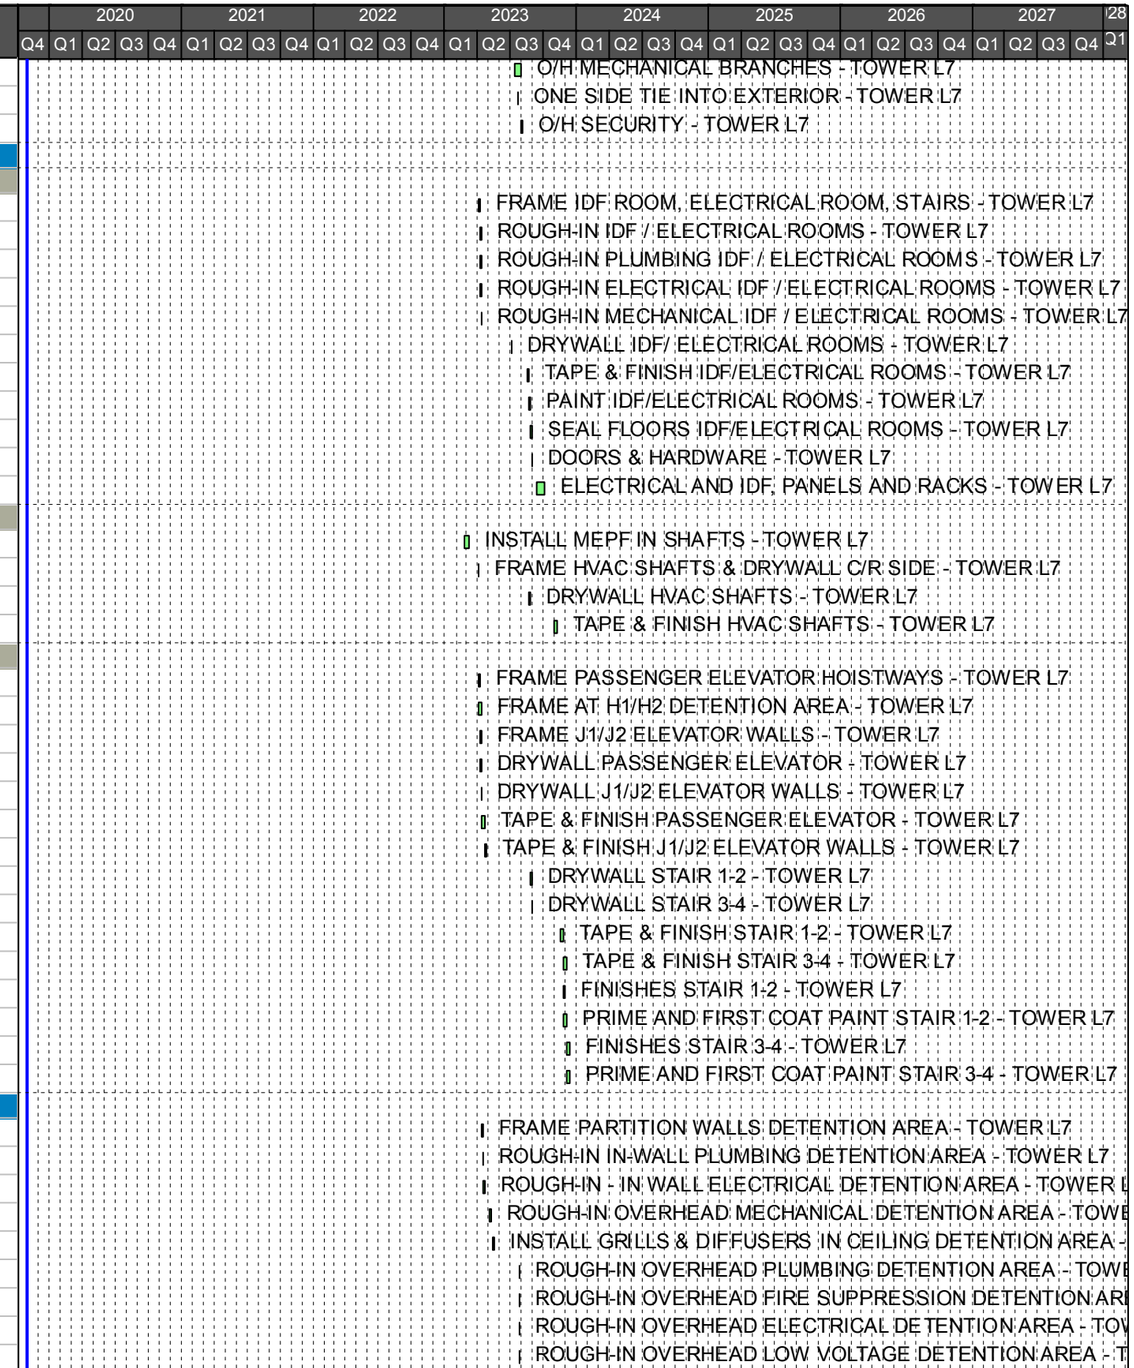

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TDR7-1000	DETENTION METAL CEILINGS DETENTION AREA - TOWER L7	5	31-Jul-23	04-Aug-23
TFIND2-940	INSTALL LIGHTING & TRIM DETENTION AREA - TOWER L7	2	31-Jul-23	01-Aug-23
TFIND2-1450	INSULATE WALLS - TOWER L6	1	31-Jul-23	31-Jul-23
TFIND2-1460	IN-WALL INSPECTION TOWER L6	1	01-Aug-23	01-Aug-23
TFIND2-840	DRYWALL PARTITION WALLS DETENTION AREA - TOWER L7	3	02-Aug-23	04-Aug-23
TFIND2-850	TAPE/ FINISH PARTITION WALLS DETENTION AREA - TOWER L7	7	03-Aug-23	11-Aug-23
TFIND2-860	PAINT DETENTION AREA - TOWER L7	5	14-Aug-23	18-Aug-23
TFIND2-880	DOORS AND HARDWARE DETENTION AREA - TOWER L7	4	21-Aug-23	24-Aug-23
TFIND2-890	DETENTION FIXTURES DETENTION AREA - TOWER L7	10	21-Aug-23	05-Sep-23
TFIND2-900	INSTALL PLUMBING COMBI UNIT'S DETENTION AREA - TOWER L7	5	21-Aug-23	25-Aug-23
TDR1-1240	CEILING GRID AND DEVICE TILES DETENTION AREA - TOWER L7	6	21-Aug-23	28-Aug-23
TFIND2-910	PLUMBING FIXTURES DETENTION AREA - TOWER L7	5	28-Aug-23	05-Sep-23
TDR1-1250	COMPLETE MECHANICAL IN CEILING DETENTION AREA - TOWER I	5	29-Aug-23	06-Sep-23
TFIND1-500	COMPLETE OVERHEAD FIRE SUPPRESSION IN CEILING - L7	2	29-Aug-23	30-Aug-23
TFIND1-510	COMPLETE ELECTRICAL IN CEILING DETENTION AREA - TOWER L7	5	29-Aug-23	06-Sep-23
TFIND1-520	COMPLETE PLUMBING IN CEILING DETENTION AREA - TOWER L7	5	29-Aug-23	06-Sep-23
TFIND1-530	COMPLETE LOW VOLTAGE IN CEILING DETENTION AREA - TOWEF	5	29-Aug-23	06-Sep-23
TFIND2-920	INSTALL INTERIOR GLAZING - TOWER L7	10	07-Sep-23	20-Sep-23
TDR1-1290	ABOVE CEILING INSPECTION DETENTION AREA - TOWER L7	1	07-Sep-23	07-Sep-23
TDR1-1330	INSTALL SEISMIC BRACING DETENTION AREA - TOWER L7	10	07-Sep-23	20-Sep-23
TFIND2-870	DROP BALANCE OF TILES DETENTION AREA - TOWER L7	3	21-Sep-23	25-Sep-23
TFIND2-980	SEAL CONCRETE FLOORS DETENTION AREA - TOWER L7	10	26-Sep-23	09-Oct-23
TFIND2-990	CASEWORK & TOPS DETENTION AREA - TOWER L7	7	17-Nov-23	29-Nov-23
TDR7-1040	TRIM DETENTION AREA - TOWER L7	3	30-Nov-23	04-Dec-23
RESTRICTED CORRIDOR				
TPG7-1010	FRAME RESTRICTED CORRIDOR WALLS - TOWER L7	5	22-Jun-23	28-Jun-23
T1-G-1220	ELECTRICAL WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L	5	29-Jun-23	06-Jul-23
TRIG1-1080	LOW-VOLTAGE WALL ROUGH-IN RESTRICTED CORRIDOR - TOWEI	5	29-Jun-23	06-Jul-23
TRIG1-1090	PLUMBING WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L7	5	29-Jun-23	06-Jul-23
T1-G-1480	INSULATE WALLS RESTRICTED CORRIDOR WALLS - TOWER L7	1	07-Jul-23	07-Jul-23
T1-G-1490	IN WALL INSPECTION RESTRICTED CORRIDOR WALLS - TOWER L7	1	10-Jul-23	10-Jul-23
TPG7-1070	DRYWALL RESTRICTED CORRIDOR - TOWER L7	5	22-Sep-23	28-Sep-23
TPG7-1260	TAPE & FINISH RESTRICTED CORRIDOR - TOWER L7	5	18-Oct-23	24-Oct-23
T1-G-1340	PRIME & PAINT RESTRICTED CORRIDOR - TOWER L7	5	25-Oct-23	31-Oct-23
T1-G-1580	PULL WIRE RESTRICTED CORRIDOR WALLS - TOWER L7	2	25-Oct-23	26-Oct-23
TPG7-1110	CEILING GRID & DEVICE TILES RESTRICTED CORRIDOR - TOWER	4	01-Nov-23	06-Nov-23
T1-G-1350	HVAC TRIM RESTRICTED CORRIDOR - TOWER L7	3	01-Nov-23	03-Nov-23
TFING1-8190	ELECTRICAL TRIM RESTRICTED CORRIDOR - TOWER L7	2	01-Nov-23	02-Nov-23
TFING1-8200	LOW VOLTAGE FINISHES RESTRICTED CORRIDOR - TOWER L7	2	07-Nov-23	08-Nov-23
TFING1-8210	FIRE SUPPRESSION HEADS RESTRICTED CORRIDOR - TOWER L7	2	07-Nov-23	08-Nov-23
T1-G-1610	INSTALL SEISMIC SUPPORTS RESTRICTED CORRIDOR - TOWER I	10	09-Nov-23	22-Nov-23
TPG7-1030	ABOVE CEILING INSPECTION RESTRICTED CORRIDOR WALLS - T	1	27-Nov-23	27-Nov-23
TPG7-1170	DROP BALANCE OF CEILING TILES RESTRICTED CORRIDOR - TOW	4	28-Nov-23	01-Dec-23
TPG7-1020	INSTALL INTERIOR GLAZING RESTRICTED CORRIDOR WALLS - TC	10	04-Dec-23	15-Dec-23
TPG7-1130	INSTALL FLOORING & BASE RESTRICTED CORRIDOR - TOWER L7	5	18-Dec-23	22-Dec-23
JURY DELIBERATION / JUDGES CHAMBERS / JUDGES RESTROOMS				
TJD7-1000	METAL PANELS & SOUND CAP TIE-IN TO EXTERIOR AT JUDICIAL S	3	12-Apr-23	14-Apr-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TJD7-1010	FRAME JURY DELIB/JUDGE'S CHAMBERS & JUDGE R/R - TOWER L7	6	26-Jun-23	03-Jul-23
TJD7-1020	ROUGH-IN MEP AT JUDICIAL SPACES - TOWER L7	10	05-Jul-23	18-Jul-23
TOHJ7-100	MECHANICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L7	7	05-Jul-23	13-Jul-23
TFINJ7-110	INSTALL DOOR FRAMES AT JUDICIAL SPACES - TOWER L7	3	05-Jul-23	07-Jul-23
TOHJ7-110	PLUMBING ROUGH-IN AT JUDICIAL SPACES - TOWER L7	5	27-Jul-23	02-Aug-23
TOHJ7-120	ELECTRICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L7	6	31-Jul-23	07-Aug-23
TOHJ7-130	LOW VOLTAGE ROUGH-IN AT JUDICIAL SPACES - TOWER L7	6	31-Jul-23	07-Aug-23
TOHJ1-260	INSULATE WALLS AT JUDICIAL SPACES - TOWER L7	1	08-Aug-23	08-Aug-23
TOHJ1-270	IN WALL INSPECTION AT JUDICIAL SPACES - TOWER L7	1	09-Aug-23	09-Aug-23
TFINJ7-150	DRYWALL WALLS AT JUDICIAL SPACES - TOWER L7	6	29-Sep-23	06-Oct-23
TJD7-1030	FINISHES AT JUDICIAL SPACES - TOWER L7	68	09-Oct-23	17-Jan-24
TFINJ7-240	TAPE & FINISH WALLS AT JUDICIAL SPACES - TOWER L7	7	25-Oct-23	02-Nov-23
TFINJ7-170	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT JUDICIAL SPA	3	03-Nov-23	07-Nov-23
TFINJ7-180	CEILING GRID & DEVICE TILES AT JUDICIAL SPACES - TOWER L7	6	08-Nov-23	15-Nov-23
TJD7-1040	MECHANICAL TRIM AT JUDICIAL SPACES - TOWER L7	5	16-Nov-23	22-Nov-23
TJD7-1050	ELECTRICAL TRIM AT JUDICIAL SPACES - TOWER L7	5	16-Nov-23	22-Nov-23
TJD7-1060	PLUMBING TRIM AT JUDICIAL SPACES - TOWER L7	5	16-Nov-23	22-Nov-23
TJD7-1070	FIRE SUPPRESSION TRIM AT JUDICIAL SPACES - TOWER L7	5	16-Nov-23	22-Nov-23
TJD7-1080	LOW VOLTAGE TRIM AT JUDICIAL SPACES - TOWER L7	5	16-Nov-23	22-Nov-23
TJD7-1110	SEISMIC SUPPORTS JUDICIAL SPACES - TOWER L7	10	27-Nov-23	08-Dec-23
TJD7-1100	ABOVE CEILING INSPECTION AT JUDICIAL SPACES - TOWER L7	1	11-Dec-23	11-Dec-23
TFINJ7-210	DROP CEILING TILE AT JUDICIAL SPACES - TOWER L7	2	12-Dec-23	13-Dec-23
TJD7-1090	INSTALL INTERIOR GLAZING AT JUDICIAL SPACES - TOWER L7	10	14-Dec-23	28-Dec-23
TJD1-1110	INSTALL CASEWORK AT JUDICIAL SPACES - TOWER L7	5	03-Jan-24	09-Jan-24
TFINJ7-190	FLOOR PREP AT JUDICIAL SPACES - TOWER L7	1	10-Jan-24	10-Jan-24
TFINJ7-200	INSTALL CARPET & BASE AT JUDICIAL SPACES - TOWER L7	4	11-Jan-24	17-Jan-24
TFINJ7-220	DOORS & HARDWARE AT JUDICIAL SPACES - TOWER L7	5	18-Jan-24	24-Jan-24
COURTROOMS				
TCR7-1000	FRAME PERIMETER WALLS AT COURTROOMS - TOWER L7	10	22-Jun-23	06-Jul-23
TCR7-1020	FLOOR LEVEL AT COURTROOMS - TOWER L7	8	07-Jul-23	18-Jul-23
TRIC2-220	MECHANICAL ROUGH-IN DROPS AT COURTROOMS - TOWER L7	8	19-Jul-23	28-Jul-23
TRIC2-230	PLUMBING ROUGH-IN DROPS AT COURTROOMS - TOWER L7	6	03-Aug-23	10-Aug-23
TRIC2-370	FIRE SUPPRESSION ROUGH-IN DROPS AT COURTROOMS - TOWEI	6	03-Aug-23	10-Aug-23
TRIC2-240	ELECTRICAL ROUGH-IN DROPS AT COURTROOMS - TOWER L7	8	08-Aug-23	17-Aug-23
TRIC2-380	LOW VOLTAGE ROUGH-IN DROPS AT COURTROOMS - TOWER L7	8	08-Aug-23	17-Aug-23
TCR7-1140	INSTALL WALL BACKING - TOWER L7	2	18-Aug-23	21-Aug-23
TCR7-1050	FRAME CEILINGS AT COURTROOMS - TOWER L7	8	22-Aug-23	31-Aug-23
TCR1-1530	INSULATE WALLS AT COURTROOMS - TOWER L7	3	22-Aug-23	24-Aug-23
TCR1-1540	IN WALL INSPECTION AT COURTROOMS - TOWER L7	1	25-Aug-23	25-Aug-23
TCR7-1060	CEILING FIXTURES PRE-DRYWALL AT COURTROOMS - TOWER L7	5	05-Sep-23	11-Sep-23
TCR7-1090	FRAME LOW WALLS AT COURTROOMS - TOWER L7	6	05-Sep-23	12-Sep-23
TCR7-1130	ACCESS FLOORING LAYOUT AT COURTROOMS - TOWER L7	3	13-Sep-23	15-Sep-23
TFINC7-100	INSTALL DOOR FRAMES AT COURTROOMS - TOWER L7	3	13-Sep-23	15-Sep-23
TCR7-1030	DRYWALL WALLS AT COURTROOMS - TOWER L7	5	09-Oct-23	13-Oct-23
TCR7-1070	DRYWALL GYP CEILINGS AT COURTROOMS - TOWER L7	6	16-Oct-23	23-Oct-23
TCR7-1240	TAPE & FINISH GYP CEILINGS AT COURTROOMS - TOWER L7	7	24-Oct-23	01-Nov-23
TCR7-1120	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT COURTROOM	3	02-Nov-23	06-Nov-23

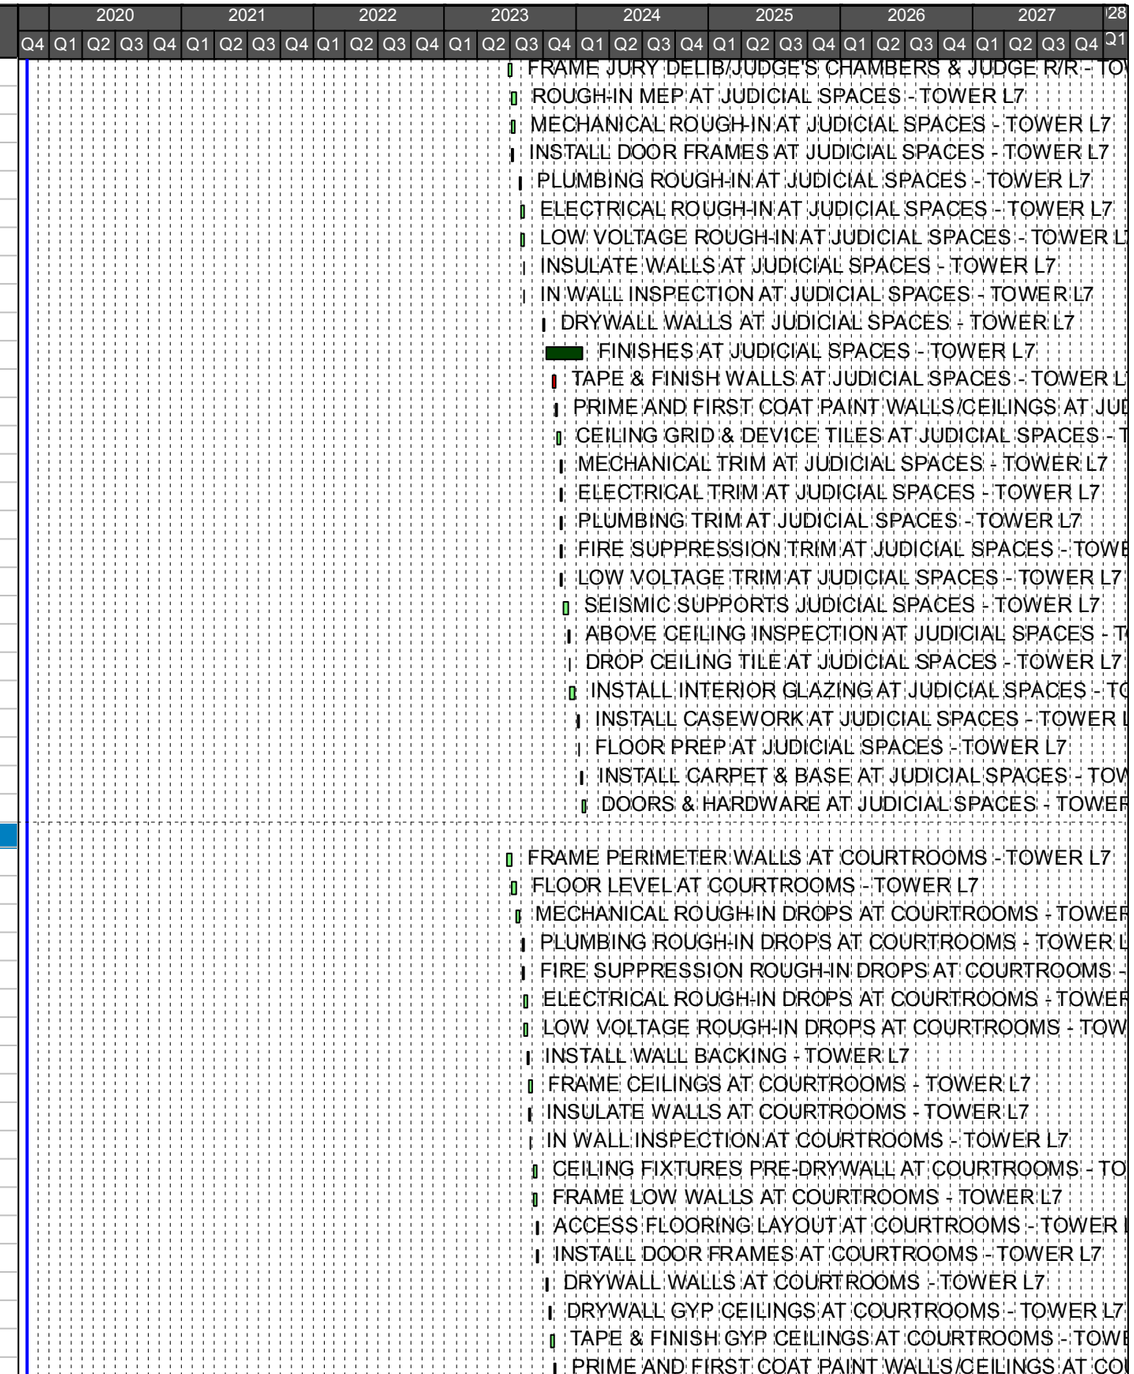

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TCR7-1040	TAPE & FINISH WALLS AT COURTROOMS - TOWER L7	6	03-Nov-23	10-Nov-23
TCR7-1080	CEILING GRID & DEVICE TILES AT COURTROOMS - TOWER L7	7	07-Nov-23	15-Nov-23
TCR7-1150	ACCESS FLOORING AT COURTROOMS - TOWER L7	12	07-Nov-23	22-Nov-23
TCR7-1100	MECHANICAL COMPLETE CEILING CONNECTIONS AT COURTROOM	5	16-Nov-23	22-Nov-23
TCR7-1260	ELECTRICAL COMPLETE CEILING CONNECTIONS AT COURTROOM	5	16-Nov-23	22-Nov-23
TCR7-1270	PLUMBING COMPLETE CEILING CONNECTIONS AT COURTROOMS	5	16-Nov-23	22-Nov-23
TCR7-1280	FIRE PROTECTION COMPLETE CEILING CONNECTIONS AT COURT	5	16-Nov-23	22-Nov-23
TCR7-1290	LOW VOLTAGE COMPLETE CEILING CONNECTIONS AT COURTROC	5	16-Nov-23	22-Nov-23
TCR7-1220	INSTALL SEISMIC SUPPORTS AT COURTROOMS - TOWER L7	10	27-Nov-23	08-Dec-23
TFINC1-350	ABOVE CEILING INSPECTION AT COURTROOMS - TOWER L7	1	11-Dec-23	11-Dec-23
TCR7-1110	DROP BALANCE OF CEILING TILES AT COURTROOMS - TOWER L7	4	12-Dec-23	15-Dec-23
TCR7-1010	INSTALL INTERIOR GLAZING AT COURTROOMS - TOWER L7	10	18-Dec-23	02-Jan-24
TCR7-1160	CASEWORK AT COURTROOMS - TOWER L7	12	10-Jan-24	26-Jan-24
TFINC7-110	INSTALL RAILING - TOWER L7	8	29-Jan-24	07-Feb-24
TCR7-1180	FINISH FLOORING & BASE AT COURTROOMS - TOWER L7	8	08-Feb-24	21-Feb-24
TCR7-1190	DOORS & HARDWARE AT COURTROOMS - TOWER L7	4	09-Feb-24	14-Feb-24
TCR7-1200	FABRIC WALL PANELS AT COURTROOMS - TOWER L7	4	15-Feb-24	22-Feb-24
TCR7-1210	FF & E AT COURTROOMS - TOWER L7	5	15-Feb-24	23-Feb-24
TCR7-1170	JURY SEATING AT COURTROOMS - TOWER L7	4	22-Feb-24	27-Feb-24
TCR7-1230	CLOSE-UP CASEWORK ELEC/LV TRIM & ACCESSORIES - TOWER L7	4	28-Feb-24	04-Mar-24
PUBLIC GALLERY				
TPG7-1100	F2 LIGHT FIXTURES AT PUBLIC GALLERY CEILINGS/MEP DROPS -	4	08-Aug-23	11-Aug-23
TPG7-1210	DROP CEILING TILE PUBLIC GALLERY - TOWER L7	4	13-Dec-23	18-Dec-23
IN-WALL ROUGH-INS				
TFING1-6800	FRAME INTERIOR WALLS PUBLIC GALLERY - TOWER L7	5	05-Jul-23	11-Jul-23
TFING1-6700	IN WALL COUNTERTOP SUPPORTS PUBLIC GALLERY - TOWER L7	2	07-Jul-23	10-Jul-23
TFING1-6900	HM DOOR FRAMES PUBLIC GALLERY - TOWER L7	2	10-Jul-23	11-Jul-23
TRIG1-820	ROUGH-IN WALL PLUMBING PUBLIC GALLERY - TOWER L7	2	11-Jul-23	12-Jul-23
TFING1-6920	INSTALL ELEVATOR DOOR FRAMES & ELEVATOR FRONTS PUBLIC	8	12-Jul-23	21-Jul-23
TFING1-6970	INSTALL STORE FRONT FRAMES PUBLIC GALLERY - TOWER L7	2	12-Jul-23	13-Jul-23
TRIG1-810	ROUGH-IN WALL LOW VOLTAGE PUBLIC GALLERY - TOWER L7	8	13-Jul-23	24-Jul-23
TRIG1-830	ROUGH-IN WALL ELECTRICAL PUBLIC GALLERY - TOWER L7	2	13-Jul-23	14-Jul-23
TRIG1-800	ROUGH-IN MECHANICAL CONTROLS PUBLIC GALLERY - TOWER L7	2	17-Jul-23	18-Jul-23
TFING1-6810	WALL BACKING PUBLIC GALLERY - TOWER L7	1	20-Jul-23	20-Jul-23
TFING1-6660	IN-WALL INSPECTION PUBLIC GALLERY - TOWER L7	1	25-Jul-23	25-Jul-23
OVERHEAD ROUGH-INS				
TPG7-1080	FRAME GYP CEILING PUBLIC GALLERY - TOWER L7	4	02-Aug-23	07-Aug-23
TRIG1-850	ROUGH-IN MECHANICAL AT HARDLIDS PUBLIC GALLERY - TOWER	2	08-Aug-23	09-Aug-23
TRIG1-840	ROUGH-IN ELECTRICAL AT HARDLIDS PUBLIC GALLERY - TOWER L	2	10-Aug-23	11-Aug-23
TFING1-6830	ABOVE CEILING INSPECTION AT HARDLIDS PUBLIC GALLERY - TO	1	14-Aug-23	14-Aug-23
FINISHES				
TFING1-6680	INSULATE WALLS PUBLIC GALLERY - TOWER L7	4	26-Jul-23	31-Jul-23
TFING1-6710	DRYWALL WALLS PUBLIC GALLERY - TOWER L7	4	16-Oct-23	19-Oct-23
TPG7-1120	DRYWALL CEILINGS PUBLIC GALLERY - TOWER L7	3	20-Oct-23	24-Oct-23
TFING1-6620	MEASURE & FAB INTERIOR GLAZING FRAMES PUBLIC GALLERY -	1	20-Oct-23	20-Oct-23
TFING1-6630	FURNISH MATERIAL FOR INTERIOR GLAZING FRAMES PUBLIC GAI	10	23-Oct-23	03-Nov-23
TFING1-6720	TAPE & FINISH PUBLIC GALLERY - TOWER L7	6	13-Nov-23	20-Nov-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TFING1-6690	PRIME & PAINT 1ST COAT PUBLIC GALLERY - TOWER L7	3	27-Nov-23	29-Nov-23
TPG2-1870	INSTALL LIGHT FIXTURES AT HARDLIDS PUBLIC GALLERY - TOWE	4	30-Nov-23	05-Dec-23
TFING1-6670	ELECTRICAL COVER PLATES PUBLIC GALLERY - TOWER L7	3	30-Nov-23	04-Dec-23
TFING1-6820	INSTALL EDGE GUARDS PUBLIC GALLERY - TOWER L7	2	30-Nov-23	01-Dec-23
TFING1-6980	INSTALL STORE FRONT GLAZING PUBLIC GALLERY - TOWER L7	5	30-Nov-23	06-Dec-23
TFING1-7030	FIRE SUPPRESSION HEADS AT HARDLIDS PUBLIC GALLERY - TOW	4	30-Nov-23	05-Dec-23
TFING1-7060	INSTALL HVAC CONTROLS PUBLIC GALLERY - TOWER L7	5	30-Nov-23	06-Dec-23
TPG7-1180	CEILING GRID / DEVICE TILES PUBLIC GALLERY - TOWER L7	4	05-Dec-23	08-Dec-23
TPG7-1200	FIRE ALARM DEVICES PUBLIC GALLERY - TOWER L7	2	11-Dec-23	12-Dec-23
TPG2-1930	HVAC DIFFUSERS & REGISTERS PUBLIC GALLERY - TOWER L7	3	11-Dec-23	13-Dec-23
TPG2-1970	INSTALL DEVICE TILES PUBLIC GALLERY - TOWER L7	3	11-Dec-23	13-Dec-23
TFING1-6850	CASEWORK PUBLIC GALLERY - TOWER L7	10	11-Dec-23	22-Dec-23
TOHG1-1320	LIGHT FIXTURES IN T-BAR CEILING PUBLIC GALLERY - TOWER L7	2	11-Dec-23	12-Dec-23
TFING1-6860	FIRE SUPPRESSION HEADS AT GRID PUBLIC GALLERY - TOWER L7	2	11-Dec-23	12-Dec-23
TFING1-6870	MECHANICAL DIFFUSERS & REGISTERS AT GRID PUBLIC GALLER	2	11-Dec-23	12-Dec-23
TFING1-6730	INSTALL SEISMIC SUPPORTS PUBLIC GALLERY - TOWER L7	10	13-Dec-23	27-Dec-23
TFING1-6950	FLOOR PREP AT LOBBY & PUBLIC GALLERY - TOWER L7	4	14-Dec-23	19-Dec-23
TPG7-1230	INSTALL FLOOR TILE IN PUBLIC GALLERY - TOWER L7	7	20-Dec-23	29-Dec-23
TFING1-6880	ABOVE CEILING INSPECTION AT T-BAR PUBLIC GALLERY - TOWE	1	28-Dec-23	28-Dec-23
TPG2-1960	DROP CEILING TILE PUBLIC GALLERY - TOWER L7	4	29-Dec-23	04-Jan-24
TPG7-1250	DOORS & HARDWARE PUBLIC GALLERY - TOWER L7	2	02-Jan-24	03-Jan-24
TFING1-6940	INSTALL FLOOR BASE AT TILE WALLS PUBLIC GALLERY - TOWER	5	02-Jan-24	08-Jan-24
TFING1-6750	INSTALL GLAZING PUBLIC GALLERY - TOWER L7	8	05-Jan-24	17-Jan-24
TFING1-6840	FIRE EXTINGUISHERS CABINETS PUBLIC GALLERY - TOWER L7	2	05-Jan-24	08-Jan-24
TPG7-1190	INSTALL WALL TILE PUBLIC GALLERY - TOWER L7	5	09-Jan-24	16-Jan-24
TFING1-6930	INSTALL METAL WALL PANELS/ TRIM PUBLIC GALLERY - TOWER L7	3	09-Jan-24	11-Jan-24
TPG7-1240	BENCHES FF&E PUBLIC GALLERY - TOWER L7	2	12-Jan-24	16-Jan-24
TPG7-1220	PLUMBING FIXTURES PUBLIC GALLERY - TOWER L7	2	17-Jan-24	18-Jan-24
TFING1-6610	OFOI VISUAL DISPLAY SURFACES PUBLIC GALLERY - TOWER L7	2	21-Mar-24	22-Mar-24
TFING1-7020	INSTALL LOW VOLTAGE PUBLIC GALLERY - TOWER L7	4	21-Mar-24	26-Mar-24
PUBLIC / STAFF RESTROOMS				
TRR7-1000	FRAME PUBLIC / STAFF RR - TOWER L7	4	12-Jul-23	17-Jul-23
TRR7-1010	ROUGH-IN MEP PUBLIC / STAFF RR - TOWER L7	15	18-Jul-23	07-Aug-23
TRIR7-100	ROUGH-IN WALL PLUMBING PUBLIC / STAFF RR - TOWER L7	5	18-Jul-23	24-Jul-23
TFINR7-110	FIELD MEASURE FOR TOILET PARTITIONS PUBLIC / STAFF RR - TO	1	18-Jul-23	18-Jul-23
TFINR7-120	FABRICATE TOILET PARTITIONS PUBLIC / STAFF RR - TOWER L7	30	19-Jul-23	29-Aug-23
TRIR7-110	ROUGH-IN WALL ELECTRICAL PUBLIC / STAFF RR - TOWER L7	5	20-Jul-23	26-Jul-23
TFINR7-140	WALL BACKING PUBLIC / STAFF RR - TOWER L7	2	27-Jul-23	28-Jul-23
TFINR7-150	INSULATE WALLS PUBLIC / STAFF RR - TOWER L7	1	31-Jul-23	31-Jul-23
TRIR7-120	ROUGH-IN MECHANICAL AT HARDLIDS PUBLIC / STAFF RR - TOWE	5	01-Aug-23	07-Aug-23
TRR7-1020	FINISHES PUBLIC / STAFF RR PUBLIC / STAFF RR - TOWER L7	12	08-Aug-23	23-Aug-23
TFINR7-300	MECHANICAL DIFFUSERS & REGISTERS PUBLIC / STAFF RR - TOW	2	08-Aug-23	09-Aug-23
TRR7-1030	MEP TRIM PUBLIC / STAFF RR PUBLIC / STAFF RR - TOWER L7	7	24-Aug-23	05-Sep-23
TFINR7-170	DRYWALL WALLS PUBLIC / STAFF RR - TOWER L7	2	18-Oct-23	19-Oct-23
TFINR7-190	FRAME HARDLID CEILINGS & SOFFITS PUBLIC / STAFF RR - TOWE	4	20-Oct-23	25-Oct-23
TFINR7-180	DRYWALL HARDLIDS & SOFFITS PUBLIC / STAFF RR - TOWER L7	3	20-Oct-23	24-Oct-23
TFINR7-200	TAPE & FINISH PUBLIC / STAFF RR - TOWER L7	7	10-Nov-23	20-Nov-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TFINR7-210	PRIME & PAINT 1ST COAT PUBLIC / STAFF RR - TOWER L7	3	22-Nov-23	28-Nov-23
TFINR7-220	FINISHES PUBLIC / STAFF RR - TOWER L7	12	29-Nov-23	14-Dec-23
TFINR7-230	FLOOR PREP AT PUBLIC / STAFF RR - TOWER L7	2	29-Nov-23	30-Nov-23
TFINR7-240	PULL & TERMINATE ELECTRICAL/ LOW VOLTAGE WIRE	2	29-Nov-23	30-Nov-23
TFINR7-250	ELECTRICAL/FIRE ALARM FINISH/DEVICES PUBLIC / STAFF RR - T	4	01-Dec-23	06-Dec-23
TFINR7-260	INSTALL FLOOR & WALL TILE IN PUBLIC / STAFF RR - TOWER L7	9	01-Dec-23	13-Dec-23
TFINR7-280	MEP TRIM PUBLIC / STAFF RR - TOWER L7	7	15-Dec-23	26-Dec-23
TFINR7-270	CASEWORK & TOPS PUBLIC / STAFF RR - TOWER L7	3	20-Dec-23	22-Dec-23
TFINR7-320	DOORS & HARDWARE PUBLIC / STAFF RR - TOWER L7	7	26-Dec-23	04-Jan-24
TFINR7-290	FIRE SUPPRESSION HEADS PUBLIC / STAFF RR - TOWER L7	1	26-Dec-23	26-Dec-23
TFINR7-310	PLUMBING FIXTURES PUBLIC / STAFF RR - TOWER L7	4	26-Dec-23	29-Dec-23
TFINR7-330	INSTALL PARTITIONS AND ACCESSORIES PUBLIC / STAFF RR - TO	7	02-Jan-24	10-Jan-24
MANLIFT BAY				
LOB7-100	FRAME MANLIFT BAY - TOWER L7	3	25-Jul-23	27-Jul-23
LOB7-110	ROUGH-IN MEP MANLIFT BAY - TOWER L7	5	28-Jul-23	03-Aug-23
LOB7-120	FINISHES MANLIFT BAY - TOWER L7	15	04-Aug-23	24-Aug-23
LOB7-130	TRIM MANLIFT BAY - TOWER L7	5	25-Aug-23	31-Aug-23
LEVEL 8				
LEVEL 8 TOWER FULL FLOOR				
MS8-1000	PRE-WELD EXTERIOR & PARTITION CLIPS	7	06-Jan-23	17-Jan-23
MS8-1030	FIREPROOF BALANCE OF FLOORS	5	26-Jan-23	01-Feb-23
MS8-1020	FIREPROOF PRIORITY WALLS/PERIMETER - TOWER L8	5	08-Feb-23	14-Feb-23
MS8-1010	EDGE OF SLAB FIRE SAFE	5	29-Mar-23	04-Apr-23
TFING1-7540	FIELD MEASURE FOR WINDOW COVERINGS - TOWER L8	1	14-Dec-23	14-Dec-23
TFING1-7550	FABRICATE WINDOW COVERINGS - TOWER L8	10	18-Mar-24	29-Mar-24
TPG8-1150	FINAL PAINT - TOWER L8	7	21-Mar-24	29-Mar-24
TFING1-7090	WINDOW COVERINGS PUBLIC GALLERY - TOWER L8	4	01-Apr-24	04-Apr-24
TFING1-7260	INSTALL SIGNAGE - TOWER L8	5	01-Apr-24	05-Apr-24
TFING1-7270	INT. CERTIFICATION & READY FOR PUNCH - TOWER L8	1	08-Apr-24	08-Apr-24
OVERHEAD ROUGH-INS				
TFING1-7080	LAYOUT FOR CLIPS AND TRACK - TOWER L8	3	13-Jan-23	18-Jan-23
TFING1-7070	INSTALL TOP TRACK - TOWER L8	7	17-Jan-23	25-Jan-23
TFING1-7510	INSTALL FIRE SUPPRESSION HANGERS - TOWER L8	4	10-Feb-23	15-Feb-23
TFING1-7500	INSTALL ELECTRICAL HANGERS - TOWER L8	4	16-Feb-23	23-Feb-23
TFING1-8330	INSTALL LOW VOLTAGE HANGERS - TOWER L8	4	16-Feb-23	23-Feb-23
TFING1-7140	INSTALL PLUMBING HANGERS - TOWER L8	5	24-Feb-23	02-Mar-23
TFING1-7490	INSTALL MECHANICAL HANGERS - TOWER L8	5	24-Feb-23	02-Mar-23
TFING1-7280	FIRE SUPPRESSION MAINS - TOWER L8	5	03-Mar-23	09-Mar-23
TOHG1-1380	O/H WASTE & VENT - TOWER L8	7	03-Mar-23	13-Mar-23
TOHG1-1340	O/H PLUMBING MAINS - TOWER L8	7	14-Mar-23	22-Mar-23
TOHG1-1760	O/H PLUMBING BRANCHES - TOWER L8	7	23-Mar-23	31-Mar-23
TOHG1-1330	O/H ELECTRICAL MAINS - TOWER L8	5	30-Mar-23	05-Apr-23
TOHG1-1670	O/H LOW VOLTAGE MAINS - TOWER L8	8	30-Mar-23	10-Apr-23
TOHG1-1370	O/H MECHANICAL MAINS - TOWER L8	10	14-Jun-23	27-Jun-23
TFING1-7290	HANG VAV'S - TOWER L8	8	16-Jun-23	27-Jun-23
TOHG1-1400	O/H HYDRONIC PIPING - TOWER L8	5	27-Jun-23	03-Jul-23
TFING1-7150	FIRE SUPPRESSION BRANCHES - TOWER L8	10	06-Jul-23	19-Jul-23

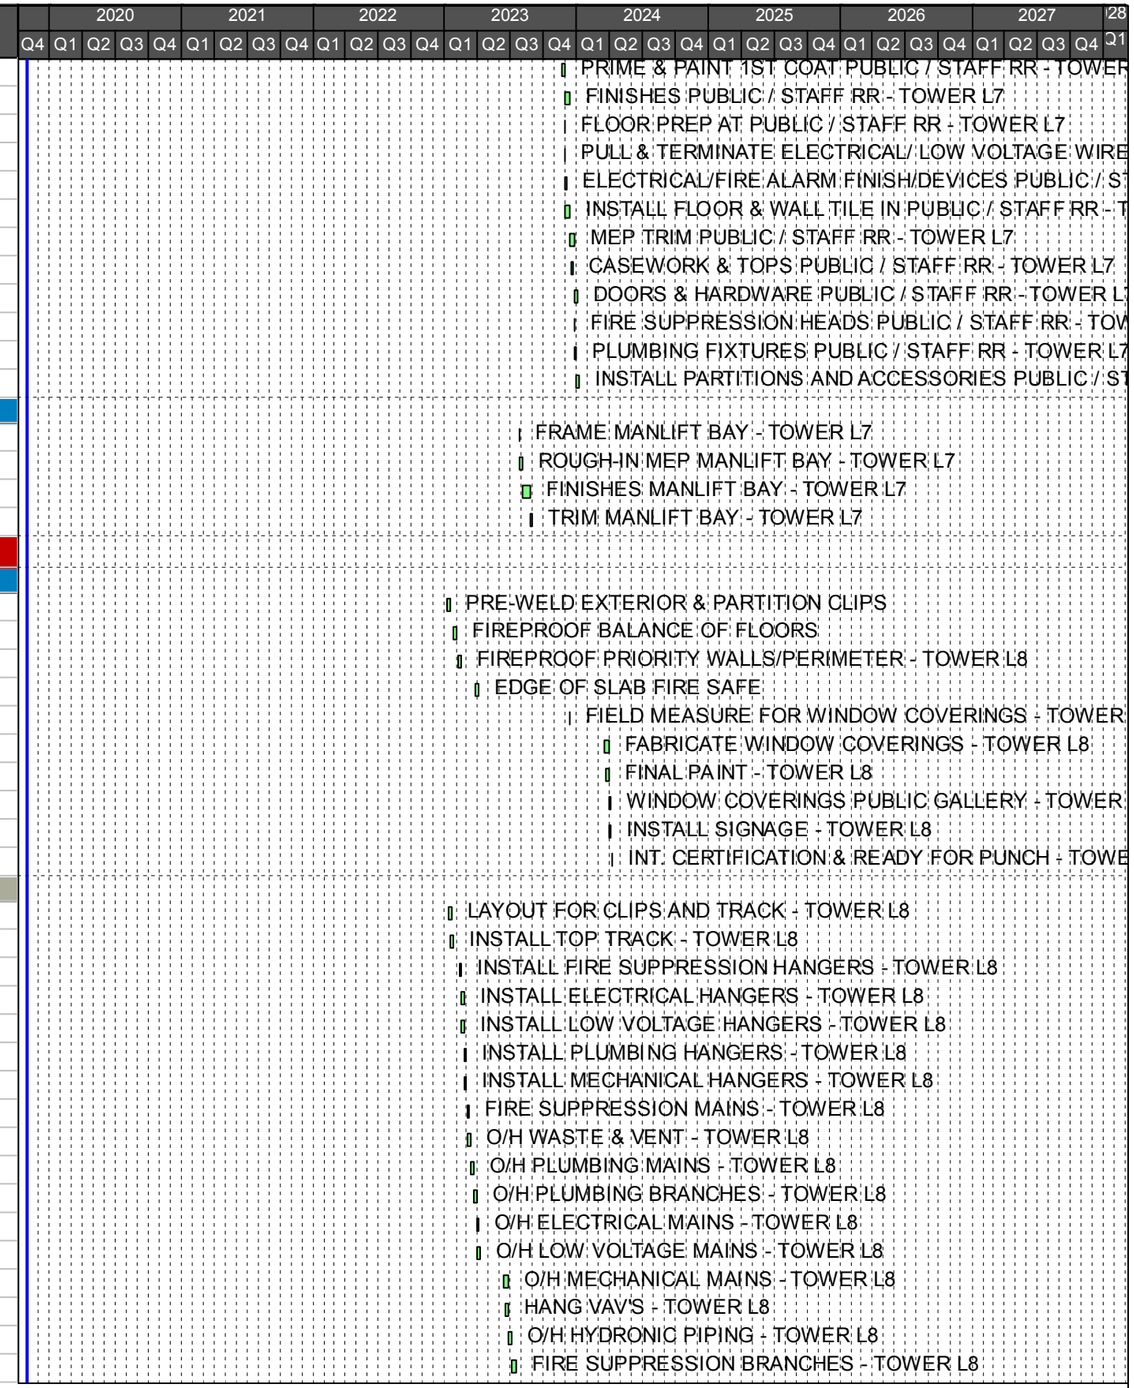

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TOHG1-1410	O/H ELECTRICAL BRANCHES - TOWER L8	3	13-Jul-23	17-Jul-23
TOHG1-1680	O/H LOW VOLTAGE BRANCHES - TOWER L8	3	13-Jul-23	17-Jul-23
TFING1-7100	O/H HVAC CONTROLS - TOWER L8	2	18-Jul-23	19-Jul-23
TOHG1-1350	O/H LOW VOLTAGE - TOWER L8	2	18-Jul-23	19-Jul-23
TOHG1-1390	O/H MECHANICAL BRANCHES - TOWER L8	15	02-Aug-23	22-Aug-23
TPG8-1000	ONE SIDE TIE INTO EXTERIOR - TOWER L8	2	11-Aug-23	14-Aug-23
TOHG1-1360	O/H SECURITY - TOWER L8	2	23-Aug-23	24-Aug-23
PRIORITY WALLS (IDF/ ELEC/ SHAFT/ STAIRS)				
IDF/ ELECTRICAL ROOM/ CENTRAL CONTROL				
TPR8-1050	FRAME IDF ROOM, ELECTRICAL ROOM, STAIRS - TOWER L8	5	18-Apr-23	24-Apr-23
TPR8-1060	ROUGH-IN IDF / ELECTRICAL ROOMS	5	25-Apr-23	01-May-23
TELECRI8-100	ROUGH-IN PLUMBING IDF / ELECTRICAL ROOMS	2	25-Apr-23	26-Apr-23
TELECRI8-110	ROUGH-IN ELECTRICAL IDF / ELECTRICAL ROOMS	4	26-Apr-23	01-May-23
TELECRI8-120	ROUGH-IN MECHANICAL IDF / ELECTRICAL ROOMS - TOWER L8	3	27-Apr-23	01-May-23
TPR8-1070	DRYWALL IDF/ ELECTRICAL ROOMS - TOWER L8	5	08-Sep-23	14-Sep-23
TPR8-1170	TAPE & FINISH IDF/ELECTRICAL ROOMS	7	13-Sep-23	21-Sep-23
TELEC8-130	PAINT IDF/ELECTRICAL ROOMS	3	22-Sep-23	26-Sep-23
TELEC8-140	SEAL FLOORS IDF/ELECTRICAL ROOMS	2	27-Sep-23	28-Sep-23
TPR8-1120	DOORS & HARDWARE	2	29-Sep-23	02-Oct-23
TPR8-1100	ELECTRICAL AND IDF, PANELS AND RACKS LEVEL 8	15	11-Oct-23	31-Oct-23
MEP SHAFTS				
TPR8-1020	INSTALL MEPF IN SHAFTS - TOWER L8	8	08-Mar-23	17-Mar-23
TPR8-1010	FRAME HVAC SHAFTS & DRYWALL C/R SIDE	3	18-Apr-23	20-Apr-23
TPR8-1110	DRYWALL HVAC SHAFTS - TOWER L8	3	05-Sep-23	07-Sep-23
TPR8-1180	TAPE & FINISH HVAC SHAFTS	7	09-Nov-23	17-Nov-23
ELEVATOR/ STAIR SHAFTS				
TPR8-1030	FRAME PASSENGER ELEVATOR HOISTWAYS L8	3	21-Apr-23	25-Apr-23
TPR8-1000	FRAME J1/J2 ELEVATOR WALLS L8	3	26-Apr-23	28-Apr-23
TPR1-2390	DRYWALL PASSENGER ELEVATOR - TOWER L8	2	26-Apr-23	27-Apr-23
TPR1-2410	TAPE & FINISH PASSENGER ELEVATOR - TOWER L8	6	28-Apr-23	05-May-23
TPR1-2400	DRYWALL J1/J2 ELEVATOR WALLS - TOWER L8	2	01-May-23	02-May-23
TPR1-2420	TAPE & FINISH J1/J2 ELEVATOR WALLS - TOWER L8	6	08-May-23	15-May-23
TPR8-1080	DRYWALL STAIR 1-2	2	08-Sep-23	11-Sep-23
TPR8-1090	DRYWALL STAIR 3-4	2	12-Sep-23	13-Sep-23
TPR8-1130	TAPE & FINISH STAIR 1-2	6	12-Sep-23	19-Sep-23
TPR8-1150	TAPE & FINISH STAIR 3-4 - TOWER L8	6	20-Sep-23	27-Sep-23
TPR8-1140	FINISHES STAIR 1-2	4	20-Sep-23	25-Sep-23
TPR8-1160	FINISHES STAIR 3-4	4	28-Sep-23	03-Oct-23
TELEC8-160	PRIME AND FIRST COAT PAINT STAIR 3-4	5	28-Sep-23	04-Oct-23
TELEC8-150	PRIME AND FIRST COAT PAINT STAIR 1-2	5	20-Nov-23	28-Nov-23
RESTRICTED CORRIDOR				
TPG8-1010	FRAME RESTRICTED CORRIDOR WALLS - TOWER L8	3	07-Jul-23	11-Jul-23
T1-G-1230	ELECTRICAL WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L	5	12-Jul-23	18-Jul-23
TRIG1-1100	LOW-VOLTAGE WALL ROUGH-IN RESTRICTED CORRIDOR - TOWE	5	12-Jul-23	18-Jul-23
TRIG1-1110	PLUMBING WALL ROUGH-IN RESTRICTED CORRIDOR - TOWER L8	5	12-Jul-23	18-Jul-23
T1-G-1500	INSULATE WALLS RESTRICTED CORRIDOR WALLS - TOWER L8	1	19-Jul-23	19-Jul-23
T1-G-1510	IN WALL INSPECTION RESTRICTED CORRIDOR WALLS - TOWER L8	1	20-Jul-23	20-Jul-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development

PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19

Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TPG8-1070	DRYWALL RESTRICTED CORRIDOR - TOWER L8	5	20-Oct-23	26-Oct-23
TPG8-1260	TAPE & FINISH RESTRICTED CORRIDOR - TOWER L8	5	21-Nov-23	29-Nov-23
T1-G-1360	PRIME & PAINT RESTRICTED CORRIDOR - TOWER L8	5	30-Nov-23	06-Dec-23
T1-G-1590	PULL WIRE RESTRICTED CORRIDOR WALLS - TOWER L8	2	30-Nov-23	01-Dec-23
TPG8-1110	CEILING GRID & DEVICE TILES RESTRICTED CORRIDOR - TOWER	4	07-Dec-23	12-Dec-23
T1-G-1370	HVAC TRIM RESTRICTED CORRIDOR - TOWER L8	3	07-Dec-23	11-Dec-23
TFING1-8220	ELECTRICAL TRIM RESTRICTED CORRIDOR - TOWER L8	2	07-Dec-23	08-Dec-23
TFING1-8230	LOW VOLTAGE FINISHES RESTRICTED CORRIDOR - TOWER L8	2	13-Dec-23	14-Dec-23
TFING1-8240	FIRE SUPPRESSION HEADS RESTRICTED CORRIDOR - TOWER L8	2	13-Dec-23	14-Dec-23
TFING1-8360	INSTALL SEISMIC SUPPORTS RESTRICTED CORRIDOR - TOWER L	10	15-Dec-23	29-Dec-23
TPG8-1030	ABOVE CEILING INSPECTION RESTRICTED CORRIDOR WALLS - T	1	02-Jan-24	02-Jan-24
TPG8-1170	DROP BALANCE OF CEILING TILES RESTRICTED CORRIDOR - TOW	4	03-Jan-24	08-Jan-24
TPG8-1020	INSTALL INTERIOR GLAZING RESTRICTED CORRIDOR WALLS - TC	10	09-Jan-24	23-Jan-24
TPG8-1130	INSTALL FLOORING & BASE RESTRICTED CORRIDOR - TOWER L8	5	24-Jan-24	30-Jan-24
PJ / CEO / JURY DELIBERATION / JUDGES CHAMBERS/COURT ADMIN				
TJD8-1000	METAL PANELS & SOUND CAP TIE-IN TO EXTERIOR - TOWER L8	3	02-Feb-23	06-Feb-23
TJD8-1010	FRAME AT JUDICIAL SPACES - TOWER L8	10	12-Jul-23	25-Jul-23
TJD8-1020	ROUGH-IN MEP AT JUDICIAL SPACES - TOWER L8	10	26-Jul-23	08-Aug-23
TRIJ8100	MECHANICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L8	7	26-Jul-23	03-Aug-23
TFINJ8-110	INSTALL DOOR FRAMES AT JUDICIAL SPACES - TOWER L8	3	26-Jul-23	28-Jul-23
TRIJ8110	PLUMBING ROUGH-IN AT JUDICIAL SPACES - TOWER L8	5	28-Jul-23	03-Aug-23
TRIJ8120	ELECTRICAL ROUGH-IN AT JUDICIAL SPACES - TOWER L8	6	01-Aug-23	08-Aug-23
TRIJ8130	LOW VOLTAGE ROUGH-IN AT JUDICIAL SPACES - TOWER L8	6	01-Aug-23	08-Aug-23
TOHJ1-280	INSULATE WALLS AT JUDICIAL SPACES - TOWER L8	1	09-Aug-23	09-Aug-23
TOHJ1-290	IN WALL INSPECTION AT JUDICIAL SPACES - TOWER L8	1	10-Aug-23	10-Aug-23
TJD8-1030	FINISHES AT JUDICIAL SPACES - TOWER L8	76	27-Oct-23	20-Feb-24
TFINJ8-220	DRYWALL WALLS AT JUDICIAL SPACES - TOWER L8	6	27-Oct-23	03-Nov-23
TFINJ8-210	TAPE & FINISH WALLS AT JUDICIAL SPACES - TOWER L8	7	30-Nov-23	08-Dec-23
TFINJ8-150	PRIME AND FIRST COAT PAINT WALLS/CEILINGS AT JUDICIAL SPA	3	11-Dec-23	13-Dec-23
TFINJ8-160	CEILING GRID & DEVICE TILES AT JUDICIAL SPACES - TOWER L8	6	14-Dec-23	21-Dec-23
TJD8-1040	MECHANICAL TRIM AT JUDICIAL SPACES - TOWER L8	5	22-Dec-23	29-Dec-23
TJD8-1050	ELECTRICAL TRIM AT JUDICIAL SPACES - TOWER L8	5	22-Dec-23	29-Dec-23
TJD8-1060	PLUMBING TRIM AT JUDICIAL SPACES - TOWER L8	5	22-Dec-23	29-Dec-23
TJD8-1070	FIRE PROTECTION TRIM AT JUDICIAL SPACES - TOWER L8	5	22-Dec-23	29-Dec-23
TJD8-1080	LOW VOLTAGE TRIM AT JUDICIAL SPACES - TOWER L8	5	22-Dec-23	29-Dec-23
TJD1-1115	INSTALL CASEWORK AT JUDICIAL SPACES - TOWER L8	5	22-Dec-23	29-Dec-23
TJD8-1110	INSTALL SEISMIC SUPPORTS JUDICIAL SPACES - TOWER L8	10	02-Jan-24	16-Jan-24
TJD8-1100	ABOVE CEILING INSPECTION AT JUDICIAL SPACES - TOWER L8	1	17-Jan-24	17-Jan-24
TFINJ8-190	DROP CEILING TILE AT JUDICIAL SPACES - TOWER L8	2	18-Jan-24	19-Jan-24
TJD8-1090	INSTALL INTERIOR GLAZING AT JUDICIAL SPACES - TOWER L8	10	22-Jan-24	02-Feb-24
TFINJ8-170	FLOOR PREP AT JUDICIAL SPACES - TOWER L8	1	05-Feb-24	05-Feb-24
TFINJ8-180	INSTALL CARPET & BASE AT JUDICIAL SPACES - TOWER L8	4	06-Feb-24	09-Feb-24
TFINJ8-200	DOORS & HARDWARE AT JUDICIAL SPACES - TOWER L8	5	12-Feb-24	20-Feb-24
COURTROOM / JUDICIAL CONFERENCE ROOM				
TCR8-1000	FRAME PERIMETER WALLS AT JUDICIAL CONFERENCE ROOM/ SH	5	06-Nov-23	10-Nov-23
TOHC8-100	O/H & I/W ROUGH-IN DROPS AT JUDICIAL CONFERENCE ROOM/ SI	10	13-Nov-23	28-Nov-23
TCR8-1020	FLOOR LEVEL AT JUDICIAL CONFERENCE ROOM/ SHELL SPACE -	3	27-Nov-23	29-Nov-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TCR8-1030	DRYWALL WALLS AT JUDICIAL CONFERENCE ROOM/ SHELL SPAC	3	30-Nov-23	04-Dec-23
TCR8-1040	TAPE & FINISH WALLS AT JUDICIAL CONFERENCE ROOM/ SHELL S	6	11-Dec-23	18-Dec-23
TCR8-1050	FRAME CEILINGS AT JUDICIAL CONFERENCE ROOM/ SHELL SPAC	5	19-Dec-23	26-Dec-23
TCR8-1060	CEILING FIXTURES PRE-DRYWALL AT JUDICIAL CONFERENCE RO	3	27-Dec-23	29-Dec-23
TCR8-1070	DRYWALL GYP CEILINGS AT JUDICIAL CONFERENCE ROOM/ SHEL	6	02-Jan-24	09-Jan-24
TCR7-1250	TAPE & FINISH GYP CEILINGS AT JUDICIAL CONFERENCE ROOM/	7	10-Jan-24	19-Jan-24
TCR8-1120	PAINT WALLS/CEILINGS AT JUDICIAL CONFERENCE ROOM/ SHELL	3	22-Jan-24	24-Jan-24
TCR8-1080	CEILING GRID & DEVICE TILES AT JUDICIAL CONFERENCE ROOM/	3	25-Jan-24	29-Jan-24
TCR8-1220	MEP TRIM AT JUDICIAL CONFERENCE ROOM/ SHELL SPACE - TOW	4	25-Jan-24	30-Jan-24
TCR8-1100	MEP COMPLETE CEILING CONNECTIONS AT JUDICIAL CONFEREN	5	30-Jan-24	05-Feb-24
TCR8-1230	CLOSE-UP CASEWORK MEP ACCESSOCLOSE-UP CASEWORK ELE	4	31-Jan-24	05-Feb-24
TCR8-1110	DROP BALANCE OF CEILING TILES AT JUDICIAL CONFERENCE RO	2	06-Feb-24	07-Feb-24
TCR8-1180	FINISH FLOORING & BASE AT JUDICIAL CONFERENCE ROOM/ SHE	8	08-Feb-24	21-Feb-24
TCR8-1190	DOORS & HARDWARE AT JUDICIAL CONFERENCE ROOM/ SHELL S	4	08-Feb-24	13-Feb-24
TCR8-1210	FF & E AT JUDICIAL CONFERENCE ROOM/ SHELL SPACE - TOWER	5	14-Feb-24	22-Feb-24
PUBLIC GALLERY				
TPG8-1100	MEP FIXTURES AT PUBLIC GALLERY	4	05-Sep-23	08-Sep-23
TPG8-1120	DRYWALL CEILINGS PUBLIC GALLERY	3	11-Sep-23	13-Sep-23
TPG8-1220	PLUMBING FIXTURES PUBLIC GALLERY - TOWER L8	2	22-Feb-24	23-Feb-24
IN-WALL ROUGH-INS				
TFING1-7300	FRAME INTERIOR WALLS PUBLIC GALLERY - TOWER L8	5	26-Jul-23	01-Aug-23
TFING1-7200	IN WALL COUNTERTOP SUPPORTS PUBLIC GALLERY - TOWER L8	2	28-Jul-23	31-Jul-23
TFING1-7400	HM DOOR FRAMES PUBLIC GALLERY - TOWER L8	2	31-Jul-23	01-Aug-23
TRIG1-880	ROUGH-IN WALL PLUMBING PUBLIC GALLERY - TOWER L8	2	01-Aug-23	02-Aug-23
TFING1-7420	INSTALL ELEVATOR DOOR FRAMES & ELEVATOR FRONTS PUBLIC	8	02-Aug-23	11-Aug-23
TFING1-7470	INSTALL STORE FRONT FRAMES PUBLIC GALLERY - TOWER L8	2	02-Aug-23	03-Aug-23
TRIG1-870	ROUGH-IN WALL LOW VOLTAGE PUBLIC GALLERY - TOWER L8	8	03-Aug-23	14-Aug-23
TRIG1-890	ROUGH-IN WALL ELECTRICAL PUBLIC GALLERY - TOWER L8	2	03-Aug-23	04-Aug-23
TRIG1-860	ROUGH-IN MECHANICAL CONTROLS PUBLIC GALLERY - TOWER L8	2	07-Aug-23	08-Aug-23
TFING1-7310	WALL BACKING PUBLIC GALLERY - TOWER L8	1	10-Aug-23	10-Aug-23
TFING1-7160	IN-WALL INSPECTION PUBLIC GALLERY - TOWER L8	1	15-Aug-23	15-Aug-23
OVERHEAD ROUGH-INS				
TPG8-1080	FRAME GYP CEILING PUBLIC GALLERY - TOWER L8	7	23-Aug-23	31-Aug-23
TRIG1-910	ROUGH-IN MECHANICAL AT HARDLIDS PUBLIC GALLERY - TOWER	2	05-Sep-23	06-Sep-23
TRIG1-900	ROUGH-IN ELECTRICAL AT HARDLIDS PUBLIC GALLERY - TOWER L	2	07-Sep-23	08-Sep-23
TFING1-7330	ABOVE CEILING INSPECTION AT HARDLIDS PUBLIC GALLERY - TO	1	11-Sep-23	11-Sep-23
TPG2-2000	DRYWALL CEILINGS PUBLIC GALLERY - TOWER L8	3	11-Dec-23	13-Dec-23
FINISHES				
TFING1-7180	INSULATE WALLS PUBLIC GALLERY - TOWER L8	4	16-Aug-23	21-Aug-23
TFING1-7210	DRYWALL WALLS PUBLIC GALLERY - TOWER L8	4	05-Dec-23	08-Dec-23
TFING1-7120	MEASURE & FAB INTERIOR GLAZING FRAMES PUBLIC GALLERY -	1	11-Dec-23	11-Dec-23
TFING1-7130	FURNISH MATERIAL FOR INTERIOR GLAZING FRAMES PUBLIC GAL	10	12-Dec-23	26-Dec-23
TFING1-7220	TAPE & FINISH PUBLIC GALLERY - TOWER L8	6	19-Dec-23	27-Dec-23
TFING1-7190	PRIME & PAINT 1ST COAT PUBLIC GALLERY - TOWER L8	3	02-Jan-24	04-Jan-24
TPG2-1990	INSTALL LIGHT FIXTURES AT HARDLIDS PUBLIC GALLERY - TOWE	4	05-Jan-24	10-Jan-24
TFING1-7170	ELECTRICAL COVER PLATES PUBLIC GALLERY - TOWER L8	3	05-Jan-24	09-Jan-24
TFING1-7480	INSTALL STORE FRONT GLAZING PUBLIC GALLERY - TOWER L8	5	05-Jan-24	11-Jan-24

Activity ID	Activity Name	Original Duration	Start	Finish
TFING1-7530	FIRE SUPPRESSION HEADS AT HARDLIDS PUBLIC GALLERY - TOW	4	05-Jan-24	10-Jan-24
TFING1-7560	INSTALL HVAC CONTROLS PUBLIC GALLERY - TOWER L8	5	05-Jan-24	11-Jan-24
TPG8-1180	CEILING GRID PUBLIC GALLERY - TOWER L8	4	10-Jan-24	16-Jan-24
TPG8-1200	FIRE ALARM DEVICES PUBLIC GALLERY - TOWER L8	2	17-Jan-24	18-Jan-24
TPG2-2050	HVAC DIFFUSERS & REGISTERS PUBLIC GALLERY - TOWER L8	3	17-Jan-24	19-Jan-24
TPG2-2090	INSTALL DEVICE TILES PUBLIC GALLERY - TOWER L8	3	17-Jan-24	19-Jan-24
TFING1-7350	CASEWORK PUBLIC GALLERY - TOWER L8	10	17-Jan-24	30-Jan-24
TOHG1-1420	LIGHT FIXTURES IN T-BAR CEILING PUBLIC GALLERY - TOWER L8	2	17-Jan-24	18-Jan-24
TFING1-7360	FIRE SUPPRESSION HEADS AT GRID PUBLIC GALLERY - TOWER L8	2	17-Jan-24	18-Jan-24
TFING1-7370	MECHANICAL DIFFUSERS & REGISTERS AT GRID PUBLIC GALLER	2	17-Jan-24	18-Jan-24
TFING1-7230	INSTALL SEISMIC SUPPORTS PUBLIC GALLERY - TOWER L8	10	19-Jan-24	01-Feb-24
TFING1-7450	FLOOR PREP AT LOBBY & PUBLIC GALLERY - TOWER L8	4	22-Jan-24	25-Jan-24
TPG8-1230	INSTALL FLOOR TILE IN PUBLIC GALLERY - TOWER L8	7	26-Jan-24	05-Feb-24
TFING1-7320	INSTALL EDGE GUARDS PUBLIC GALLERY - TOWER L8	2	31-Jan-24	01-Feb-24
TFING1-7390	PLUMBING FIXTURES PUBLIC GALLERY - TOWER L8	2	31-Jan-24	01-Feb-24
TFING1-7520	INSTALL LOW VOLTAGE TRIM PUBLIC GALLERY - TOWER L8	4	31-Jan-24	05-Feb-24
TFING1-7380	ABOVE CEILING INSPECTION AT T-BAR PUBLIC GALLERY - TOWER	1	02-Feb-24	02-Feb-24
TPG8-1210	DROP CEILING TILE PUBLIC GALLERY - TOWER L8	4	05-Feb-24	08-Feb-24
TPG8-1250	DOORS & HARDWARE PUBLIC GALLERY - TOWER L8	2	06-Feb-24	07-Feb-24
TFING1-7440	INSTALL FLOOR BASE AT TILE WALLS PUBLIC GALLERY - TOWER	5	06-Feb-24	12-Feb-24
TFING1-7250	INSTALL GLAZING PUBLIC GALLERY - TOWER L8	8	09-Feb-24	22-Feb-24
TFING1-7340	FIRE EXTINGUISHERS CABINETS PUBLIC GALLERY - TOWER L8	2	09-Feb-24	12-Feb-24
TPG8-1190	INSTALL WALL TILE PUBLIC GALLERY - TOWER L8	5	13-Feb-24	21-Feb-24
TFING1-7430	INSTALL METAL WALL PANELS/ TRIM PUBLIC GALLERY - TOWER L8	3	13-Feb-24	15-Feb-24
TPG8-1240	BENCHES FF&E PUBLIC GALLERY	2	20-Feb-24	21-Feb-24
TFING1-7110	OFOI VISUAL DISPLAY SURFACES PUBLIC GALLERY - TOWER L8	2	01-Apr-24	02-Apr-24
MANLIFT BAY				
LOB8-100	FRAME MANLIFT BAY - TOWER L8	3	25-Jul-23	27-Jul-23
LOB8-110	ROUGH-IN MEP MANLIFT BAY - TOWER L8	5	28-Jul-23	03-Aug-23
LOB8-120	FINISHES MANLIFT BAY - TOWER L8	15	04-Aug-23	24-Aug-23
LOB8-130	TRIM MANLIFT BAY - TOWER L8	5	25-Aug-23	31-Aug-23
PUBLIC / STAFF RESTROOMS				
TRR8-1000	FRAME PUBLIC / STAFF RR - TOWER L8	4	27-Jul-23	01-Aug-23
TRR8-1010	ROUGH-IN MEP PUBLIC / STAFF RR - TOWER L8	15	27-Jul-23	16-Aug-23
TRIR7-130	ROUGH-IN WALL PLUMBING - TOWER L8	5	02-Aug-23	08-Aug-23
TFINR7-370	FIELD MEASURE FOR TOILET PARTITIONS - TOWER L8	1	02-Aug-23	02-Aug-23
TFINR7-380	FABRICATE TOILET PARTITIONS - TOWER L8	30	03-Aug-23	15-Sep-23
TRR8-1020	FINISHES PUBLIC / STAFF RR - TOWER L8	12	17-Aug-23	05-Sep-23
TRIR7-140	ROUGH-IN WALL ELECTRICAL - TOWER L8	5	17-Aug-23	23-Aug-23
TRIR7-150	ROUGH-IN MECHANICAL AT HARDLIDS - TOWER L8	5	24-Aug-23	30-Aug-23
TFINR7-390	WALL BACKING - TOWER L8	2	24-Aug-23	25-Aug-23
TFINR7-400	INSULATE WALLS - TOWER L8	1	28-Aug-23	28-Aug-23
TFINR7-540	MECHANICAL DIFFUSERS & REGISTERS - TOWER L8	2	31-Aug-23	05-Sep-23
TFINR7-410	DRYWALL WALLS - TOWER L8	2	07-Dec-23	08-Dec-23
TFINR7-420	FRAME HARDLIDS CEILINGS & SOFFITS - TOWER L8	4	11-Dec-23	14-Dec-23
TFINR7-430	DRYWALL HARDLIDS & SOFFITS - TOWER L8	3	11-Dec-23	13-Dec-23
TFINR7-440	TAPE & FINISH - TOWER L8	7	18-Dec-23	27-Dec-23

Activity ID	Activity Name	Original Duration	Start	Finish
TFINR7-450	PRIME & PAINT 1ST COAT - TOWER L8	3	29-Dec-23	03-Jan-24
TFINR7-460	FINISHES - TOWER L8	12	04-Jan-24	22-Jan-24
TFINR7-470	FLOOR PREP AT - TOWER L8	2	04-Jan-24	05-Jan-24
TFINR7-480	PULL & TERMINATE ELECTRICAL/ LOW VOLTAGE WIRE	2	04-Jan-24	05-Jan-24
TFINR7-490	ELECTRICAL/FIRE ALARM FINISH/DEVICES - TOWER L8	4	08-Jan-24	11-Jan-24
TFINR7-500	INSTALL FLOOR & WALL TILE IN - TOWER L8	9	08-Jan-24	19-Jan-24
TRR8-1030	MEP TRIM PUBLIC / STAFF RR - TOWER L8	5	23-Jan-24	29-Jan-24
TFINR7-520	CASEWORK & TOPS - TOWER L8	3	26-Jan-24	30-Jan-24
TFINR7-550	DOORS & HARDWARE - TOWER L8	7	31-Jan-24	08-Feb-24
TFINR7-530	FIRE SUPPRESSION HEADS - TOWER L8	1	31-Jan-24	31-Jan-24
TFINR7-560	PLUMBING FIXTURES - TOWER L8	4	31-Jan-24	05-Feb-24
TFINR7-570	INSTALL PARTITIONS AND ACCESSORIES - TOWER L8	7	06-Feb-24	14-Feb-24
LEVEL 9				
LEVEL 9 TOWER FULL FLOOR				
TFIN9-100	INSTALL TROLLEY HOIST ACCESS HATCH - TOWER L9	1	30-Dec-22	30-Dec-22
TFIN9-110	FRAME PENTHOUSE - TOWER L9	7	07-Feb-23	15-Feb-23
TRI9100	MECHANICAL IN WALL ROUGH-IN - TOWER L9	2	16-Feb-23	21-Feb-23
TRI9110	ELECTRICAL IN WALL ROUGH-IN - TOWER L9	3	16-Feb-23	22-Feb-23
TRI9120	PLUMBING IN WALL ROUGH-IN - TOWER L9	10	16-Feb-23	03-Mar-23
TFIN9-150	SHEATH PENTHOUSE - TOWER L9	5	06-Mar-23	10-Mar-23
RM9-1010	INSTALL MEPF IN SHAFTS - TOWER L9	8	20-Mar-23	29-Mar-23
TFIN9-160	DRYWALL ELECTRICAL ROOM - TOWER L9	4	29-Mar-23	03-Apr-23
RM9-1030	DRYWALL ELEVATOR / PENTHOUSE WALLS - TOWER L9	4	30-Mar-23	04-Apr-23
TFIN9-290	TAPE & FINISH ELECTRICAL ROOM - TOWER L9	7	03-Apr-23	11-Apr-23
RM9-1060	TAPE & FINISH ELEVATOR / PENTHOUSE WALLS - TOWER L9	7	04-Apr-23	12-Apr-23
TFIN9-180	PRIME AND FIRST COAT PAINT ELECTRICAL ROOM - TOWER L9	2	12-Apr-23	13-Apr-23
RM9-1040	DOORS AND HARDWARE - TOWER L9	5	13-Apr-23	19-Apr-23
TFIN9-170	PRIME AND FIRST COAT PAINT PENTHOUSE - TOWER L9	4	13-Apr-23	18-Apr-23
RM9-1050	ELECTRICAL AND IDF, PANELS AND RACKS - TOWER L9	7	14-Apr-23	24-Apr-23
RM9-1070	INTALL TEMP HVAC CONTROLS FOR TEMPORARY BUILDING CONI	5	14-Apr-23	20-Apr-23
TFIN9-200	INSTALL FLOORING PENTHOUSE - TOWER L9	4	19-Apr-23	24-Apr-23
TFIN9-210	INSTALL FIRE SUPPRESSION TRIM - TOWER L9	2	19-Apr-23	20-Apr-23
TFIN9-220	INSTALL TROLLEY SYSTEM - TOWER L9	5	19-Apr-23	25-Apr-23
TFIN9-230	PULL WIRE PENTHOUSE - TOWER L9	5	25-Apr-23	01-May-23
TFIN9-240	INSTALL LIGHT FIXTURES - TOWER L9	5	02-May-23	08-May-23
TFIN9-250	INSTALL ELECTRICAL TRIM - TOWER L9	3	02-May-23	04-May-23
TFIN9-260	INSTALL FIRE ALARM TRIM - TOWER L9	2	02-May-23	03-May-23
TFIN9-270	INSTALL MECHANICAL TRIM/MECHANICAL CONTROLS - TOWER L9	2	02-May-23	03-May-23
TFIN9-280	INSTALL TELECOM - TOWER L9	2	02-May-23	03-May-23
TFIN9-300	INSTALL SECURITY - TOWER L9	2	02-May-23	03-May-23
LOW-RISE				
LEVEL 1				
FULL FLOOR				
TFING1-1370	FIELD MEASURE FOR WINDOW COVERINGS - TOWER L1	1	17-Jul-23	17-Jul-23
LFING1-120	EXPANSION JOINT AT TOWER CONNECTION - LOW RISE L1	5	19-Jul-23	25-Jul-23
LFING1-140	MEASURE & FAB INTERIOR GLASS - LOW RISE L1	10	25-Jul-23	07-Aug-23
TFING1-1360	FABRICATE WINDOW COVERINGS - TOWER L1	10	10-Aug-23	23-Aug-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
LFING1-250	INSTALL GLAZING - LOW RISE L1	8	14-Aug-23	23-Aug-23
LFING1-320	WINDOW COVERINGS - LOW RISE L1	4	24-Aug-23	29-Aug-23
LFING1-340	FINAL PAINT - LOW RISE L1	7	16-Nov-23	28-Nov-23
LFING1-280	INSTALL SIGNAGE - LOW RISE L1	5	08-Dec-23	14-Dec-23
LFING1-350	LOW RISE L1 INT. CERTIFICATION & READY FOR PUNCH	1	15-Dec-23	15-Dec-23
OVERHEAD ROUGH-IN'S				
LRI1-110	PRE-WELD EXTERIOR & PARTITION CLIPS - LOW RISE L1	7	08-Feb-23	16-Feb-23
LS2-150	FIREPROOF PRIORITY WALLS/PERIMETER - LOW RISE L1	5	15-Feb-23	23-Feb-23
LRI1-100	FIREPROOF BALANCE OF FLOORS - LOW RISE L1	5	21-Feb-23	27-Feb-23
LPG1-1000	ONE SIDE TIE INTO EXTERIOR	5	24-Feb-23	02-Mar-23
LRI1-120	LAYOUT FOR CLIPS AND TRACK - LOW RISE L1	3	03-Mar-23	07-Mar-23
LOH1-100	INSTALL PLUMBING HANGERS - LOW RISE L1	4	03-Mar-23	08-Mar-23
LOH1-110	INSTALL MECHANICAL HANGERS - LOW RISE L1	4	03-Mar-23	08-Mar-23
LOH1-120	INSTALL ELECTRICAL HANGERS - LOW RISE L1	4	03-Mar-23	08-Mar-23
LOH1-130	INSTALL FIRE SUPPRESSION HANGERS - LOW RISE L1	4	03-Mar-23	08-Mar-23
LRI1-130	INSTALL TOP TRACK INTERFERENCE WALLS - LOW RISE L1	4	06-Mar-23	09-Mar-23
LRI1-140	FRAME INTERFERENCE WALLS - LOW RISE L1	7	10-Mar-23	20-Mar-23
LRI1-150	TOP TRACK INTERIOR WALLS REMAINING AREAS - LOW RISE L1	4	10-Mar-23	15-Mar-23
LRI1-160	TOP DOWN INTERFERENCE WALLS - LOW RISE L1	5	21-Mar-23	27-Mar-23
LRI1-170	INSPECTION OF INTERFERENCE HEAD OF WALL - LOW RISE L1	3	28-Mar-23	30-Mar-23
LRI1-180	FIRE TAPE HEAD OF WALL AT INTERFERENCE WALLS - LOW RISE	3	28-Mar-23	30-Mar-23
LOHG1-120	O/H FIRE SUPPRESSION MAINS- LOW RISE L1	5	31-Mar-23	06-Apr-23
LOHG1-100	O/H MECHANICAL MAINS - LOW RISE L1	8	07-Apr-23	18-Apr-23
LOHG1-180	O/H FIRE SUPPRESSION BRANCHES - LOW RISE L1	3	07-Apr-23	11-Apr-23
LOHG1-150	O/H HYDRONIC PIPING - LOW RISE L1	5	14-Apr-23	20-Apr-23
LOHG1-130	O/H PLUMBING MAINS MAINS - LOW RISE L1	7	19-Apr-23	27-Apr-23
LOHG1-140	O/H MECHANICAL CONTROLS - LOW RISE L1	3	21-Apr-23	25-Apr-23
LOHG1-220	O/H PLUMBING BRANCHES - LOW RISE L1	5	21-Apr-23	27-Apr-23
LOHG1-110	O/H ELECTRICAL MAINS - LOW RISE L1	5	28-Apr-23	04-May-23
LOHG1-230	O/H LOW VOLTAGE MAINS - LOW RISE L1	5	28-Apr-23	04-May-23
LOHG1-160	O/H LOW VOLTAGE BRANCHES - LOW RISE L1	5	05-May-23	11-May-23
LOHG1-170	O/H ELECTRICAL BRANCHES - LOW RISE L1	5	05-May-23	11-May-23
LOHG1-190	O/H MECHANICAL BRANCHES - LOW RISE L1	7	17-May-23	25-May-23
PRIORITY ROOMS (ELECTRICAL/ IDF/ AV ROOMS)				
IDF/ ELECTRICAL ROOM/ CENTRAL CONTROL				
LPR1-1010	FRAME IDF ROOM - LOW RISE L1	5	10-Mar-23	16-Mar-23
LPR1-1030	ROUGH-IN IDF ROOM - LOW RISE L1	5	17-Mar-23	23-Mar-23
LPR1-1040	DRYWALL IDF ROOM - LOW RISE L1	4	24-Mar-23	29-Mar-23
LPR1-1080	TAPE & FINISH IDF ROOM - LOW RISE L1	6	30-Mar-23	06-Apr-23
LPR1-1090	PAINT/SEAL FLOORS IDF ROOM - LOW RISE L1	4	07-Apr-23	12-Apr-23
LPR1-1050	ELECTRICAL AND IDF, PANELS AND RACKS - LOW RISE L1	15	13-Apr-23	03-May-23
MEP SHAFTS				
LPR1-1020	INSTALL MEPF IN SHAFTS - LOW RISE L1	8	10-Mar-23	21-Mar-23
LPR1-1000	FRAME HVAC SHAFTS - LOW RISE L1	3	17-Mar-23	21-Mar-23
LPR1-1060	DRYWALL HVAC SHAFTS - LOW RISE L1	3	30-Mar-23	03-Apr-23
LPR1-1070	TAPE & FINISH HVAC SHAFTS - LOW RISE L1	7	07-Apr-23	17-Apr-23
OFFICES / EXT TICKET COUNTER				

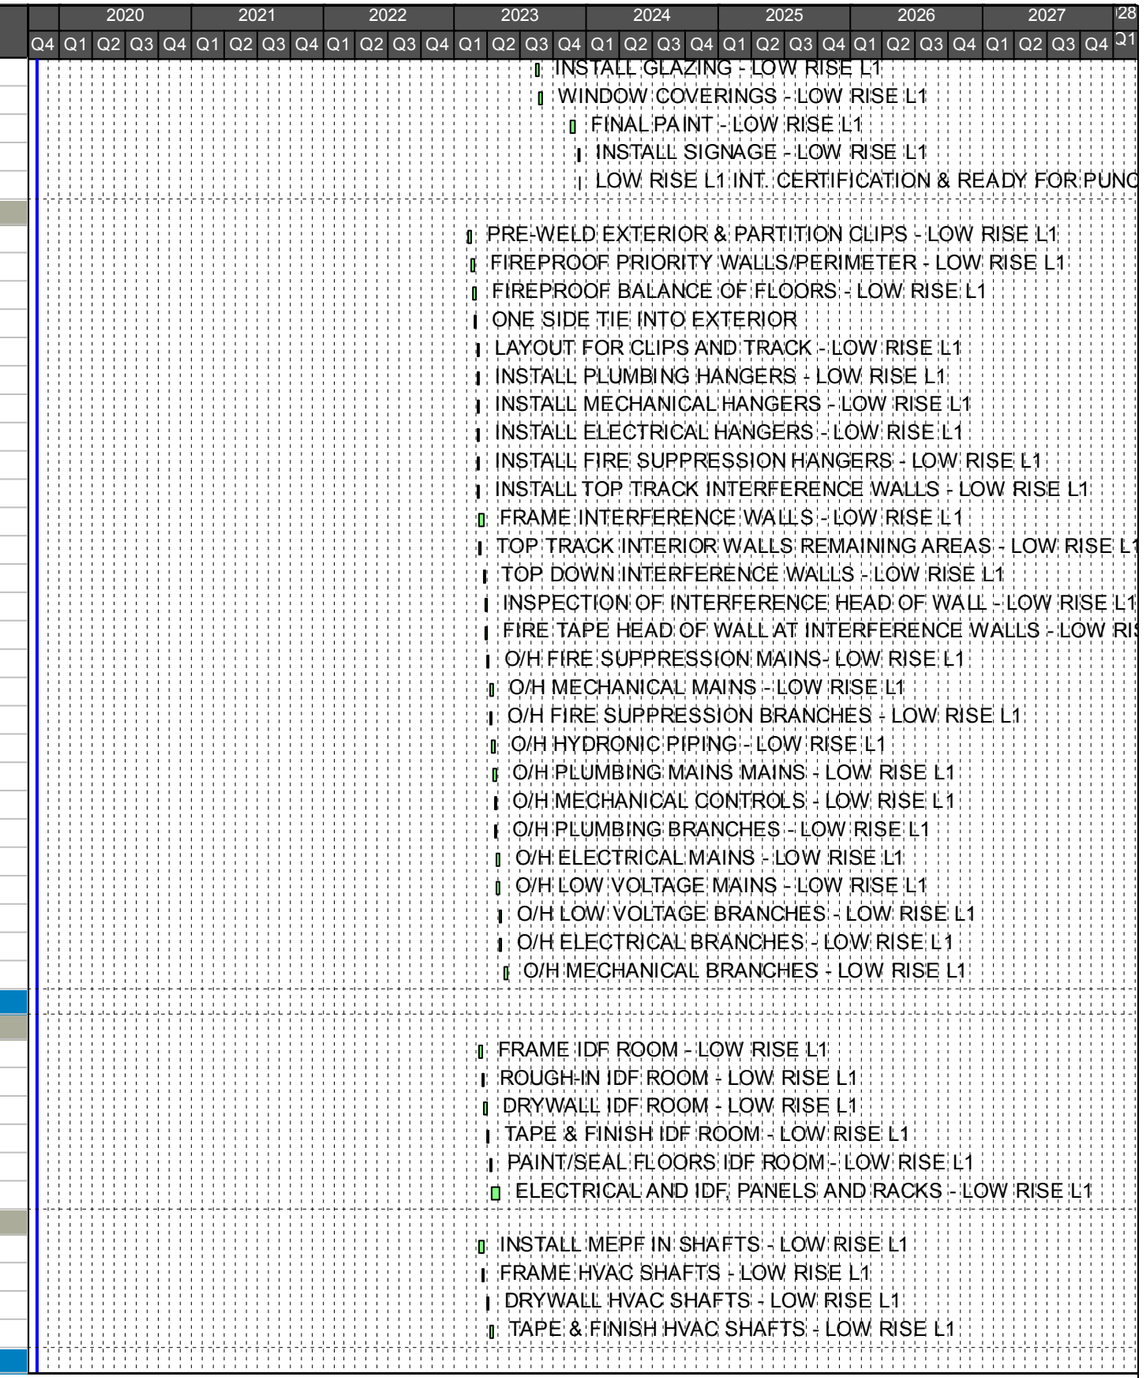

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
LOETC1-1000	FRAME WALLS OFFICES - LOW RISE L1	10	19-Apr-23	02-May-23
LRIO1-100	ROUGH-IN PLUMBING OFFICES - LOW RISE L1	5	03-May-23	09-May-23
LFINO1-100	INSTALL DOOR FRAMES OFFICES - LOW RISE L1	3	03-May-23	05-May-23
LJA1-1510	FRAME SOFFIT OFFICE SPACES - LOW RISE L1	5	03-May-23	09-May-23
LRIO1-160	ROUGH-IN FIRE SUPPRESSION OFFICES - LOW RISE L1	5	03-May-23	09-May-23
LRIO1-110	ROUGH-IN ELECTRICAL OFFICES - LOW RISE L1	7	10-May-23	18-May-23
LRIO1-150	ROUGH-IN LOW VOLTAGE OFFICES - LOW RISE L1	7	10-May-23	18-May-23
LRIO1-120	ROUGH-IN MECHANICAL OFFICES - LOW RISE L1	3	19-May-23	23-May-23
LRIO1-130	INSULATE WALLS - LOW RISE L1	1	24-May-23	24-May-23
LRIO1-140	IN WALL INSPECTION - LOW RISE L1	1	25-May-23	25-May-23
LOETC1-1020	DRYWALL OFFICES - LOW RISE L1	10	30-May-23	12-Jun-23
LOETC1-1110	TAPE & FINISH OFFICES - LOW RISE L1	12	31-May-23	15-Jun-23
LOETC1-1030	PRIME AND FIRST COAT PAINT OFFICES - LOW RISE L1	5	16-Jun-23	22-Jun-23
LOETC1-1040	CEILING GRID / DEVICE TILES OFFICES - LOW RISE L1	10	23-Jun-23	07-Jul-23
LFINO1-110	FLOOR PREP OFFICES - LOW RISE L1	1	23-Jun-23	23-Jun-23
LFINO1-120	INSTALL FLOOR AND WALL TILE OFFICES - LOW RISE L1	4	26-Jun-23	29-Jun-23
LOETC1-1060	MECHANICAL CEILING COMPLETION OFFICES - LOW RISE L1	5	10-Jul-23	14-Jul-23
LOETC1-1070	CASEWORK / FF&E OFFICES - LOW RISE L1	6	10-Jul-23	17-Jul-23
LOETC1-1130	ELECTRICAL CEILING COMPLETION OFFICES - LOW RISE L1	5	10-Jul-23	14-Jul-23
LOETC1-1140	PLUMBING CEILING COMPLETION OFFICES - LOW RISE L1	5	10-Jul-23	14-Jul-23
LOETC1-1150	FIRE SUPPRESSION CEILING COMPLETION OFFICES - LOW RISE L1	5	10-Jul-23	14-Jul-23
LOETC1-1160	LOW VOLTAGE CEILING COMPLETION OFFICES - LOW RISE L1	5	10-Jul-23	14-Jul-23
LOETC1-1120	ABOVE CEILING INSPECTION - LOW RISE L1	1	17-Jul-23	17-Jul-23
LOETC1-1080	DROP BALANCE OF CEILING TILES OFFICES - LOW RISE L1	5	18-Jul-23	24-Jul-23
LOETC1-1090	INSTALL CARPET OFFICES - LOW RISE L1	8	18-Jul-23	27-Jul-23
LFINO1-130	INSTALL PLUMBING FIXTURES OFFICES - LOW RISE L1	2	18-Jul-23	19-Jul-23
LOETC1-1100	DOORS AND HARDWARE OFFICES - LOW RISE L1	8	28-Jul-23	08-Aug-23
ENTRY LOBBY & QUEUING				
ROUGH-IN'S				
LRI1-190	FRAME INTERIOR WALLS - LOW RISE L1	10	03-May-23	16-May-23
LRI1-200	IN WALL COUNTERTOP SUPPORTS - LOW RISE L1	3	05-May-23	09-May-23
LPG1-1040	FRAME HARDLID CEILINGS & SOFFITS - LOW RISE L1	7	05-May-23	15-May-23
LRIG1-100	ROUGH-IN WALL PLUMBING - LOW RISE L1	5	10-May-23	16-May-23
LRI1-210	HM DOOR FRAMES - LOW RISE L1	5	10-May-23	16-May-23
LOH1-260	ROUGH IN LOW VOLTAGE AT HARDLIDS AND SOFFITS - LOW RISE	4	16-May-23	19-May-23
LOH1-270	FIRE SUPPRESSION HEADS AT HARDLIDS AND SOFFITS - LOW RI	2	16-May-23	17-May-23
LRIG1-120	ROUGH-IN WALL ELECTRICAL - LOW RISE L1	8	19-May-23	01-Jun-23
LRIG1-130	ROUGH-IN MECHANICAL CONTROLS - LOW RISE L1	8	23-May-23	05-Jun-23
LRIG1-110	ROUGH-IN WALL LOW VOLTAGE - LOW RISE L1	8	23-May-23	05-Jun-23
LRI1-260	WALL BACKING - LOW RISE L1	5	30-May-23	05-Jun-23
LOHG1-210	ROUGH-IN MECHANICAL AT HARDLIDS AND SOFFITS - LOW RISE L1	4	30-May-23	02-Jun-23
LOHG1-200	ROUGH-IN ELECTRICAL AT HARDLIDS AND SOFFITS - LOW RISE L1	4	02-Jun-23	07-Jun-23
LRI1-270	WALL FRAMING INSPECTION PUBLIC GALLERY - LOW RISE L1	1	06-Jun-23	06-Jun-23
LOH1-280	CEILING CLOSE-IN INSPECTION AT HARDLIDS AND SOFFITS - LOW	1	08-Jun-23	08-Jun-23
FINISHES				
LRI1-300	INSULATE WALLS - LOW RISE L1	2	07-Jun-23	08-Jun-23
LRI1-330	IN WALL INSPECTION - LOW RISE L1	1	09-Jun-23	09-Jun-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
LRI1-310	DRYWALL WALLS - LOW RISE L1	8	13-Jun-23	22-Jun-23
LPG1-1050	DRYWALL HARDLIDS & SOFFITS - LOW RISE L1	5	20-Jun-23	26-Jun-23
LRI1-320	TAPE & FINISH - LOW RISE L1	11	23-Jun-23	10-Jul-23
LPG1-1060	PRIME & PAINT 1ST COAT - LOW RISE L1	7	06-Jul-23	14-Jul-23
LOH1-290	CEILING GRID - LOW RISE L1	10	12-Jul-23	25-Jul-23
LFING1-110	INSTALL STORE FRONT FRAMES	6	17-Jul-23	24-Jul-23
LOH1-300	ELECTRICAL TRIM AT HARDLIDS AND SOFFITS - LOW RISE L1	4	17-Jul-23	20-Jul-23
LOH1-310	LOW VOLTAGE TRIM AT HARDLIDS AND SOFFITS - LOW RISE L1	4	21-Jul-23	26-Jul-23
LFING1-150	INSTALL INTERIOR GLAZING - LOW RISE L1	2	25-Jul-23	26-Jul-23
LOH1-340	ELECTRICAL TERMINATE & TRIM AT T-BAR - LOW RISE L1	6	26-Jul-23	02-Aug-23
LFING1-160	CASEWORK & TOPS - LOW RISE L1	3	26-Jul-23	28-Jul-23
LOH1-350	MECHANICAL DIFFUSERS & REGISTERS AT T-BAR - LOW RISE L1	4	26-Jul-23	31-Jul-23
LOH1-360	LOW VOLTAGE TERMINATE & TRIM AT T-BAR - LOW RISE L1	7	26-Jul-23	03-Aug-23
LOH1-370	FIRE SUPPRESSION HEADS AT T-BAR - LOW RISE L1	2	26-Jul-23	27-Jul-23
LOH1-320	FIRE SUPPRESSION TRIM AT HARDLIDS AND SOFFITS - LOW RISE	1	27-Jul-23	27-Jul-23
LFING1-170	INSTALL SERVICE COUNTER/WINDOW - LOW RISE L1 (REVIEW DU	5	28-Jul-23	03-Aug-23
LOH1-330	MECHANICAL GRILLS AND DIFFUSERS AT HARDLIDS AND SOFFITS	2	28-Jul-23	31-Jul-23
LFING1-190	SET CONTROL ROOM CONSOLE - LOW RISE L1	3	31-Jul-23	02-Aug-23
LFING1-210	PLUMBING FIXTURES - LOW RISE L1	5	31-Jul-23	04-Aug-23
LPG1-1130	INSTALL FLOORING - LOW RISE L1	12	31-Jul-23	15-Aug-23
LRI1-340	INSTALL SEISMIC SUPPORTS - LOW RISE L1	10	04-Aug-23	17-Aug-23
LFING1-300	INSTALL FLOOR BASE - LOW RISE L1	5	08-Aug-23	14-Aug-23
LFING1-240	DOORS & HARDWARE - LOW RISE L1	7	09-Aug-23	17-Aug-23
LFING1-220	ABOVE CEILING INSPECTION AT T-BAR - LOW RISE L1	1	18-Aug-23	18-Aug-23
LPG1-1100	DROP CEILING TILE AT T-BAR - LOW RISE L1	8	21-Aug-23	30-Aug-23
LFING1-100	FLOOR PREP AT LOBBY & PUBLIC GALLERY	4	13-Sep-23	18-Sep-23
LFING1-130	INSTALL FEATURE WALL STONE	10	19-Sep-23	02-Oct-23
LFING1-180	INSTALL FLOOR TILE IN LOBBY AND PUBLIC GALLERY	15	03-Oct-23	23-Oct-23
LPG1-1120	BENCHES / FF&E	15	24-Oct-23	13-Nov-23
LFING1-290	INSTALL FLOOR BASE AT TILE WALLS	5	24-Oct-23	30-Oct-23
LFING1-260	INSTALL SECURITY SCREENING EQUIPMENT	15	24-Oct-23	13-Nov-23
LFING1-310	INSTALL WALL TILE	5	25-Oct-23	31-Oct-23
LFING1-200	INSTALL EDGE GUARDS - LOW RISE L1	2	01-Nov-23	02-Nov-23
LFING1-270	FIRE EXTINGUISHERS CABINETS - LOW RISE L1	2	01-Nov-23	02-Nov-23
LFING1-330	OFOI VISUAL DISPLAY SURFACES - LOW RISE L1	2	14-Nov-23	15-Nov-23
KITCHEN & CAFE				
OVERHEAD ROUGH-INS				
LFINK1-100	FRAME KITCHEN & CAFE- LOW RISE L1	4	17-May-23	22-May-23
LOHK1-100	ROUGH-IN O/H MECHANICAL KITCHEN & CAFE- LOW RISE L1	3	16-Jun-23	20-Jun-23
LOHK1-110	ROUGH-IN O/H PLUMBING KITCHEN & CAFE- LOW RISE L1	4	21-Jun-23	26-Jun-23
LOHK1-120	ROUGH-IN O/H ELECTRICAL KITCHEN & CAFE- LOW RISE L1	4	23-Jun-23	28-Jun-23
LOHK1-130	ROUGH-IN O/H LOW VOLTAGE KITCHEN & CAFE- LOW RISE L1	2	29-Jun-23	30-Jun-23
ROUGH-INS AND FINISHES				
LFINK1-110	TOP DOWN DRYWALL KITCHEN & CAFE- LOW RISE L1	2	23-May-23	24-May-23
LFINK1-130	INSTALL DOOR FRAMES KITCHEN & CAFE- LOW RISE L1	1	23-May-23	23-May-23
LRIK1-100	ROUGH-IN WALL PLUMBING KITCHEN & CAFE- LOW RISE L1	5	25-May-23	02-Jun-23
LRIK1-110	ROUGH-IN WALL ELECTRICAL KITCHEN & CAFE- LOW RISE L1	5	02-Jun-23	08-Jun-23

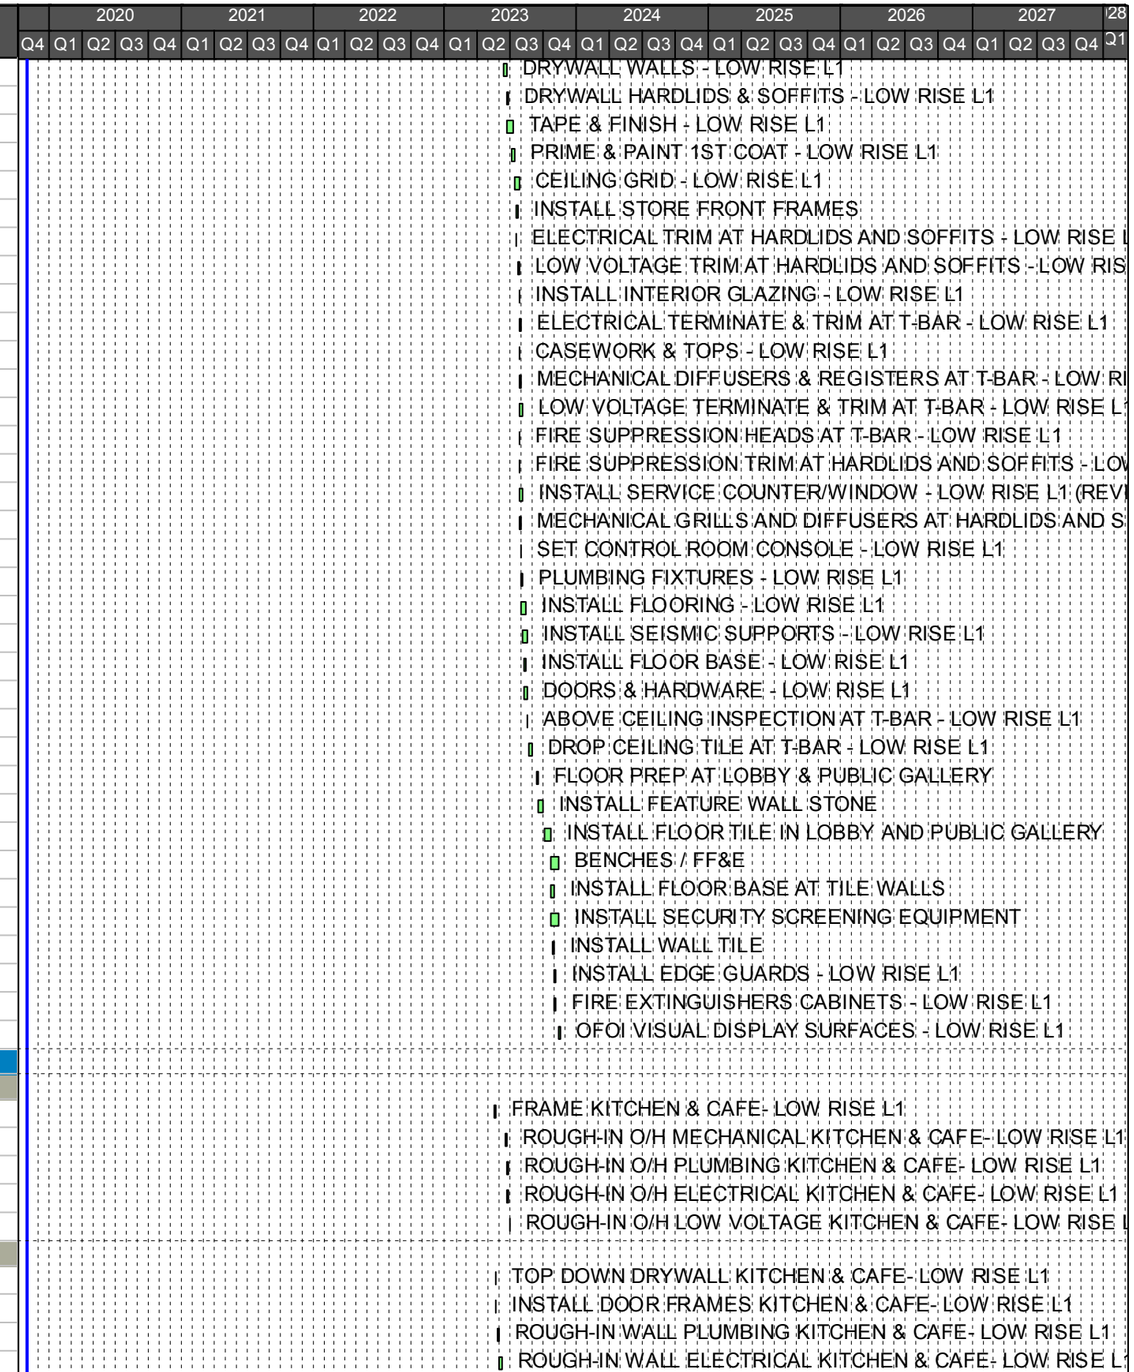

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
LRIK1-120	ROUGH-IN IN WALL MECHANICAL KITCHEN & CAFE- LOW RISE L1	5	09-Jun-23	15-Jun-23
LFINK1-120	WALL BACKING KITCHEN & CAFE- LOW RISE L1	2	16-Jun-23	19-Jun-23
LFINK1-140	INSULATE WALLS KITCHEN & CAFE- LOW RISE L1	1	20-Jun-23	20-Jun-23
LFINK1-260	IN WALL INSPECTION KITCHEN & CAFE- LOW RISE L1	1	21-Jun-23	21-Jun-23
LFINK1-150	DRYWALL KITCHEN & CAFE- LOW RISE L1	3	23-Jun-23	27-Jun-23
LFINK1-160	TAPE & FINISH AND FINISH KITCHEN & CAFE- LOW RISE L1	7	11-Jul-23	19-Jul-23
LFINK1-170	PRIME & PAINT 1ST COAT KITCHEN & CAFE- LOW RISE L1	3	21-Jul-23	25-Jul-23
LFINK1-180	FLOOR PREP AT KITCHEN & CAFE- LOW RISE L1	2	26-Jul-23	27-Jul-23
LFINK1-210	INSTALL WALL PROTECTION KITCHEN & CAFE- LOW RISE L1	3	26-Jul-23	28-Jul-23
LFINK1-190	PULL & TERMINATE ELECTRICAL/ LOW VOLTAGE WIRE	2	28-Jul-23	31-Jul-23
LFINK1-200	INSTALL T-BAR CEILINGS KITCHEN & CAFE- LOW RISE L1	3	28-Jul-23	01-Aug-23
LFINK1-240	INSTALL FLOOR & WALL TILE IN KITCHEN & CAFE- LOW RISE L1	5	31-Jul-23	04-Aug-23
LFINK1-220	ELECTRICAL/LOW VOLTAGE DEVICES KITCHEN & CAFE- LOW RISI	4	02-Aug-23	07-Aug-23
LFINK1-230	MECHANICAL DIFFUSERS & REGISTERS KITCHEN & CAFE- LOW R	2	02-Aug-23	03-Aug-23
LFINK1-250	CASEWORK & TOPS KITCHEN & CAFE- LOW RISE L1	3	07-Aug-23	09-Aug-23
LFINK1-270	FIRE SUPPRESSION HEADS KITCHEN & CAFE- LOW RISE L1	1	10-Aug-23	10-Aug-23
LFINK1-280	PLUMBING FIXTURES KITCHEN & CAFE- LOW RISE L1	4	10-Aug-23	15-Aug-23
LFINK1-290	SET & INSTALL KITCHEN EQUIPMENT KITCHEN & CAFE- LOW RISE	2	10-Aug-23	11-Aug-23
LFINK1-340	INSTALL SEISMIC SUPPORTS KITCHEN & CAFE- LOW RISE L1	10	11-Aug-23	24-Aug-23
LFINK1-300	CONNECT KITCHEN EQUIPMENT KITCHEN & CAFE- LOW RISE L1	4	14-Aug-23	17-Aug-23
LFINK1-310	ABOVE CEILING INSPECTION KITCHEN & CAFE- LOW RISE L1	1	25-Aug-23	25-Aug-23
LFINK1-320	DOORS & HARDWARE KITCHEN & CAFE- LOW RISE L1	7	29-Nov-23	07-Dec-23
LFINK1-330	DROP REMAINING CEILING TILES KITCHEN & CAFE- LOW RISE L1	1	29-Nov-23	29-Nov-23
MULTI-USER RESTROOMS				
LRR1-1000	FRAME WALLS AND CEILINGS RESTROOM- LOW RISE L1	5	23-May-23	31-May-23
LFINR1-150	FRAME HARDLID CEILINGS & SOFFITS RESTROOM - LOW RISE L1	5	01-Jun-23	07-Jun-23
LFINR1-100	FIELD MEASURE FOR TOILET PARTITIONS RESTROOM - LOW RISE	1	01-Jun-23	01-Jun-23
LRIR1-100	ROUGH-IN WALL PLUMBING RESTROOM - LOW RISE L1	5	05-Jun-23	09-Jun-23
LRIR1-110	ROUGH-IN WALL ELECTRICAL RESTROOM - LOW RISE L1	5	09-Jun-23	15-Jun-23
LRIR1-130	ROUGH-IN WALL LOW VOLTAGE RESTROOM - LOW RISE L1	5	09-Jun-23	15-Jun-23
LFINR1-120	WALL BACKING RESTROOM - LOW RISE L1	2	16-Jun-23	19-Jun-23
LFINR1-130	INSULATE WALLS RESTROOM - LOW RISE L1	1	20-Jun-23	20-Jun-23
LRIR1-120	ROUGH-IN MECHANICAL AT HARDLIDS RESTROOM - LOW RISE L1	5	21-Jun-23	27-Jun-23
LFINR1-140	DRYWALL WALLS RESTROOM - LOW RISE L1	2	28-Jun-23	29-Jun-23
LOHR1-110	ROUGH-IN PLUMBING AT HARDLIDS RESTROOM - LOW RISE L1	4	28-Jun-23	03-Jul-23
LOHR1-120	ROUGH-IN ELECTRICAL AT HARDLIDS RESTROOM - LOW RISE L1	4	30-Jun-23	06-Jul-23
LOHR1-130	ROUGH-IN LOW VOLTAGE AT HARDLIDS RESTROOM - LOW RISE L1	2	07-Jul-23	10-Jul-23
T1-R-610	CEILING CLOSE-IN INSPECTION AT HARDLIDS RESTROOM - LOW F	1	07-Jul-23	07-Jul-23
LFINR1-160	DRYWALL HARDLIDS & SOFFITS RESTROOM - LOW RISE L1	3	11-Jul-23	13-Jul-23
LFINR1-170	TAPE & FINISH AND FINISH RESTROOM - LOW RISE L1	7	20-Jul-23	28-Jul-23
LFINR1-180	PRIME & PAINT 1ST COAT RESTROOM - LOW RISE L1	3	01-Aug-23	03-Aug-23
LFINR1-190	FLOOR PREP AT RESTROOM - LOW RISE L1	2	04-Aug-23	07-Aug-23
LFINR1-220	INSTALL FLOOR & WALL TILE IN RESTROOM - LOW RISE L1	9	08-Aug-23	18-Aug-23
LFINR1-230	CASEWORK & TOPS RESTROOM - LOW RISE L1	3	21-Aug-23	23-Aug-23
LFINR1-200	PULL & TERMINATE ELECTRICAL/ LOW VOLTAGE WIRE	2	21-Aug-23	22-Aug-23
LFINR1-210	ELECTRICAL/LOW VOLTAGE TRIM RESTROOM - LOW RISE L1	4	23-Aug-23	28-Aug-23
LFINR1-240	FIRE SUPPRESSION HEADS RESTROOM - LOW RISE L1	1	24-Aug-23	24-Aug-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
LFINR1-250	MECHANICAL DIFFUSERS & REGISTERS RESTROOM - LOW RISE L1	2	24-Aug-23	25-Aug-23
LFINR1-260	PLUMBING FIXTURES RESTROOM - LOW RISE L1	4	28-Aug-23	31-Aug-23
LFINR1-270	DOORS & HARDWARE RESTROOM - LOW RISE L1	3	05-Sep-23	07-Sep-23
LFINR1-280	INSTALL PARTITIONS AND ACCESSORIES RESTROOM - LOW RISE	3	08-Sep-23	12-Sep-23
JURY ASSEMBLY/ WAITING AREA/ LAW OFFICES				
LJA1-1010	FRAME WALLS JURY ASSEMBY & OFFICES EAST - LOW RISE L1	10	01-Jun-23	14-Jun-23
LJA1-1520	ELECTRICAL WALL ROUGH-IN JURY ASSEMBY & OFFICES EAST -	8	01-Jun-23	12-Jun-23
LJA1-1540	LOW VOLTAGE WALL ROUGH-IN JURY ASSEMBY & OFFICES EAST	8	01-Jun-23	12-Jun-23
LJA1-1530	PLUMBING WALL ROUGH-IN JURY ASSEMBY & OFFICES EAST - LO	5	06-Jun-23	12-Jun-23
LJA1-1020	MECHANICAL WALL ROUGH-IN JURY ASSEMBY & OFFICES EAST -	5	15-Jun-23	21-Jun-23
LJA1-1000	OVERHEAD OPERABLE PARTITION SUPPORTS JURY ASSEMBY &	3	15-Jun-23	19-Jun-23
LJA1-1030	FRAME CEILING SOFFITS JURY ASSEMBY & OFFICES EAST - LOW	5	15-Jun-23	21-Jun-23
LRIJ1-100	ROUGH-IN PLUMBING JURY ASSEMBY & OFFICES EAST - LOW RIS	5	15-Jun-23	21-Jun-23
LFINJ1-100	INSTALL DOOR FRAMES JURY ASSEMBY & OFFICES EAST - LOW	3	15-Jun-23	19-Jun-23
LRIJ1-200	ROUGH-IN FIRE SUPPRESSION JURY ASSEMBY & OFFICES EAST	5	15-Jun-23	21-Jun-23
LJA1-1170	FRAME AROUND OPERABLE PARTITION JURY ASSEMBY & OFFICE	5	22-Jun-23	28-Jun-23
LJA1-1050	DRYWALL CEILINGS JURY ASSEMBY & OFFICES EAST - LOW RISE	3	30-Jun-23	05-Jul-23
LJA1-1180	DRYWALL/ SOUND ATTENUATION OPERABLE PARTITION JURY AS	4	30-Jun-23	06-Jul-23
LJA1-1150	TAPE & FINISH CEILINGS JURY ASSEMBY & OFFICES EAST - LOW	5	06-Jul-23	12-Jul-23
LRIJ1-110	ROUGH-IN ELECTRICAL JURY ASSEMBY & OFFICES EAST - LOW F	7	07-Jul-23	17-Jul-23
LJA1-1190	TAPE & FINISH AROUND OPERABLE PARTITION JURY ASSEMBY &	3	07-Jul-23	11-Jul-23
LRIJ1-190	ROUGH-IN LOW VOLTAGE JURY ASSEMBY & OFFICES EAST - LOW	7	07-Jul-23	17-Jul-23
LJA1-1070	INSTALL OVERHEAD OPERABLE PARTITION JURY ASSEMBLY - LO	3	13-Jul-23	17-Jul-23
LRIJ1-120	ROUGH-IN MECHANICAL JURY ASSEMBY & OFFICES EAST - LOW	3	13-Jul-23	17-Jul-23
LRIJ1-210	INSULATE WALLS JURY ASSEMBY & OFFICES EAST - LOW RISE L1	1	18-Jul-23	18-Jul-23
LRIJ1-220	IN WALL INSPECTION JURY ASSEMBY & OFFICES EAST - LOW RIS	1	19-Jul-23	19-Jul-23
LJA1-1040	DRYWALL WALLS JURY ASSEMBY & OFFICES EAST - LOW RISE L1	10	20-Jul-23	02-Aug-23
LJA1-1160	TAPE & FINISH WALLS JURY ASSEMBY & OFFICES EAST - LOW RI	7	31-Jul-23	08-Aug-23
LJA1-1060	PRIME AND FIRST COAT PAINT JURY ASSEMBY & OFFICES EAST	5	09-Aug-23	15-Aug-23
LJA1-1200	PAINT AROUND OPERABLE PARTITION JURY ASSEMBY & OFFICES	1	15-Aug-23	15-Aug-23
LJA1-1080	CEILING GRID / DEVICE TILES JURY ASSEMBY & OFFICES EAST -	5	16-Aug-23	22-Aug-23
LFINJ1-110	FLOOR PREP JURY ASSEMBY & OFFICES EAST - LOW RISE L1	1	16-Aug-23	16-Aug-23
LFINJ1-120	INSTALL FLOOR AND WALL TILE JURY ASSEMBY & OFFICES EAST	6	17-Aug-23	24-Aug-23
LJA1-1100	MECHANICAL CEILING COMPLETION JURY ASSEMBY & OFFICES E	5	23-Aug-23	29-Aug-23
LJA1-1550	ELECTRICAL CEILING COMPLETION JURY ASSEMBY & OFFICES E	5	23-Aug-23	29-Aug-23
LJA1-1560	PLUMBING CEILING COMPLETION JURY ASSEMBY & OFFICES EA	5	23-Aug-23	29-Aug-23
LJA1-1570	FIRE SUPPRESSION CEILING COMPLETION JURY ASSEMBY & OFI	5	23-Aug-23	29-Aug-23
LJA1-1580	LOW VOLTAGE CEILING COMPLETION JURY ASSEMBY & OFFICES	5	23-Aug-23	29-Aug-23
LJA1-1110	CASEWORK / FF&E JURY ASSEMBY & OFFICES EAST - LOW RISE	5	24-Aug-23	30-Aug-23
LFINJ1-130	INSTALL PLUMBING FIXTURES JURY ASSEMBY & OFFICES EAST -	2	25-Aug-23	28-Aug-23
LJA1-1310	INSTALL TOILET ACCESSORIES JURY ASSEMBY & OFFICES EAST	2	30-Aug-23	31-Aug-23
LJA1-1590	ABOVE CEILING INSPECTION JURY ASSEMBY & OFFICES EAST -	1	30-Aug-23	30-Aug-23
LJA1-1130	INSTALL CARPET JURY ASSEMBY & OFFICES EAST - LOW RISE L1	3	31-Aug-23	06-Sep-23
LJA1-1120	DROP BALANCE OF CEILING TILES JURY ASSEMBY & OFFICES EA	3	05-Sep-23	07-Sep-23
LJA1-1140	DOORS AND HARDWARE JURY ASSEMBY & OFFICES EAST - LOW	2	07-Sep-23	08-Sep-23
LEVEL 2				
FULL FLOOR				

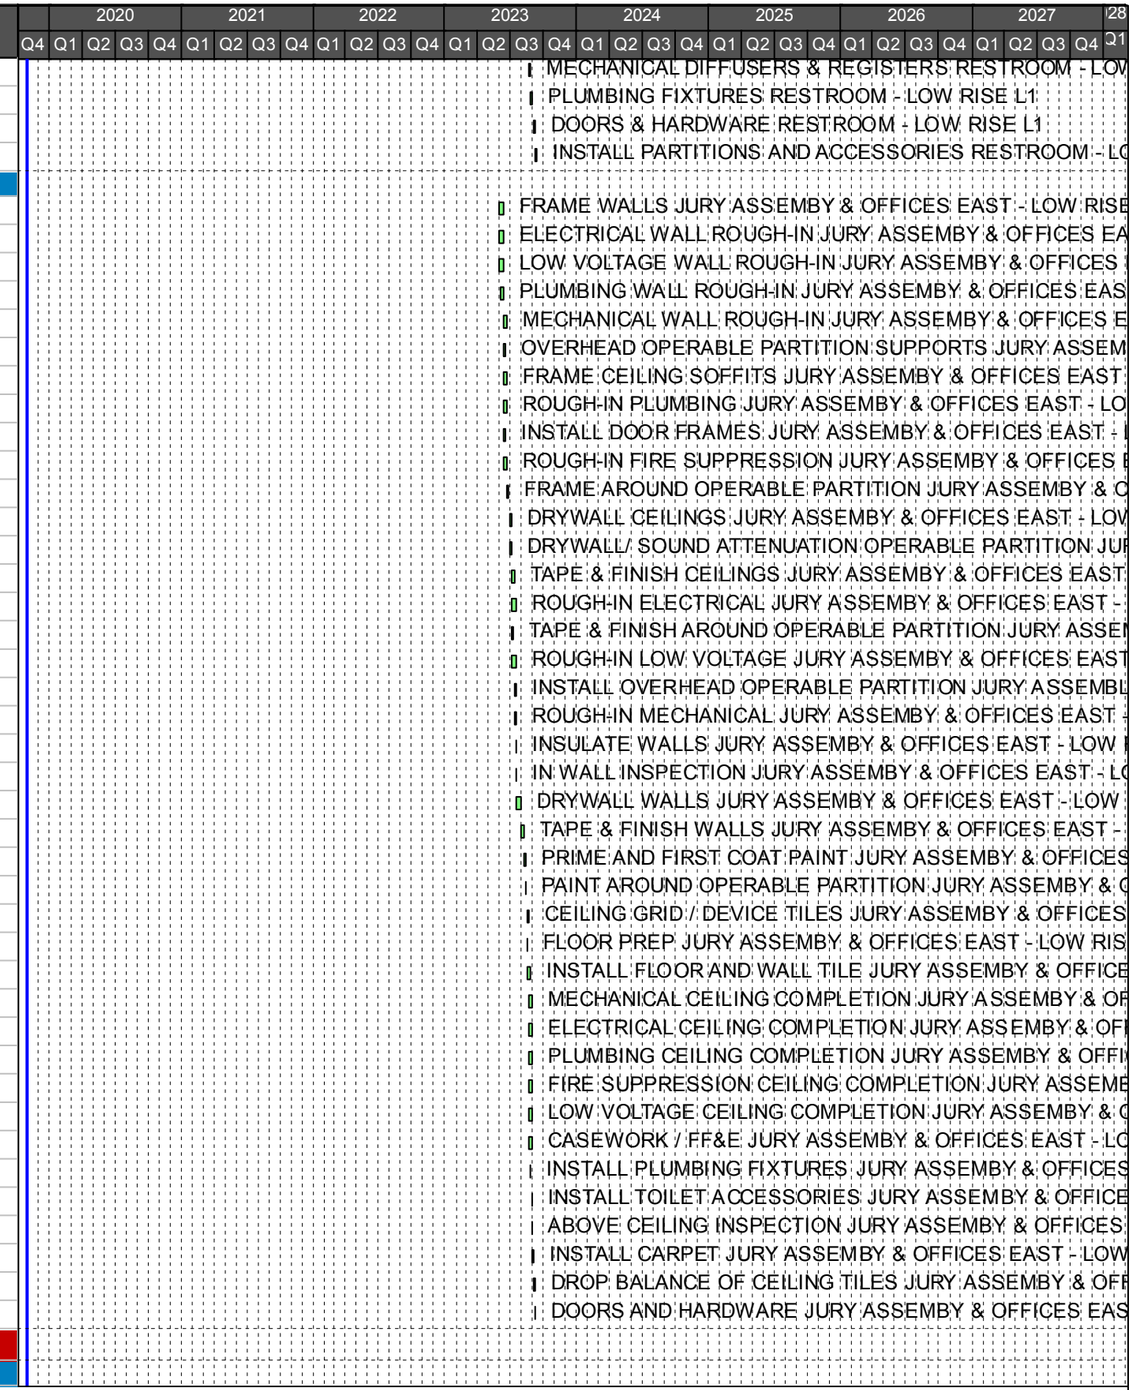

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
TFING1-1390	FIELD MEASURE FOR WINDOW COVERINGS - TOWER L2	1	15-Sep-23	15-Sep-23
L2-G-670	MEASURE & FAB INTERIOR GLASS PUBLIC GALLERY - LOW RISE L2	10	04-Oct-23	17-Oct-23
TFING1-1380	FABRICATE WINDOW COVERINGS - TOWER L1	10	25-Oct-23	07-Nov-23
L2-G-790	INSTALL GLAZING PUBLIC GALLERY - LOW RISE L2	8	27-Oct-23	07-Nov-23
L2-G-820	INSTALL SIGNAGE - LOW RISE L2	5	02-Nov-23	08-Nov-23
L2-G-870	WINDOW COVERINGS PUBLIC GALLERY - LOW RISE L2	4	08-Nov-23	13-Nov-23
L2-G-890	FINAL PAINT - LOW RISE L2	7	21-Nov-23	01-Dec-23
L2-G-900	LOW RISE L2 INT. CERTIFICATION & READY FOR PUNCH	1	06-Dec-23	06-Dec-23
OVERHEAD ROUGH-IN'S				
LS2-100	PRE-WELD EXTERIOR & PARTITION CLIPS - LOW RISE L2	7	15-Feb-23	27-Feb-23
LS2-110	FIREPROOF PRIORITY WALLS/PERIMETER - LOW RISE L2	5	28-Feb-23	06-Mar-23
LS2-130	FIREPROOF BALANCE OF FLOORS - LOW RISE L2	5	07-Mar-23	13-Mar-23
L2-G-410	LAYOUT FOR CLIPS AND TRACK - LOW RISE L2	3	08-Mar-23	10-Mar-23
L2-G-100	INSTALL PLUMBING HANGERS - LOW RISE L2	4	08-Mar-23	13-Mar-23
L2-G-910	INSTALL HVAC HANGERS - LOW RISE L2	4	08-Mar-23	13-Mar-23
L2-G-920	INSTALL ELECTRICAL HANGERS - LOW RISE L2	4	08-Mar-23	13-Mar-23
L2-G-930	INSTALL FIRE SUPPRESSION HANGERS - LOW RISE L2	4	08-Mar-23	13-Mar-23
L2-G-430	FRAME INTERFERENCE WALLS - LOW RISE L2	7	21-Mar-23	29-Mar-23
LOHG2-120	O/H FIRE SUPPRESSION MAINS - LOW RISE L2	5	10-Apr-23	14-Apr-23
LS2-140	EDGE OF SLAB FIRE SAFE	5	25-Apr-23	01-May-23
LPG2-1020	ONE SIDE TIE INTO EXTERIOR - LOW RISE L2	5	02-May-23	08-May-23
LOHG2-100	O/H MECHANICAL MAINS - LOW RISE L2	8	04-May-23	15-May-23
LOHG2-110	O/H ELECTRICAL MAINS - LOW RISE L2	5	05-May-23	11-May-23
LOHG2-240	O/H LOW VOLTAGE MAINS - LOW RISE L2	5	05-May-23	11-May-23
LOHG2-130	O/H PLUMBING MAINS - LOW RISE L2	7	11-May-23	19-May-23
LOHG2-140	O/H MECHANICAL CONTROLS - LOW RISE L2	3	11-May-23	15-May-23
LOHG2-150	O/H HYDRONIC PIPING - LOW RISE L2	5	11-May-23	17-May-23
LOHG2-160	O/H LOW VOLTAGE BRANCHES - LOW RISE L2	5	12-May-23	18-May-23
LOHG2-170	O/H ELECTRICAL BRANCHES - LOW RISE L2	5	12-May-23	18-May-23
LOHG2-190	O/H MECHANICAL BRANCHES - LOW RISE L2	7	16-May-23	24-May-23
LOHG2-230	O/H PLUMBING BRANCHES - LOW RISE L2	5	22-May-23	30-May-23
PRIORITY ROOMS (ELECTRICAL/ IDF/ AV ROOMS)				
IDF/ ELECTRICAL ROOM				
LPR1-1120	FRAME IDF ROOM - LOW RISE L2	5	22-Mar-23	28-Mar-23
LPR1-1130	ROUGH-IN IDF ROOM - LOW RISE L2	5	29-Mar-23	04-Apr-23
LPR1-1140	DRYWALL IDF ROOM - LOW RISE L2	4	03-Aug-23	08-Aug-23
LPR1-1150	TAPE & FINISH IDF ROOM - LOW RISE L2	6	09-Aug-23	16-Aug-23
LPR1-1160	PAINT/SEAL FLOORS IDF ROOM - LOW RISE L2	4	17-Aug-23	22-Aug-23
LPR1-1170	ELECTRICAL AND IDF, PANELS AND RACKS - LOW RISE L2	15	31-Aug-23	22-Sep-23
MEP SHAFTS				
LPR1-1110	INSTALL MEPF IN SHAFTS - LOW RISE L2	8	22-Mar-23	31-Mar-23
LPR1-1100	FRAME HVAC SHAFTS - LOW RISE L2	3	29-Mar-23	31-Mar-23
LPR1-1180	DRYWALL HVAC SHAFTS - LOW RISE L2	3	09-Aug-23	11-Aug-23
LPR1-1190	TAPE & FINISH HVAC SHAFTS - LOW RISE L2	7	17-Aug-23	25-Aug-23
PUBLIC GALLERY				
ROUGH-IN'S				
L2-G-420	INSTALL TOP TRACK INTERFERENCE WALLS PUBLIC GALLERY - L	4	10-Mar-23	15-Mar-23
L2-G-440	TOP TRACK INTERIOR WALLS REMAINING AREAS PUBLIC GALLEF	4	16-Mar-23	21-Mar-23

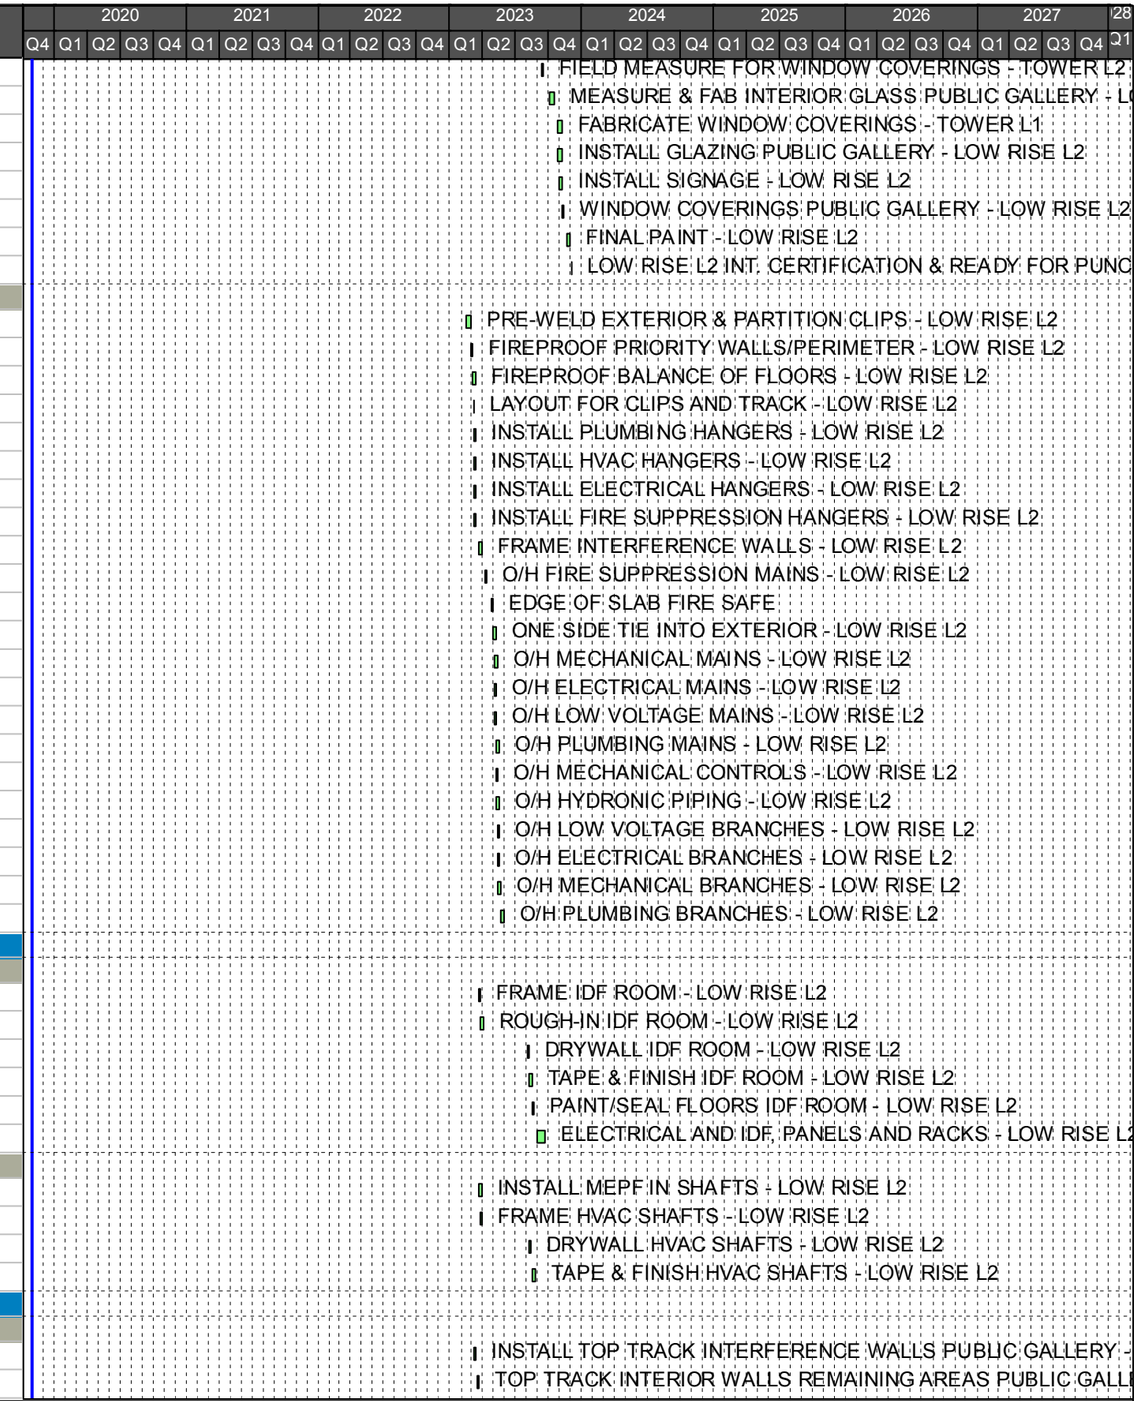

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
L2-G-450	TOP DOWN INTERFERENCE WALLS PUBLIC GALLERY - LOW RISE	5	30-Mar-23	05-Apr-23
L2-G-460	INSPECTION OF INTERFERENCE HEAD OF WALL PUBLIC GALLERY	3	05-Apr-23	07-Apr-23
L2-G-470	FIRE TAPE HEAD OF WALL AT INTERFERENCE WALLS PUBLIC GAI	3	05-Apr-23	07-Apr-23
LOHG2-180	O/H FIRE SUPPRESSION BRANCHES - LOW RISE L2	3	17-Apr-23	19-Apr-23
LPG2-1250	ROUGH-IN FIRE SUPPRESSION GALLERY CEILING PUBLIC GALLEF	3	20-Apr-23	24-Apr-23
LPG2-1010	INSTALL TEMPORARY DECK & DANCE FLOOR FOR GALLERY CEILI	5	17-May-23	23-May-23
LPG2-1070	FRAME WALLS PUBLIC GALLERY - LOW RISE L2	8	15-Jun-23	26-Jun-23
LPG2-1090	FRAME SOFFITS AND CEILINGS PUBLIC GALLERY - LOW RISE L2	7	27-Jun-23	06-Jul-23
LPG2-1040	FRAME GALLERY CEILING PUBLIC GALLERY - LOW RISE L2	10	27-Jun-23	11-Jul-23
L2-G-490	IN WALL COUNTERTOP SUPPORTS PUBLIC GALLERY - LOW RISE I	3	27-Jun-23	29-Jun-23
L2-G-510	ROUGH-IN WALL PLUMBING PUBLIC GALLERY - LOW RISE L2	5	27-Jun-23	03-Jul-23
L2-G-500	HM DOOR FRAMES PUBLIC GALLERY - LOW RISE L2	5	27-Jun-23	03-Jul-23
L2-G-520	ROUGH-IN WALL LOW VOLTAGE PUBLIC GALLERY - LOW RISE L2	8	05-Jul-23	14-Jul-23
L2-G-530	ROUGH-IN WALL ELECTRICAL PUBLIC GALLERY - LOW RISE L2	8	05-Jul-23	14-Jul-23
L2-G-540	ROUGH-IN MECHANICAL CONTROLS PUBLIC GALLERY - LOW RISE	8	07-Jul-23	18-Jul-23
L2-G-590	INSULATE WALLS PUBLIC GALLERY - LOW RISE L2	2	19-Jul-23	20-Jul-23
L2-G-550	WALL BACKING PUBLIC GALLERY - LOW RISE L2	2	21-Jul-23	24-Jul-23
L2-G-580	IN WALL INSPECTION PUBLIC GALLERY - LOW RISE L2	1	25-Jul-23	25-Jul-23
L2-G-260	CEILING CLOSE-IN INSPECTION AT HARDLIDS AND SOFFITS PUBL	1	26-Jul-23	26-Jul-23
FINISHES				
L2-G-840	INSTALL FLOOR BASE PUBLIC GALLERY - LOW RISE L2	5	14-Apr-22	20-Apr-22
LOHG2-210	ROUGH IN LOW VOLTAGE AT HARDLIDS AND SOFFITS PUBLIC GAI	4	19-May-23	24-May-23
LOHG2-220	ROUGH-IN ELECTRICAL AT HARDLIDS AND SOFFITS PUBLIC GALLE	4	24-May-23	31-May-23
LPG2-1240	ROUGH-IN ELECTRICAL GALLERY CEILING PUBLIC GALLERY - LOV	4	01-Jun-23	06-Jun-23
L2-G-250	ROUGH-IN FIRE SUPPRESSION AT HARDLIDS AND SOFFITS PUBLI	2	07-Jul-23	10-Jul-23
LPG2-1230	DRYWALL GALLERY CEILING PUBLIC GALLERY - LOW RISE L2	4	12-Jul-23	17-Jul-23
LOHG2-200	ROUGH-IN MECHANICAL AT HARDLIDS AND SOFFITS PUBLIC GALL	4	18-Jul-23	21-Jul-23
LPG2-1080	DRYWALL WALLS AT HARDLIDS AND SOFFITS PUBLIC GALLERY - I	3	14-Aug-23	16-Aug-23
LPG2-1110	DRYWALL CEILINGS AT HARDLIDS AND SOFFITS PUBLIC GALLERY	3	17-Aug-23	21-Aug-23
L2-G-610	TAPE & FINISH PUBLIC GALLERY - LOW RISE L2	11	22-Aug-23	07-Sep-23
LPG2-1120	PRIME & PAINT 1ST COAT PUBLIC GALLERY - LOW RISE L2	5	08-Sep-23	14-Sep-23
LPG2-1050	REMOVE TEMPORARY DECK & DANCE FLOOR FOR GALLERY CEIL	3	08-Sep-23	12-Sep-23
LPG2-1060	STOREFRONT FRAMES/ GUARDRAIL AT GALLERY OPENING PUBLI	15	13-Sep-23	03-Oct-23
LPG2-1130	CEILING GRID / DEVICE TILES PUBLIC GALLERY - LOW RISE L2	10	15-Sep-23	28-Sep-23
L2-G-630	FLOOR PREP AT LOBBY & PUBLIC GALLERY - LOW RISE L2	4	15-Sep-23	20-Sep-23
L2-G-650	EXPANSION JOINT AT TOWER CONNECTION PUBLIC GALLERY - LC	5	15-Sep-23	21-Sep-23
L2-G-290	ELECTRICAL TERMINATE & TRIM AT HARDLIDS AND SOFFITS PUBI	4	15-Sep-23	20-Sep-23
L2-G-300	LOW VOLTAGE TERMINATE & TRIM AT HARDLIDS AND SOFFITS PU	4	15-Sep-23	20-Sep-23
L2-G-310	FIRE SUPPRESSION TRIM AT HARDLIDS AND SOFFITS PUBLIC GAI	1	15-Sep-23	15-Sep-23
L2-G-320	MECHANICAL GRILLS AND DIFFUSERS AT HARDLIDS AND SOFFITS	2	15-Sep-23	18-Sep-23
L2-G-850	INSTALL FLOOR BASE AT TILE WALLS PUBLIC GALLERY - LOW RIS	5	21-Sep-23	27-Sep-23
L2-G-860	INSTALL WALL TILE PUBLIC GALLERY - LOW RISE L2	5	22-Sep-23	28-Sep-23
LPG2-1140	LIGHT FIXTURES AT CEILINGS/MEP DROPS PUBLIC GALLERY - LO	4	29-Sep-23	04-Oct-23
L2-G-330	ELECTRICAL TERMINATE & TRIM AT T-BAR PUBLIC GALLERY - LOV	6	29-Sep-23	06-Oct-23
L2-G-340	MECHANICAL DIFFUSERS & REGISTERS AT T-BAR PUBLIC GALLEF	4	29-Sep-23	04-Oct-23
L2-G-350	LOW VOLTAGE TERMINATE & TRIM AT T-BAR PUBLIC GALLERY - L	7	29-Sep-23	09-Oct-23
L2-G-360	FIRE SUPPRESSION HEADS AT T-BAR PUBLIC GALLERY - LOW RIS	2	29-Sep-23	02-Oct-23

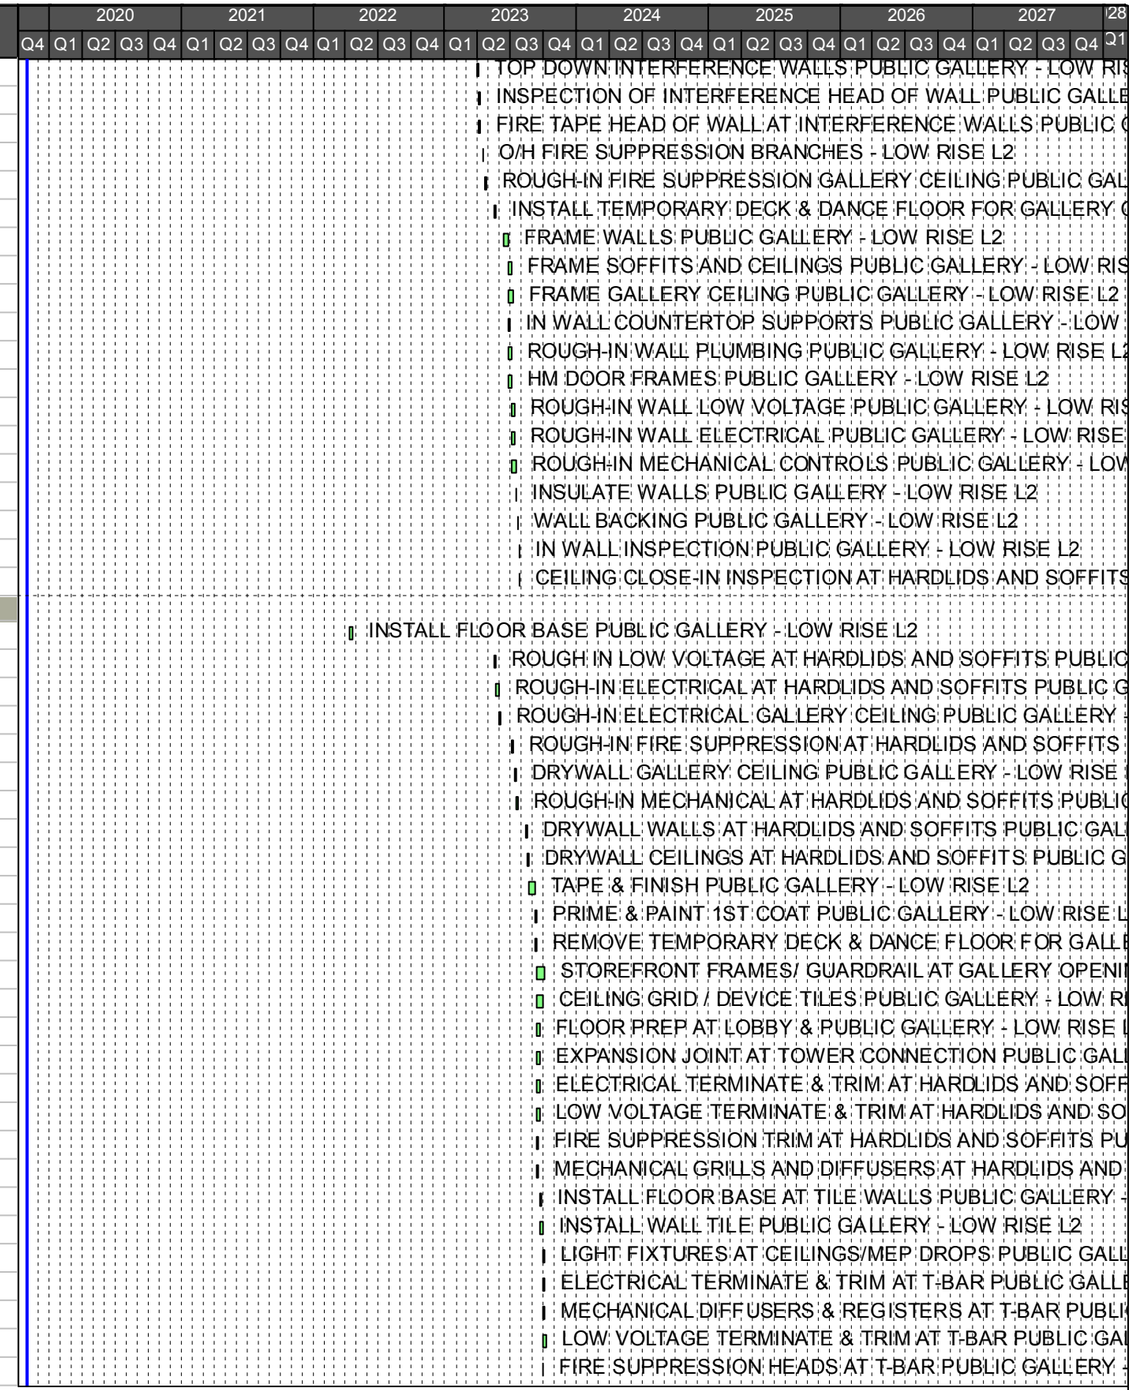

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
LOHG2-250	INSTALL SESIMIC SUPPORTS - LOW RISE L2	10	03-Oct-23	16-Oct-23
LPG2-1170	INSTALL FLOOR TILE IN LOBBY AND PUBLIC GALLERY	10	04-Oct-23	17-Oct-23
L2-G-760	ABOVE CEILING INSPECTION AT T-BAR PUBLIC GALLERY - LOW R	1	17-Oct-23	17-Oct-23
LPG2-1180	BENCHES / FF&E PUBLIC GALLERY - LOW RISE L2	15	18-Oct-23	07-Nov-23
LPG2-1160	DROP CEILING TILES PUBLIC GALLERY - LOW RISE L2	4	18-Oct-23	23-Oct-23
L2-G-690	CASEWORK & TOPS PUBLIC GALLERY - LOW RISE L2	3	18-Oct-23	20-Oct-23
L2-G-700	INSTALL SERVICE COUNTER/WINDOW PUBLIC GALLERY - LOW RI	5	20-Oct-23	26-Oct-23
L2-G-720	INSTALL EDGE GUARDS PUBLIC GALLERY - LOW RISE L2	2	23-Oct-23	24-Oct-23
L2-G-730	PLUMBING FIXTURES PUBLIC GALLERY - LOW RISE L2	5	23-Oct-23	27-Oct-23
L2-G-780	DOORS & HARDWARE PUBLIC GALLERY - LOW RISE L2	7	24-Oct-23	01-Nov-23
L2-G-810	FIRE EXTINGUISHERS CABINETS PUBLIC GALLERY - LOW RISE L2	2	27-Oct-23	30-Oct-23
L2-G-880	OFOI VISUAL DISPLAY SURFACES PUBLIC GALLERY - LOW RISE L2	2	04-Dec-23	05-Dec-23
STAFF RESTROOMS				
LRR2-1000	FRAME STAFF RESTROOM - LOW RISE RESTROOM	8	27-Jun-23	07-Jul-23
LRIR2-100	ROUGH-IN WALL PLUMBING RESTROOM - LOW RISE L2	5	10-Jul-23	14-Jul-23
LRIR2-110	ROUGH-IN WALL ELECTRICAL RESTROOM - LOW RISE L2	5	17-Jul-23	21-Jul-23
LRIR2-120	ROUGH-IN MECHANICAL AT HARDLIDS RESTROOM - LOW RISE L2	5	24-Jul-23	28-Jul-23
T1-R-1460	WALL BACKING RESTROOM - LOW RISE L2	2	31-Jul-23	01-Aug-23
T1-R-1470	INSULATE WALLS RESTROOM - LOW RISE L2	1	02-Aug-23	02-Aug-23
T1-R-1480	DRYWALL WALLS RESTROOM - LOW RISE L2	2	17-Aug-23	18-Aug-23
T1-R-1500	DRYWALL HARDLIDS & SOFFITS RESTROOM - LOW RISE L2	3	18-Aug-23	22-Aug-23
T1-R-1490	FRAME HARDLID CEILINGS & SOFFITS RESTROOM - LOW RISE L2	5	21-Aug-23	25-Aug-23
TJD2-1310	FIELD MEASURE FOR TOILET PARTITIONS	1	23-Aug-23	23-Aug-23
TJD2-1320	FABRICATE TOILET PARTITIONS	30	24-Aug-23	06-Oct-23
T1-R-1510	TAPE & FINISH RESTROOM - LOW RISE L2	7	08-Sep-23	18-Sep-23
T1-R-1520	PRIME & PAINT 1ST COAT RESTROOM - LOW RISE L2	3	20-Sep-23	22-Sep-23
T1-R-1530	FLOOR PREP AT RESTROOM	2	25-Sep-23	26-Sep-23
T1-R-1540	PULL & TERMINATE ELECTRICAL/ LOW VOLTAGE WIRE	2	25-Sep-23	26-Sep-23
L1-R-1550	ELECTRICAL/FIRE ALARM FINISH/DEVICES RESTROOM - LOW RIS	4	27-Sep-23	02-Oct-23
T1-R-1560	INSTALL FLOOR & WALL TILE IN RESTROOM	9	27-Sep-23	09-Oct-23
T1-R-1570	CASEWORK & TOPS RESTROOM - LOW RISE L2	3	23-Oct-23	25-Oct-23
T1-R-1580	FIRE SUPPRESSION HEADS RESTROOM - LOW RISE L2	1	26-Oct-23	26-Oct-23
T1-R-1590	MECHANICAL DIFFUSERS & REGISTERS RESTROOM - LOW RISE L2	2	26-Oct-23	27-Oct-23
T1-R-1600	PLUMBING FIXTURES RESTROOM - LOW RISE L2	4	30-Oct-23	02-Nov-23
T1-R-1610	DOORS & HARDWARE RESTROOM - LOW RISE L2	2	03-Nov-23	06-Nov-23
T1-R-1620	INSTALL PARTITIONS AND ACCESSORIES RESTROOM - LOW RISE	5	08-Nov-23	14-Nov-23
COURT OFFICES				
LJA1-1210	FRAME WALLS OFFICE SPACES - LOW RISE L2	10	10-Jul-23	21-Jul-23
LJA1-1330	FRAME SOFFIT OFFICE SPACES - LOW RISE L2	5	24-Jul-23	28-Jul-23
LRIJ1-150	ROUGH-IN PLUMBING OFFICE SPACES - LOW RISE L2	5	24-Jul-23	28-Jul-23
LFINJ1-170	INSTALL DOOR FRAMES OFFICE SPACES - LOW RISE L2	3	24-Jul-23	26-Jul-23
LRIJ1-250	ROUGH-IN FIRE SUPPRESSION OFFICE SPACES - LOW RISE L2	5	24-Jul-23	28-Jul-23
LRIJ1-140	ROUGH-IN ELECTRICAL OFFICE SPACES - LOW RISE L2	7	25-Jul-23	02-Aug-23
LRIJ1-240	ROUGH-IN LOW VOLTAGE OFFICE SPACES - LOW RISE L2	7	25-Jul-23	02-Aug-23
LRIJ1-130	ROUGH-IN MECHANICAL OFFICE SPACES - LOW RISE L2	3	31-Jul-23	02-Aug-23
LRIJ1-230	IN WALL INSPECTION OFFICE SPACES - LOW RISE L2	1	03-Aug-23	03-Aug-23
LJA1-1230	DRYWALL WALLS OFFICE SPACES - LOW RISE L2	12	21-Aug-23	07-Sep-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
LJA1-1340	DRYWALL SOFFIT OFFICE SPACES - LOW RISE L2	3	05-Sep-23	07-Sep-23
LJA1-1370	TAPE & FINISH WALLS OFFICE SPACES - LOW RISE L2	10	19-Sep-23	02-Oct-23
LJA1-1360	TAPE & FINISH SOFFIT OFFICE SPACES - LOW RISE L2	5	26-Sep-23	02-Oct-23
LJA1-1240	PRIME AND FIRST COAT PAINT OFFICE SPACES - LOW RISE L2	5	03-Oct-23	09-Oct-23
LJA1-1250	CEILING GRID / DEVICE TILES OFFICE SPACES - LOW RISE L2	9	10-Oct-23	20-Oct-23
LPG2-1100	ACCESS FLOORING - LOW RISE L2	4	23-Oct-23	26-Oct-23
LJA1-1260	COMPLETE MECHANICAL OFFICE SPACES - LOW RISE L2	5	23-Oct-23	27-Oct-23
LJA1-1600	COMPLETE ELECTRICAL OFFICE SPACES - LOW RISE L2	5	23-Oct-23	27-Oct-23
LJA1-1610	COMPLETE PLUMBING OFFICE SPACES - LOW RISE L2	5	23-Oct-23	27-Oct-23
LJA1-1620	COMPLETE FIRE SUPPRESSION OFFICE SPACES - LOW RISE L2	5	23-Oct-23	27-Oct-23
LJA1-1630	COMPLETE LOW VOLTAGE OFFICE SPACES - LOW RISE L2	5	23-Oct-23	27-Oct-23
LJA1-1280	CASEWORK / FF&E OFFICE SPACES - LOW RISE L2	5	27-Oct-23	02-Nov-23
LJA1-1640	ABOVE CEILING INSPECTION- LOW RISE L2	1	30-Oct-23	30-Oct-23
LJA1-1270	DROP BALANCE OF CEILING TILES OFFICE SPACES - LOW RISE L2	3	31-Oct-23	02-Nov-23
LJA1-1290	INSTALL CARPET OFFICE SPACES - LOW RISE L2	8	03-Nov-23	14-Nov-23
LFINJ1-180	INSTALL PLUMBING FIXTURES OFFICE SPACES - LOW RISE L2	3	03-Nov-23	07-Nov-23
LJA1-1300	DOORS AND HARDWARE OFFICE SPACES - LOW RISE L2	4	15-Nov-23	20-Nov-23
LEVEL 3				
FULL FLOOR				
TFING1-1410	FIELD MEASURE FOR WINDOW COVERINGS - TOWER L1	1	25-Oct-23	25-Oct-23
L3-G-620	MEASURE & FAB INTERIOR GLASS PUBLIC GALLERY - LOW RISE L3	10	02-Nov-23	15-Nov-23
TFING1-1400	FABRICATE WINDOW COVERINGS - TOWER L1	10	27-Nov-23	08-Dec-23
L3-G-790	INSTALL GLAZING PUBLIC GALLERY - LOW RISE L3	8	29-Nov-23	08-Dec-23
L3-G-820	INSTALL SIGNAGE - LOW RISE L3	5	05-Dec-23	11-Dec-23
L3-G-870	WINDOW COVERINGS PUBLIC GALLERY - LOW RISE L3	4	11-Dec-23	14-Dec-23
L3-G-890	FINAL PAINT - LOW RISE L3	7	03-Jan-24	11-Jan-24
OVERHEAD ROUGH-IN'S				
LS3-100	PRE-WELD EXTERIOR & PARTITION CLIPS - LOW RISE L3	7	14-Feb-23	24-Feb-23
LS3-110	FIREPROOF PRIORITY WALLS/PERIMETER - LOW RISE L3	5	07-Mar-23	13-Mar-23
LS3-120	FIREPROOF BALANCE OF FLOORS - LOW RISE L3	5	14-Mar-23	20-Mar-23
L3-G-130	LAYOUT FOR CLIPS AND TRACK - LOW RISE L3	3	21-Mar-23	23-Mar-23
L3-G-140	INSTALL ELECTRICAL HANGERS - LOW RISE L3	4	21-Mar-23	24-Mar-23
L3-G-910	INSTALL FIRE SUPPRESSION HANGERS - LOW RISE L3	4	21-Mar-23	24-Mar-23
L3-G-150	INSTALL TOP TRACK INTERFERENCE WALLS - LOW RISE L3	4	22-Mar-23	27-Mar-23
L3-G-170	TOP TRACK INTERIOR WALLS REMAINING AREAS - LOW RISE L3	4	28-Mar-23	31-Mar-23
L3-G-160	FRAME INTERFERENCE WALLS - LOW RISE L3	7	30-Mar-23	07-Apr-23
L3-G-180	TOP DOWN INTERFERENCE WALLS - LOW RISE L3	5	10-Apr-23	14-Apr-23
L3-G-190	INSPECTION OF INTERFERENCE HEAD OF WALL- LOW RISE L3	3	14-Apr-23	18-Apr-23
L3-G-200	FIRE TAPE HEAD OF WALL AT INTERFERENCE WALLS - LOW RISE	3	14-Apr-23	18-Apr-23
LOHG3-120	O/H FIRE SUPPRESSION MAINS - LOW RISE L3	5	19-Apr-23	25-Apr-23
LS3-140	EDGE OF SLAB FIRE SAFE - LOW RISE L3	5	25-Apr-23	01-May-23
LOHG3-180	O/H FIRE SUPPRESSION BRANCHES - LOW RISE L3	3	26-Apr-23	28-Apr-23
LPG3-1000	ONE SIDE TIE INTO EXTERIOR - LOW RISE L3	5	09-May-23	15-May-23
LOHG3-110	O/H ELECTRICAL MAINS - LOW RISE L3	5	12-May-23	18-May-23
LOHG3-210	O/H LOW VOLTAGE MAINS - LOW RISE L3	5	12-May-23	18-May-23
LOHG3-100	O/H MECHANICAL MAINS - LOW RISE L3	8	16-May-23	25-May-23
LOHG3-160	O/H LOW VOLTAGE BRANCHES - LOW RISE L3	5	23-May-23	31-May-23

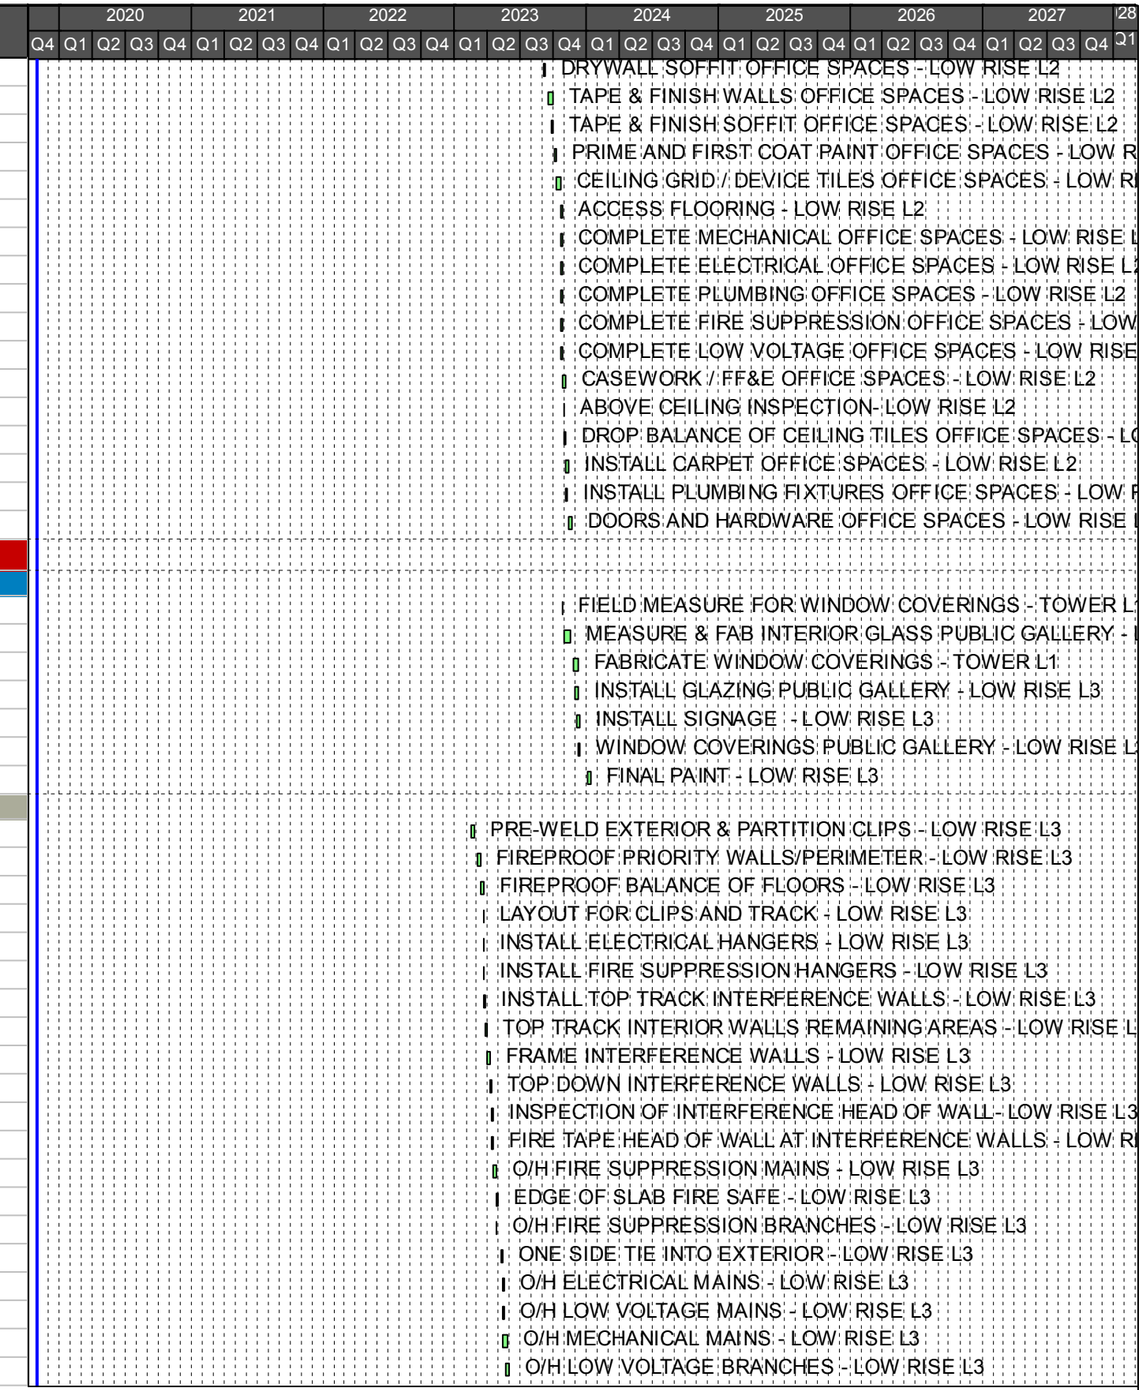

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
LOHG3-140	O/H MECHANICAL CONTROLS - LOW RISE L3	3	23-May-23	25-May-23
LOHG3-150	O/H HYDRONIC PIPING - LOW RISE L3	5	23-May-23	31-May-23
LOHG3-170	O/H ELECTRICAL BRANCHES - LOW RISE L3	5	23-May-23	31-May-23
LOHG3-130	O/H PLUMBING MAINS - LOW RISE L3	7	31-May-23	08-Jun-23
LOHG3-200	O/H PLUMBING BRANCHES - LOW RISE L3	5	09-Jun-23	15-Jun-23
LOHG3-190	O/H MECHANICAL BRANCHES - LOW RISE L3	7	07-Aug-23	15-Aug-23
PRIORITY ROOMS (ELECTRICAL/ IDF/ AV ROOMS)				
IDF/ ELECTRICAL ROOM/ SERVER/ MDF				
LPR3-1010	FRAME MDF / UPS / COMPUTER ROOMS - LOW RISE L3	4	16-May-23	19-May-23
LPR3-1030	ROUGH-IN MDF / UPS / COMPUTER ROOMS - LOW RISE L3	5	22-May-23	30-May-23
LPR3-1040	DRYWALL MDF/UPS COMPUTER ROOMS - LOW RISE L3	8	08-Sep-23	19-Sep-23
LPR3-1080	TAPE & FINISH MDF/UPS COMPUTER ROOMS - LOW RISE L3	10	13-Sep-23	26-Sep-23
LPR3-1090	PAINT/SEAL FLOORS MDF/UPS COMPUTER ROOMS - LOW RISE L3	3	27-Sep-23	29-Sep-23
LPR3-1050	ELECTRICAL AND IDF, PANELS AND RACKS - LOW RISE L3	15	11-Oct-23	31-Oct-23
MEP SHAFTS				
LPR3-1020	INSTALL MEPF IN SHAFTS - LOW RISE L3	8	03-Apr-23	12-Apr-23
LPR3-1000	FRAME HVAC SHAFTS - LOW RISE L3	3	16-May-23	18-May-23
LPR3-1060	DRYWALL HVAC SHAFTS - LOW RISE L3	3	20-Sep-23	22-Sep-23
LPR3-1070	TAPE & FINISH HVAC SHAFTS - LOW RISE L3	7	27-Sep-23	05-Oct-23
PUBLIC GALLERY				
ROUGH-IN'S				
L3-G-240	FRAME INTERIOR WALLS - LOW RISE L3	10	24-Jul-23	04-Aug-23
L3-G-290	IN WALL COUNTERTOP SUPPORTS PUBLIC GALLERY - LOW RISE	3	26-Jul-23	28-Jul-23
L3-G-320	HM DOOR FRAMES PUBLIC GALLERY - LOW RISE L3	5	31-Jul-23	04-Aug-23
LPG3-1020	FRAME CEILINGS PUBLIC GALLERY - LOW RISE L3	8	07-Aug-23	16-Aug-23
L3-G-420	FRAME HARDLID CEILINGS & SOFFITS PUBLIC GALLERY - LOW RI	7	07-Aug-23	15-Aug-23
L3-G-450	ROUGH-IN ELECTRICAL AT HARDLIDS AND SOFFITS PUBLIC GALLE	4	16-Aug-23	21-Aug-23
L3-G-460	ROUGH-IN MECHANICAL AT HARDLIDS AND SOFFITS PUBLIC GALL	4	16-Aug-23	21-Aug-23
L3-G-470	ROUGH IN LOW VOLTAGE AT HARDLIDS AND SOFFITS PUBLIC GAL	4	16-Aug-23	21-Aug-23
L3-G-480	FIRE SUPPRESSION HEADS AT HARDLIDS AND SOFFITS PUBLIC G	2	16-Aug-23	17-Aug-23
L3-G-330	ROUGH-IN WALL PLUMBING PUBLIC GALLERY - LOW RISE L3	5	24-Aug-23	30-Aug-23
L3-G-340	ROUGH-IN WALL LOW VOLTAGE PUBLIC GALLERY - LOW RISE L3	8	31-Aug-23	13-Sep-23
L3-G-360	ROUGH-IN WALL ELECTRICAL PUBLIC GALLERY - LOW RISE L3	8	31-Aug-23	13-Sep-23
L3-G-370	ROUGH-IN MECHANICAL CONTROLS PUBLIC GALLERY - LOW RISE	8	06-Sep-23	15-Sep-23
L3-G-390	WALL FRAMING INSPECTION PUBLIC GALLERY - LOW RISE L3	1	25-Sep-23	25-Sep-23
L3-G-490	CEILING CLOSE-IN INSPECTION AT HARDLIDS AND SOFFITS PUBL	1	25-Sep-23	25-Sep-23
FINISHES				
LPG3-1130	BENCHES / FF&E PUBLIC GALLERY - LOW RISE L3	15	01-Apr-22	21-Apr-22
L3-G-600	FIRE SUPPRESSION TRIM AT HARDLIDS AND SOFFITS PUBLIC GAL	1	18-Aug-23	18-Aug-23
L3-G-580	ELECTRICAL TERMINATE & TRIM AT HARDLIDS AND SOFFITS PUBL	4	22-Aug-23	25-Aug-23
L3-G-590	LOW VOLTAGE TERMINATE & TRIM AT HARDLIDS AND SOFFITS PU	4	22-Aug-23	25-Aug-23
L3-G-610	MECHANICAL GRILLS AND DIFFUSERS AT HARDLIDS AND SOFFITS	2	22-Aug-23	23-Aug-23
L3-G-380	WALL BACKING PUBLIC GALLERY - LOW RISE L3	8	11-Sep-23	20-Sep-23
L3-G-430	INSULATE WALLS PUBLIC GALLERY - LOW RISE L3	2	21-Sep-23	22-Sep-23
LPG3-1030	DRYWALL CEILINGS PUBLIC GALLERY - LOW RISE L3	4	26-Sep-23	29-Sep-23
L3-G-210	DRYWALL WALLS PUBLIC GALLERY - LOW RISE L3	10	26-Sep-23	09-Oct-23
LPG3-1150	TAPE & FINISH WALLS & SOFFIT PUBLIC GALLERY - LOW RISE L3	7	03-Oct-23	11-Oct-23
LPG3-1050	ACCESS FLOORING AT PUBLIC COUNTER PUBLIC GALLERY - LOW	4	12-Oct-23	17-Oct-23

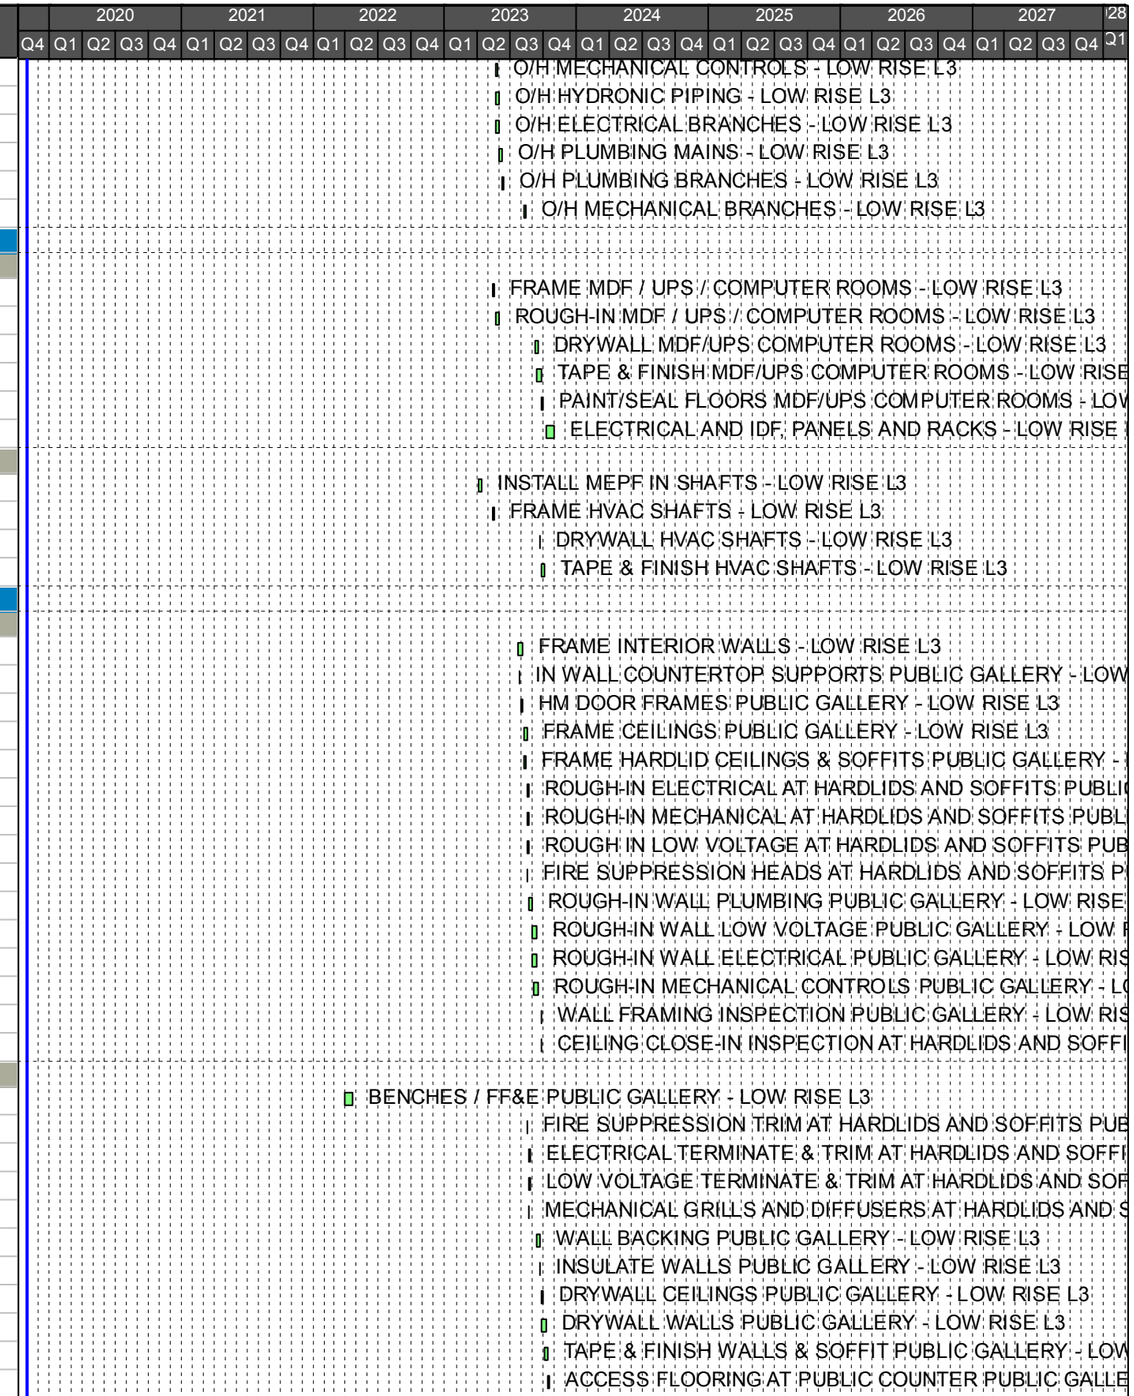

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
LPG3-1070	PAINT WALLS/CEILINGS PUBLIC GALLERY - LOW RISE L3	5	18-Oct-23	24-Oct-23
LPG3-1080	CEILING GRID / DEVICE TILES PUBLIC GALLERY - LOW RISE L3	10	25-Oct-23	07-Nov-23
L3-G-530	CEILING GRID PUBLIC GALLERY - LOW RISE L3	10	25-Oct-23	07-Nov-23
L3-G-550	INSTALL STORE FRONT FRAMES	6	25-Oct-23	01-Nov-23
L3-G-630	INSTALL STORE FRONT GLAZING	2	02-Nov-23	03-Nov-23
L3-G-740	INSTALL FLOOR TILE IN LOBBY AND PUBLIC GALLERY	15	06-Nov-23	28-Nov-23
LPG3-1090	LIGHT FIXTURES AT CEILINGS/MEP DROPS PUBLIC GALLERY - LO	4	08-Nov-23	13-Nov-23
LPG3-1100	WALL FINISHES PUBLIC GALLERY - LOW RISE L3	10	08-Nov-23	21-Nov-23
L3-G-640	ELECTRICAL TERMINATE & TRIM AT T-BAR PUBLIC GALLERY - LOV	6	08-Nov-23	15-Nov-23
L3-G-650	CASEWORK & TOPS PUBLIC GALLERY - LOW RISE L3	3	08-Nov-23	10-Nov-23
L3-G-660	MECHANICAL DIFFUSERS & REGISTERS AT T-BAR PUBLIC GALLEF	4	08-Nov-23	13-Nov-23
L3-G-670	LOW VOLTAGE TERMINATE & TRIM AT T-BAR PUBLIC GALLERY - L	7	08-Nov-23	16-Nov-23
L3-G-680	FIRE SUPPRESSION HEADS AT T-BAR PUBLIC GALLERY - LOW RIS	2	08-Nov-23	09-Nov-23
L3-G-690	INSTALL SERVICE COUNTER/WINDOW PUBLIC GALLERY - LOW RI	5	10-Nov-23	16-Nov-23
L3-G-700	SET CONTROL ROOM CONSOLE PUBLIC GALLERY - LOW RISE L3	3	13-Nov-23	15-Nov-23
L3-G-710	INSTALL EDGE GUARDS PUBLIC GALLERY - LOW RISE L3	2	13-Nov-23	14-Nov-23
L3-G-720	PLUMBING FIXTURES PUBLIC GALLERY - LOW RISE L3	5	13-Nov-23	17-Nov-23
L3-G-730	INSTALL FLOORING PUBLIC GALLERY - LOW RISE L3	12	13-Nov-23	30-Nov-23
LPG3-1110	DROP CEILING TILES PUBLIC GALLERY - LOW RISE L3	4	14-Nov-23	17-Nov-23
L3-G-760	INSTALL SEISMIC SUPPORTS - LOW RISE L2	10	17-Nov-23	04-Dec-23
L3-G-840	INSTALL FLOOR BASE PUBLIC GALLERY - LOW RISE L3	5	21-Nov-23	29-Nov-23
LPG3-1140	MEP TRIM PUBLIC GALLERY - LOW RISE L3	15	22-Nov-23	14-Dec-23
L3-G-780	DOORS & HARDWARE PUBLIC GALLERY - LOW RISE L3	7	22-Nov-23	04-Dec-23
L3-G-830	BENCHES / FF&E	15	29-Nov-23	19-Dec-23
L3-G-850	INSTALL FLOOR BASE AT TILE WALLS	5	29-Nov-23	05-Dec-23
L3-G-860	INSTALL WALL TILE	5	30-Nov-23	06-Dec-23
L3-G-750	ABOVE CEILING INSPECTION AT T-BAR PUBLIC GALLERY - LOW R	1	05-Dec-23	05-Dec-23
L3-G-770	DROP CEILING TILE AT T-BAR PUBLIC GALLERY - LOW RISE L3	8	06-Dec-23	15-Dec-23
L3-G-810	FIRE EXTINGUISHERS CABINETS PUBLIC GALLERY - LOW RISE L3	2	18-Dec-23	19-Dec-23
L3-G-880	OFOI VISUAL DISPLAY SURFACES PUBLIC GALLERY - LOW RISE L3	2	20-Dec-23	21-Dec-23
L3-G-900	LOW RISE L3 INT. CERTIFICATION & READY FOR PUNCH	1	12-Jan-24	12-Jan-24
STAFF RESTROOMS				
LRR3-1000	FRAME STAFF RESTROOM - LOW RISE L3	8	07-Aug-23	16-Aug-23
T1-R-1200	ROUGH-IN WALL PLUMBING RESTROOM - LOW RISE L3	5	17-Aug-23	23-Aug-23
TJD2-1330	FIELD MEASURE FOR TOILET PARTITIONS	1	17-Aug-23	17-Aug-23
TJD2-1340	FABRICATE TOILET PARTITIONS RESTROOM - LOW RISE L3	30	18-Aug-23	02-Oct-23
T1-R-1210	ROUGH-IN WALL ELECTRICAL RESTROOM - LOW RISE L3	5	24-Aug-23	30-Aug-23
T1-R-1220	ROUGH-IN MECHANICAL AT HARDLIDS RESTROOM - LOW RISE L3	5	31-Aug-23	08-Sep-23
T1-R-1230	WALL BACKING RESTROOM - LOW RISE L3	2	31-Aug-23	05-Sep-23
T1-R-1240	INSULATE WALLS RESTROOM - LOW RISE L3	1	06-Sep-23	06-Sep-23
T1-R-1250	DRYWALL WALLS RESTROOM - LOW RISE L3	2	10-Oct-23	11-Oct-23
T1-R-1260	FRAME HARDLID CEILINGS & SOFFITS RESTROOM - LOW RISE L3	5	12-Oct-23	18-Oct-23
T1-R-1270	DRYWALL HARDLIDS & SOFFITS RESTROOM - LOW RISE L3	3	12-Oct-23	16-Oct-23
T1-R-1280	TAPE & FINISH RESTROOM - LOW RISE L3	7	17-Oct-23	25-Oct-23
T1-R-1290	PRIME & PAINT 1ST COAT RESTROOM - LOW RISE L3	3	27-Oct-23	31-Oct-23
T1-R-1300	FLOOR PREP AT RESTROOM - LOW RISE L3	2	01-Nov-23	02-Nov-23
T1-R-1310	PULL & TERMINATE ELECTRICAL/ LOW VOLTAGE WIRE	2	01-Nov-23	02-Nov-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
L1-R-1320	ELECTRICAL/FIRE ALARM FINISH/DEVICES RESTROOM - LOW RIS	4	03-Nov-23	08-Nov-23
T1-R-1330	INSTALL FLOOR & WALL TILE IN RESTROOM - LOW RISE L3	9	03-Nov-23	15-Nov-23
T1-R-1340	CASEWORK & TOPS RESTROOM - LOW RISE L3	3	16-Nov-23	20-Nov-23
T1-R-1350	FIRE SUPPRESSION HEADS RESTROOM - LOW RISE L3	1	21-Nov-23	21-Nov-23
T1-R-1360	MECHANICAL DIFFUSERS & REGISTERS RESTROOM - LOW RISE L3	2	21-Nov-23	22-Nov-23
T1-R-1370	PLUMBING FIXTURES RESTROOM - LOW RISE L3	4	27-Nov-23	30-Nov-23
T1-R-1380	DOORS & HARDWARE RESTROOM - LOW RISE L3	2	01-Dec-23	04-Dec-23
T1-R-1390	INSTALL PARTITIONS AND ACCESSORIES RESTROOM - LOW RISE	5	06-Dec-23	12-Dec-23
COURT OFFICES				
LJA1-1380	FRAME WALLS OFFICE SPACES - LOW RISE L3	10	17-Aug-23	30-Aug-23
LJA1-1470	FRAME SOFFIT OFFICE SPACES - LOW RISE L3	5	31-Aug-23	08-Sep-23
LRIJ1-180	ROUGH-IN PLUMBING OFFICE SPACES - LOW RISE L3	5	31-Aug-23	08-Sep-23
LFINJ1-200	INSTALL DOOR FRAMES OFFICE SPACES - LOW RISE L3	3	31-Aug-23	06-Sep-23
LRIJ1-280	ROUGH-IN FIRE SUPPRESSION OFFICE SPACES - LOW RISE L3	5	31-Aug-23	08-Sep-23
LRIJ1-170	ROUGH-IN ELECTRICAL OFFICE SPACES - LOW RISE L3	7	05-Sep-23	13-Sep-23
LRIJ1-270	ROUGH-IN LOW VOLTAGE OFFICE SPACES - LOW RISE L3	7	05-Sep-23	13-Sep-23
LRIJ1-160	ROUGH-IN MECHANICAL OFFICE SPACES - LOW RISE L3	3	11-Sep-23	13-Sep-23
LRIJ1-260	IN WALL INSPECTION OFFICE SPACES - LOW RISE L3	1	14-Sep-23	14-Sep-23
LJA1-1390	DRYWALL WALLS OFFICE SPACES - LOW RISE L3	12	12-Oct-23	27-Oct-23
LJA1-1500	TAPE & FINISH WALLS OFFICE SPACES - LOW RISE L3	10	26-Oct-23	08-Nov-23
LJA1-1480	DRYWALL SOFFIT OFFICE SPACES - LOW RISE L3	3	30-Oct-23	01-Nov-23
LJA1-1490	TAPE & FINISH SOFFIT OFFICE SPACES - LOW RISE L3	5	02-Nov-23	08-Nov-23
LJA1-1400	PRIME AND FIRST COAT PAINT OFFICE SPACES - LOW RISE L3	5	09-Nov-23	15-Nov-23
LJA1-1410	CEILING GRID / DEVICE TILES OFFICE SPACES - LOW RISE L3	9	16-Nov-23	30-Nov-23
LPG2-1220	ACCESS FLOORING - LOW RISE L3	4	01-Dec-23	06-Dec-23
LJA1-1420	COMPLETE MECHANICAL OFFICE SPACES - LOW RISE L3	5	01-Dec-23	07-Dec-23
LJA1-1650	COMPLETE ELECTRICAL OFFICE SPACES - LOW RISE L3	5	01-Dec-23	07-Dec-23
LJA1-1660	COMPLETE PLUMBING OFFICE SPACES - LOW RISE L3	5	01-Dec-23	07-Dec-23
LJA1-1670	COMPLETE FIRE SUPPRESSION OFFICE SPACES - LOW RISE L3	5	01-Dec-23	07-Dec-23
LJA1-1680	COMPLETE LOW VOLTAGE OFFICE SPACES - LOW RISE L3	5	01-Dec-23	07-Dec-23
LJA1-1440	CASEWORK / FF&E OFFICE SPACES - LOW RISE L3	5	07-Dec-23	13-Dec-23
LJA1-1690	ABOVE CEILING INSPECTION OFFICE SPACES - LOW RISE L3	1	08-Dec-23	08-Dec-23
LJA1-1430	DROP BALANCE OF CEILING TILES OFFICE SPACES - LOW RISE L3	3	11-Dec-23	13-Dec-23
LJA1-1450	INSTALL CARPET OFFICE SPACES - LOW RISE L3	8	14-Dec-23	26-Dec-23
LFINJ1-210	INSTALL PLUMBING FIXTURES OFFICE SPACES - LOW RISE L3	3	14-Dec-23	18-Dec-23
LJA1-1460	DOORS AND HARDWARE OFFICE SPACES - LOW RISE L3	4	27-Dec-23	02-Jan-24
CONVEYANCES				
H ELEVATORS				
ELEVH1-1000	ELEVATOR H1 INSTALLATION	40	15-Sep-23	09-Nov-23
ELEVH2-1000	ELEVATOR H2 INSTALLATION	40	10-Nov-23	10-Jan-24
J ELEVATORS				
ELEVJ2-1010	ELEVATOR J2 - INSTALL FOR CONSTRUCTION USE	40	16-May-23	13-Jul-23
ELEVJ2-1020	ELEVATOR J2 - TESTING FOR CONSTRUCTION USE	5	14-Jul-23	20-Jul-23
ELEVJ1-1000	ELEVATOR J1 INSTALLATION	40	19-Jul-23	14-Sep-23
ELEVJ2-1030	ELEVATOR J2 - CONSTRUCTION USE	100	21-Jul-23	13-Dec-23
ELEVJ2-1000	ELEVATOR J2 - RECONDITION FOR PERMANENT	10	14-Dec-23	28-Dec-23

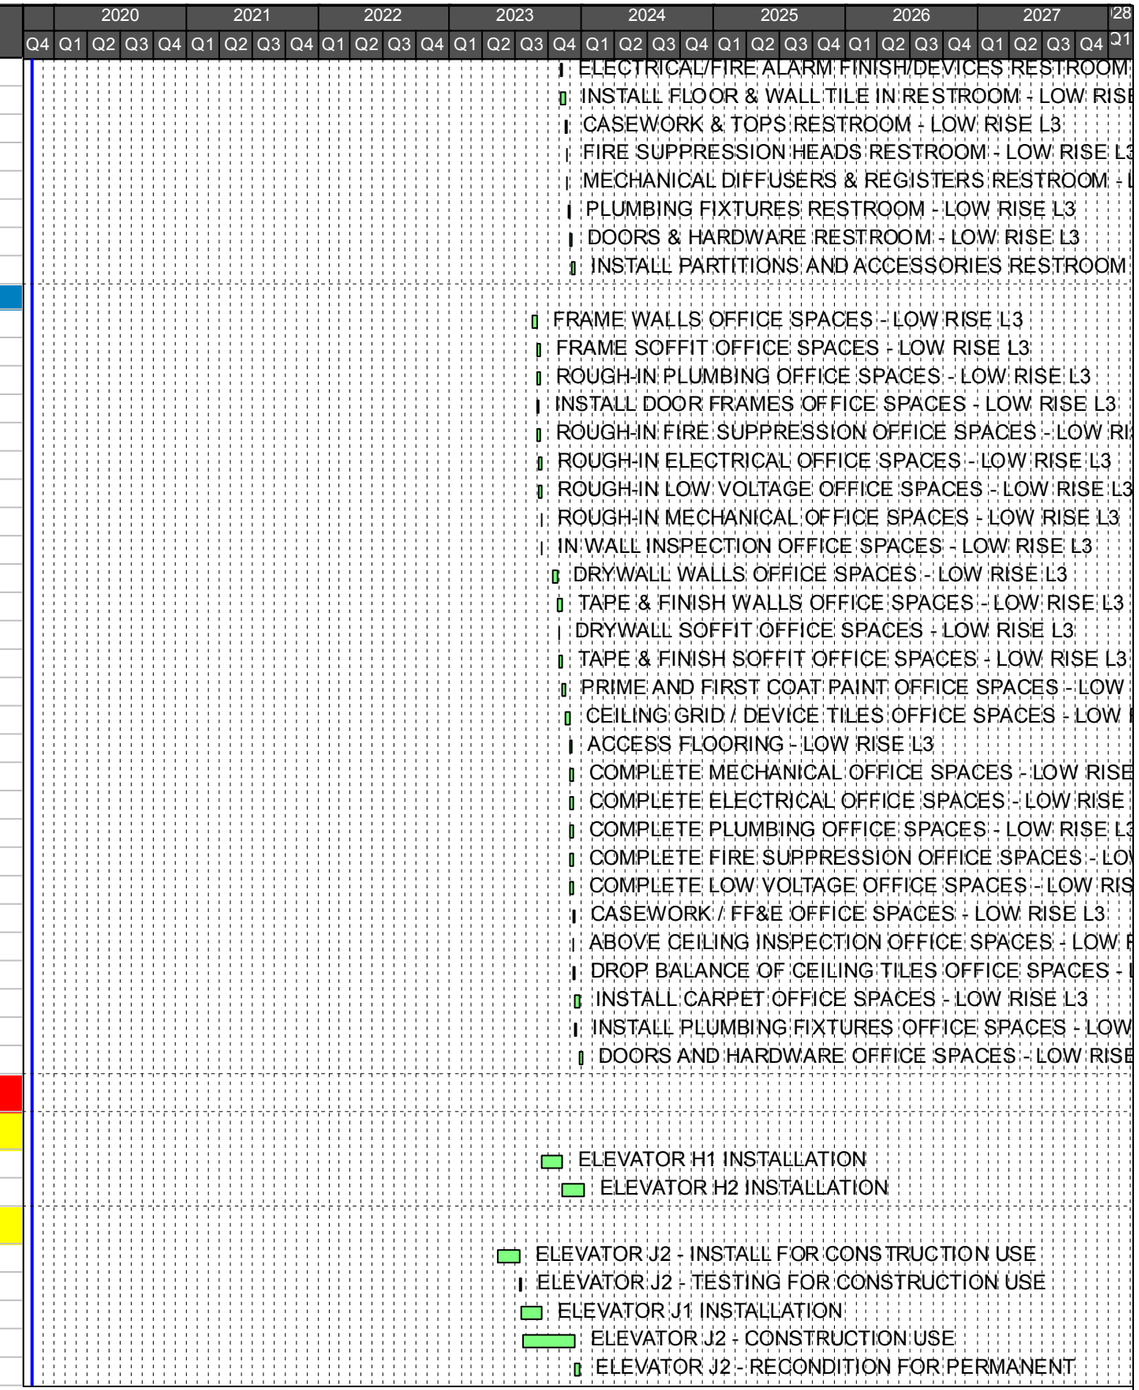

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
P ELEVATORS				
ELEVP1-1000	ELEVATOR P1, P2, P3 INSTALLATION	50	10-Nov-23	25-Jan-24
ELEVP4-1000	ELEVATOR P4, P5, P6 INSTALLATION	50	26-Jan-24	08-Apr-24
ELEVP1-1010	ELEVATOR P1 - TEST AND PROTECT	10	26-Jan-24	08-Feb-24
ELEVTST-1000	ELEVATOR FINAL TESTING	10	09-Apr-24	22-Apr-24
FINAL SITEWORK				
NORTH AREA				
GENERAL SITE				
SW-N-100	DEMO EXISTING SIDEWALK AND GUTTER AT 10TH STREET - NOR	3	09-Aug-23	11-Aug-23
SW-N-120	ROUGH GRADE - NORTH SITE - NORTH SITE	3	14-Aug-23	16-Aug-23
SW-N-130	U/G ELECTRICAL - NORTH SITE - NORTH SITE	4	17-Aug-23	22-Aug-23
SW-N-140	INSTALL IRRIGATION SLEEVES - NORTH SITE	2	21-Aug-23	22-Aug-23
SW-N-150	INSTALL SUBGRADE DRAINAGE - NORTH SITE	4	22-Aug-23	25-Aug-23
SW-N-320	INSTALL LIGHT POLES - NORTH SITE	10	22-Nov-23	07-Dec-23
SW-N-420	F/R/P FLAGPOLE FOUNDATION - NORTH SITE	2	11-Dec-23	12-Dec-23
SW-N-490	INSTALL STAIR HANDRAIL - NORTH SITE	4	07-Mar-24	12-Mar-24
SW-N-110	INSTALL SITE ELECTRICAL FINISHES - NORTH SITE	10	15-Mar-24	28-Mar-24
SW-N-390	INSTALL IRRIGATION - NORTH SITE	4	15-Mar-24	20-Mar-24
SW-N-400	PLACE TREES AND PLANTS - NORTH SITE	5	21-Mar-24	27-Mar-24
SW-N-410	PLACE GROUNDCOVER - NORTH SITE	2	28-Mar-24	29-Mar-24
SW-N-430	INSTALL FLAGPOLE - NORTH SITE	1	01-Apr-24	01-Apr-24
SW-N-450	INSTALL FF&E	3	01-Apr-24	03-Apr-24
SW-N-440	INSTALL SITE SIGNAGE - NORTH SITE	5	04-Apr-24	10-Apr-24
RAMPS, WALLS, AND STAIRS				
SW-N-160	EXCAVATE FOUNDATIONS FOR CIP WALLS - NORTH SITE	2	22-Aug-23	23-Aug-23
SW-N-190	REBAR CIP WALL FOUNDATIONS - NORTH SITE	2	24-Aug-23	25-Aug-23
SW-N-460	PRE - POUR INSPECTION - WALL FOUNDATIONS - NORTH SITE	1	25-Aug-23	25-Aug-23
SW-N-200	POUR CIP WALL FOUNDATIONS - NORTH SITE	2	28-Aug-23	29-Aug-23
SW-N-220	ONE SIDE FORM CIP WALLS - NORTH SITE	5	30-Aug-23	07-Sep-23
SW-N-230	ELECTRICAL ROUGH-IN CIP WALLS - NORTH SITE	2	08-Sep-23	11-Sep-23
SW-N-240	REBAR CIP WALLS - NORTH SITE	2	12-Sep-23	13-Sep-23
SW-N-250	SECOND SIDE FORM CIP WALLS - NORTH SITE	2	14-Sep-23	15-Sep-23
SW-N-470	PRE - POUR INSPECTION - SECOND SIDE FORM CIP WALLS NORT	1	15-Sep-23	15-Sep-23
SW-N-260	POUR CIP WALLS - NORTH SITE	2	18-Sep-23	19-Sep-23
SW-N-270	CURE & STRIP CIP WALLS - NORTH SITE	4	07-Nov-23	10-Nov-23
SW-N-290	BACKFILL/ FINE GRADE/ AB - NORTH SITE	3	13-Nov-23	15-Nov-23
CURBS AND SIDEWALKS				
SW-N-170	EXCAVATE TRAFFIC SIGNAL FOUNDATION AT G & 10th STREET - N	1	23-Aug-23	23-Aug-23
SW-N-180	INSTALL TRAFFIC SIGNAL FOUNDATION AT G & 10th STREET - NOF	3	24-Aug-23	28-Aug-23
SW-N-210	ROUGH- IN TRAFFIC SIGNAL CONTROLS AT G & 10th STREET - NOI	4	29-Aug-23	05-Sep-23
SW-N-280	INSTALL LANDSCAPE AND HARDSCAPE DRAINS - NORTH SITE	5	13-Nov-23	17-Nov-23
SW-N-300	FINE GRADE & PLACE A/B - NORTH SITE	2	20-Nov-23	21-Nov-23
SW-N-310	F/R/P CURB, GUTTERS, & PADS - NORTH SITE	5	22-Nov-23	30-Nov-23
SW-N-330	CURE CURB, GUTTERS, & PADS - NORTH SITE	2	01-Dec-23	02-Dec-23
SW-N-340	FORM SIDEWALKS - NORTH SITE	5	04-Dec-23	08-Dec-23
SW-N-350	REINFORCE SIDEWALKS - NORTH SITE	5	07-Dec-23	13-Dec-23

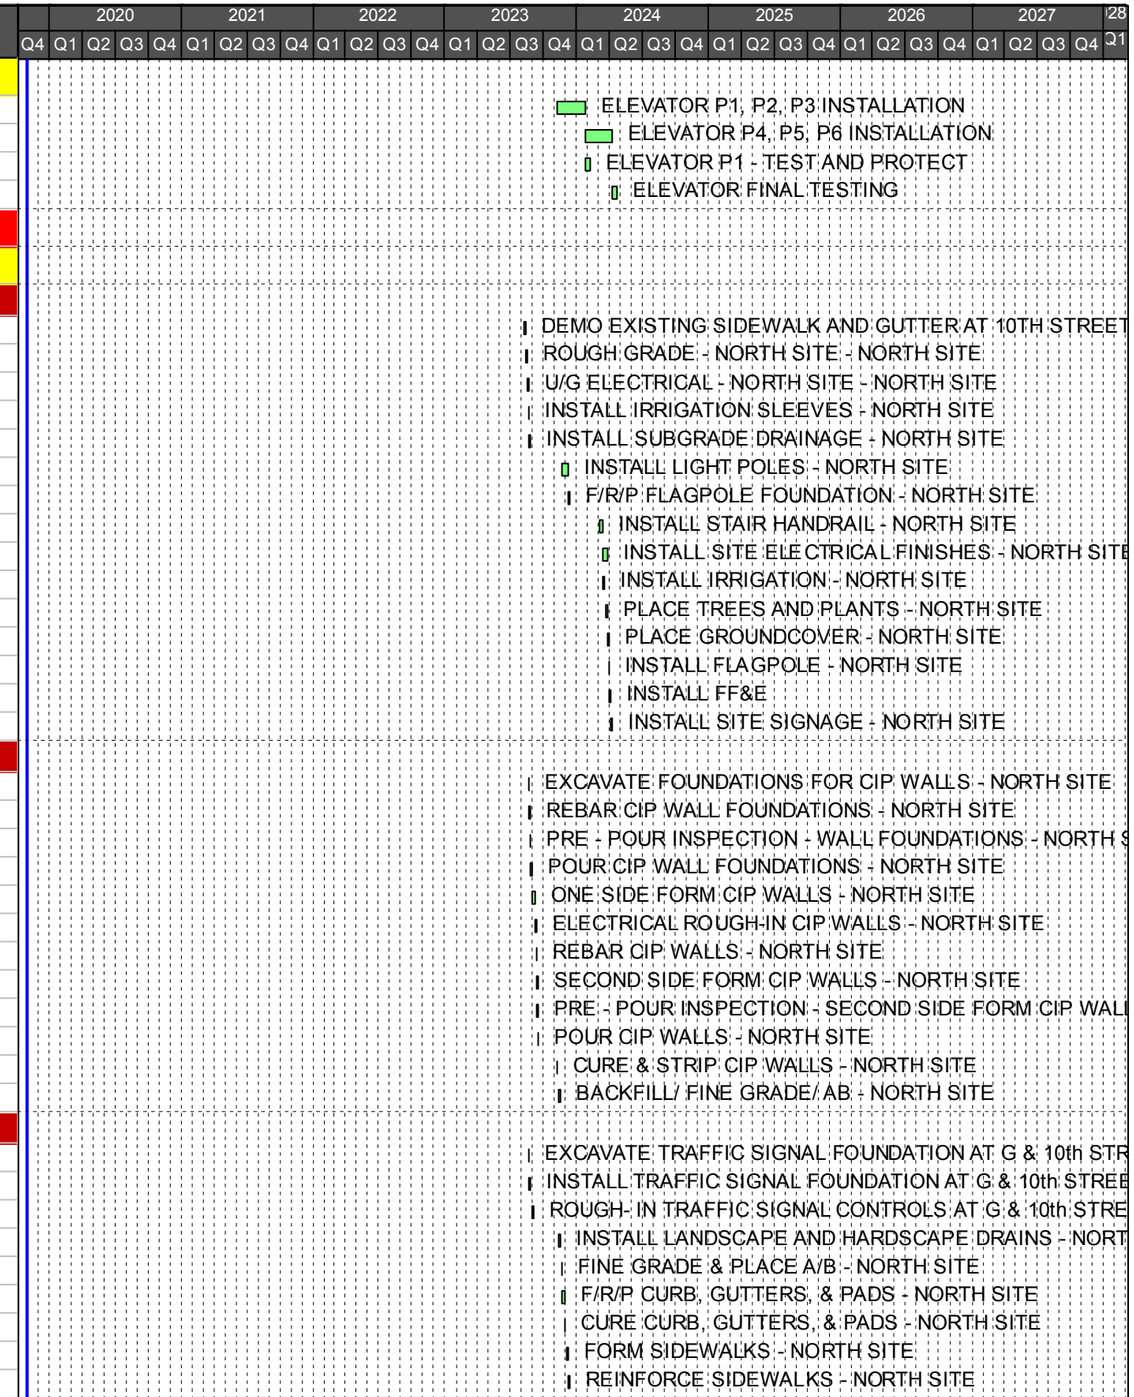

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
SW-N-360	INSTALL BOLLARDS AND LANDSCAPE GRATES - NORTH SITE	3	07-Mar-24	11-Mar-24
SW-N-480	PRE - POUR INSPECTION SIDEWALKS NORTH SITE	1	11-Mar-24	11-Mar-24
SW-N-370	POUR SIDEWALKS - NORTH SITE	3	12-Mar-24	14-Mar-24
SW-N-380	INSTALL TRAFFIC SIGNAL AT G & 10th STREET - NORTH SITE	10	15-Mar-24	28-Mar-24
SOUTH AREA				
GENERAL SITE				
SW-S-110	DEMO EXISTING SIDEWALK AND GUTTER AT 9TH STREET - SOUTI	3	17-Aug-23	21-Aug-23
SW-S-130	ROUGH GRADE - SOUTH SITE - SOUTH SITE	3	22-Aug-23	24-Aug-23
SW-S-140	U/G ELECTRICAL - SOUTH SITE - SOUTH SITE	4	25-Aug-23	30-Aug-23
SW-E-430	EXCAVATE BIO RETENTION SWALE - SOUTH SITE	2	25-Aug-23	28-Aug-23
SW-S-150	INSTALL IRRIGATION SLEEVES - SOUTH SITE	2	29-Aug-23	30-Aug-23
SW-E-440	INSTALL BIO RETENTION DRAIN - SOUTH SIDE	4	29-Aug-23	05-Sep-23
SW-S-160	INSTALL SUBGRADE DRAINAGE - SOUTH SITE	4	30-Aug-23	06-Sep-23
SW-E-450	BACKFILL BIO RETENTION SWALE - SOUTH SITE	2	06-Sep-23	07-Sep-23
SW-S-330	INSTALL LIGHT POLES - SOUTH SITE	10	08-Nov-23	21-Nov-23
SW-N-500	INSTALL STAIR HANDRAIL - SOUTH SITE	4	07-Mar-24	12-Mar-24
SW-S-120	INSTALL SITE ELECTRICAL FINISHES - SOUTH SITE	10	15-Mar-24	28-Mar-24
SW-S-400	INSTALL IRRIGATION - SOUTH SITE	4	15-Mar-24	20-Mar-24
SW-S-410	PLACE TREES AND PLANTS - SOUTH SITE	5	21-Mar-24	27-Mar-24
SW-S-420	PLACE GROUNDCOVER - SOUTH SITE	2	28-Mar-24	29-Mar-24
SW-S-570	INSTALL FF&E	3	01-Apr-24	03-Apr-24
RAMPS, WALLS, AND STAIRS				
SW-S-170	EXCAVATE FOUNDATIONS FOR CIP WALLS - SOUTH SITE	2	08-Sep-23	11-Sep-23
SW-S-200	REBAR CIP WALL FOUNDATIONS - SOUTH SITE	2	12-Sep-23	13-Sep-23
SW-S-580	PRE - POUR INSPECTION - CIP WALL FOUNDATIONS SOUTH SITE	1	13-Sep-23	13-Sep-23
SW-S-210	POUR CIP WALL FOUNDATIONS - SOUTH SITE	2	14-Sep-23	15-Sep-23
SW-S-230	ONE SIDE FORM CIP WALLS - SOUTH SITE	5	18-Sep-23	22-Sep-23
SW-S-240	ELECTRICAL ROUGH-IN CIP WALLS - SOUTH SITE	2	25-Sep-23	26-Sep-23
SW-S-250	REBAR CIP WALLS - SOUTH SITE	2	27-Sep-23	28-Sep-23
SW-S-260	SECOND SIDE FORM CIP WALLS - SOUTH SITE	2	29-Sep-23	02-Oct-23
SW-S-590	PRE - POUR INSPECTION - CIP WALLS SOUTH SITE	1	02-Oct-23	02-Oct-23
SW-S-270	POUR CIP WALLS - SOUTH SITE	2	03-Oct-23	04-Oct-23
SW-S-280	CURE & STRIP CIP WALLS - SOUTH SITE	4	24-Oct-23	27-Oct-23
SW-S-300	BACKFILL/ FINE GRADE/ AB - SOUTH SITE	3	30-Oct-23	01-Nov-23
CURBS AND SIDEWALKS				
SW-S-180	EXCAVATE TRAFFIC SIGNAL FOUNDATION AT H & 10th STREET - S	1	31-Aug-23	31-Aug-23
SW-S-190	INSTALL TRAFFIC SIGNAL FOUNDATION AT H & 10th STREET - SOU	3	05-Sep-23	07-Sep-23
SW-S-220	ROUGH- IN TRAFFIC SIGNAL CONTROLS AT H & 10th STREET - SOU	4	08-Sep-23	13-Sep-23
SW-S-290	INSTALL LANDSCAPE AND HARDSCAPE DRAINS - SOUTH SITE	5	30-Oct-23	03-Nov-23
SW-S-310	FINE GRADE & PLACE A/B - SOUTH SITE	2	06-Nov-23	07-Nov-23
SW-S-320	F/R/P CURB, GUTTERS, & PADS - SOUTH SITE	5	08-Nov-23	14-Nov-23
SW-S-340	CURE CURB, GUTTERS, & PADS - SOUTH SITE	2	15-Nov-23	16-Nov-23
SW-S-350	FORM SIDEWALKS - SOUTH SITE	5	17-Nov-23	27-Nov-23
SW-S-360	REINFORCE SIDEWALKS - SOUTH SITE	5	17-Nov-23	27-Nov-23
SW-S-370	INSTALL BOLLARDS AND LANDSCAPE GRATES - SOUTH SITE	3	07-Mar-24	11-Mar-24
SW-S-600	PRE - POUR INSPECTION - SIDEWALKS SOUTH SITE	1	11-Mar-24	11-Mar-24

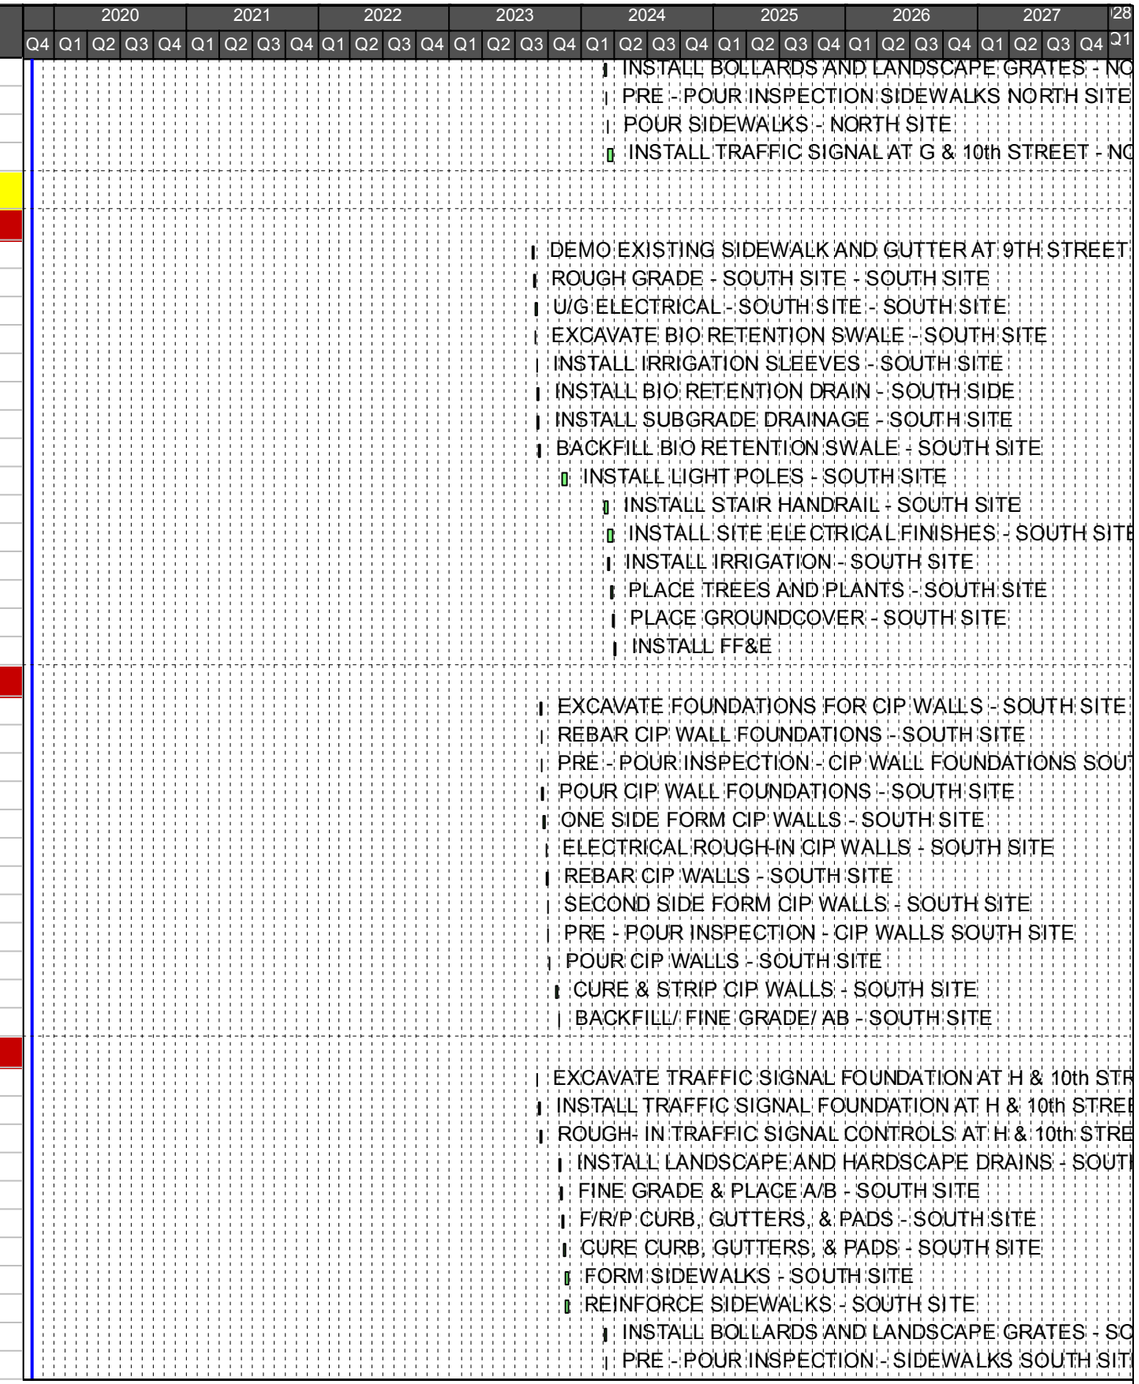

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
SW-S-380	POUR SIDEWALKS - SOUTH SITE	3	12-Mar-24	14-Mar-24
SW-S-390	INSTALL TRAFFIC SIGNAL AT H & 10th STREET - SOUTH SITE	10	15-Mar-24	28-Mar-24
SERVICE YARD ENCLOSURE				
SW-S-430	EXCAVATE SERVICE YARD ENCLOSURE FOOTINGS - SOUTH SITE	2	25-Aug-23	28-Aug-23
SW-S-440	INSTALL REBAR SERVICE YARD ENCLOSURE FOOTINGS - SOUTH	1	29-Aug-23	29-Aug-23
SW-S-450	INSTALL A/B's SERVICE YARD ENCLOSURE FOOTINGS - SOUTH SI	3	30-Aug-23	05-Sep-23
SW-S-490	F/R/P TRASH ENCLOSURE - SOUTH SITE	3	31-Aug-23	06-Sep-23
SW-S-480	INSTALL BOLLARDS SERVICE YARD ENCLOSURE - SOUTH SITE	2	05-Sep-23	06-Sep-23
SW-S-610	PRE - POUR INSPECTION - SERVICE YARD ENCLOSURE FOOTINGS	1	05-Sep-23	05-Sep-23
SW-S-460	POUR SERVICE YARD ENCLOSURE FOOTINGS - SOUTH SITE	1	06-Sep-23	06-Sep-23
SW-S-470	CURE SERVICE YARD ENCLOSURE FOOTINGS - SOUTH SITE	7	07-Sep-23	13-Sep-23
SW-S-550	F/R/P EQUIPMENT PADS AND CURBS - SOUTH SITE	2	07-Sep-23	08-Sep-23
SW-S-500	INSTALL HSS & GROUT - SOUTH SITE - SOUTH SITE	2	14-Sep-23	15-Sep-23
SW-S-510	FINE GRADE AND PLACE AB - SOUTH SITE	2	18-Sep-23	19-Sep-23
SW-S-520	PAVE SERVICE YARD - SOUTH SITE	1	20-Sep-23	20-Sep-23
SW-S-530	INSTALL SERVICE YARD STEEL CROSS MEMBERS & GATE - SOUT	5	21-Sep-23	27-Sep-23
SW-S-540	INSTALL SERVICE YARD METAL PANELS - SOUTH SITE	4	28-Sep-23	03-Oct-23
SW-S-620	INSTALL AUTOMATIC DIESEL FUEL PORT	10	28-Sep-23	11-Oct-23
SW-S-560	INSTALL SERVICE YARD EQUIPMENT - SOUTH SITE	3	12-Oct-23	16-Oct-23
EAST AREA				
GENERAL SITE				
SW-E-110	DEMO EXISTING SIDEWALK AND GUTTER AT G STREET - EAST SI	3	14-Aug-23	16-Aug-23
SW-E-130	ROUGH GRADE - EAST SITE - EAST SITE	3	17-Aug-23	21-Aug-23
SW-E-140	U/G ELECTRICAL - EAST SITE - EAST SITE	4	22-Aug-23	25-Aug-23
SW-E-180	EXCAVATE BIO RETENTION SWALE - EAST SITE	2	22-Aug-23	23-Aug-23
SW-E-150	INSTALL IRRIGATION SLEEVES - EAST SITE	2	24-Aug-23	25-Aug-23
SW-E-190	INSTALL BIO RETENTION DRAIN - EAST SITE	4	24-Aug-23	29-Aug-23
SW-E-160	INSTALL SUBGRADE DRAINAGE - EAST SITE	4	25-Aug-23	30-Aug-23
SW-E-220	BACKFILL BIO RETENTION SWALE - EAST SITE	2	30-Aug-23	31-Aug-23
SW-E-330	INSTALL LIGHT POLE - EAST SITE	4	18-Oct-23	23-Oct-23
SW-N-510	INSTALL STAIR HANDRAIL - EAST SITE	4	07-Mar-24	12-Mar-24
SW-E-400	INSTALL IRRIGATION - EAST SITE	4	15-Mar-24	20-Mar-24
SW-E-410	PLACE TREES AND PLANTS - EAST SITE	5	21-Mar-24	27-Mar-24
SW-E-420	PLACE GROUNDCOVER - EAST SITE	2	28-Mar-24	29-Mar-24
SW-E-510	INSTALL FF&E	10	01-Apr-24	12-Apr-24
RAMPS, WALLS, AND STAIRS				
SW-E-170	EXCAVATE FOUNDATIONS FOR CIP WALLS - EAST SITE	2	05-Sep-23	06-Sep-23
SW-E-200	REBAR CIP WALL FOUNDATIONS - EAST SITE	2	07-Sep-23	08-Sep-23
SW-E-390	PRE - POUR INSPECTION - CIP WALL FOUNDATIONS EAST SITE	1	11-Sep-23	11-Sep-23
SW-E-210	POUR CIP WALL FOUNDATIONS - EAST SITE	2	12-Sep-23	13-Sep-23
SW-E-230	ONE SIDE FORM CIP WALLS - EAST SITE	5	14-Sep-23	20-Sep-23
SW-E-240	ELECTRICAL ROUGH-IN CIP WALLS - EAST SITE	2	21-Sep-23	22-Sep-23
SW-E-250	REBAR CIP WALLS - EAST SITE	2	25-Sep-23	26-Sep-23
SW-E-260	SECOND SIDE FORM CIP WALLS - EAST SITE	2	27-Sep-23	28-Sep-23
SW-E-520	PRE - POUR INSPECTION - CIP WALLS EAST SITE	1	28-Sep-23	28-Sep-23
SW-E-270	POUR CIP WALLS - EAST SITE	2	29-Sep-23	02-Oct-23

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
SW-E-280	CURE & STRIP CIP WALLS - EAST SITE	4	03-Oct-23	06-Oct-23
SW-E-300	BACKFILL/ FINE GRADE/ AB AT CIP WALLS - EAST SITE	3	09-Oct-23	11-Oct-23
CURBS AND SIDEWALKS				
SW-E-290	INSTALL LANDSCAPE AND HARDSCAPE DRAINS - EAST SITE	5	09-Oct-23	13-Oct-23
SW-E-310	FINE GRADE & PLACE A/B - EAST SITE	2	16-Oct-23	17-Oct-23
SW-E-320	F/R/P CURB, GUTTERS, & PADS - EAST SITE	10	18-Oct-23	31-Oct-23
SW-E-340	CURE CURB, GUTTERS, & PADS - EAST SITE	2	01-Nov-23	02-Nov-23
SW-E-350	FORM SIDEWALKS - EAST SITE	7	07-Nov-23	15-Nov-23
SW-E-360	REINFORCE SIDEWALKS - EAST SITE	5	09-Nov-23	15-Nov-23
SW-E-370	INSTALL BOLLARDS AND LANDSCAPE GRATES - EAST SITE	3	07-Mar-24	11-Mar-24
SW-E-530	PRE - POUR INSPECTION - SIDEWALKS EAST SITE	1	11-Mar-24	11-Mar-24
SW-E-380	POUR SIDEWALKS - EAST SITE	3	12-Mar-24	14-Mar-24
PAVING				
SW-E-490	PAVE PARKING LOT	1	12-Oct-23	12-Oct-23
SW-E-550	CURE	30	13-Oct-23	27-Nov-23
SW-E-560	STRIP FORMS	10	28-Nov-23	11-Dec-23
SW-E-460	DEMO AC AT 10TH STREET	2	15-Mar-24	18-Mar-24
SW-E-470	PREPARE SUBGRADE FOR PAVING AT 10TH ST.	2	19-Mar-24	20-Mar-24
SW-E-480	PAVE 10 STREET	1	21-Mar-24	21-Mar-24
SW-E-540	CURE	30	22-Mar-24	02-May-24
SW-E-500	STRIPING - ALL AREAS	10	03-May-24	16-May-24
WEST AREA				
GENERAL SITE				
SW-W-100	DEMO EXISTING SIDEWALK AND GUTTER AT H STREET - WEST S	3	04-Aug-23	08-Aug-23
SW-W-110	ROUGH GRADE - WEST SITE	3	09-Aug-23	11-Aug-23
SW-W-120	U/G ELECTRICAL - WEST SITE	4	14-Aug-23	17-Aug-23
SW-W-130	INSTALL IRRIGATION SLEEVES - WEST SITE	2	16-Aug-23	17-Aug-23
SW-W-140	INSTALL SUBGRADE DRAINAGE - WEST SITE	4	17-Aug-23	22-Aug-23
SW-W-420	INSTALL LIGHT POLES - WEST SITE	10	15-Nov-23	30-Nov-23
SW-W-410	INSTALL SITE ELECTRICAL FINISHES - WEST SITE	10	13-Dec-23	27-Dec-23
SW-W-430	INSTALL IRRIGATION - WEST SITE	4	13-Dec-23	18-Dec-23
SW-W-500	INSTALL SECURITY ENCLOSURE	10	13-Dec-23	27-Dec-23
SW-W-440	PLACE TREES AND PLANTS - WEST SITE	5	19-Dec-23	26-Dec-23
SW-W-450	PLACE GROUNDCOVER - WEST SITE	2	27-Dec-23	28-Dec-23
SW-N-520	INSTALL STAIR HANDRAIL - WEST SITE	4	07-Mar-24	12-Mar-24
SW-W-510	INSTALL FF&E	3	13-Mar-24	15-Mar-24
RAMPS, WALLS, AND STAIRS				
SW-W-170	EXCAVATE FOUNDATIONS FOR CIP WALLS - WEST SITE	2	17-Aug-23	18-Aug-23
SW-W-220	REBAR CIP WALL FOUNDATIONS - WEST SITE	2	21-Aug-23	22-Aug-23
SW-W-520	PRE - POUR INSPECTION - CIP WALL FOUNDATIONS WEST SITE	1	22-Aug-23	22-Aug-23
SW-W-230	POUR CIP WALL FOUNDATIONS - WEST SITE	2	23-Aug-23	24-Aug-23
SW-W-180	ONE SIDE FORM CIP WALLS - WEST SITE	5	25-Aug-23	31-Aug-23
SW-W-190	ELECTRICAL ROUGH-IN CIP WALLS - WEST SITE	2	05-Sep-23	06-Sep-23
SW-W-200	REBAR CIP WALLS - WEST SITE	2	07-Sep-23	08-Sep-23
SW-W-240	SECOND SIDE FORM CIP WALLS - WEST SITE	2	11-Sep-23	12-Sep-23
SW-W-530	PRE - POUR INSPECTION - CIP WALLS WEST SITE	1	12-Sep-23	12-Sep-23

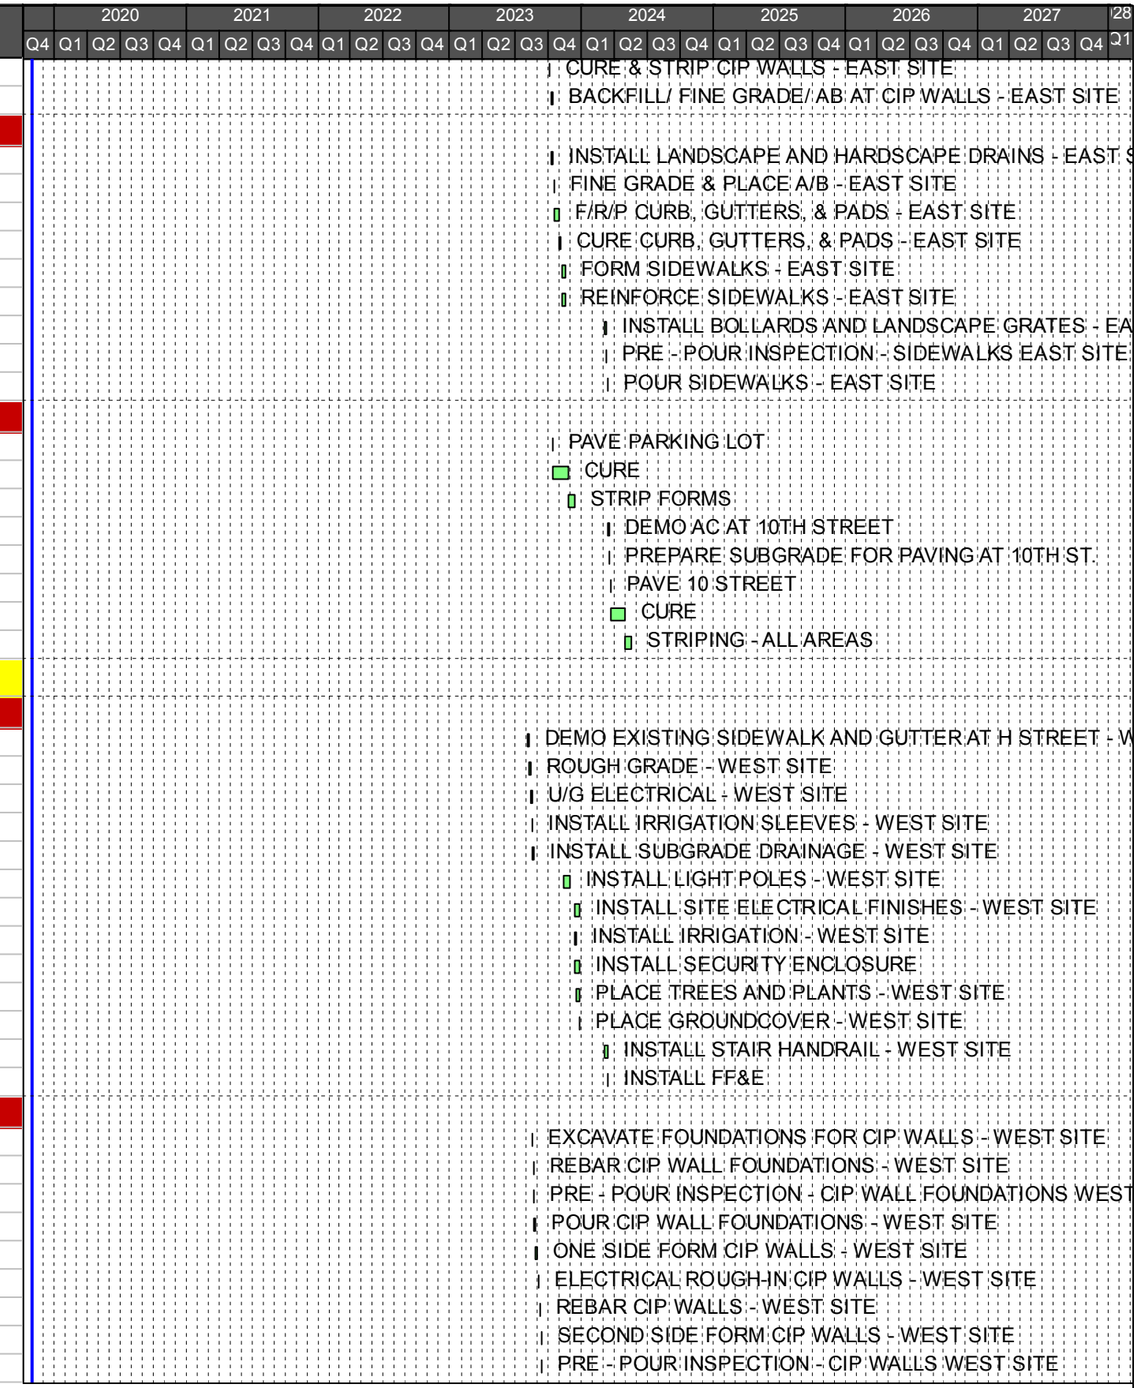

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
SW-W-210	POUR CIP WALLS - WEST SITE	2	13-Sep-23	14-Sep-23
SW-W-250	CURE & STRIP CIP WALLS - WEST SITE	4	31-Oct-23	03-Nov-23
SW-W-490	BACKFILL/ FINE GRADE/ AB - WEST SITE	3	06-Nov-23	08-Nov-23
CURBS AND SIDEWALKS				
SW-W-340	EXCAVATE TRAFFIC SIGNAL FOUNDATION AT H & 10th STREET - W	1	18-Aug-23	18-Aug-23
SW-W-160	INSTALL TRAFFIC SIGNAL FOUNDATION AT H & 10th STREET - WES	3	21-Aug-23	23-Aug-23
SW-W-150	ROUGH- IN TRAFFIC SIGNAL CONTROLS AT H & 10th STREET - WE	4	24-Aug-23	29-Aug-23
SW-W-330	INSTALL LANDSCAPE AND HARDSCAPE DRAINS - WEST SITE	5	06-Nov-23	10-Nov-23
SW-W-270	FINE GRADE & PLACE A/B - WEST SITE	2	13-Nov-23	14-Nov-23
SW-W-260	F/R/P CURB, GUTTERS, & PADS - WEST SITE	5	15-Nov-23	21-Nov-23
SW-W-280	CURE CURB, GUTTERS, & PADS - WEST SITE	2	22-Nov-23	23-Nov-23
SW-W-290	FORM SIDEWALKS - WEST SITE	5	01-Dec-23	07-Dec-23
SW-W-300	REINFORCE SIDEWALKS - WEST SITE	5	01-Dec-23	07-Dec-23
SW-W-310	INSTALL BOLLARDS AND LANDSCAPE GRATES - WEST SITE	3	05-Dec-23	07-Dec-23
SW-W-540	PRE - POUR INSPECTION - SIDEWALKS WEST SITE	1	07-Dec-23	07-Dec-23
SW-W-320	POUR SIDEWALKS - WEST SITE	3	08-Dec-23	12-Dec-23
SW-W-350	INSTALL TRAFFIC SIGNAL AT H & 10th STREET - WEST SITE	10	13-Dec-23	27-Dec-23
JUDGES PARKING ENTRANCE				
SW-W-360	EXCAVATE BARRIER BEAM BASESAT H & 10th STREET - WEST SITE	1	22-Nov-23	22-Nov-23
SW-W-460	FORM JUDGES ENTRANCE RAMP - WEST SITE	2	22-Nov-23	27-Nov-23
SW-W-370	FORM/ TEMPLATE/ REINFORCE BARRIER BEAM BASESAT H & 10tl	3	27-Nov-23	29-Nov-23
SW-W-400	INSTALL LOOP DETECTOR ASSEMBLY - WEST SITE	1	28-Nov-23	28-Nov-23
SW-W-470	REINFORCE JUDGES ENTRANCE RAMP - WEST SITE	1	28-Nov-23	28-Nov-23
SW-W-550	PRE - POUR INSPECTION - JUDGES ENTRANCE RAMP WEST SITE	1	28-Nov-23	28-Nov-23
SW-W-480	POUR JUDGES ENTRANCE RAMP - WEST SITE	1	29-Nov-23	29-Nov-23
SW-W-560	PRE - POUR INSPECTION - BARRIER BEAM BASES	1	29-Nov-23	29-Nov-23
SW-W-380	POUR BARRIER BEAM BASESAT H & 10th STREET - WEST SITE	1	30-Nov-23	30-Nov-23
SW-W-390	INSTALL AUTOMATIC GATE OPENER - WEST SITE	10	13-Dec-23	27-Dec-23
START-UP COMMISSIONING & PUNCHLIST				
PUNCHLIST & COMPLETION				
IWLAEPB-1000	INCOMPLETE WORK LIST - BASEMENT	5	14-Jun-23	20-Jun-23
IWLAEPB-1010	A/E PUNCH LIST - BASEMENT	15	21-Jun-23	12-Jul-23
IWLAEP1-1000	INCOMPLETE WORK LIST - LEVEL 1	5	26-Jan-24	01-Feb-24
IWLAEP1-1010	A/E PUNCH LIST - LEVEL 1	15	02-Feb-24	26-Feb-24
IWLAEPBEXT-1000	INCOMPLETE WORK LIST - BUILDING EXTERIOR	5	02-Feb-24	08-Feb-24
IWLAEP2-1000	INCOMPLETE WORK LIST - LEVEL 2	5	07-Feb-24	13-Feb-24
IWLAEPBEXT-1010	A/E PUNCH LIST - BUILDING EXTERIOR	15	09-Feb-24	04-Mar-24
IWLAEP2-1010	A/E PUNCH LIST - LEVEL 2	15	14-Feb-24	07-Mar-24
IWLAEP3-1000	INCOMPLETE WORK LIST - LEVEL 3	5	20-Feb-24	26-Feb-24
IWLAEP3-1010	A/E PUNCH LIST - LEVEL 3	15	27-Feb-24	18-Mar-24
IWLAEP4-1000	INCOMPLETE WORK LIST - LEVEL 4	5	29-Feb-24	06-Mar-24
IWLAEP4-1010	A/E PUNCH LIST - LEVEL 4	15	07-Mar-24	27-Mar-24
IWLAEP5-1000	INCOMPLETE WORK LIST - LEVEL 5	5	11-Mar-24	15-Mar-24
IWLAEP5-1010	A/E PUNCH LIST - LEVEL 5	15	18-Mar-24	05-Apr-24
IWLAEP6-1000	INCOMPLETE WORK LIST - LEVEL 6	5	20-Mar-24	26-Mar-24
IWLAEP6-1010	A/E PUNCH LIST - LEVEL 6	15	27-Mar-24	16-Apr-24

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
IWLAEP7-1000	INCOMPLETE WORK LIST - LEVEL 7	5	29-Mar-24	04-Apr-24
IWLAEP1-1020	INCOMPLETE WORK LIST - STAIRS	5	01-Apr-24	05-Apr-24
IWLAEP7-1010	A/E PUNCH LIST - LEVEL 7	15	05-Apr-24	25-Apr-24
IWLAEP1-1030	A/E PUNCH LIST - STAIRS	15	08-Apr-24	26-Apr-24
IWLAEP8-1000	INCOMPLETE WORK LIST - LEVEL 8	5	09-Apr-24	15-Apr-24
IWLAEPM-1000	INCOMPLETE WORK LIST - MECH. LEVEL	5	16-Apr-24	22-Apr-24
IWLAEP8-1010	A/E PUNCH LIST - LEVEL 8	15	16-Apr-24	06-May-24
IWLAEPM-1010	A/E PUNCH LIST - MECH. LEVEL	15	23-Apr-24	13-May-24
IWLAEPSITE-1000	INCOMPLETE WORK LIST - EXTERIOR, LANDSCAPE/HARDSCAPE	5	17-May-24	23-May-24
IWLAEPSITE-1010	A/E PUNCH LIST - EXTERIOR, LANDSCAPE/HARDSCAPE	15	17-May-24	10-Jun-24
START-UP/ TESTING/ COMMISSIONING				
DIV 21 FIRE SUPPRESSION				
A5340	START-UP AND TEST FIRE SUPPRESSION SYSTEM	5	01-Feb-24	07-Feb-24
A5380	IOR TESTING & INSPECTION OF FIRE SUPPRESSION SYSTEM	2	08-Feb-24	09-Feb-24
DIV 22 PLUMBING				
BOOSTER PUMPS (COLD WATER)				
A5390	START-UP AND TEST BOOSTER PUMPS	5	06-Feb-24	12-Feb-24
A5400	IOR TESTING & INSPECTION OF BOOSTER PUMPS	5	13-Feb-24	21-Feb-24
A5350	WATER CHLORINATION FLUSHING/ TEST	5	22-Feb-24	28-Feb-24
DIV 23 HVAC				
AHU's				
A5950	BUILDING TEMP CONDITIONING REQUIRED	0		24-May-23
A5830	HYDRONIC WATER TREATMENT	5	02-Jun-23	08-Jun-23
A5840	START PERMANENT AHUS's FOR TEMP CONDITIONING	0		24-Jan-24
TAB-1080	TAB - MECH LEVELS	10	25-Jan-24	07-Feb-24
TAB-1010	TAB - BASEMENT	5	20-Mar-24	26-Mar-24
TAB-1020	TAB - LEVEL 1	10	27-Mar-24	09-Apr-24
TAB-1030	TAB - LEVEL 2	10	04-Apr-24	17-Apr-24
TAB-1040	TAB - LEVEL 3	10	12-Apr-24	25-Apr-24
TAB-1050	TAB - LEVEL 4	5	26-Apr-24	02-May-24
TAB-1090	TAB - LEVEL 5	5	03-May-24	09-May-24
TAB-1070	TAB - LEVEL 6	5	10-May-24	16-May-24
TAB-1100	TAB - LEVEL 7	5	17-May-24	23-May-24
TAB-1110	TAB - LEVEL 8	5	28-May-24	03-Jun-24
TAB-1120	FINAL TAB & SMOKE TESTING	10	04-Jun-24	17-Jun-24
TAB-1130	PREPARE TAB REPORT	10	18-Jun-24	01-Jul-24
CONTROLS / BMS				
A5530	CONTROL SYSTEM POINT-TO-POINT & PRE-TEST - LEVEL 1	10	01-Feb-24	14-Feb-24
A5540	CONTROL SYSTEM POINT-TO-POINT & PRE-TEST - LEVEL 2	10	15-Feb-24	01-Mar-24
A5550	CONTROL SYSTEM POINT-TO-POINT & PRE-TEST - LEVEL 3	10	04-Mar-24	15-Mar-24
A5560	CONTROL SYSTEM POINT-TO-POINT & PRE-TEST - LEVEL 4	10	18-Mar-24	29-Mar-24
A5980	CONTROL SYSTEM POINT-TO-POINT & PRE-TEST - LEVEL 6	10	18-Mar-24	29-Mar-24
A5570	CONTROL SYSTEM POINT-TO-POINT & PRE-TEST - LEVEL 5	10	01-Apr-24	12-Apr-24
A5590	CONTROL SYSTEM POINT-TO-POINT & PRE-TEST - LEVEL 7	10	15-Apr-24	26-Apr-24
A5600	CONTROL SYSTEM POINT-TO-POINT & PRE-TEST - LEVEL 8	10	29-Apr-24	10-May-24

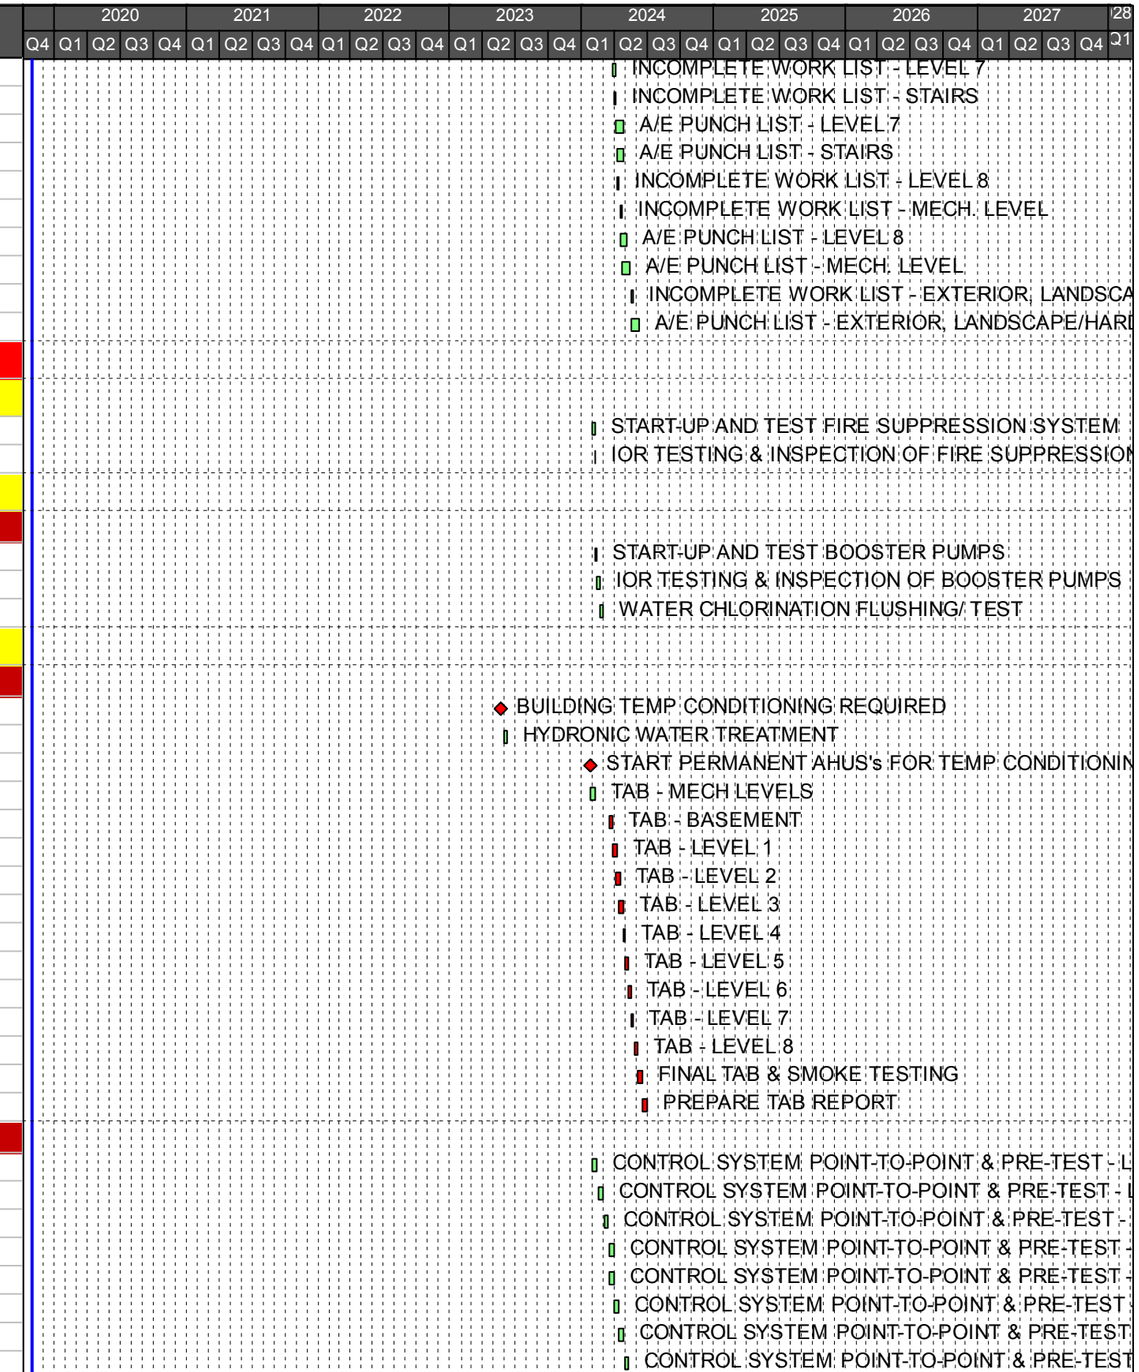

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
DIV 26 ELECTRICAL SYSTEMS				
EMERGENCY POWER				
GENRATOR TESTING				
A5490	TEST & INSPECT GENERATOR	10	01-Feb-24	14-Feb-24
A5500	STARTUP/ LOAD BANK TESTING	1	15-Feb-24	15-Feb-24
LIGHTING SYSTEM				
A5480	START-UP & TEST LIGHTING CONTROLS	10	26-Jan-24	08-Feb-24
NORMAL				
MAIN SWITCH A				
DISTRIBUTION AND START-UP				
PP-1180	PULL MAIN FEEDERS TO PANELS L0-L9 - MSA	10	25-May-23	09-Jun-23
PP-1160	PULL CONDUCTORS AND LAND TO PANELS L0-L9 - MSA	25	01-Nov-23	07-Dec-23
PP-1170	TERMINATE PANELS BASEMENT TO ROOF - MSA	15	08-Dec-23	29-Dec-23
PP-1190	ENERGIZE ROOF TOP PANELS - MSA	1	31-Jan-24	31-Jan-24
MAIN SWITCH B				
DISTRIBUTION AND START-UP				
PP-1100	PULL MAIN FEEDERS TO PANELS L0-L9 - MSB	5	25-May-23	02-Jun-23
PP-1090	TERMINATE PANELS TO EQUIPMENT L4/L9 - MSB	15	05-Jun-23	23-Jun-23
PP-1140	ENERGIZE ROOF TOP PANELS - MSB	1	26-Jun-23	26-Jun-23
MECHANICAL				
PP-1120	ENERGIZE AHU'S - LOW RISE ROOF L4	10	27-Jun-23	11-Jul-23
PP-1150	ENERGIZE AHU'S - TOWER ROOF L9	10	30-Jun-23	14-Jul-23
ELEVATORS				
PP-1000	ESTABLISH POWER TO ELEVATOR PANELS	15	27-Jun-23	18-Jul-23
A1350	PERM. POWER REQUIRED FOR ELEVATORS	0		18-Jul-23
TEL/ DATA				
CONV-100	PROCURE NETWORK EQUIPMENT	130	27-Mar-23	29-Sep-23
CONV-120	MDF ROOM READY	0	02-Oct-23	
CONV-140	INSTALL NETWORK EQUIPMENT	40	02-Oct-23	28-Nov-23
CONV-110	PROGRAM & INTEGRATION	56	23-Jan-24	11-Apr-24
FIRE ALARM				
SUPB-1000	FLS STARTUP / PRE-TEST- BASEMENT	6	01-Feb-24	08-Feb-24
SUP1-1000	FLS STARTUP / PRE-TEST - LEVEL 1	12	09-Feb-24	28-Feb-24
SUPM-1000	FLS STARTUP / PRE-TEST - MECH. LEVEL	5	22-Feb-24	28-Feb-24
SUP2-1000	FLS STARTUP / PRE-TEST - LEVEL 2	8	29-Feb-24	11-Mar-24
SUP3-1000	FLS STARTUP / PRE-TEST - LEVEL 3	8	12-Mar-24	21-Mar-24
SUP4-1000	FLS STARTUP / PRE-TEST - LEVEL 4	7	22-Mar-24	01-Apr-24
SUP5-1000	FLS STARTUP / PRE-TEST - LEVEL 5	7	02-Apr-24	10-Apr-24
SUP6-1000	FLS STARTUP / PRE-TEST - LEVEL 6	7	11-Apr-24	19-Apr-24
SUP7-1000	FLS STARTUP / PRE-TEST - LEVEL 7	7	22-Apr-24	30-Apr-24
SUP8-1000	FLS STARTUP / PRE-TEST - LEVEL 8	7	01-May-24	09-May-24
SUP8-1010	FLS FINAL FIRE ALARM INTERFACE TESTING	15	10-May-24	03-Jun-24
DIV 28 SAFETY & SECURITY				
A5360	START-UP/ PRETEST SECURITY SYSTEM - LEVEL 1	5	07-Sep-23	13-Sep-23
A5610	START-UP/ PRETEST SECURITY SYSTEM - LEVEL 2	5	05-Feb-24	09-Feb-24
A5620	START-UP/ PRETEST SECURITY SYSTEM - LEVEL 3	5	14-Feb-24	22-Feb-24

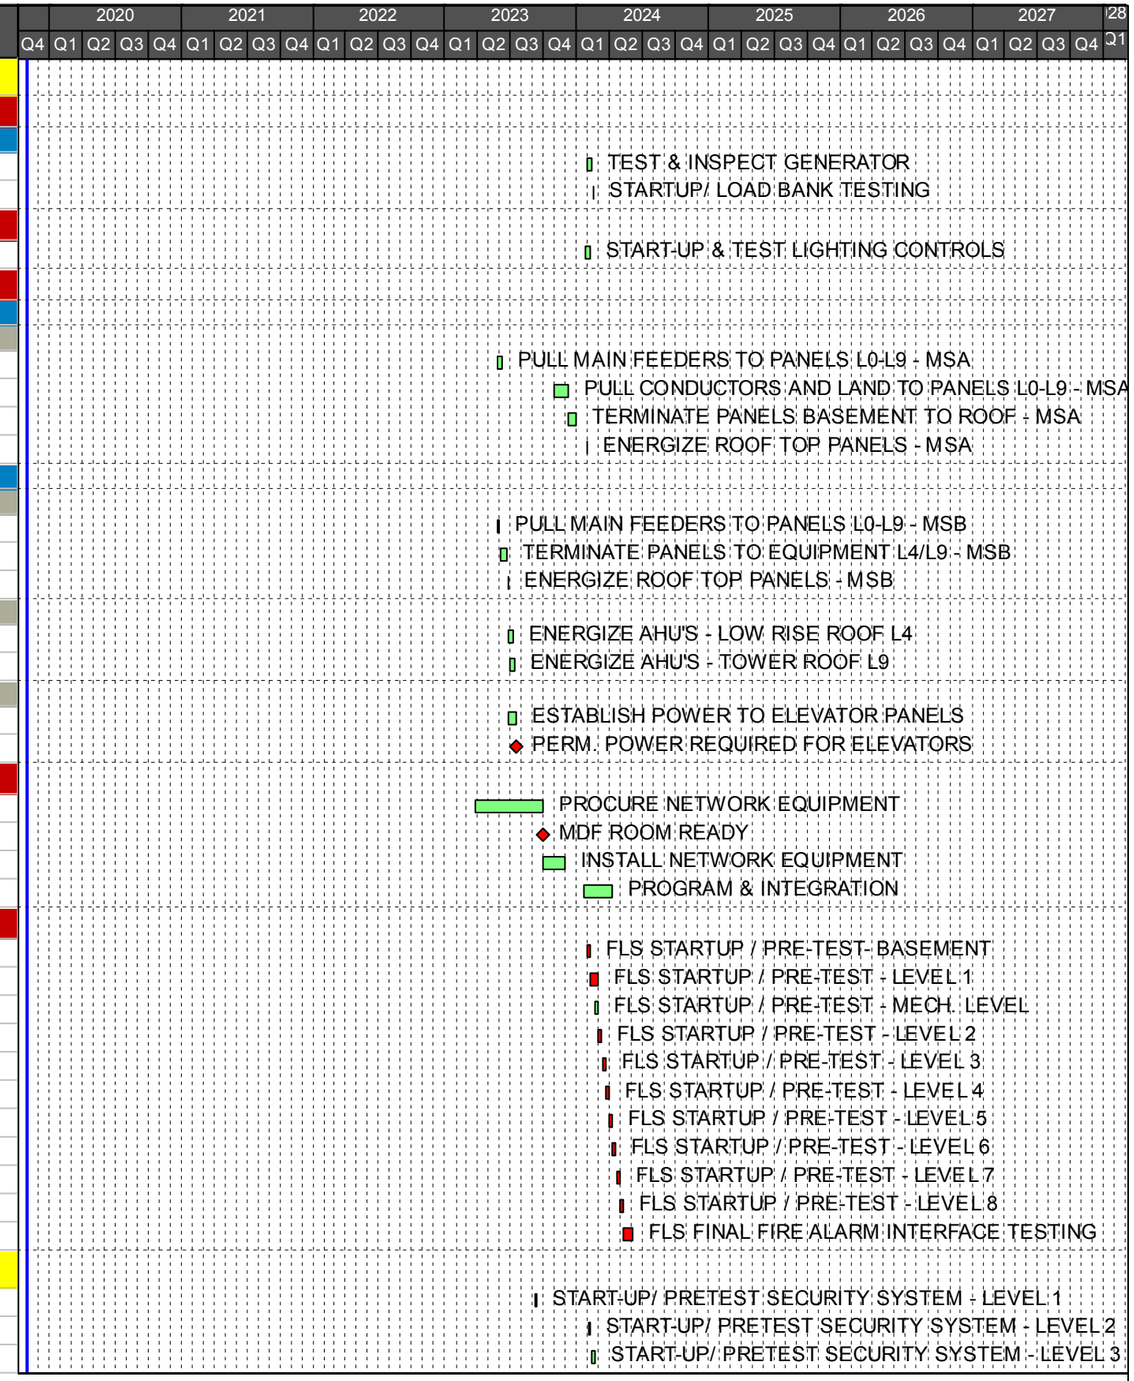

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21

Activity ID	Activity Name	Original Duration	Start	Finish
A5630	START-UP/ PRETEST SECURITY SYSTEM - LEVEL 4	5	27-Feb-24	04-Mar-24
A5640	START-UP/ PRETEST SECURITY SYSTEM - LEVEL 5	5	07-Mar-24	13-Mar-24
A5650	START-UP/ PRETEST SECURITY SYSTEM - LEVEL 6	5	18-Mar-24	22-Mar-24
A5660	START-UP/ PRETEST SECURITY SYSTEM - LEVEL 7	5	27-Mar-24	02-Apr-24
A5960	START-UP/ PRETEST SECURITY SYSTEM - LEVEL 8	5	03-Apr-24	09-Apr-24
A5970	START-UP/ PRETEST SECURITY SYSTEM - LEVEL 9	5	10-Apr-24	16-Apr-24
FINAL CLOSEOUT AND INSPECTIONS				
A2275	FIRE/LIFE SAFETY TESTING & INSPECTIONS	10	02-Jul-24	16-Jul-24
A2355	FINAL PUNCHLIST & CORRECTIONS	20	17-Jul-24	13-Aug-24
A1530	RAIN DAY IMPACT ALLOWANCE (65CD's X .714 = 46WD's)	46	14-Aug-24	18-Oct-24
A1540	SUBSTANTIAL COMPLETION	0		18-Oct-24
A1550	AVAILABLE FOR OWNER OCCUPANCY	0		18-Oct-24*
A1560	PROJECT CLOSEOUT	20	21-Oct-24	15-Nov-24
A1570	FINAL PROJECT COMPLETION	0		15-Nov-24

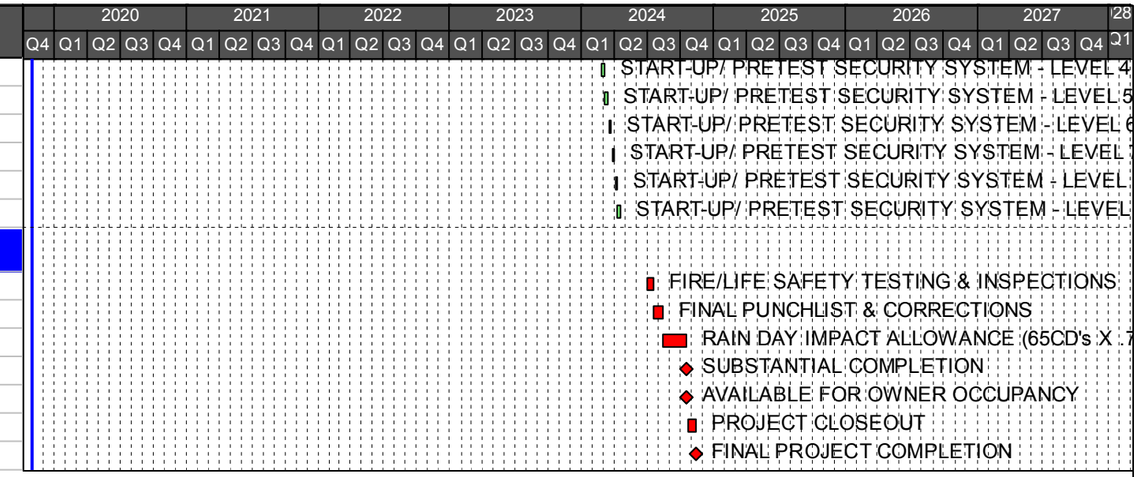

Remaining Level of Effort
Actual Level of Effort
Remaining Work
Critical Remaining Work
Actual Work
Secondary Baseline

New Modesto Courthouse - Master - Baseline Development
PRELIMINARY SCHEDULE - UNDER DEVELOPMENT

Data Date: 01-Nov-19
Issue Date: 02-Jun-21
